Hadley 3 Week Schedule (Interior)
3-19-2016

ID	Task Name	Duration	Start
1	**MEP Roof Down**	**127 days?**	**Tue 3/8/16**
2	**L5 Zone 1 (532-561)**	**79 days?**	**Tue 3/8/16**
3	Hang and tape soffits/Texture/PV/	7 days	Tue 3/8/16
4	Paint	2 days	Thu 3/17/16
5	Gypcrete	3 days	Mon 3/21/16
6	Gypcrete dry time	10 days	Thu 3/24/16
7	Electrical trim	5 days	Thu 3/31/16
8	Fire/Sprinkler Trim	1 day?	Thu 3/31/16
9	Install cabinets	6 days	Mon 4/4/16
10	Install Flooring	5 days	Tue 4/12/16
11	Install counter tops	3 days	Tue 4/19/16
12	Intsall Backsplash	3 days	Fri 4/22/16
13	Doors and Millwork	5 days	Wed 4/27/16
14	Paint doors and millwork	10 days	Wed 5/4/16
15	Closet Shelves	3 days	Wed 5/18/16
16	Deliver Appliances	3 days	Wed 5/18/16
17	Plumbing trim	4 days	Mon 5/23/16
18	Final Paint Walls	3 days	Fri 5/27/16
19	Window coverings	2 days	Wed 6/1/16
20	Final Clean	6 days	Fri 6/3/16
21	Punch List	7 days	Mon 6/13/16
22	Fluff Clean	3 days	Wed 6/22/16
23			
24	**L4 Zone 1 (432-461)**	**81 days?**	**Thu 3/10/16**
25	Drywall Hang/Tape	5 days	Thu 3/10/16
26	Hang and tape soffits/Texture/PV/	5 days	Thu 3/17/16
27	Paint	2 days	Thu 3/24/16
28	Gypcrete	3 days	Mon 3/28/16
29	Gypcrete dry time	10 days	Thu 3/31/16
30	Electrical trim	5 days	Thu 4/7/16
31	Fire/Sprinkler Trim	1 day?	Thu 4/7/16
32	Install cabinets	6 days	Mon 4/11/16
33	Install Flooring	5 days	Tue 4/19/16
34	Install counter tops	3 days	Tue 4/26/16
35	Intsall Backsplash	3 days	Fri 4/29/16
36	Doors and Millwork	5 days	Wed 5/4/16

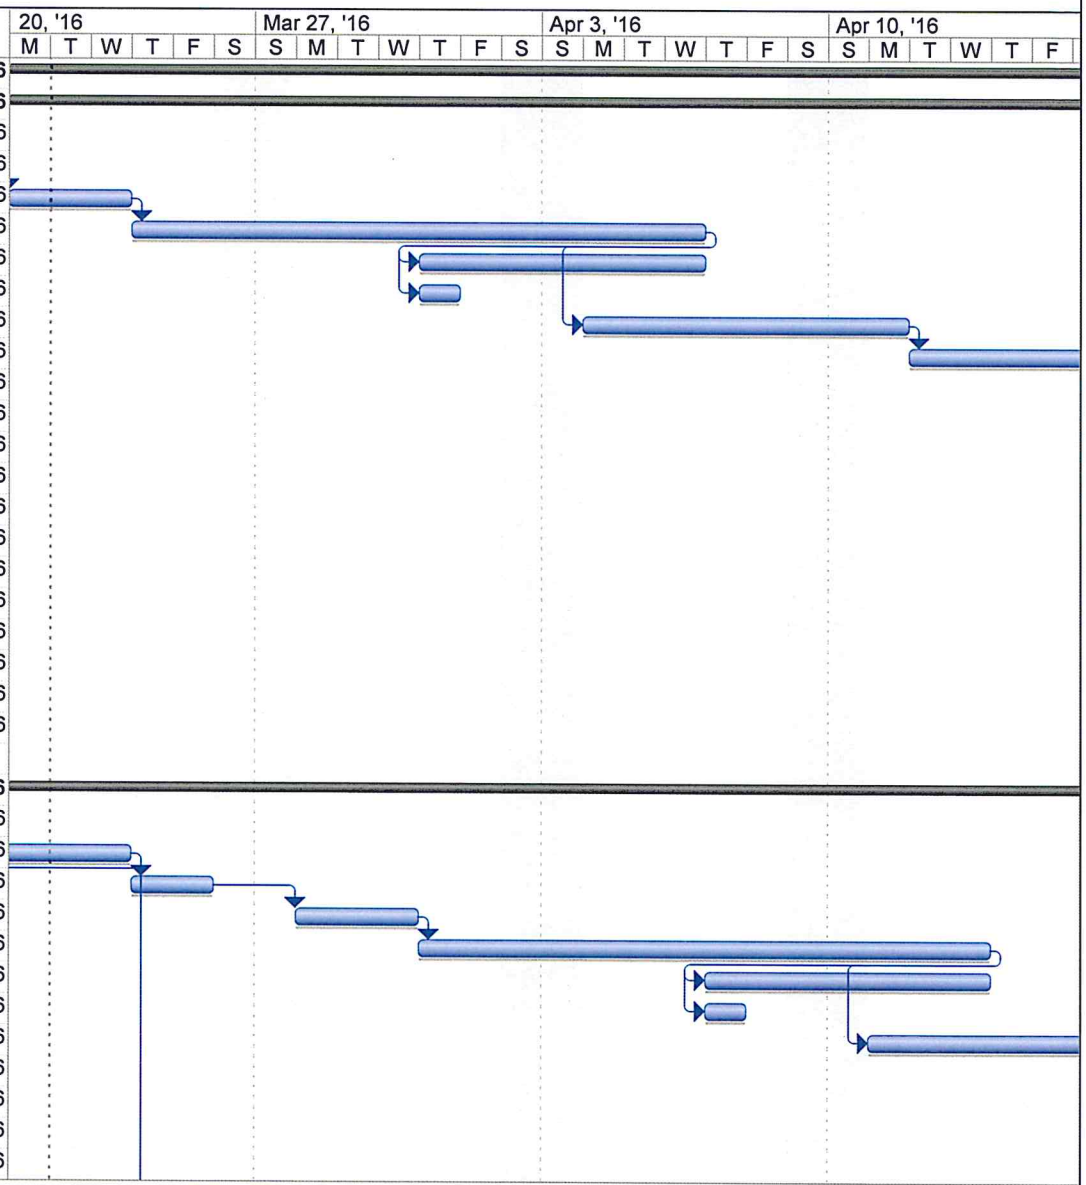

Project: MI Finish 3-19
Date: Tue 3/22/16

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

Hadley 3 Week Schedule (Interior)
3-19-2016

ID	Task Name	Duration	Start
37	Paint doors and millwork	10 days	Wed 5/11/16
38	Closet Shelves	3 days	Wed 5/25/16
39	Deliver Appliances	3 days	Wed 5/25/16
40	Plumbing trim	4 days	Mon 5/30/16
41	Final Paint Walls	3 days	Fri 6/3/16
42	Window coverings	2 days	Wed 6/8/16
43	Final Clean	5 days	Fri 6/10/16
44	Punch List	7 days	Fri 6/17/16
45	Fluff Clean	3 days	Tue 6/28/16
46			
47	**L6 Zone 1 (632-661)**	**82 days?**	**Thu 3/17/16**
48	Drywall Hang/Tape	5 days	Thu 3/17/16
49	Hang and tape soffits/Texture/PV/	5 days	Thu 3/24/16
50	Paint	2 days	Thu 3/31/16
51	Gypcrete	3 days	Mon 4/4/16
52	Gypcrete dry time	10 days	Thu 4/7/16
53	Electrical trim	5 days	Thu 4/14/16
54	Fire/Sprinkler Trim	1 day?	Thu 4/14/16
55	Install cabinets	6 days	Mon 4/18/16
56	Install Flooring	5 days	Tue 4/26/16
57	Install counter tops	3 days	Tue 5/3/16
58	Intsall Backsplash	3 days	Fri 5/6/16
59	Doors and Millwork	5 days	Wed 5/11/16
60	Paint doors and millwork	10 days	Wed 5/18/16
61	Closet Shelves	3 days	Wed 6/1/16
62	Deliver Appliances	3 days	Wed 6/1/16
63	Plumbing trim	4 days	Mon 6/6/16
64	Final Paint Walls	3 days	Fri 6/10/16
65	Window coverings	2 days	Wed 6/15/16
66	Final Clean	6 days	Fri 6/17/16
67	Punch List	7 days	Mon 6/27/16
68	Fluff Clean	3 days	Wed 7/6/16
69			
70	**L3 Zone 1 (332-360)**	**81 days?**	**Mon 3/14/16**
71	Insulation Inspection	1 day	Mon 3/14/16
72	Drywall Hang/Tape	10 days	Tue 3/15/16

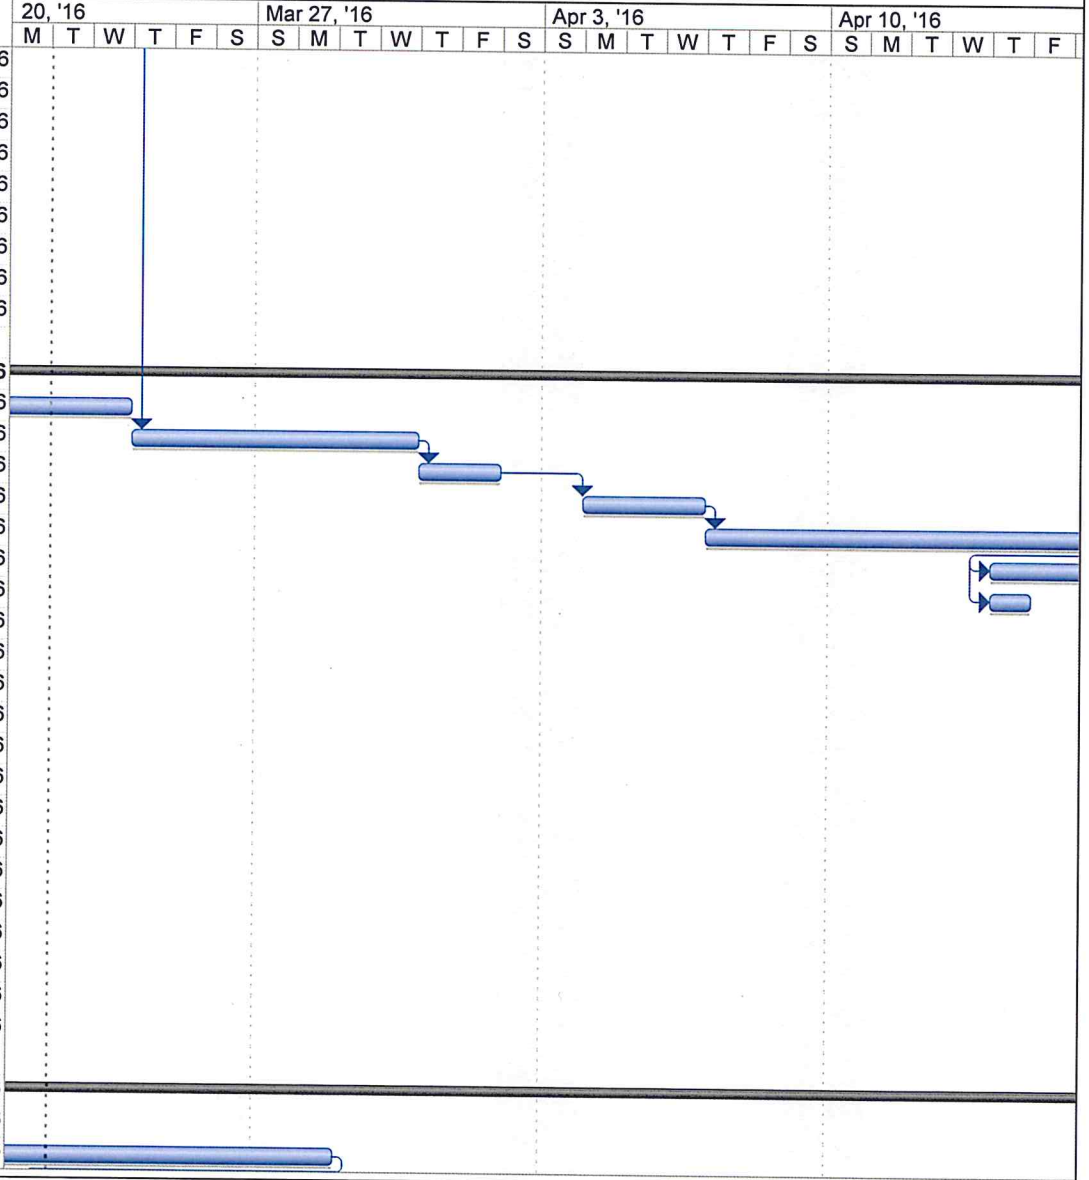

Project: MI Finish 3-19
Date: Tue 3/22/16

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

Hadley 3 Week Schedule (Interior)
3-19-2016

ID	Task Name	Duration	Start
73	Frame soffits	2 days	Tue 3/22/16
74	Electrical at soffits	1 day	Thu 3/24/16
75	Vent soffits	2 days	Fri 3/25/16
76	HVAC/ Electrical inspection at sof	1 day	Tue 3/29/16
77	Hang and tape soffits/Texture/PV/	5 days	Wed 3/30/16
78	Paint	3 days	Wed 4/6/16
79	Electrical trim	5 days	Mon 4/11/16
80	Fire/Sprinkler Trim	1 day?	Mon 4/11/16
81	Install cabinets	6 days	Tue 4/12/16
82	Install Flooring	5 days	Wed 4/20/16
83	Install counter tops	3 days	Wed 4/27/16
84	Intsall Backsplash	3 days	Mon 5/2/16
85	Doors and Millwork	5 days	Thu 5/5/16
86	Paint doors and millwork	10 days	Thu 5/12/16
87	Closet Shelves	3 days	Thu 5/26/16
88	Deliver Appliances	3 days	Thu 5/26/16
89	Plumbing trim	4 days	Tue 5/31/16
90	Final Paint Walls	3 days	Mon 6/6/16
91	Window coverings	2 days	Thu 6/9/16
92	Final Clean	6 days	Mon 6/13/16
93	Punch List	7 days	Tue 6/21/16
94	Fluff Clean	3 days	Thu 6/30/16
95			
96	**L5 Zone 2 (521-531)**	**96 days?**	**Thu 3/17/16**
97	Fire Caulk	2 days	Thu 3/17/16
98	Install tubs	2 days	Thu 3/17/16
99	Framing inspection	1 day	Mon 3/21/16
100	Insulation	3 days	Tue 3/22/16
101	Insulation Inspection	1 day	Fri 3/25/16
102	Drywall Hang/Tape	5 days	Mon 3/28/16
103	Frame soffits	2 days	Thu 3/31/16
104	Electrical at soffits	1 day	Mon 4/4/16
105	Vent soffits	2 days	Tue 4/5/16
106	HVAC/ Electrical inspection at sof	1 day	Thu 4/7/16
107	Hang and tape soffits/Texture/PV/	7 days	Fri 4/8/16
108	Paint	3 days	Tue 4/19/16

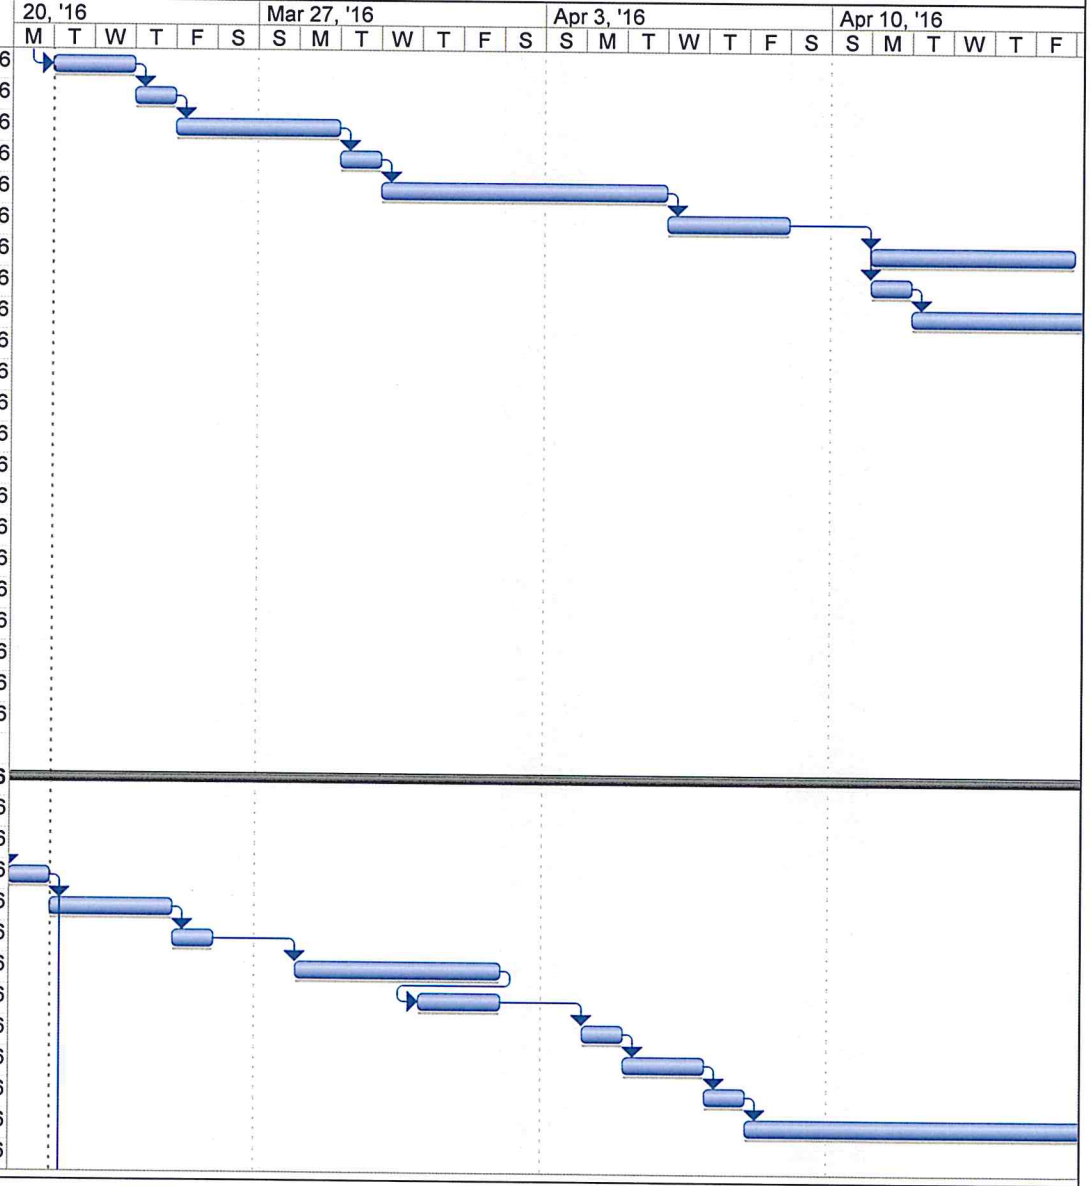

Project: MI Finish 3-19
Date: Tue 3/22/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
3-19-2016

ID	Task Name	Duration	Start
109	Gypcrete	3 days	Fri 4/22/16
110	Gypcrete dry time	10 days	Wed 4/27/16
111	Electrical trim	5 days	Wed 5/4/16
112	Fire/Sprinkler Trim	1 day?	Wed 5/4/16
113	Install cabinets	6 days	Fri 5/6/16
114	Install Flooring	5 days	Mon 5/16/16
115	Install counter tops	3 days	Mon 5/23/16
116	Intsall Backsplash	3 days	Thu 5/26/16
117	Doors and Millwork	5 days	Tue 5/31/16
118	Paint doors and millwork	10 days	Tue 6/7/16
119	Closet Shelves	3 days	Tue 6/21/16
120	Deliver Appliances	3 days	Tue 6/21/16
121	Plumbing trim	4 days	Fri 6/24/16
122	Final Paint Walls	3 days	Thu 6/30/16
123	Window coverings	2 days	Tue 7/5/16
124	Final Clean	6 days	Thu 7/7/16
125	Punch List	7 days	Fri 7/15/16
126	Fluff Clean	3 days	Tue 7/26/16
127			
128	**L4 Zone 2 (421-431)**	**94 days?**	**Tue 3/22/16**
129	Fire Caulk	2 days	Tue 3/22/16
130	Install tubs	2 days	Tue 3/22/16
131	Framing inspection	1 day	Thu 3/24/16
132	Insulation	3 days	Fri 3/25/16
133	Insulation Inspection	1 day	Wed 3/30/16
134	Drywall Hang/Tape	5 days	Thu 3/31/16
135	Frame soffits	2 days	Tue 4/5/16
136	Electrical at soffits	1 day	Thu 4/7/16
137	Vent soffits	2 days	Fri 4/8/16
138	HVAC/ Electrical inspection at sof	1 day	Tue 4/12/16
139	Hang and tape soffits/Texture/PV/	5 days	Wed 4/13/16
140	Paint	3 days	Wed 4/20/16
141	Gypcrete	3 days	Mon 4/25/16
142	Gypcrete dry time	10 days	Thu 4/28/16
143	Electrical trim	5 days	Thu 5/5/16
144	Fire/Sprinkler Trim	1 day?	Thu 5/5/16

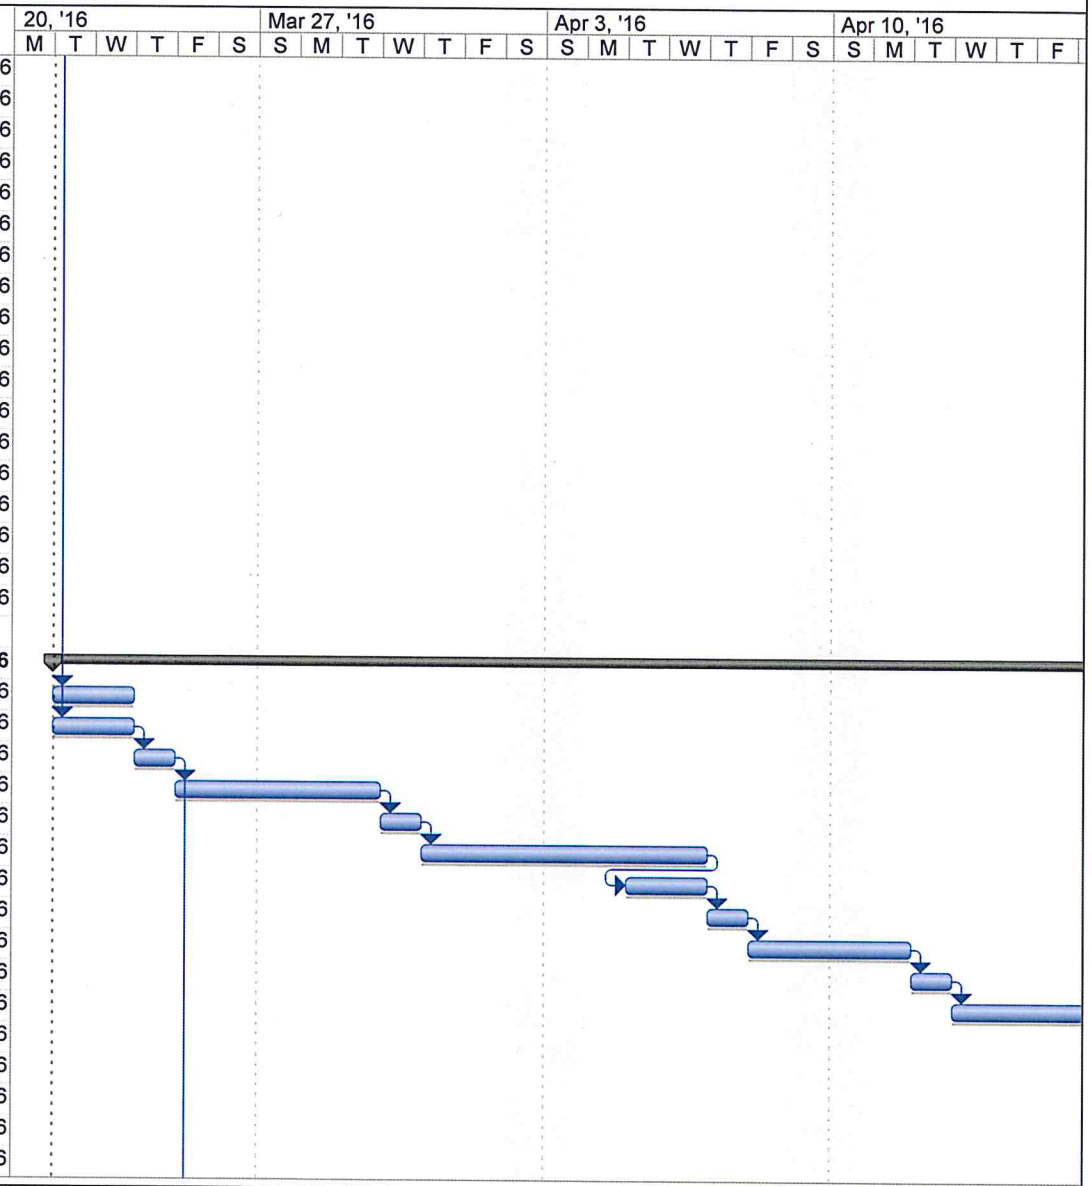

Project: MI Finish 3-19
Date: Tue 3/22/16

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

Hadley 3 Week Schedule (Interior)
3-19-2016

ID	Task Name	Duration	Start
145	Install cabinets	6 days	Mon 5/9/16
146	Install Flooring	5 days	Tue 5/17/16
147	Install counter tops	3 days	Tue 5/24/16
148	Intsall Backsplash	3 days	Fri 5/27/16
149	Doors and Millwork	5 days	Wed 6/1/16
150	Paint doors and millwork	10 days	Wed 6/8/16
151	Closet Shelves	3 days	Wed 6/22/16
152	Deliver Appliances	3 days	Wed 6/22/16
153	Plumbing trim	4 days	Mon 6/27/16
154	Final Paint Walls	3 days	Fri 7/1/16
155	Window coverings	2 days	Wed 7/6/16
156	Final Clean	6 days	Fri 7/8/16
157	Punch List	7 days	Mon 7/18/16
158	Fluff Clean	3 days	Wed 7/27/16
159			
160	**L6 Zone 2 (621-631)**	**94 days?**	**Fri 3/25/16**
161	Fire Caulk	2 days	Fri 3/25/16
162	Install tubs	2 days	Fri 3/25/16
163	Framing inspection	1 day	Tue 3/29/16
164	Insulation	3 days	Wed 3/30/16
165	Insulation Inspection	1 day	Mon 4/4/16
166	Drywall Hang/Tape	5 days	Tue 4/5/16
167	Frame soffits	2 days	Fri 4/8/16
168	Electrical at soffits	1 day	Tue 4/12/16
169	Vent soffits	2 days	Wed 4/13/16
170	HVAC/ Electrical inspection at sof	1 day	Fri 4/15/16
171	Hang and tape soffits/Texture/PV/	5 days	Mon 4/18/16
172	Paint	3 days	Mon 4/25/16
173	Gypcrete	3 days	Thu 4/28/16
174	Gypcrete dry time	10 days	Tue 5/3/16
175	Electrical trim	5 days	Tue 5/10/16
176	Fire/Sprinkler Trim	1 day?	Mon 5/9/16
177	Install cabinets	6 days	Thu 5/12/16
178	Install Flooring	5 days	Fri 5/20/16
179	Install counter tops	3 days	Fri 5/27/16
180	Intsall Backsplash	3 days	Wed 6/1/16

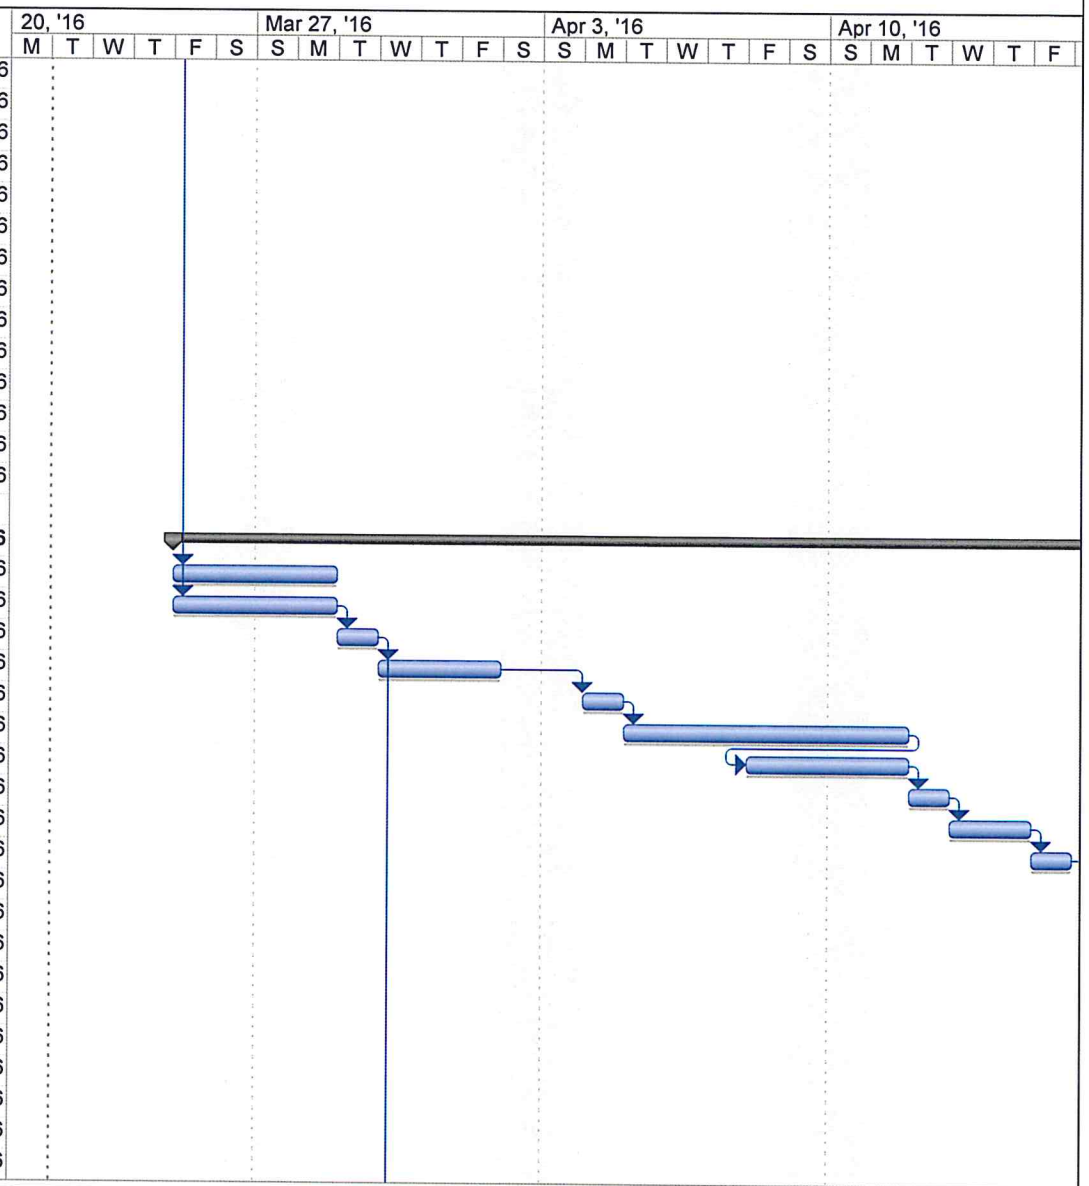

Project: MI Finish 3-19
Date: Tue 3/22/16

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

Hadley 3 Week Schedule (Interior)
3-19-2016

ID	Task Name	Duration	Start
181	Doors and Millwork	5 days	Mon 6/6/16
182	Paint doors and millwork	10 days	Mon 6/13/16
183	Closet Shelves	3 days	Mon 6/27/16
184	Deliver Appliances	3 days	Mon 6/27/16
185	Plumbing trim	4 days	Thu 6/30/16
186	Final Paint Walls	3 days	Wed 7/6/16
187	Window coverings	2 days	Mon 7/11/16
188	Final Clean	6 days	Wed 7/13/16
189	Punch List	7 days	Thu 7/21/16
190	Fluff Clean	3 days	Mon 8/1/16
191			
192	**L3 Zone 2 (321-331)**	**87 days?**	**Wed 3/30/16**
193	Fire Caulk	2 days	Wed 3/30/16
194	Install tubs	2 days	Wed 3/30/16
195	Framing inspection	1 day	Fri 4/1/16
196	Insulation	3 days	Mon 4/4/16
197	Insulation Inspection	1 day	Thu 4/7/16
198	Drywall Hang/Tape	10 days	Fri 4/8/16
199	Frame soffits	2 days	Fri 4/15/16
200	Electrical at soffits	1 day	Tue 4/19/16
201	Vent soffits	2 days	Wed 4/20/16
202	HVAC/ Electrical inspection at sof	1 day	Fri 4/22/16
203	Hang and tape soffits/Texture/PV/	5 days	Mon 4/25/16
204	Paint	3 days	Mon 5/2/16
205	Electrical trim	5 days	Thu 5/5/16
206	Fire/Sprinkler Trim	1 day?	Thu 5/5/16
207	Install cabinets	6 days	Fri 5/6/16
208	Install Flooring	5 days	Mon 5/16/16
209	Install counter tops	3 days	Mon 5/23/16
210	Intsall Backsplash	3 days	Thu 5/26/16
211	Doors and Millwork	5 days	Tue 5/31/16
212	Paint doors and millwork	10 days	Tue 6/7/16
213	Closet Shelves	3 days	Tue 6/21/16
214	Deliver Appliances	3 days	Tue 6/21/16
215	Plumbing trim	4 days	Fri 6/24/16
216	Final Paint Walls	3 days	Thu 6/30/16

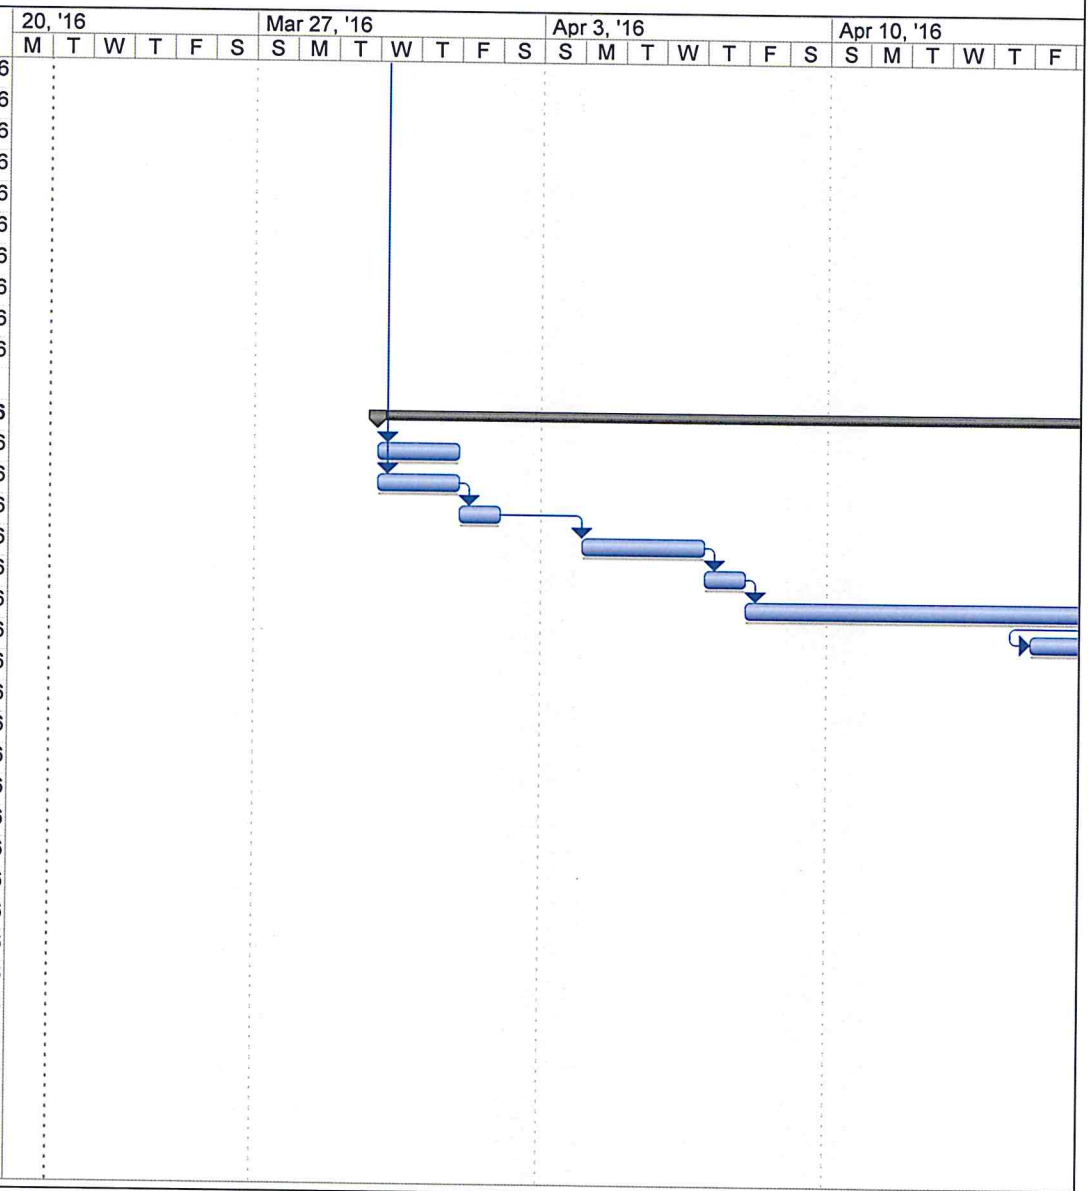

Project: MI Finish 3-19
Date: Tue 3/22/16

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

Hadley 3 Week Schedule (Interior)
3-19-2016

ID	Task Name	Duration	Start
217	Window coverings	2 days	Tue 7/5/16
218	Final Clean	6 days	Thu 7/7/16
219	Punch List	7 days	Fri 7/15/16
220	Fluff Clean	3 days	Tue 7/26/16
221			
222	**L5 Zone 3 (501-519)**	**106 days?**	**Thu 3/17/16**
223	Sandblast	7 days	Thu 3/17/16
224	Plumbing/Electrical/Lowvolt Inspe	1 day	Mon 3/28/16
225	Fire Caulk	2 days	Tue 3/29/16
226	Insulate for pre rock at tubs	1 day	Thu 3/31/16
227	Pre rock for tubs/ accoustic	1 day	Fri 4/1/16
228	Framing inspection	1 day	Mon 4/4/16
229	Insulation	3 days	Tue 4/5/16
230	Insulation Inspection	1 day	Fri 4/8/16
231	Drywall Hang/Tape	10 days	Mon 4/11/16
232	Frame soffits	2 days	Mon 4/18/16
233	Electrical at soffits	1 day	Wed 4/20/16
234	Vent soffits	2 days	Thu 4/21/16
235	HVAC/ Electrical inspection at sof	1 day	Mon 4/25/16
236	Hang and tape soffits/Texture/PV/	5 days	Tue 4/26/16
237	Paint	3 days	Tue 5/3/16
238	Gypcrete	3 days	Fri 5/6/16
239	Gypcrete dry time	10 days	Wed 5/11/16
240	Electrical trim	5 days	Wed 5/18/16
241	Fire/Sprinkler Trim	1 day?	Wed 5/18/16
242	Install cabinets	6 days	Fri 5/20/16
243	Install Flooring	5 days	Mon 5/30/16
244	Install counter tops	3 days	Mon 6/6/16
245	Intsall Backsplash	3 days	Thu 6/9/16
246	Doors and Millwork	5 days	Tue 6/14/16
247	Paint doors and millwork	10 days	Tue 6/21/16
248	Closet Shelves	3 days	Tue 7/5/16
249	Deliver Appliances	3 days	Tue 7/5/16
250	Plumbing trim	4 days	Fri 7/8/16
251	Final Paint Walls	3 days	Thu 7/14/16
252	Window coverings	2 days	Tue 7/19/16

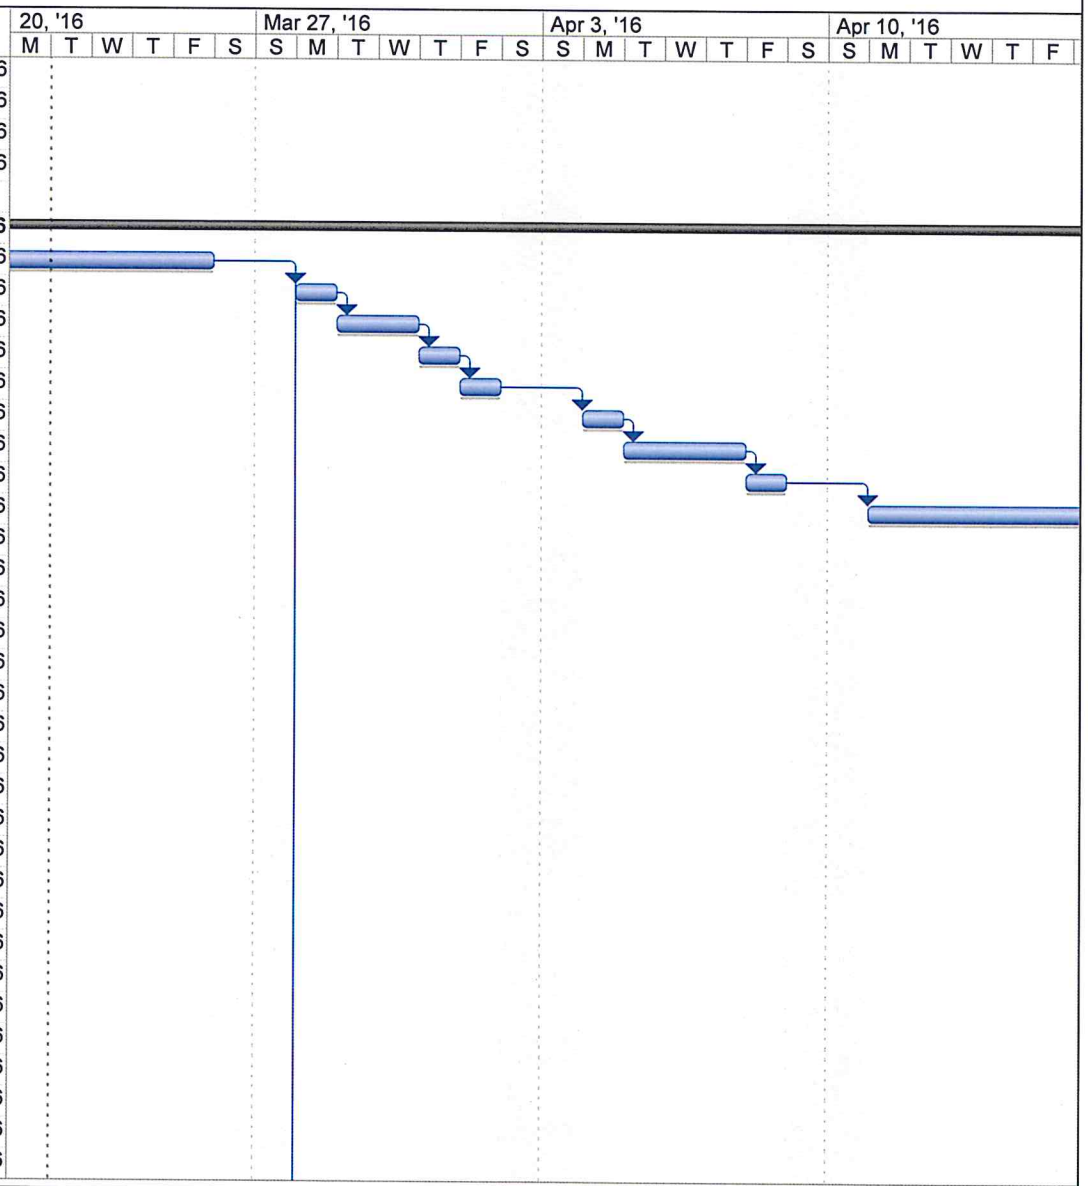

Project: MI Finish 3-19
Date: Tue 3/22/16

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline
