Hadley 3 Week Schedule (Interior)
5-16-2016

INTERIOR

ID	Task Name	Duration	Start	Finish	Predecessors
1	**MEP Roof Down**	**77 days?**	**Tue 3/8/16**	**Wed 6/22/16**	
2	**L5 Zone 1 (532-561)**	**70 days?**	**Tue 3/8/16**	**Mon 6/13/16**	
3	Hang and tape soffits/Texture/PV/	7 days	Tue 3/8/16	Wed 3/16/16	
4	Paint	2 days	Thu 3/17/16	Fri 3/18/16	3
5	Gypcrete	3 days	Mon 3/21/16	Wed 3/23/16	4
6	Gypcrete dry time	10 days	Thu 3/24/16	Wed 4/6/16	5
7	Electrical trim	5 days	Thu 3/31/16	Wed 4/6/16	6FS-5 days
8	Fire/Sprinkler Trim	1 day?	Thu 3/31/16	Thu 3/31/16	6FS-5 days
9	Install cabinets	8 days	Mon 4/4/16	Wed 4/13/16	6FS-3 days
10	Measure Counter top	1 day	Thu 4/14/16	Thu 4/14/16	9
11	Install Flooring	5 days	Wed 4/13/16	Tue 4/19/16	9FS-1 day
12	Install counter tops	3 days	Thu 4/21/16	Mon 4/25/16	9FS+5 days
13	Intsall Backsplash	3 days	Tue 4/26/16	Thu 4/28/16	12
14	Doors and Millwork	5 days	Fri 4/29/16	Thu 5/5/16	13
15	Drywall Repair ADA	10 days	Fri 5/6/16	Thu 5/19/16	14
16	Paint doors and millwork	10 days	Fri 5/13/16	Thu 5/26/16	15FS-5 days
17	Closet Shelves	3 days	Fri 5/27/16	Tue 5/31/16	16
18	Deliver Appliances	3 days	Fri 5/27/16	Tue 5/31/16	16
19	Plumbing trim	4 days	Wed 6/1/16	Mon 6/6/16	18
20	Final Paint Walls	3 days	Tue 6/7/16	Thu 6/9/16	19
21	Window coverings	2 days	Fri 6/10/16	Mon 6/13/16	20
22					
23	**L4 Zone 1 (432-461)**	**70 days**	**Thu 3/10/16**	**Wed 6/15/16**	
24	Drywall Hang/Tape	5 days	Thu 3/10/16	Wed 3/16/16	3FS-5 days
25	Hang and tape soffits/Texture/PV/	5 days	Thu 3/17/16	Wed 3/23/16	3
26	Paint	2 days	Mon 3/28/16	Tue 3/29/16	25
27	Gypcrete	3 days	Wed 3/30/16	Fri 4/1/16	26
28	Gypcrete dry time	15 days	Mon 4/4/16	Fri 4/22/16	27
29	Electrical trim	5 days	Mon 4/18/16	Fri 4/22/16	28FS-5 days
30	Fire/Sprinkler Trim	5 days	Mon 4/18/16	Fri 4/22/16	28FS-5 days
31	Install cabinets	6 days	Mon 4/25/16	Mon 5/2/16	28
32	Measure Counter top	1 day	Tue 5/3/16	Tue 5/3/16	31
33	Install Flooring	5 days	Wed 5/4/16	Tue 5/10/16	32
34	Install counter tops	3 days	Wed 5/11/16	Fri 5/13/16	33
35	Intsall Backsplash	3 days	Mon 5/16/16	Wed 5/18/16	34
36	Doors and Millwork	5 days	Thu 5/19/16	Wed 5/25/16	35

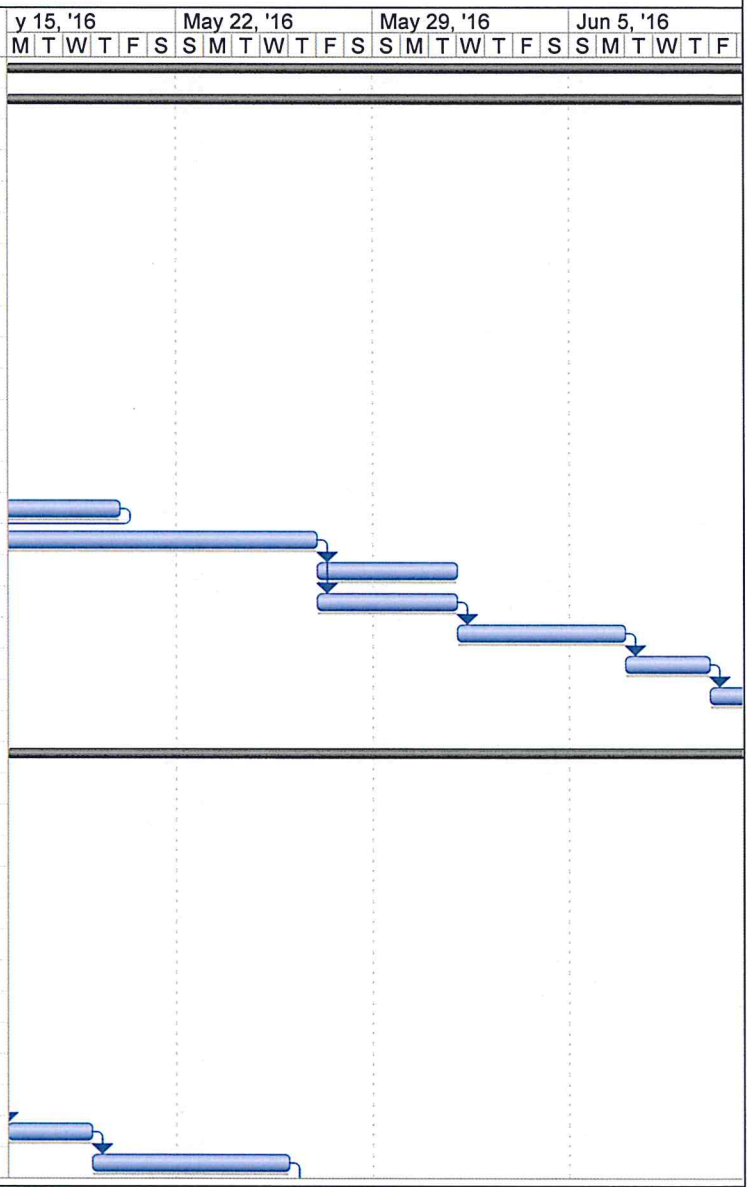

Project: MI Finish 5-16P
Date: Mon 5/16/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
5-16-2016

ID	Task Name	Duration	Start	Finish	Predecessors
37	Drywall Repair ADA	5 days	Thu 5/26/16	Wed 6/1/16	36
38	Paint doors and millwork	10 days	Thu 6/2/16	Wed 6/15/16	37
39					
40	**L6 Zone 1 (632-661)**	**70 days**	**Thu 3/17/16**	**Wed 6/22/16**	
41	Drywall Hang/Tape	5 days	Thu 3/17/16	Wed 3/23/16	25FS-5 days
42	Hang and tape soffits/Texture/PV/	9 days	Thu 3/24/16	Tue 4/5/16	25
43	Paint	3 days	Wed 4/6/16	Fri 4/8/16	42
44	Gypcrete	3 days	Mon 4/11/16	Wed 4/13/16	43
45	Gypcrete dry time	12 days	Thu 4/14/16	Fri 4/29/16	44
46	Electrical trim	5 days	Mon 4/25/16	Fri 4/29/16	45FS-5 days
47	Fire/Sprinkler Trim	1 day	Mon 4/25/16	Mon 4/25/16	45FS-5 days
48	Install cabinets	6 days	Mon 5/2/16	Mon 5/9/16	45
49	Install Flooring	5 days	Tue 5/10/16	Mon 5/16/16	48
50	Install counter tops	3 days	Tue 5/17/16	Thu 5/19/16	49
51	Intsall Backsplash	3 days	Fri 5/20/16	Tue 5/24/16	50
52	Drywall Repair ADA	6 days	Wed 5/25/16	Wed 6/1/16	51
53	Doors and Millwork	5 days	Thu 6/2/16	Wed 6/8/16	52
54	Paint doors and millwork	10 days	Thu 6/9/16	Wed 6/22/16	53
55					
56	**L3 Zone 1 (332-360)**	**68 days**	**Mon 3/14/16**	**Wed 6/15/16**	
57	Insulation Inspection	1 day	Mon 3/14/16	Mon 3/14/16	3FS-3 days
58	Drywall Hang/Tape	10 days	Tue 3/15/16	Mon 3/28/16	57
59	Frame soffits	2 days	Tue 3/22/16	Wed 3/23/16	58FS-5 days
60	Electrical at soffits	1 day	Thu 3/24/16	Thu 3/24/16	59
61	Vent soffits	2 days	Mon 3/28/16	Tue 3/29/16	60
62	HVAC/ Electrical inspection at sof	1 day	Wed 3/30/16	Wed 3/30/16	61
63	Hang and tape soffits/Texture/PV/	8 days	Thu 3/31/16	Mon 4/11/16	62
64	Paint	3 days	Tue 4/12/16	Thu 4/14/16	63
65	Electrical trim	5 days	Fri 4/15/16	Thu 4/21/16	64
66	Fire/Sprinkler Trim	1 day	Fri 4/15/16	Fri 4/15/16	64
67	Install cabinets	6 days	Tue 5/10/16	Tue 5/17/16	48
68	Install Flooring	5 days	Wed 5/18/16	Tue 5/24/16	67
69	Install counter tops	3 days	Wed 5/25/16	Fri 5/27/16	68
70	Intsall Backsplash	3 days	Mon 5/30/16	Wed 6/1/16	69
71	Drywall Repair ADA	5 days	Thu 6/2/16	Wed 6/8/16	70
72	Doors and Millwork	5 days	Thu 6/9/16	Wed 6/15/16	71

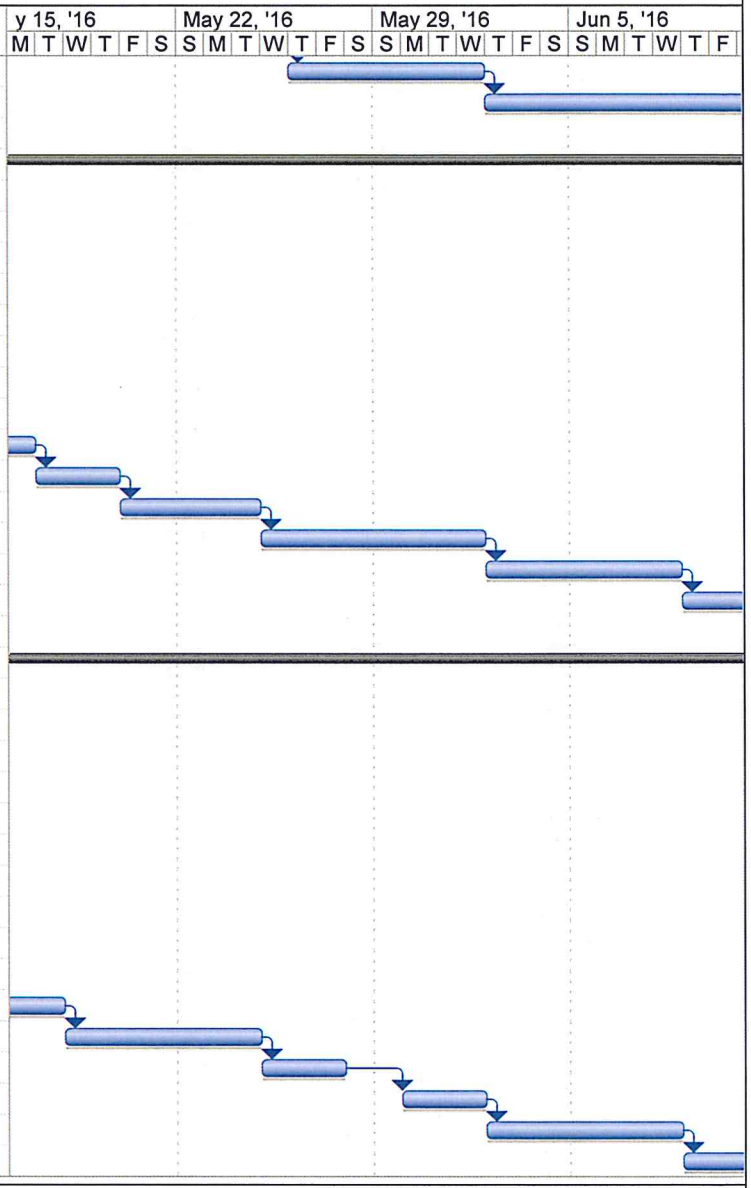

Project: MI Finish 5-16P
Date: Mon 5/16/16

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

Hadley 3 Week Schedule (Interior)
5-16-2016

ID	Task Name	Duration	Start	Finish	Predecessors
73					
74	**L5 Zone 2 (501-531)**	**61 days**	**Wed 3/30/16**	**Wed 6/22/16**	
75	Pre-rock at tubs	1 day	Wed 3/30/16	Wed 3/30/16	
76	Install tubs	3 days	Thu 3/31/16	Mon 4/4/16	75
77	Elec, Plmb Inspections	1 day	Tue 4/5/16	Tue 4/5/16	76
78	Fire Caulk	2 days	Wed 4/6/16	Thu 4/7/16	77
79	Framing inspection	1 day	Fri 4/8/16	Fri 4/8/16	78
80	Insulation	3 days	Mon 4/11/16	Wed 4/13/16	79
81	Insulation Inspection	1 day	Thu 4/14/16	Thu 4/14/16	80
82	Drywall Hang/Tape	6 days	Fri 4/15/16	Fri 4/22/16	81
83	Frame soffits	5 days	Fri 4/22/16	Thu 4/28/16	82FS-1 day
84	Electrical at soffits	2 days	Wed 4/27/16	Thu 4/28/16	83FS-2 days
85	Vent soffits	5 days	Wed 4/27/16	Tue 5/3/16	84FS-2 days
86	Firecaulk soffits	2 days	Mon 5/2/16	Tue 5/3/16	85FS-2 days
87	HVAC/ Electrical inspection at sof	1 day	Wed 5/4/16	Wed 5/4/16	86
88	Hang and tape soffits/Texture/PV/	11 days	Thu 5/5/16	Thu 5/19/16	87
89	Paint	4 days	Fri 5/20/16	Wed 5/25/16	88
90	Gypcrete	3 days	Thu 5/26/16	Mon 5/30/16	89
91	Gypcrete dry time	10 days	Tue 5/31/16	Mon 6/13/16	90
92	Electrical trim	5 days	Tue 6/7/16	Mon 6/13/16	91FS-5 days
93	Fire/Sprinkler Trim	3 days	Tue 6/7/16	Thu 6/9/16	91FS-5 days
94	Install cabinets	10 days	Thu 6/9/16	Wed 6/22/16	91FS-3 days
95					
96	**L4 Zone 2 (401-431)**	**59 days**	**Thu 3/31/16**	**Tue 6/21/16**	
97	Elec, Plmb RI	13 days	Thu 3/31/16	Mon 4/18/16	75
98	Install tubs	6 days	Mon 4/11/16	Mon 4/18/16	118
99	Elec, Plmb Inspections	1 day	Tue 4/19/16	Tue 4/19/16	98
100	Fire Caulk	2 days	Wed 4/20/16	Thu 4/21/16	99
101	Framing inspection	1 day	Fri 4/22/16	Fri 4/22/16	100
102	Insulation	4 days	Mon 4/25/16	Thu 4/28/16	101
103	Insulation Inspection	1 day	Fri 4/29/16	Fri 4/29/16	102
104	Drywall Hang/Tape	5 days	Mon 5/2/16	Fri 5/6/16	103
105	Frame soffits	5 days	Fri 5/6/16	Thu 5/12/16	104FS-1 day
106	Electrical at soffits	2 days	Wed 5/11/16	Thu 5/12/16	105FS-2 days
107	Vent soffits	5 days	Wed 5/11/16	Tue 5/17/16	106FS-2 days
108	Firecaulk soffits	2 days	Mon 5/16/16	Tue 5/17/16	107FS-2 days

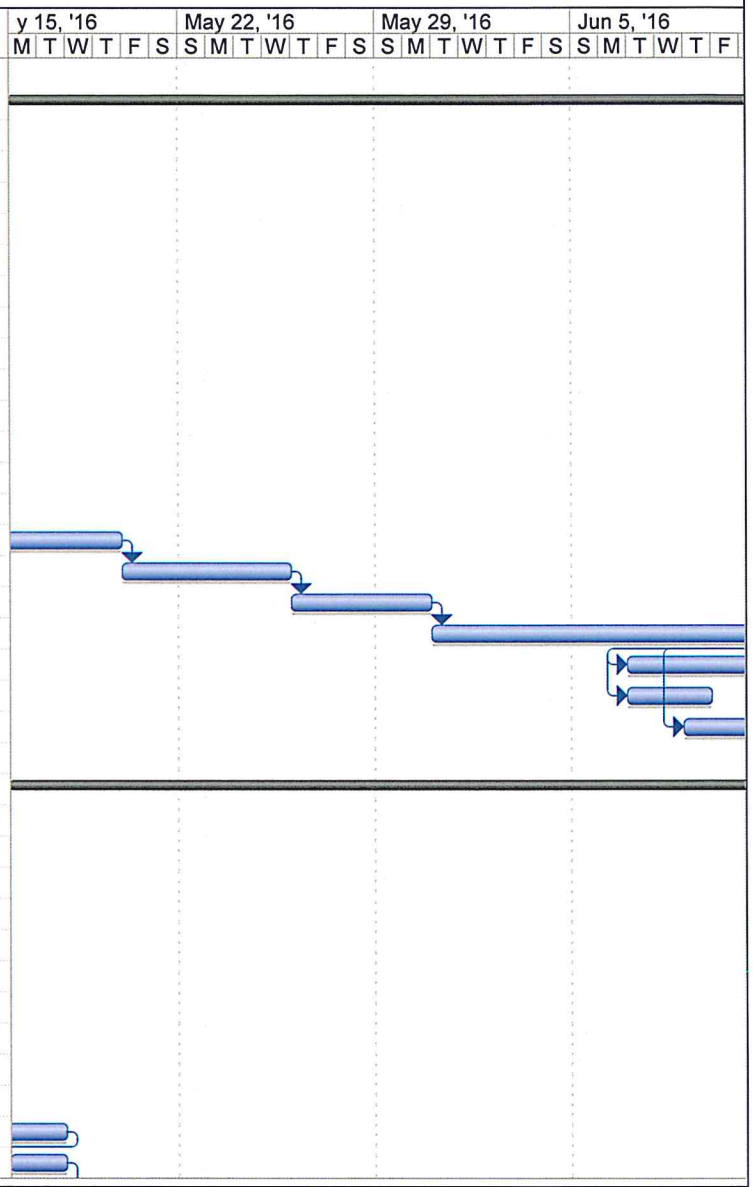

Project: MI Finish 5-16P
Date: Mon 5/16/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
5-16-2016

ID	Task Name	Duration	Start	Finish	Predecessors
109	HVAC/ Electrical inspection at soffits	1 day	Wed 5/18/16	Wed 5/18/16	108
110	Hang and tape soffits/Texture/PVA	7 days	Thu 5/19/16	Fri 5/27/16	109
111	Paint	4 days	Mon 5/30/16	Thu 6/2/16	110
112	Gypcrete	3 days	Fri 6/3/16	Tue 6/7/16	111
113	Gypcrete dry time	10 days	Wed 6/8/16	Tue 6/21/16	112
114					
115	**L6 Zone 2 (601-631)**	**53 days**	**Wed 3/30/16**	**Fri 6/10/16**	
116	Sandblast	4 days	Wed 3/30/16	Mon 4/4/16	
117	Elec, Plmb RI	10 days	Tue 4/19/16	Mon 5/2/16	97
118	Install tubs	4 days	Tue 4/5/16	Fri 4/8/16	76
119	Elec, Plmb Inspections	1 day	Tue 5/3/16	Tue 5/3/16	117
120	Fire Caulk	2 days	Wed 5/4/16	Thu 5/5/16	119
121	Framing inspection	1 day	Fri 5/6/16	Fri 5/6/16	120
122	Insulation	4 days	Mon 5/9/16	Thu 5/12/16	121
123	Insulation Inspection	1 day	Fri 5/13/16	Fri 5/13/16	122
124	Drywall Hang/Tape	5 days	Mon 5/16/16	Fri 5/20/16	123
125	Frame soffits	5 days	Fri 5/20/16	Thu 5/26/16	124FS-1 day
126	Electrical at soffits	2 days	Wed 5/25/16	Thu 5/26/16	125FS-2 days
127	Vent soffits	5 days	Wed 5/25/16	Tue 5/31/16	126FS-2 days
128	Firecaulk soffits	2 days	Mon 5/30/16	Tue 5/31/16	127FS-2 days
129	HVAC/ Electrical inspection at soffits	1 day	Wed 6/1/16	Wed 6/1/16	128
130	Hang and tape soffits/Texture/PVA	7 days	Thu 6/2/16	Fri 6/10/16	129
131					
132	**L3 Zone 2 (301-331)**	**51 days**	**Tue 4/5/16**	**Tue 6/14/16**	
133	Sandblast	5 days	Tue 4/5/16	Mon 4/11/16	116
134	Install tubs	5 days	Tue 4/19/16	Mon 4/25/16	98
135	elec rough in	10 days	Tue 5/3/16	Mon 5/16/16	117
136	Elec, Plmb Inspections	1 day	Tue 5/17/16	Tue 5/17/16	135
137	Fire Caulk	2 days	Wed 5/18/16	Thu 5/19/16	136
138	Framing inspection	1 day	Fri 5/20/16	Fri 5/20/16	137
139	Insulation	4 days	Mon 5/23/16	Thu 5/26/16	138
140	Insulation Inspection	1 day	Fri 5/27/16	Fri 5/27/16	139
141	Drywall Hang/Tape	5 days	Mon 5/30/16	Fri 6/3/16	140
142	Frame soffits	5 days	Fri 6/3/16	Thu 6/9/16	141FS-1 day
143	Electrical at soffits	2 days	Wed 6/8/16	Thu 6/9/16	142FS-2 days
144	Vent soffits	5 days	Wed 6/8/16	Tue 6/14/16	143FS-2 days

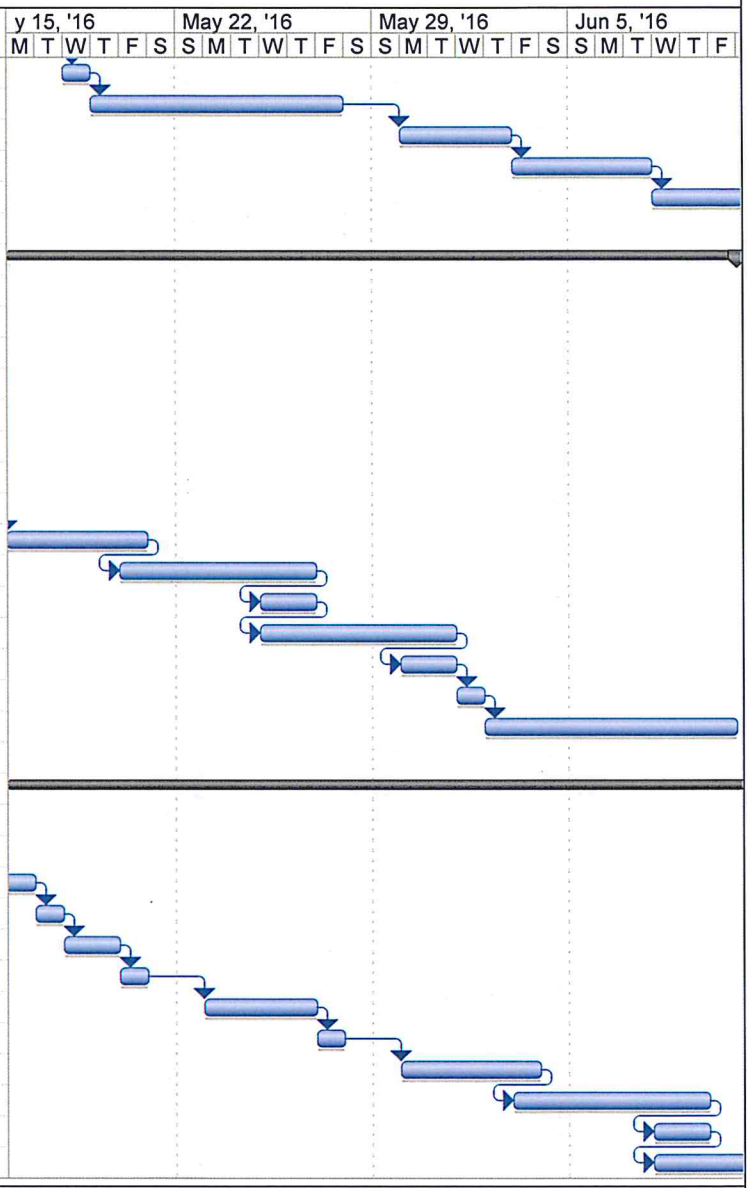

Project: MI Finish 5-16P
Date: Mon 5/16/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
