Hadley 3 Week Schedule (Interior)
5-31-2016

Interior

ID	Task Name	Duration	Start	Finish	Predecessors
1	**MEP Roof Down**	**84 days?**	**Tue 3/8/16**	**Fri 7/1/16**	
2	**L5 Zone 1 (532-561)**	**80 days?**	**Tue 3/8/16**	**Mon 6/27/16**	
3	Hang and tape soffits/Texture/PV/	7 days	Tue 3/8/16	Wed 3/16/16	
4	Paint	2 days	Thu 3/17/16	Fri 3/18/16	3
5	Gypcrete	3 days	Mon 3/21/16	Wed 3/23/16	4
6	Gypcrete dry time	10 days	Thu 3/24/16	Wed 4/6/16	5
7	Electrical trim	5 days	Thu 3/31/16	Wed 4/6/16	6FS-5 days
8	Fire/Sprinkler Trim	1 day?	Thu 3/31/16	Thu 3/31/16	6FS-5 days
9	Install cabinets	8 days	Mon 4/4/16	Wed 4/13/16	6FS-3 days
10	Measure Counter top	1 day	Thu 4/14/16	Thu 4/14/16	9
11	Install Flooring	5 days	Wed 4/13/16	Tue 4/19/16	9FS-1 day
12	Install counter tops	3 days	Thu 4/21/16	Mon 4/25/16	9FS+5 days
13	Intsall Backsplash	3 days	Tue 4/26/16	Thu 4/28/16	12
14	Doors and Millwork	5 days	Fri 4/29/16	Thu 5/5/16	13
15	Drywall Repair ADA	17 days	Fri 5/6/16	Mon 5/30/16	14
16	Paint doors and millwork	8 days	Tue 5/31/16	Thu 6/9/16	15
17	Closet Shelves	3 days	Fri 6/10/16	Tue 6/14/16	16
18	Deliver Appliances	3 days	Fri 6/10/16	Tue 6/14/16	16
19	Plumbing trim	4 days	Wed 6/15/16	Mon 6/20/16	18
20	Final Paint Walls	3 days	Tue 6/21/16	Thu 6/23/16	19
21	Window coverings	2 days	Fri 6/24/16	Mon 6/27/16	20
22					
23	**L4 Zone 1 (432-461)**	**77 days**	**Thu 3/10/16**	**Fri 6/24/16**	
24	Drywall Hang/Tape	5 days	Thu 3/10/16	Wed 3/16/16	3FS-5 days
25	Hang and tape soffits/Texture/PV/	5 days	Thu 3/17/16	Wed 3/23/16	3
26	Paint	2 days	Mon 3/28/16	Tue 3/29/16	25
27	Gypcrete	3 days	Wed 3/30/16	Fri 4/1/16	26
28	Gypcrete dry time	15 days	Mon 4/4/16	Fri 4/22/16	27
29	Electrical trim	5 days	Mon 4/18/16	Fri 4/22/16	28FS-5 days
30	Fire/Sprinkler Trim	5 days	Mon 4/18/16	Fri 4/22/16	28FS-5 days
31	Install cabinets	6 days	Mon 4/25/16	Mon 5/2/16	28
32	Measure Counter top	1 day	Tue 5/3/16	Tue 5/3/16	31
33	Install Flooring	5 days	Wed 5/4/16	Tue 5/10/16	32
34	Install counter tops	6 days	Wed 5/11/16	Wed 5/18/16	33
35	Intsall Backsplash	5 days	Tue 5/31/16	Mon 6/6/16	
36	Doors and Millwork	5 days	Thu 5/19/16	Wed 5/25/16	34

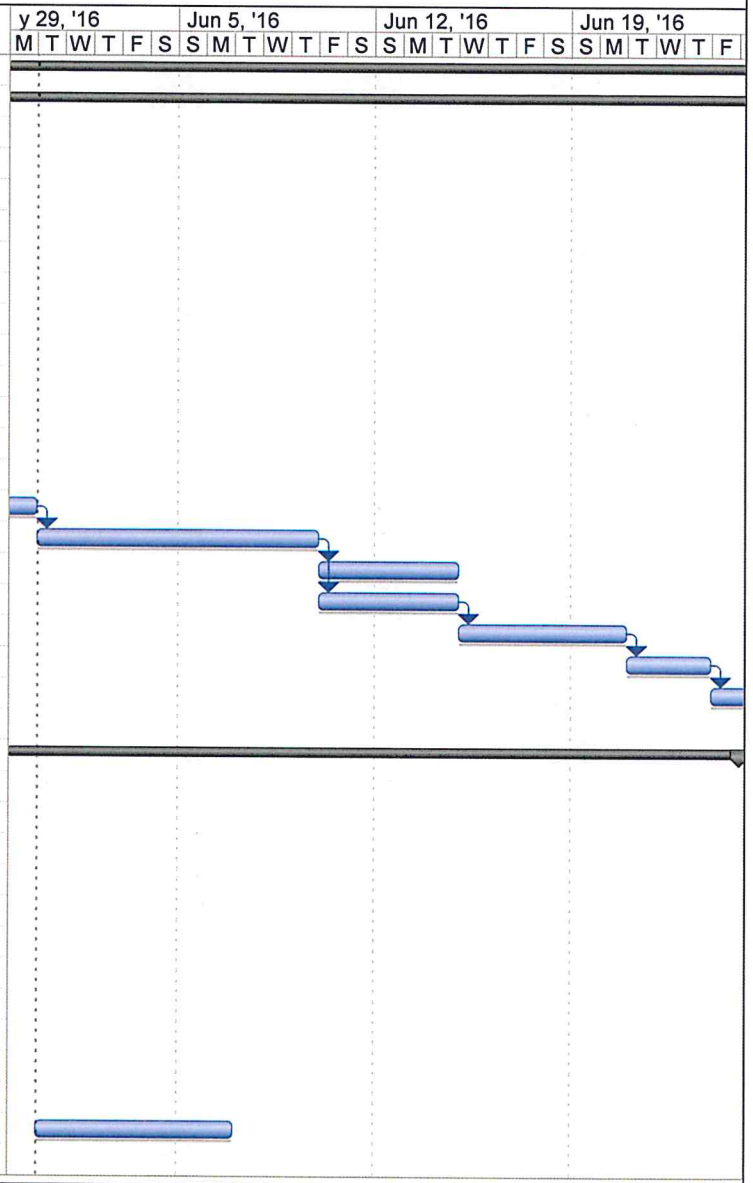

Project: MI Finish 5-31p
Date: Tue 5/31/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
5-31-2016

ID	Task Name	Duration	Start	Finish	Predecessors
37	Drywall Repair ADA	7 days	Thu 5/26/16	Fri 6/3/16	36
38	Paint doors and millwork	8 days	Mon 6/6/16	Wed 6/15/16	37
39	Closet Shelves	3 days	Thu 6/16/16	Mon 6/20/16	38
40	Deliver Appliances	3 days	Thu 6/16/16	Mon 6/20/16	38
41	Plumbing trim	4 days	Tue 6/21/16	Fri 6/24/16	40
42					
43	**L6 Zone 1 (632-661)**	**74 days**	**Thu 3/17/16**	**Tue 6/28/16**	
44	Drywall Hang/Tape	5 days	Thu 3/17/16	Wed 3/23/16	25FS-5 days
45	Hang and tape soffits/Texture/PV/	9 days	Thu 3/24/16	Tue 4/5/16	25
46	Paint	3 days	Wed 4/6/16	Fri 4/8/16	45
47	Gypcrete	3 days	Mon 4/11/16	Wed 4/13/16	46
48	Gypcrete dry time	12 days	Thu 4/14/16	Fri 4/29/16	47
49	Electrical trim	5 days	Mon 4/25/16	Fri 4/29/16	48FS-5 days
50	Fire/Sprinkler Trim	1 day	Mon 4/25/16	Mon 4/25/16	48FS-5 days
51	Install cabinets	6 days	Mon 5/2/16	Mon 5/9/16	48
52	Install Flooring	5 days	Tue 5/10/16	Mon 5/16/16	51
53	Install counter tops	3 days	Tue 5/17/16	Thu 5/19/16	52
54	Intsall Backsplash	3 days	Thu 6/2/16	Mon 6/6/16	
55	Drywall Repair ADA	5 days	Fri 5/20/16	Thu 5/26/16	53
56	Doors and Millwork	5 days	Fri 5/27/16	Thu 6/2/16	55
57	Paint doors and millwork	8 days	Fri 6/3/16	Tue 6/14/16	56
58	Closet Shelves	3 days	Wed 6/15/16	Fri 6/17/16	57
59	Deliver Appliances	3 days	Wed 6/15/16	Fri 6/17/16	57
60	Plumbing trim	4 days	Mon 6/20/16	Thu 6/23/16	59
61	Final Paint Walls	3 days	Fri 6/24/16	Tue 6/28/16	60
62					
63	**L3 Zone 1 (332-360)**	**78 days**	**Mon 3/14/16**	**Wed 6/29/16**	
64	Insulation Inspection	1 day	Mon 3/14/16	Mon 3/14/16	3FS-3 days
65	Drywall Hang/Tape	10 days	Tue 3/15/16	Mon 3/28/16	64
66	Frame soffits	2 days	Tue 3/22/16	Wed 3/23/16	65FS-5 days
67	Electrical at soffits	1 day	Thu 3/24/16	Thu 3/24/16	66
68	Vent soffits	2 days	Mon 3/28/16	Tue 3/29/16	67
69	HVAC/ Electrical inspection at sof	1 day	Wed 3/30/16	Wed 3/30/16	68
70	Hang and tape soffits/Texture/PV/	8 days	Thu 3/31/16	Mon 4/11/16	69
71	Paint	3 days	Tue 4/12/16	Thu 4/14/16	70
72	Electrical trim	5 days	Fri 4/15/16	Thu 4/21/16	71

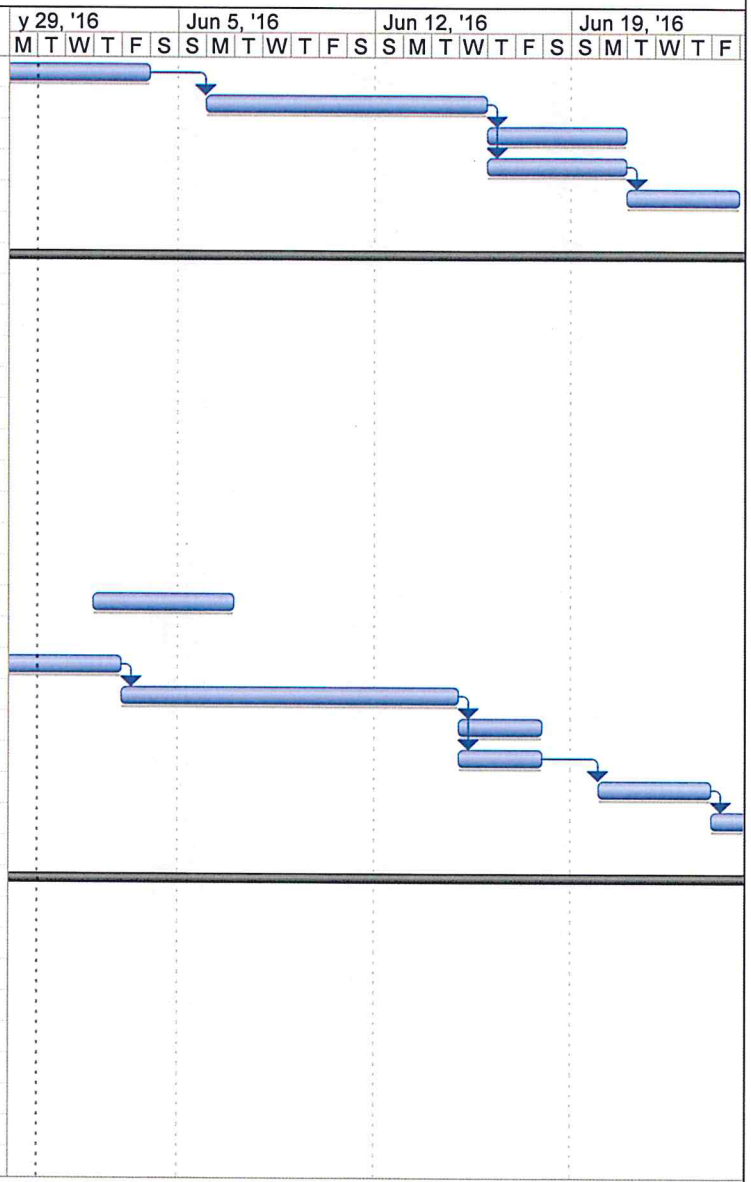

Project: MI Finish 5-31p
Date: Tue 5/31/16

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

Hadley 3 Week Schedule (Interior)
5-31-2016

ID	Task Name	Duration	Start	Finish	Predecessors
73	Fire/Sprinkler Trim	1 day	Fri 4/15/16	Fri 4/15/16	71
74	Install cabinets	6 days	Tue 5/10/16	Tue 5/17/16	51
75	Install Flooring	5 days	Wed 5/18/16	Tue 5/24/16	74
76	Install counter tops	6 days	Wed 5/25/16	Wed 6/1/16	75
77	Intsall Backsplash	5 days	Mon 6/6/16	Fri 6/10/16	
78	Drywall Repair ADA	5 days	Thu 6/2/16	Wed 6/8/16	76
79	Doors and Millwork	5 days	Thu 6/9/16	Wed 6/15/16	78
80	Paint doors and millwork	10 days	Thu 6/16/16	Wed 6/29/16	79
81					
82	**L5 Zone 2 (501-531)**	**68 days**	**Wed 3/30/16**	**Fri 7/1/16**	
83	Pre-rock at tubs	1 day	Wed 3/30/16	Wed 3/30/16	
84	Install tubs	3 days	Thu 3/31/16	Mon 4/4/16	83
85	Elec, Plmb Inspections	1 day	Tue 4/5/16	Tue 4/5/16	84
86	Fire Caulk	2 days	Wed 4/6/16	Thu 4/7/16	85
87	Framing inspection	1 day	Fri 4/8/16	Fri 4/8/16	86
88	Insulation	3 days	Mon 4/11/16	Wed 4/13/16	87
89	Insulation Inspection	1 day	Thu 4/14/16	Thu 4/14/16	88
90	Drywall Hang/Tape	6 days	Fri 4/15/16	Fri 4/22/16	89
91	Frame soffits	5 days	Fri 4/22/16	Thu 4/28/16	90FS-1 day
92	Electrical at soffits	2 days	Wed 4/27/16	Thu 4/28/16	91FS-2 days
93	Vent soffits	5 days	Wed 4/27/16	Tue 5/3/16	92FS-2 days
94	Firecaulk soffits	2 days	Mon 5/2/16	Tue 5/3/16	93FS-2 days
95	HVAC/ Electrical inspection at sof	1 day	Wed 5/4/16	Wed 5/4/16	94
96	Hang and tape soffits/Texture/PV/	14 days	Thu 5/5/16	Tue 5/24/16	95
97	Paint	3 days	Wed 5/25/16	Fri 5/27/16	96
98	Gypcrete	3 days	Mon 5/30/16	Wed 6/1/16	97
99	Gypcrete dry time	10 days	Thu 6/2/16	Wed 6/15/16	98
100	Electrical trim	5 days	Thu 6/9/16	Wed 6/15/16	99FS-5 days
101	Fire/Sprinkler Trim	3 days	Thu 6/9/16	Mon 6/13/16	99FS-5 days
102	Install cabinets	10 days	Mon 6/13/16	Fri 6/24/16	99FS-3 days
103	Install Flooring	10 days	Mon 6/20/16	Fri 7/1/16	102FS-5 days
104					
105	**L4 Zone 2 (401-431)**	**67 days**	**Thu 3/31/16**	**Fri 7/1/16**	
106	Elec, Plmb RI	13 days	Thu 3/31/16	Mon 4/18/16	83
107	Install tubs	6 days	Mon 4/11/16	Mon 4/18/16	127
108	Elec, Plmb Inspections	1 day	Tue 4/19/16	Tue 4/19/16	107

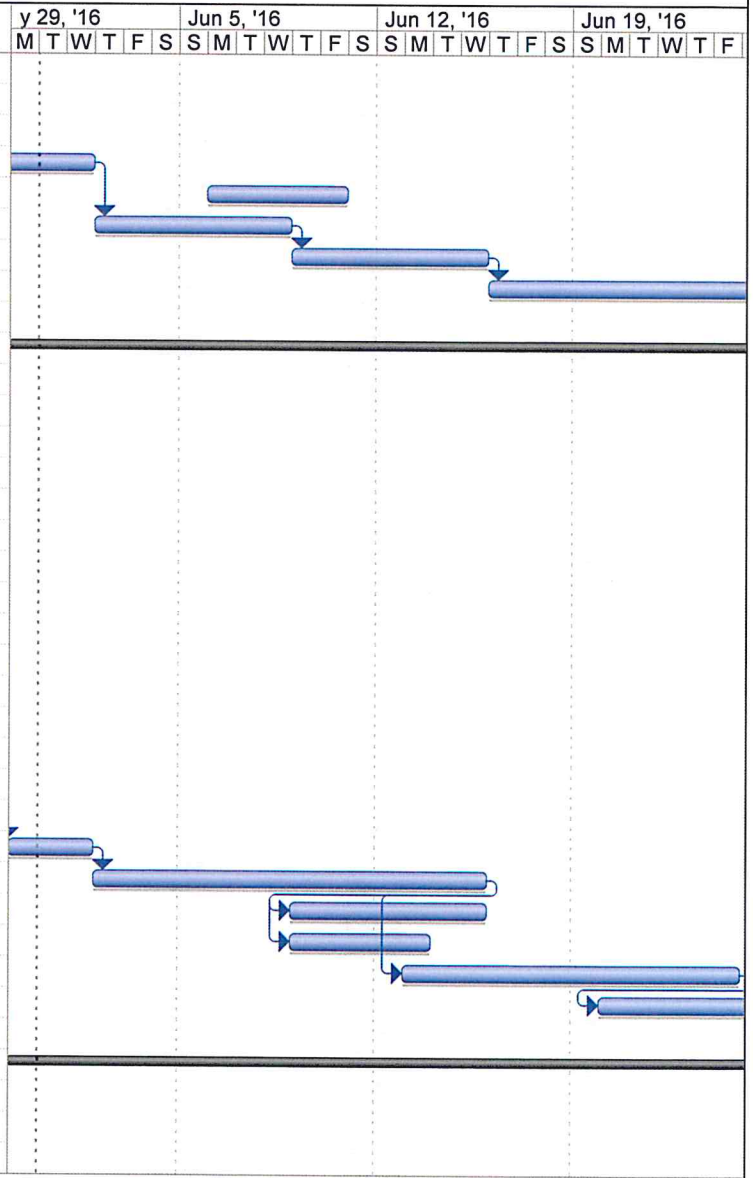

Project: MI Finish 5-31p
Date: Tue 5/31/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
5-31-2016

ID	Task Name	Duration	Start	Finish	Predecessors
109	Fire Caulk	2 days	Wed 4/20/16	Thu 4/21/16	108
110	Framing inspection	1 day	Fri 4/22/16	Fri 4/22/16	109
111	Insulation	4 days	Mon 4/25/16	Thu 4/28/16	110
112	Insulation Inspection	1 day	Fri 4/29/16	Fri 4/29/16	111
113	Drywall Hang/Tape	5 days	Mon 5/2/16	Fri 5/6/16	112
114	Frame soffits	13 days	Fri 5/6/16	Tue 5/24/16	113FS-1 day
115	Electrical at soffits	2 days	Mon 5/23/16	Tue 5/24/16	114FS-2 days
116	Vent soffits	3 days	Mon 5/23/16	Wed 5/25/16	115FS-2 days
117	Firecaulk soffits	2 days	Tue 5/24/16	Wed 5/25/16	116FS-2 days
118	HVAC/ Electrical inspection at soffits	1 day	Thu 5/26/16	Thu 5/26/16	117
119	Hang and tape soffits/Texture/PVA	9 days	Fri 5/27/16	Wed 6/8/16	118
120	Paint	4 days	Thu 6/9/16	Tue 6/14/16	119
121	Gypcrete	3 days	Wed 6/15/16	Fri 6/17/16	120
122	Gypcrete dry time	10 days	Mon 6/20/16	Fri 7/1/16	121
123					
124	**L6 Zone 2 (601-631)**	**63 days**	**Wed 3/30/16**	**Fri 6/24/16**	
125	Sandblast	4 days	Wed 3/30/16	Mon 4/4/16	
126	Elec, Plmb RI	10 days	Tue 4/19/16	Mon 5/2/16	106
127	Install tubs	4 days	Tue 4/5/16	Fri 4/8/16	84
128	Elec, Plmb Inspections	1 day	Tue 5/3/16	Tue 5/3/16	126
129	Fire Caulk	2 days	Wed 5/4/16	Thu 5/5/16	128
130	Framing inspection	1 day	Fri 5/6/16	Fri 5/6/16	129
131	Insulation	4 days	Mon 5/9/16	Thu 5/12/16	130
132	Insulation Inspection	1 day	Fri 5/13/16	Fri 5/13/16	131
133	Drywall Hang/Tape	9 days	Mon 5/16/16	Thu 5/26/16	132
134	Frame soffits	7 days	Thu 5/26/16	Fri 6/3/16	133FS-1 day
135	Electrical at soffits	2 days	Thu 6/2/16	Fri 6/3/16	134FS-2 days
136	Vent soffits	5 days	Thu 6/2/16	Wed 6/8/16	135FS-2 days
137	Firecaulk soffits	2 days	Tue 6/7/16	Wed 6/8/16	136FS-2 days
138	HVAC/ Electrical inspection at soffits	1 day	Thu 6/9/16	Thu 6/9/16	137
139	Hang and tape soffits/Texture/PVA	7 days	Fri 6/10/16	Mon 6/20/16	138
140	Paint	4 days	Tue 6/21/16	Fri 6/24/16	139
141					
142	**L3 Zone 2 (301-331)**	**61 days**	**Tue 4/5/16**	**Tue 6/28/16**	
143	Sandblast	5 days	Tue 4/5/16	Mon 4/11/16	125
144	Install tubs	5 days	Tue 4/19/16	Mon 4/25/16	107

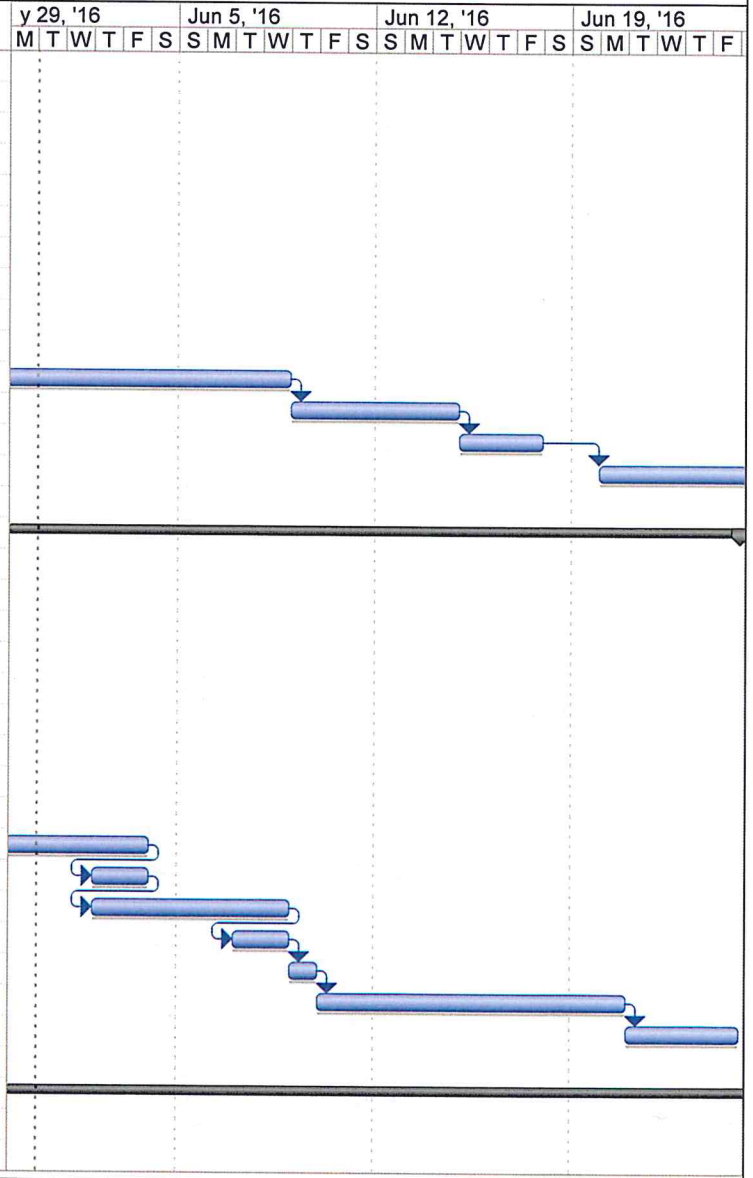

Project: MI Finish 5-31p
Date: Tue 5/31/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
5-31-2016

ID	Task Name	Duration	Start	Finish	Predecessors
145	elec rough in	10 days	Tue 5/3/16	Mon 5/16/16	126
146	Elec, Plmb Inspections	1 day	Tue 5/17/16	Tue 5/17/16	145
147	Fire Caulk	2 days	Wed 5/18/16	Thu 5/19/16	146
148	Framing inspection	1 day	Fri 5/20/16	Fri 5/20/16	147
149	Insulation	4 days	Mon 5/23/16	Thu 5/26/16	148
150	Insulation Inspection	1 day	Fri 5/27/16	Fri 5/27/16	149
151	Drywall Hang/Tape	7 days	Mon 5/30/16	Tue 6/7/16	150
152	Frame soffits	5 days	Tue 6/7/16	Mon 6/13/16	151FS-1 day
153	Electrical at soffits	2 days	Fri 6/10/16	Mon 6/13/16	152FS-2 days
154	Vent soffits	5 days	Fri 6/10/16	Thu 6/16/16	153FS-2 days
155	Firecaulk soffits	2 days	Wed 6/15/16	Thu 6/16/16	154FS-2 days
156	HVAC/ Electrical inspection at soffits	1 day	Fri 6/17/16	Fri 6/17/16	155
157	Hang and tape soffits/Texture/PVA	7 days	Mon 6/20/16	Tue 6/28/16	156

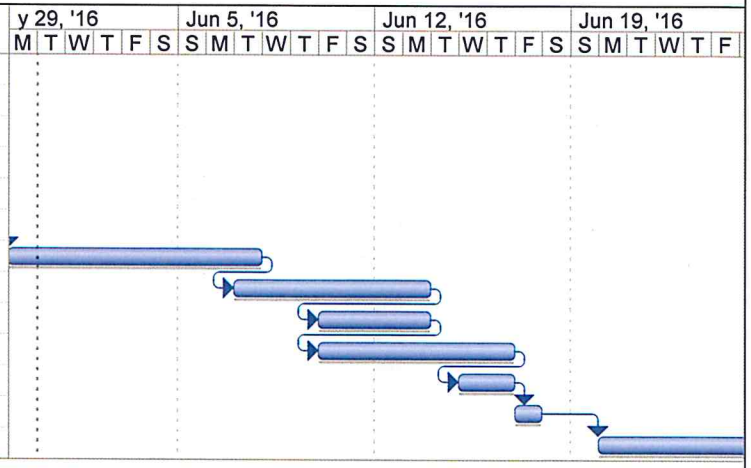

Project: MI Finish 5-31p
Date: Tue 5/31/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
