Hadley 3 Week Schedule (Interior)
12-7-2015

ID	Task Name	Duration	Start	Finish
109	Plumbing RI Levels L3-L6 Test Z1	3 days	Mon 12/7/15	Wed 12/9/15
110	Plumbing RI Levels L3-L6 Inspect	2 days	Thu 12/10/15	Fri 12/11/15
111	Plumbing RI Levels P-L3 Test Z3	3 days	Mon 12/14/15	Wed 12/16/15
112	Plumbing RI Levels P-L3 Inspect	2 days	Thu 12/17/15	Fri 12/18/15
113				
114	**L5 Zone 2**	**15 days**	**Fri 11/20/15**	**Thu 12/10/15**
115	Framing Pick Up	10 days	Fri 11/20/15	Thu 12/3/15
116	Plumbing RI Drain Waste and Ver	5 days	Tue 12/1/15	Mon 12/7/15
117	Plumbing RI Water Supply	2 days	Tue 12/8/15	Wed 12/9/15
118	Fire Sprinkler Rough In	3 days	Fri 12/4/15	Tue 12/8/15
119	Electrical Box And Drill	3 days	Tue 12/8/15	Thu 12/10/15
120	Low Volt Box and Drill	1 day	Thu 12/10/15	Thu 12/10/15
121	HVAC Exhaust/AC Port Drill	2 days	Tue 12/8/15	Wed 12/9/15
122				
123	**L6 Zone 2**	**16 days**	**Thu 12/3/15**	**Thu 12/24/15**
124	Framing Pick Up	10 days	Thu 12/3/15	Wed 12/16/15
125	Plumbing RI Drain Waste and Ver	10 days	Tue 12/8/15	Mon 12/21/15
126	Plumbing RI Water Supply	2 days	Tue 12/22/15	Wed 12/23/15
127	Fire Sprinkler Rough In	3 days	Thu 12/17/15	Mon 12/21/15
128	Electrical Box And Drill	3 days	Tue 12/22/15	Thu 12/24/15
129	Low Volt Box and Drill	1 day	Thu 12/24/15	Thu 12/24/15
130	HVAC Exhaust/AC Port Drill	2 days	Tue 12/22/15	Wed 12/23/15
131				
132	**L4 Zone 4**	**17 days**	**Tue 12/8/15**	**Wed 12/30/15**
133	Framing Pick Up	8 days	Wed 12/16/15	Fri 12/25/15
134	Plumbing RI Drain Waste and Ver	10 days	Tue 12/8/15	Mon 12/21/15
135	Plumbing RI Water Supply	2 days	Tue 12/22/15	Wed 12/23/15
136	Fire Sprinkler Rough In	3 days	Mon 12/28/15	Wed 12/30/15
137	Electrical Box And Drill	3 days	Tue 12/22/15	Thu 12/24/15
138	Low Volt Box and Drill	1 day	Thu 12/24/15	Thu 12/24/15
139	HVAC Exhaust/AC Port Drill	2 days	Tue 12/22/15	Wed 12/23/15
140				
141	**L5 Zone 4**	**13 days**	**Tue 12/22/15**	**Thu 1/7/16**
142	Framing Pick Up	7 days	Fri 12/25/15	Mon 1/4/16
143	Plumbing RI Drain Waste and Ver	9 days	Tue 12/22/15	Fri 1/1/16
144	Plumbing RI Water Supply	2 days	Mon 1/4/16	Tue 1/5/16

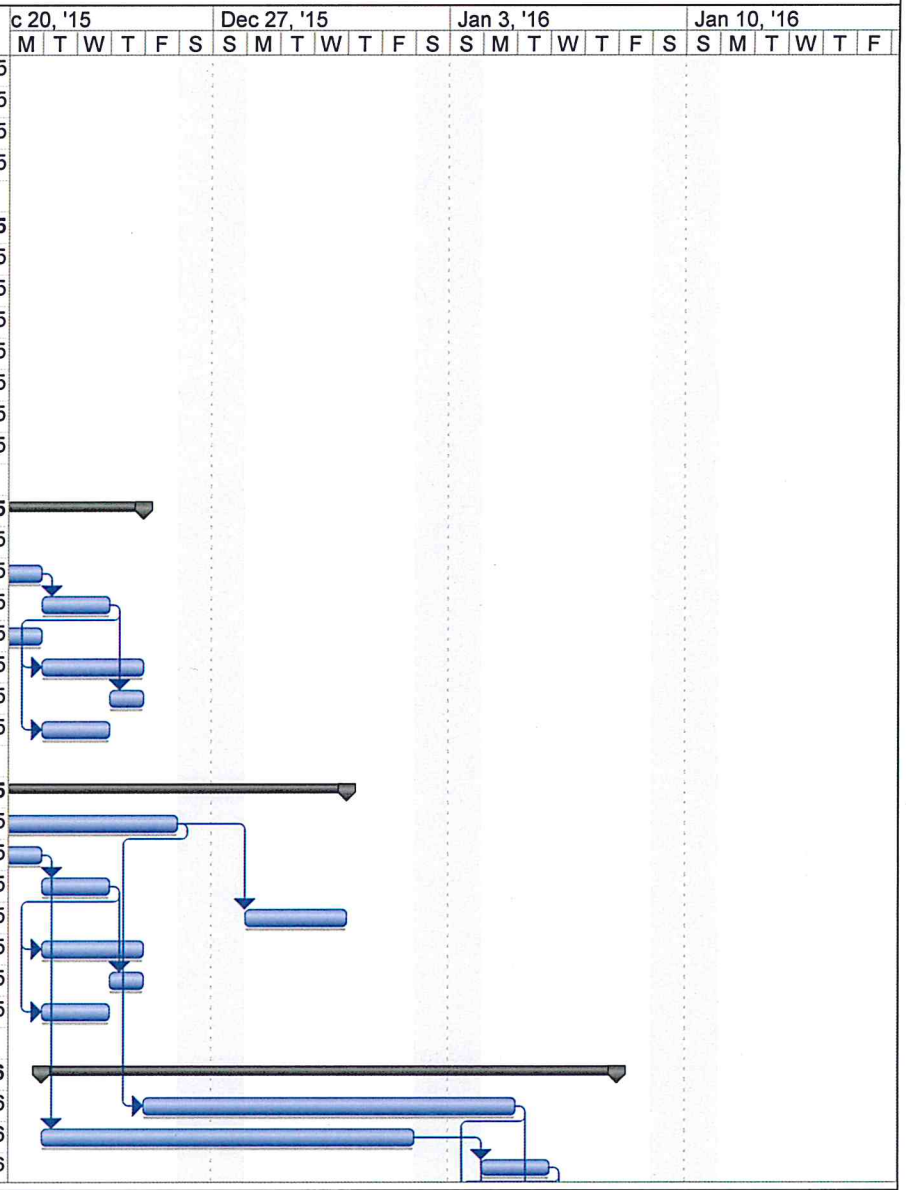

Project: MI MPE RI 12-21
Date: Mon 12/21/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
12-7-2015

ID	Task Name	Duration	Start	Finish
145	Fire Sprinkler Rough In	3 days	Tue 1/5/16	Thu 1/7/16
146	Electrical Box And Drill	3 days	Mon 1/4/16	Wed 1/6/16
147	Low Volt Box and Drill	1 day	Wed 1/6/16	Wed 1/6/16
148	HVAC Exhaust/AC Port Drill	2 days	Mon 1/4/16	Tue 1/5/16
149				
150	**L6 Zone 4**	**11 days**	**Mon 1/4/16**	**Mon 1/18/16**
151	Framing Pick Up	4 days	Mon 1/4/16	Thu 1/7/16
152	Plumbing RI Drain Waste and Ver	8 days	Mon 1/4/16	Wed 1/13/16
153	Plumbing RI Water Supply	2 days	Thu 1/14/16	Fri 1/15/16
154	Fire Sprinkler Rough In	5 days	Fri 1/8/16	Thu 1/14/16
155	Electrical Box And Drill	3 days	Thu 1/14/16	Mon 1/18/16
156	Low Volt Box and Drill	1 day	Mon 1/18/16	Mon 1/18/16
157	HVAC Exhaust/AC Port Drill	2 days	Thu 1/14/16	Fri 1/15/16
158				
159	**L3-L6 Zones 2 and 4**	**11 days**	**Fri 1/15/16**	**Fri 1/29/16**
160	Fire Sprinkler Test	3 days	Fri 1/15/16	Tue 1/19/16
161	Fire Sprinkler Inspection	2 days	Wed 1/20/16	Thu 1/21/16
162	Plumbing RI Levels P-L3 Test	3 days	Mon 1/18/16	Wed 1/20/16
163	Plumbing RI Levels P-L3 Inspect :	2 days	Thu 1/21/16	Fri 1/22/16
164	Plumbing RI Levels P-L3 Test	3 days	Mon 1/25/16	Wed 1/27/16
165	Plumbing RI Levels P-L3 Inspect :	2 days	Thu 1/28/16	Fri 1/29/16
166				
167	**MEP Roof Down**	**175 days**	**Fri 10/2/15**	**Thu 6/2/16**
168	**L6 Zone 1 (West Side)**	**73 days**	**Mon 11/23/15**	**Wed 3/2/16**
169	Roofing Installed	15 days	Mon 11/23/15	Fri 12/11/15
170	Electrical RI	14 days	Mon 12/14/15	Thu 12/31/15
171	Low volt RI	4 days	Mon 12/28/15	Thu 12/31/15
172	Plumbing/Electrical/Lowvolt Inspe	4 days	Fri 1/1/16	Wed 1/6/16
173	Framing inspection	1 day	Thu 1/7/16	Thu 1/7/16
174	Insulation	4 days	Fri 1/8/16	Wed 1/13/16
175	Insulation Inspection	1 day	Thu 1/14/16	Thu 1/14/16
176	Drywall Hang/Tape/Texture/PVA	15 days	Fri 1/15/16	Thu 2/4/16
177	Frame soffits	4 days	Fri 1/22/16	Wed 1/27/16
178	Vent soffits	4 days	Thu 1/28/16	Tue 2/2/16
179	Electrical at soffits	2 days	Wed 2/3/16	Thu 2/4/16
180	HVAC/ Electrical inspection at sof	1 day	Fri 2/5/16	Fri 2/5/16

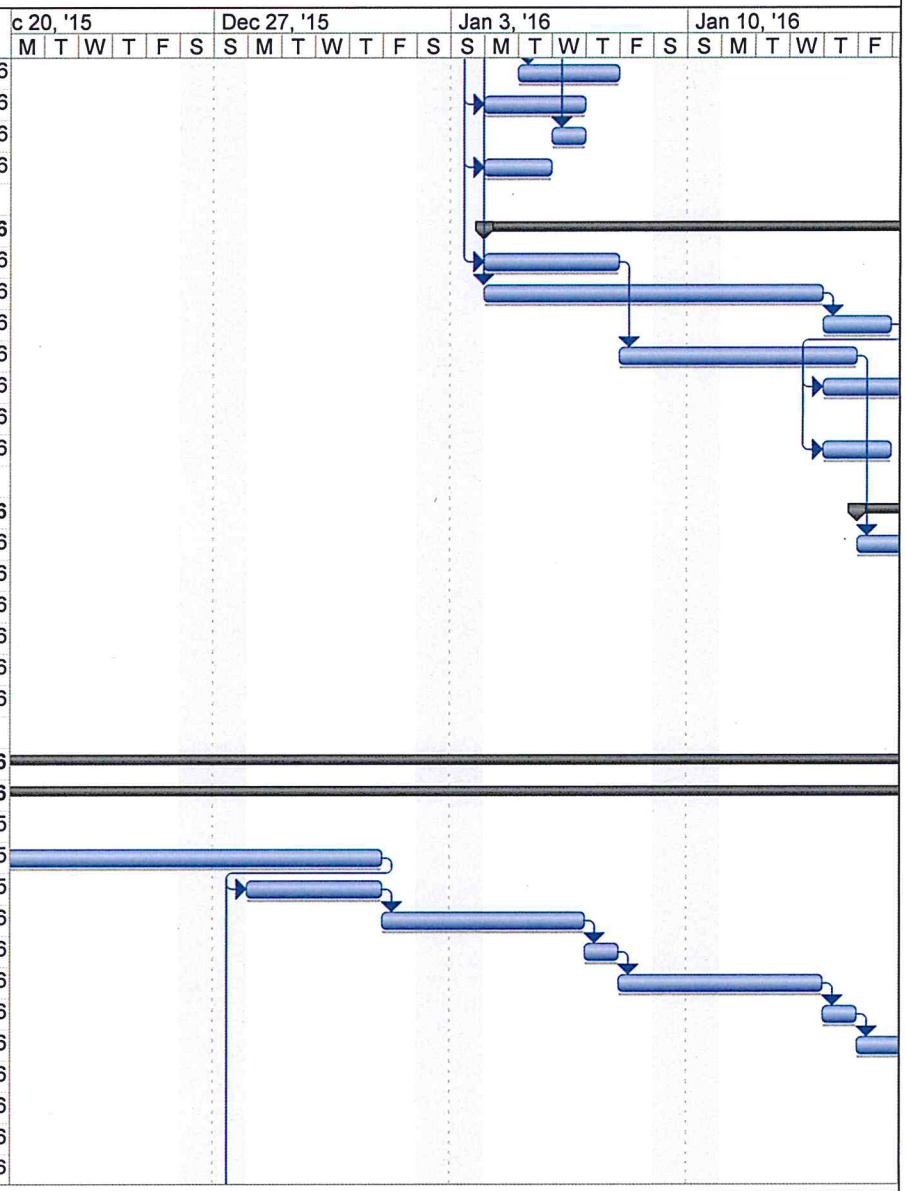

Project: MI MPE RI 12-21
Date: Mon 12/21/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
12-7-2015

ID	Task Name	Duration	Start	Finish
181	Hang and tape soffits	5 days	Mon 2/8/16	Fri 2/12/16
182	Paint	5 days	Mon 2/15/16	Fri 2/19/16
183	Gypcrete	3 days	Mon 2/15/16	Wed 2/17/16
184	Gypcrete dry time	10 days	Thu 2/18/16	Wed 3/2/16
185	Electrical trim	5 days	Thu 2/11/16	Wed 2/17/16
186	Install cabinets	5 days	Thu 2/18/16	Wed 2/24/16
187				
188	Zone 1 Electrical Unit Feeders, L :	10 days	Mon 12/14/15	Fri 12/25/15
189				
190	**L6-3 Zone 1 Tubs**	**11 days**	**Mon 12/7/15**	**Mon 12/21/15**
191	Insulate at Tubs	2 days	Mon 12/7/15	Tue 12/8/15
192	Pre Rock at Tubs	2 days	Wed 12/9/15	Thu 12/10/15
193	Gypcrete at Tubs	3 days	Fri 12/11/15	Tue 12/15/15
194	Install Tubs	4 days	Wed 12/16/15	Mon 12/21/15
195				
196	**L6 Zone 2 (East Side)**	**146 days**	**Fri 10/2/15**	**Fri 4/22/16**
197	Roof framing complete	35 days	Mon 11/23/15	Fri 1/8/16
198	Roofing installed	14 days	Mon 1/11/16	Thu 1/28/16
199	Electrical RI	10 days	Fri 1/29/16	Thu 2/11/16
200	Low volt RI	4 days	Wed 2/10/16	Mon 2/15/16
201	Plumbing/Electrical/Lowvolt Inspe	4 days	Tue 2/16/16	Fri 2/19/16
202	Framing inspection	1 day	Mon 2/22/16	Mon 2/22/16
203	Insulation	4 days	Tue 2/23/16	Fri 2/26/16
204	Insulation Inspection	1 day	Mon 2/29/16	Mon 2/29/16
205	Drywall Hang/Tape/Texture/PVA	15 days	Tue 3/1/16	Mon 3/21/16
206	Frame soffits	4 days	Tue 3/8/16	Fri 3/11/16
207	Vent soffits	4 days	Mon 3/14/16	Thu 3/17/16
208	Electrical at soffits	2 days	Fri 3/18/16	Mon 3/21/16
209	HVAC/ Electrical inspection at sof	1 day	Tue 3/22/16	Tue 3/22/16
210	Hang and tape soffits	5 days	Wed 3/23/16	Tue 3/29/16
211	Paint	5 days	Wed 3/30/16	Tue 4/5/16
212	Gypcrete	3 days	Wed 4/6/16	Fri 4/8/16
213	Gypcrete dry time	10 days	Mon 4/11/16	Fri 4/22/16
214	Electrical trim	5 days	Mon 4/4/16	Fri 4/8/16
215	Install cabinets	5 days	Mon 4/11/16	Fri 4/15/16
216				

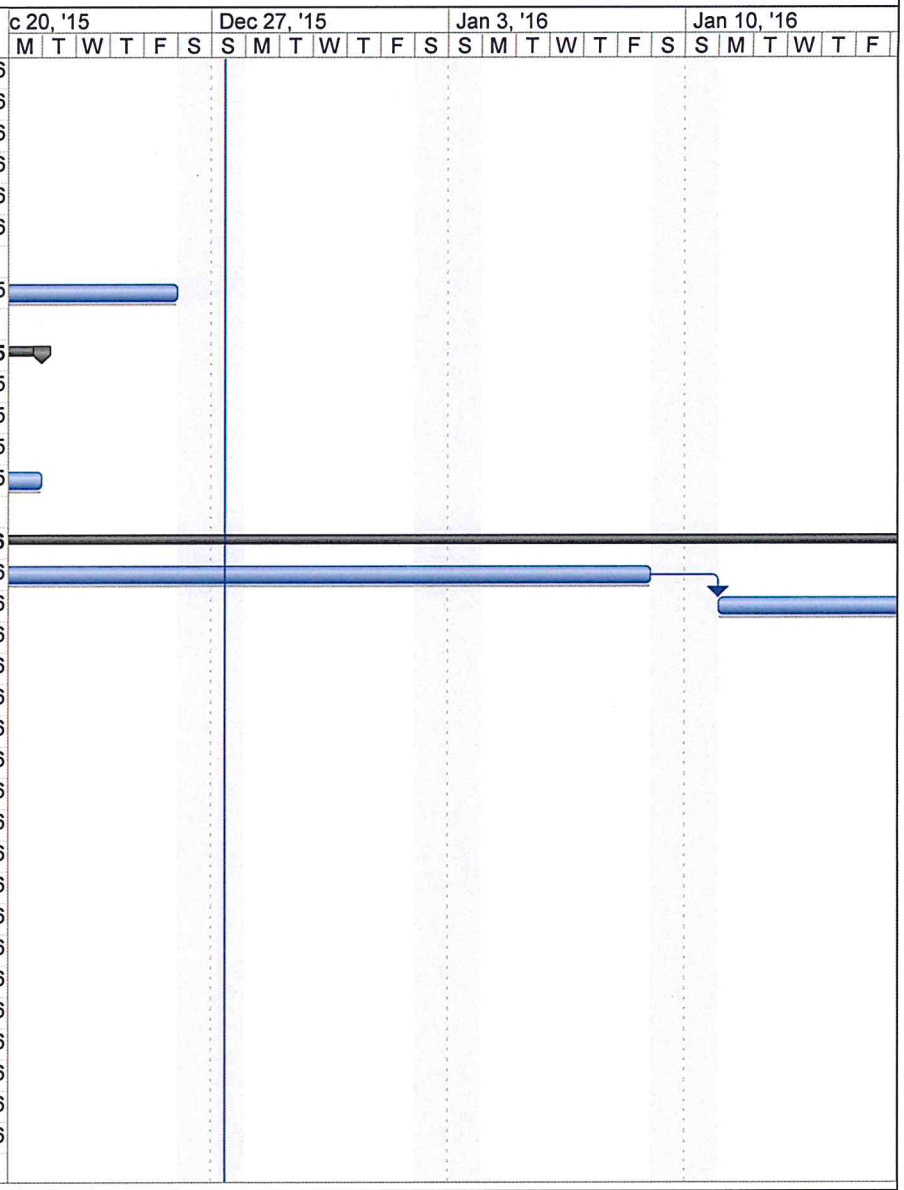

Project: MI MPE RI 12-21
Date: Mon 12/21/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
12-7-2015

ID	Task Name	Duration	Start	Finish
217				
218	Electrical Unit Feeders Zone 2, L :	8 days	Fri 1/29/16	Tue 2/9/16
219				
220	**L6-3 Zone 2 Tubs**	**8 days**	**Fri 10/2/15**	**Tue 10/13/15**
221	Insulate at Tubs	2 days	Fri 10/2/15	Mon 10/5/15
222	Pre Rock at Tubs	2 days	Tue 10/6/15	Wed 10/7/15
223	Install Tubs	4 days	Thu 10/8/15	Tue 10/13/15
224				
225	**L5 Zone 1 (West Side)**	**56 days**	**Mon 12/28/15**	**Mon 3/14/16**
226	Electrical RI	10 days	Mon 12/28/15	Fri 1/8/16
227	Low volt RI	4 days	Thu 1/7/16	Tue 1/12/16
228	Plumbing/Electrical/Lowvolt Inspe	4 days	Wed 1/13/16	Mon 1/18/16
229	Framing inspection	1 day	Tue 1/19/16	Tue 1/19/16
230	Insulation	4 days	Wed 1/20/16	Mon 1/25/16
231	Insulation Inspection	1 day	Tue 1/26/16	Tue 1/26/16
232	Drywall Hang/Tape/Texture/PVA	15 days	Wed 1/27/16	Tue 2/16/16
233	Frame soffits	4 days	Wed 2/3/16	Mon 2/8/16
234	Vent soffits	4 days	Tue 2/9/16	Fri 2/12/16
235	Electrical at soffits	2 days	Mon 2/15/16	Tue 2/16/16
236	HVAC/ Electrical inspection at sof	1 day	Wed 2/17/16	Wed 2/17/16
237	Hang and tape soffits	5 days	Thu 2/18/16	Wed 2/24/16
238	Paint	5 days	Thu 2/25/16	Wed 3/2/16
239	Gypcrete	3 days	Thu 2/25/16	Mon 2/29/16
240	Gypcrete dry time	10 days	Tue 3/1/16	Mon 3/14/16
241	Electrical trim	5 days	Tue 2/23/16	Mon 2/29/16
242	Install cabinets	5 days	Tue 3/1/16	Mon 3/7/16
243				
244	**L5 Zone 2 (East Side)**	**56 days**	**Fri 2/12/16**	**Fri 4/29/16**
245	Electrical RI	10 days	Fri 2/12/16	Thu 2/25/16
246	Low volt RI	4 days	Wed 2/24/16	Mon 2/29/16
247	Plumbing/Electrical/Lowvolt Inspe	4 days	Tue 3/1/16	Fri 3/4/16
248	Framing inspection	1 day	Mon 3/7/16	Mon 3/7/16
249	Insulation	4 days	Tue 3/8/16	Fri 3/11/16
250	Insulation Inspection	1 day	Mon 3/14/16	Mon 3/14/16
251	Drywall Hang/Tape/Texture/PVA	15 days	Tue 3/15/16	Mon 4/4/16
252	Frame soffits	4 days	Tue 3/22/16	Fri 3/25/16

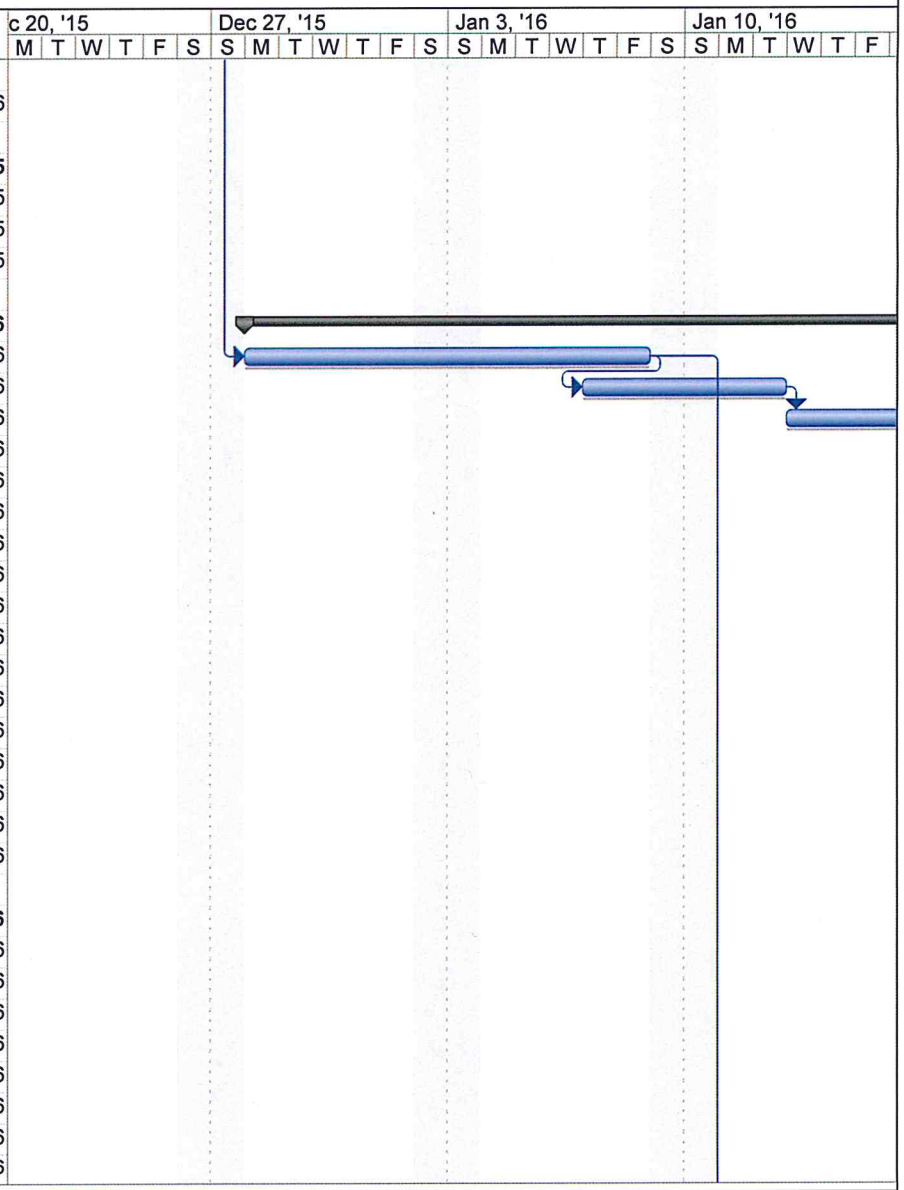

Project: MI MPE RI 12-21
Date: Mon 12/21/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
