Hadley 3 Week Schedule (Interior)
4-23-2016

Interior

ID	Task Name	Duration	Start	Finish	Predecessors
1	**MEP Roof Down**	**169 days?**	**Fri 10/2/15**	**Wed 5/25/16**	
2	**L5 Zone 1 (532-561)**	**56 days?**	**Tue 3/8/16**	**Tue 5/24/16**	
3	Hang and tape soffits/Texture/PV/	7 days	Tue 3/8/16	Wed 3/16/16	
4	Paint	2 days	Thu 3/17/16	Fri 3/18/16	3
5	Gypcrete	3 days	Mon 3/21/16	Wed 3/23/16	4
6	Gypcrete dry time	10 days	Thu 3/24/16	Wed 4/6/16	5
7	Electrical trim	5 days	Thu 3/31/16	Wed 4/6/16	6FS-5 days
8	Fire/Sprinkler Trim	1 day?	Thu 3/31/16	Thu 3/31/16	6FS-5 days
9	Install cabinets	8 days	Mon 4/4/16	Wed 4/13/16	6FS-3 days
10	Measure Counter top	1 day	Thu 4/14/16	Thu 4/14/16	9
11	Install Flooring	5 days	Wed 4/13/16	Tue 4/19/16	9FS-1 day
12	Install counter tops	3 days	Thu 4/21/16	Mon 4/25/16	9FS+5 days
13	Intsall Backsplash	3 days	Tue 4/26/16	Thu 4/28/16	12
14	Doors and Millwork	5 days	Fri 4/29/16	Thu 5/5/16	13
15	Paint doors and millwork	10 days	Fri 5/6/16	Thu 5/19/16	14
16	Closet Shelves	3 days	Fri 5/20/16	Tue 5/24/16	15
17	Deliver Appliances	3 days	Fri 5/20/16	Tue 5/24/16	15
18					
19	**L4 Zone 1 (432-461)**	**55 days**	**Thu 3/10/16**	**Wed 5/25/16**	
20	Drywall Hang/Tape	5 days	Thu 3/10/16	Wed 3/16/16	3FS-5 days
21	Hang and tape soffits/Texture/PV/	5 days	Thu 3/17/16	Wed 3/23/16	3
22	Paint	2 days	Mon 3/28/16	Tue 3/29/16	21
23	Gypcrete	3 days	Wed 3/30/16	Fri 4/1/16	22
24	Gypcrete dry time	15 days	Mon 4/4/16	Fri 4/22/16	23
25	Electrical trim	5 days	Mon 4/18/16	Fri 4/22/16	24FS-5 days
26	Fire/Sprinkler Trim	5 days	Mon 4/18/16	Fri 4/22/16	24FS-5 days
27	Install cabinets	6 days	Mon 4/25/16	Mon 5/2/16	24
28	Measure Counter top	1 day	Tue 5/3/16	Tue 5/3/16	27
29	Install Flooring	5 days	Wed 5/4/16	Tue 5/10/16	28
30	Install counter tops	3 days	Wed 5/11/16	Fri 5/13/16	29
31	Intsall Backsplash	3 days	Mon 5/16/16	Wed 5/18/16	30
32	Doors and Millwork	5 days	Thu 5/19/16	Wed 5/25/16	31
33					
34	**L6 Zone 1 (632-661)**	**49 days**	**Thu 3/17/16**	**Tue 5/24/16**	
35	Drywall Hang/Tape	5 days	Thu 3/17/16	Wed 3/23/16	21FS-5 days
36	Hang and tape soffits/Texture/PV/	9 days	Thu 3/24/16	Tue 4/5/16	21

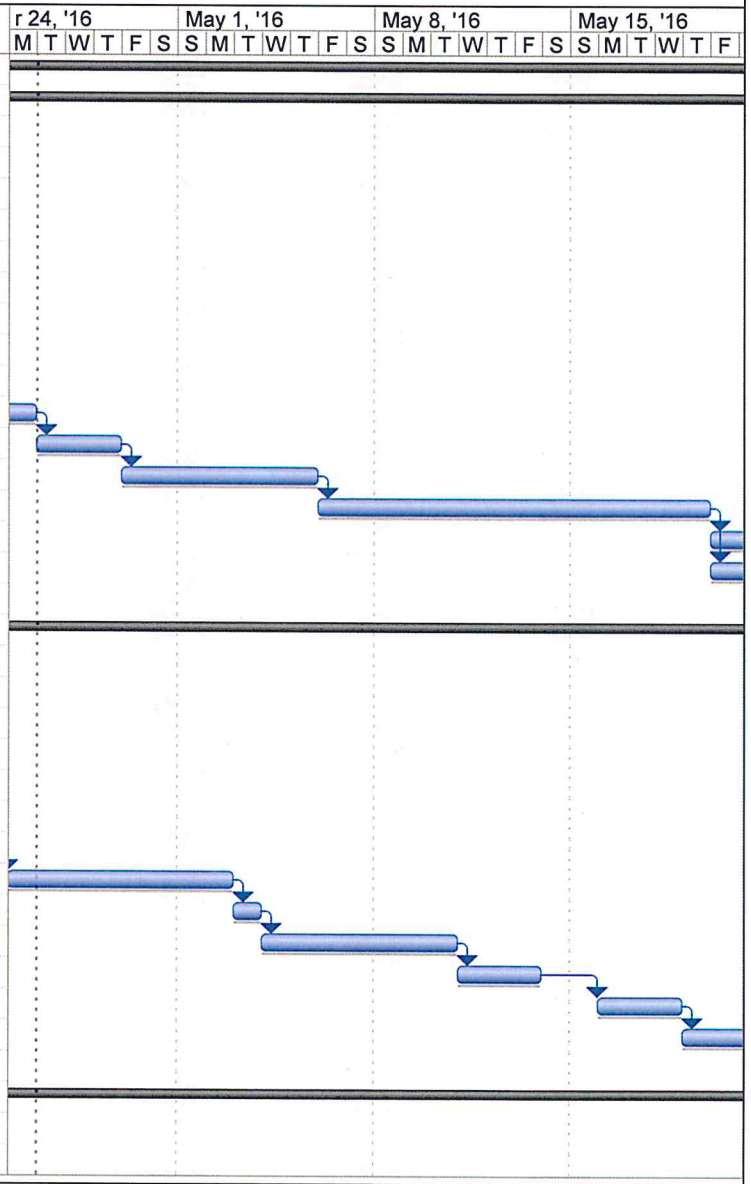

Project: MI Finish 4-23p-1
Date: Tue 4/26/16

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

Hadley 3 Week Schedule (Interior)
4-23-2016

ID	Task Name	Duration	Start	Finish	Predecessors
37	Paint	3 days	Wed 4/6/16	Fri 4/8/16	36
38	Gypcrete	3 days	Mon 4/11/16	Wed 4/13/16	37
39	Gypcrete dry time	12 days	Thu 4/14/16	Fri 4/29/16	38
40	Electrical trim	5 days	Mon 4/25/16	Fri 4/29/16	39FS-5 days
41	Fire/Sprinkler Trim	1 day	Mon 4/25/16	Mon 4/25/16	39FS-5 days
42	Install cabinets	6 days	Mon 5/2/16	Mon 5/9/16	39
43	Install Flooring	5 days	Tue 5/10/16	Mon 5/16/16	42
44	Install counter tops	3 days	Tue 5/17/16	Thu 5/19/16	43
45	Intsall Backsplash	3 days	Fri 5/20/16	Tue 5/24/16	44
46					
47	**L3 Zone 1 (332-360)**	**168 days**	**Fri 10/2/15**	**Tue 5/24/16**	
48	Fire/Sprinkler Trim	1 day	Fri 10/2/15	Fri 10/2/15	
49	Install cabinets	6 days	Tue 5/10/16	Tue 5/17/16	42
50	Install Flooring	5 days	Wed 5/18/16	Tue 5/24/16	49
51					
52	**L5 Zone 2 (501-531)**	**40 days**	**Wed 3/30/16**	**Tue 5/24/16**	
53	Pre-rock at tubs	1 day	Wed 3/30/16	Wed 3/30/16	
54	Install tubs	3 days	Thu 3/31/16	Mon 4/4/16	53
55	Elec, Plmb Inspections	1 day	Tue 4/5/16	Tue 4/5/16	54
56	Fire Caulk	2 days	Wed 4/6/16	Thu 4/7/16	55
57	Framing inspection	1 day	Fri 4/8/16	Fri 4/8/16	56
58	Insulation	3 days	Mon 4/11/16	Wed 4/13/16	57
59	Insulation Inspection	1 day	Thu 4/14/16	Thu 4/14/16	58
60	Drywall Hang/Tape	6 days	Fri 4/15/16	Fri 4/22/16	59
61	Frame soffits	5 days	Fri 4/22/16	Thu 4/28/16	60FS-1 day
62	Electrical at soffits	2 days	Wed 4/27/16	Thu 4/28/16	61FS-2 days
63	Vent soffits	5 days	Wed 4/27/16	Tue 5/3/16	62FS-2 days
64	Firecaulk soffits	2 days	Mon 5/2/16	Tue 5/3/16	63FS-2 days
65	HVAC/ Electrical inspection at sof	1 day	Wed 5/4/16	Wed 5/4/16	64
66	Hang and tape soffits/Texture/PV/	7 days	Thu 5/5/16	Fri 5/13/16	65
67	Paint	4 days	Mon 5/16/16	Thu 5/19/16	66
68	Gypcrete	3 days	Fri 5/20/16	Tue 5/24/16	67
69					
70	**L4 Zone 2 (401-431)**	**42 days**	**Thu 3/31/16**	**Fri 5/27/16**	
71	Elec, Plmb RI	13 days	Thu 3/31/16	Mon 4/18/16	53
72	Install tubs	6 days	Mon 4/11/16	Mon 4/18/16	89

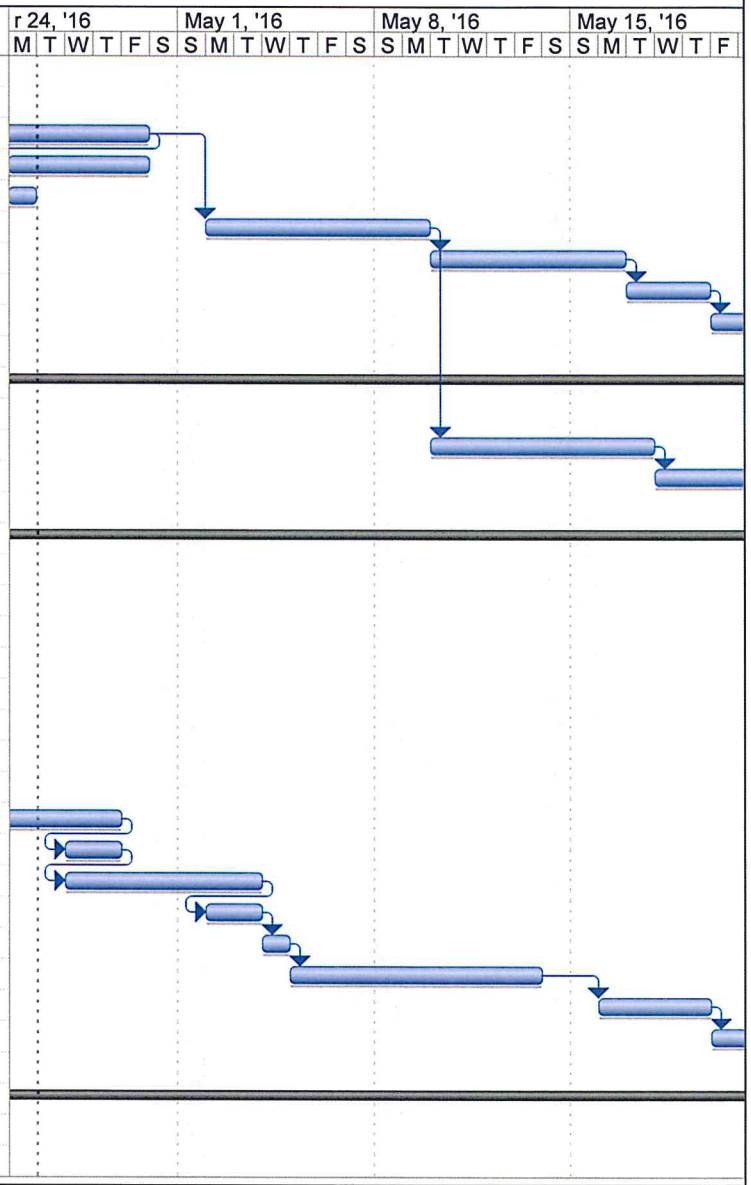

Project: MI Finish 4-23p-1
Date: Tue 4/26/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
4-23-2016

ID	Task Name	Duration	Start	Finish	Predecessors
73	Elec, Plmb Inspections	1 day	Tue 4/19/16	Tue 4/19/16	72
74	Fire Caulk	2 days	Wed 4/20/16	Thu 4/21/16	73
75	Framing inspection	1 day	Fri 4/22/16	Fri 4/22/16	74
76	Insulation	4 days	Mon 4/25/16	Thu 4/28/16	75
77	Insulation Inspection	1 day	Fri 4/29/16	Fri 4/29/16	76
78	Drywall Hang/Tape	5 days	Mon 5/2/16	Fri 5/6/16	77
79	Frame soffits	5 days	Fri 5/6/16	Thu 5/12/16	78FS-1 day
80	Electrical at soffits	2 days	Wed 5/11/16	Thu 5/12/16	79FS-2 days
81	Vent soffits	5 days	Wed 5/11/16	Tue 5/17/16	80FS-2 days
82	Firecaulk soffits	2 days	Mon 5/16/16	Tue 5/17/16	81FS-2 days
83	HVAC/ Electrical inspection at soffits	1 day	Wed 5/18/16	Wed 5/18/16	82
84	Hang and tape soffits/Texture/PVA	7 days	Thu 5/19/16	Fri 5/27/16	83
85					
86	**L6 Zone 2 (601-631)**	**42 days**	**Wed 3/30/16**	**Thu 5/26/16**	
87	Sandblast	4 days	Wed 3/30/16	Mon 4/4/16	
88	Elec, Plmb RI	10 days	Tue 4/19/16	Mon 5/2/16	71
89	Install tubs	4 days	Tue 4/5/16	Fri 4/8/16	54
90	Elec, Plmb Inspections	1 day	Tue 5/3/16	Tue 5/3/16	88
91	Fire Caulk	2 days	Wed 5/4/16	Thu 5/5/16	90
92	Framing inspection	1 day	Fri 5/6/16	Fri 5/6/16	91
93	Insulation	4 days	Mon 5/9/16	Thu 5/12/16	92
94	Insulation Inspection	1 day	Fri 5/13/16	Fri 5/13/16	93
95	Drywall Hang/Tape	5 days	Mon 5/16/16	Fri 5/20/16	94
96	Frame soffits	5 days	Fri 5/20/16	Thu 5/26/16	95FS-1 day
97					
98	**L3 Zone 2 (301-331)**	**34 days**	**Tue 4/5/16**	**Fri 5/20/16**	
99	Sandblast	5 days	Tue 4/5/16	Mon 4/11/16	87
100	Install tubs	5 days	Tue 4/19/16	Mon 4/25/16	72
101	elec rough in	10 days	Tue 5/3/16	Mon 5/16/16	88
102	Elec, Plmb Inspections	1 day	Tue 5/17/16	Tue 5/17/16	101
103	Fire Caulk	2 days	Wed 5/18/16	Thu 5/19/16	102
104	Framing inspection	1 day	Fri 5/20/16	Fri 5/20/16	103

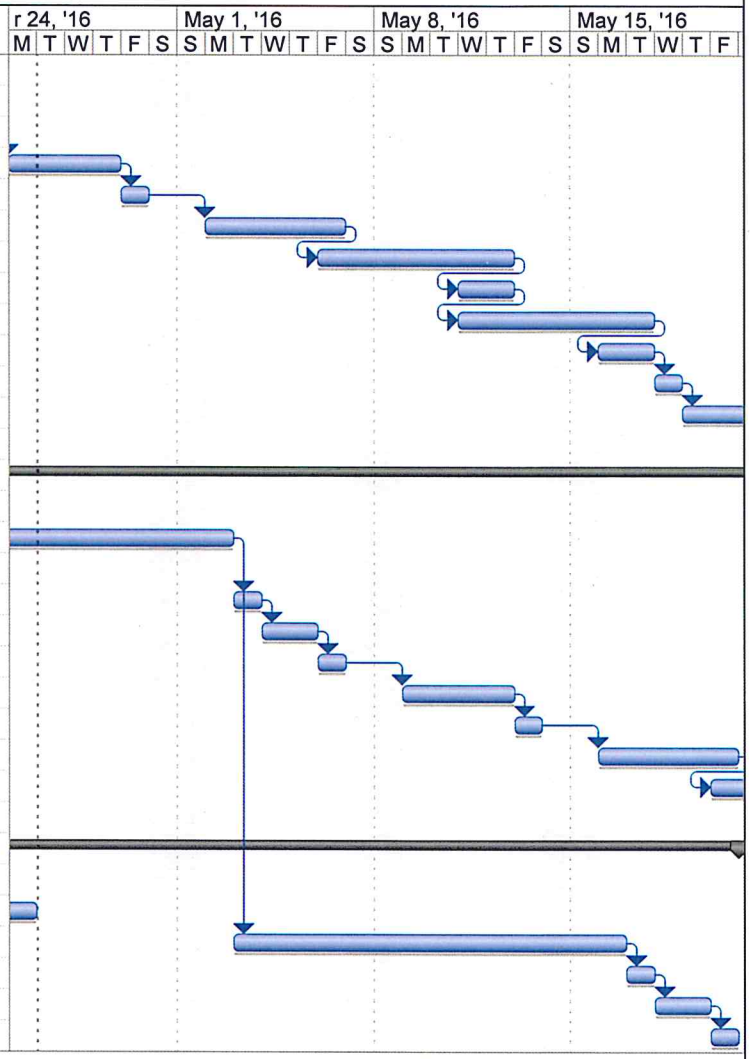

Project: MI Finish 4-23p-1
Date: Tue 4/26/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
