Hadley 3 Week Schedule (Interior)
5-23-2016

Interiors

ID	Task Name	Duration	Start	Finish	Predecessors
1	**MEP Roof Down**	**82 days?**	**Tue 3/8/16**	**Wed 6/29/16**	
2	**L5 Zone 1 (532-561)**	**74 days?**	**Tue 3/8/16**	**Fri 6/17/16**	
3	Hang and tape soffits/Texture/PV/	7 days	Tue 3/8/16	Wed 3/16/16	
4	Paint	2 days	Thu 3/17/16	Fri 3/18/16	3
5	Gypcrete	3 days	Mon 3/21/16	Wed 3/23/16	4
6	Gypcrete dry time	10 days	Thu 3/24/16	Wed 4/6/16	5
7	Electrical trim	5 days	Thu 3/31/16	Wed 4/6/16	6FS-5 days
8	Fire/Sprinkler Trim	1 day?	Thu 3/31/16	Thu 3/31/16	6FS-5 days
9	Install cabinets	8 days	Mon 4/4/16	Wed 4/13/16	6FS-3 days
10	Measure Counter top	1 day	Thu 4/14/16	Thu 4/14/16	9
11	Install Flooring	5 days	Wed 4/13/16	Tue 4/19/16	9FS-1 day
12	Install counter tops	3 days	Thu 4/21/16	Mon 4/25/16	9FS+5 days
13	Intsall Backsplash	3 days	Tue 4/26/16	Thu 4/28/16	12
14	Doors and Millwork	5 days	Fri 4/29/16	Thu 5/5/16	13
15	Drywall Repair ADA	11 days	Fri 5/6/16	Fri 5/20/16	14
16	Paint doors and millwork	8 days	Mon 5/23/16	Wed 6/1/16	15
17	Closet Shelves	3 days	Thu 6/2/16	Mon 6/6/16	16
18	Deliver Appliances	3 days	Thu 6/2/16	Mon 6/6/16	16
19	Plumbing trim	4 days	Tue 6/7/16	Fri 6/10/16	18
20	Final Paint Walls	3 days	Mon 6/13/16	Wed 6/15/16	19
21	Window coverings	2 days	Thu 6/16/16	Fri 6/17/16	20
22					
23	**L4 Zone 1 (432-461)**	**73 days**	**Thu 3/10/16**	**Mon 6/20/16**	
24	Drywall Hang/Tape	5 days	Thu 3/10/16	Wed 3/16/16	3FS-5 days
25	Hang and tape soffits/Texture/PV/	5 days	Thu 3/17/16	Wed 3/23/16	3
26	Paint	2 days	Mon 3/28/16	Tue 3/29/16	25
27	Gypcrete	3 days	Wed 3/30/16	Fri 4/1/16	26
28	Gypcrete dry time	15 days	Mon 4/4/16	Fri 4/22/16	27
29	Electrical trim	5 days	Mon 4/18/16	Fri 4/22/16	28FS-5 days
30	Fire/Sprinkler Trim	5 days	Mon 4/18/16	Fri 4/22/16	28FS-5 days
31	Install cabinets	6 days	Mon 4/25/16	Mon 5/2/16	28
32	Measure Counter top	1 day	Tue 5/3/16	Tue 5/3/16	31
33	Install Flooring	5 days	Wed 5/4/16	Tue 5/10/16	32
34	Install counter tops	3 days	Wed 5/11/16	Fri 5/13/16	33
35	Intsall Backsplash	3 days	Mon 5/16/16	Wed 5/18/16	34
36	Doors and Millwork	5 days	Thu 5/19/16	Wed 5/25/16	35

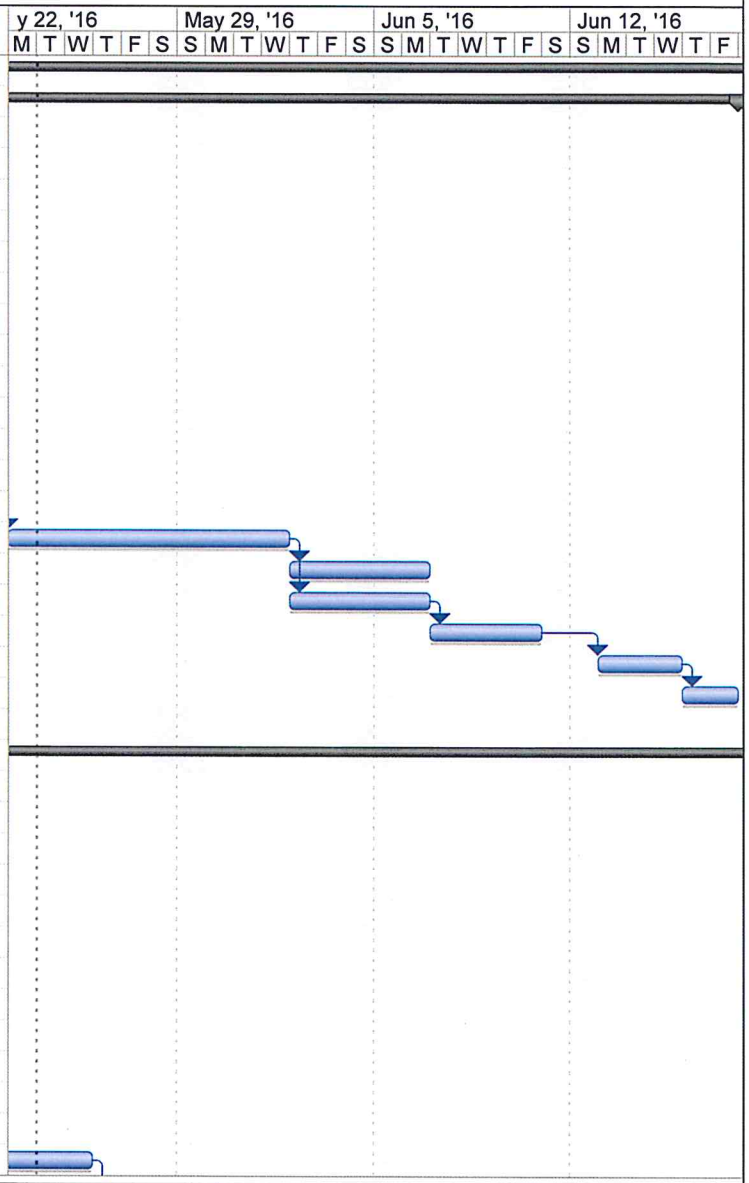

Project: MI Finish 5-23p
Date: Tue 5/24/16

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

Hadley 3 Week Schedule (Interior)
5-23-2016

ID	Task Name	Duration	Start	Finish	Predecessors
37	Drywall Repair ADA	5 days	Thu 5/26/16	Wed 6/1/16	36
38	Paint doors and millwork	10 days	Thu 6/2/16	Wed 6/15/16	37
39	Closet Shelves	3 days	Thu 6/16/16	Mon 6/20/16	38
40	Deliver Appliances	3 days	Thu 6/16/16	Mon 6/20/16	38
41					
42	**L6 Zone 1 (632-661)**	**69 days**	**Thu 3/17/16**	**Tue 6/21/16**	
43	Drywall Hang/Tape	5 days	Thu 3/17/16	Wed 3/23/16	25FS-5 days
44	Hang and tape soffits/Texture/PV/	9 days	Thu 3/24/16	Tue 4/5/16	25
45	Paint	3 days	Wed 4/6/16	Fri 4/8/16	44
46	Gypcrete	3 days	Mon 4/11/16	Wed 4/13/16	45
47	Gypcrete dry time	12 days	Thu 4/14/16	Fri 4/29/16	46
48	Electrical trim	5 days	Mon 4/25/16	Fri 4/29/16	47FS-5 days
49	Fire/Sprinkler Trim	1 day	Mon 4/25/16	Mon 4/25/16	47FS-5 days
50	Install cabinets	6 days	Mon 5/2/16	Mon 5/9/16	47
51	Install Flooring	5 days	Tue 5/10/16	Mon 5/16/16	50
52	Install counter tops	3 days	Tue 5/17/16	Thu 5/19/16	51
53	Intsall Backsplash	3 days	Fri 5/20/16	Tue 5/24/16	52
54	Drywall Repair ADA	5 days	Wed 5/25/16	Tue 5/31/16	53
55	Doors and Millwork	5 days	Wed 6/1/16	Tue 6/7/16	54
56	Paint doors and millwork	10 days	Wed 6/8/16	Tue 6/21/16	55
57					
58	**L3 Zone 1 (332-360)**	**78 days**	**Mon 3/14/16**	**Wed 6/29/16**	
59	Insulation Inspection	1 day	Mon 3/14/16	Mon 3/14/16	3FS-3 days
60	Drywall Hang/Tape	10 days	Tue 3/15/16	Mon 3/28/16	59
61	Frame soffits	2 days	Tue 3/22/16	Wed 3/23/16	60FS-5 days
62	Electrical at soffits	1 day	Thu 3/24/16	Thu 3/24/16	61
63	Vent soffits	2 days	Mon 3/28/16	Tue 3/29/16	62
64	HVAC/ Electrical inspection at sof	1 day	Wed 3/30/16	Wed 3/30/16	63
65	Hang and tape soffits/Texture/PV/	8 days	Thu 3/31/16	Mon 4/11/16	64
66	Paint	3 days	Tue 4/12/16	Thu 4/14/16	65
67	Electrical trim	5 days	Fri 4/15/16	Thu 4/21/16	66
68	Fire/Sprinkler Trim	1 day	Fri 4/15/16	Fri 4/15/16	66
69	Install cabinets	6 days	Tue 5/10/16	Tue 5/17/16	50
70	Install Flooring	5 days	Wed 5/18/16	Tue 5/24/16	69
71	Install counter tops	3 days	Wed 5/25/16	Fri 5/27/16	70
72	Intsall Backsplash	3 days	Mon 5/30/16	Wed 6/1/16	71

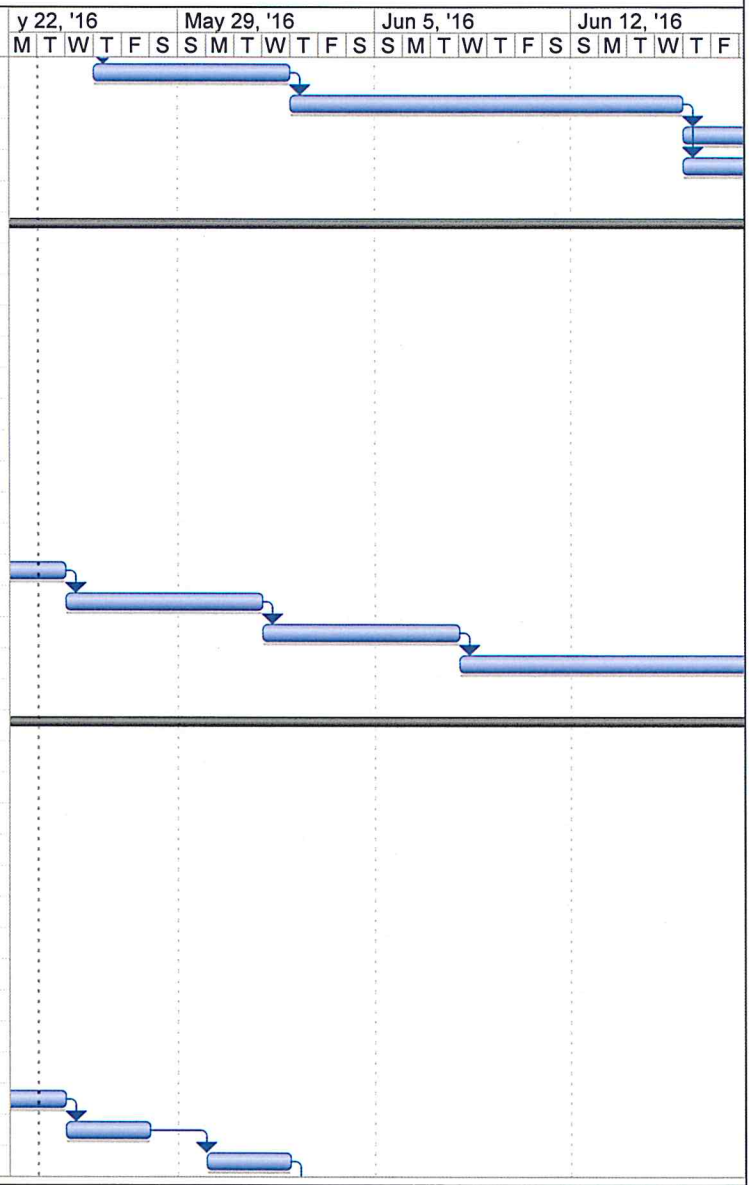

Project: MI Finish 5-23p
Date: Tue 5/24/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
5-23-2016

ID	Task Name	Duration	Start	Finish	Predecessors
73	Drywall Repair ADA	5 days	Thu 6/2/16	Wed 6/8/16	72
74	Doors and Millwork	5 days	Thu 6/9/16	Wed 6/15/16	73
75	Paint doors and millwork	10 days	Thu 6/16/16	Wed 6/29/16	74
76					
77	**L5 Zone 2 (501-531)**	**63 days**	**Wed 3/30/16**	**Fri 6/24/16**	
78	Pre-rock at tubs	1 day	Wed 3/30/16	Wed 3/30/16	
79	Install tubs	3 days	Thu 3/31/16	Mon 4/4/16	78
80	Elec, Plmb Inspections	1 day	Tue 4/5/16	Tue 4/5/16	79
81	Fire Caulk	2 days	Wed 4/6/16	Thu 4/7/16	80
82	Framing inspection	1 day	Fri 4/8/16	Fri 4/8/16	81
83	Insulation	3 days	Mon 4/11/16	Wed 4/13/16	82
84	Insulation Inspection	1 day	Thu 4/14/16	Thu 4/14/16	83
85	Drywall Hang/Tape	6 days	Fri 4/15/16	Fri 4/22/16	84
86	Frame soffits	5 days	Fri 4/22/16	Thu 4/28/16	85FS-1 day
87	Electrical at soffits	2 days	Wed 4/27/16	Thu 4/28/16	86FS-2 days
88	Vent soffits	5 days	Wed 4/27/16	Tue 5/3/16	87FS-2 days
89	Firecaulk soffits	2 days	Mon 5/2/16	Tue 5/3/16	88FS-2 days
90	HVAC/ Electrical inspection at sof	1 day	Wed 5/4/16	Wed 5/4/16	89
91	Hang and tape soffits/Texture/PV/	14 days	Thu 5/5/16	Tue 5/24/16	90
92	Paint	3 days	Wed 5/25/16	Fri 5/27/16	91
93	Gypcrete	3 days	Mon 5/30/16	Wed 6/1/16	92
94	Gypcrete dry time	10 days	Thu 6/2/16	Wed 6/15/16	93
95	Electrical trim	5 days	Thu 6/9/16	Wed 6/15/16	94FS-5 days
96	Fire/Sprinkler Trim	3 days	Thu 6/9/16	Mon 6/13/16	94FS-5 days
97	Install cabinets	10 days	Mon 6/13/16	Fri 6/24/16	94FS-3 days
98					
99	**L4 Zone 2 (401-431)**	**65 days**	**Thu 3/31/16**	**Wed 6/29/16**	
100	Elec, Plmb RI	13 days	Thu 3/31/16	Mon 4/18/16	78
101	Install tubs	6 days	Mon 4/11/16	Mon 4/18/16	121
102	Elec, Plmb Inspections	1 day	Tue 4/19/16	Tue 4/19/16	101
103	Fire Caulk	2 days	Wed 4/20/16	Thu 4/21/16	102
104	Framing inspection	1 day	Fri 4/22/16	Fri 4/22/16	103
105	Insulation	4 days	Mon 4/25/16	Thu 4/28/16	104
106	Insulation Inspection	1 day	Fri 4/29/16	Fri 4/29/16	105
107	Drywall Hang/Tape	5 days	Mon 5/2/16	Fri 5/6/16	106
108	Frame soffits	13 days	Fri 5/6/16	Tue 5/24/16	107FS-1 day

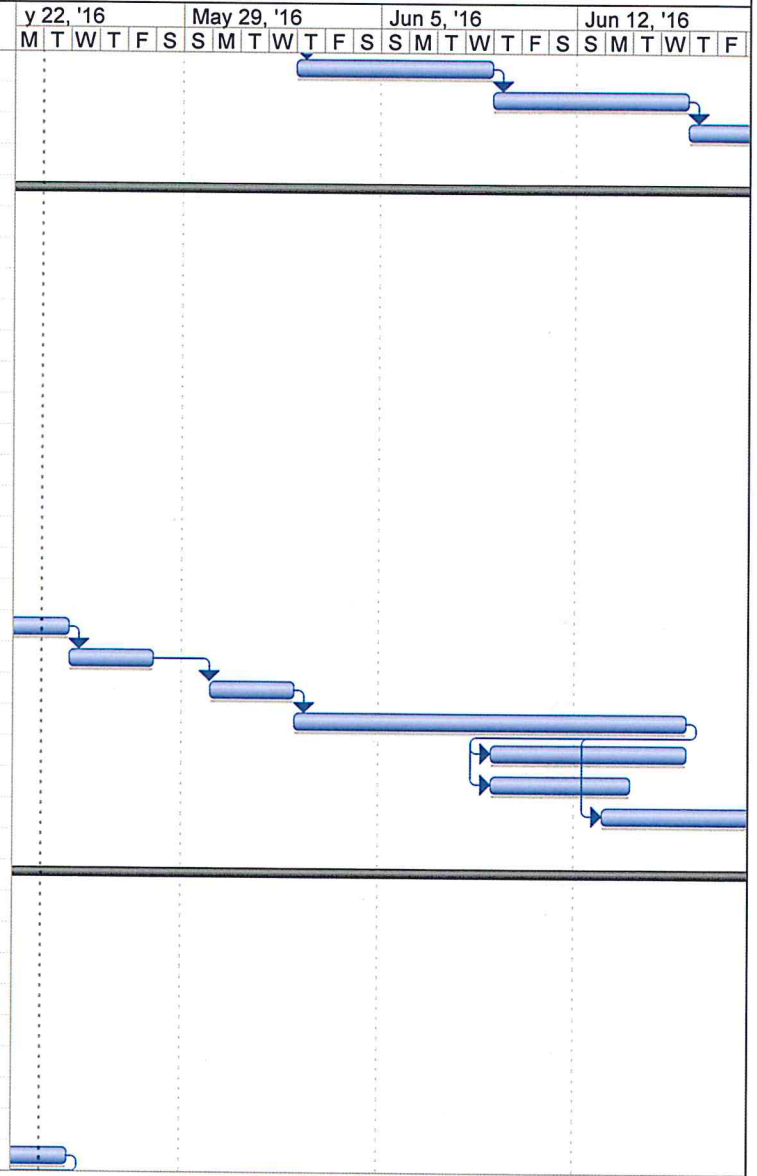

Project: MI Finish 5-23p
Date: Tue 5/24/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
5-23-2016

ID	Task Name	Duration	Start	Finish	Predecessors
109	Electrical at soffits	2 days	Mon 5/23/16	Tue 5/24/16	108FS-2 days
110	Vent soffits	3 days	Mon 5/23/16	Wed 5/25/16	109FS-2 days
111	Firecaulk soffits	2 days	Tue 5/24/16	Wed 5/25/16	110FS-2 days
112	HVAC/ Electrical inspection at soffits	1 day	Thu 5/26/16	Thu 5/26/16	111
113	Hang and tape soffits/Texture/PVA	7 days	Fri 5/27/16	Mon 6/6/16	112
114	Paint	4 days	Tue 6/7/16	Fri 6/10/16	113
115	Gypcrete	3 days	Mon 6/13/16	Wed 6/15/16	114
116	Gypcrete dry time	10 days	Thu 6/16/16	Wed 6/29/16	115
117					
118	**L6 Zone 2 (601-631)**	**61 days**	**Wed 3/30/16**	**Wed 6/22/16**	
119	Sandblast	4 days	Wed 3/30/16	Mon 4/4/16	
120	Elec, Plmb RI	10 days	Tue 4/19/16	Mon 5/2/16	100
121	Install tubs	4 days	Tue 4/5/16	Fri 4/8/16	79
122	Elec, Plmb Inspections	1 day	Tue 5/3/16	Tue 5/3/16	120
123	Fire Caulk	2 days	Wed 5/4/16	Thu 5/5/16	122
124	Framing inspection	1 day	Fri 5/6/16	Fri 5/6/16	123
125	Insulation	4 days	Mon 5/9/16	Thu 5/12/16	124
126	Insulation Inspection	1 day	Fri 5/13/16	Fri 5/13/16	125
127	Drywall Hang/Tape	9 days	Mon 5/16/16	Thu 5/26/16	126
128	Frame soffits	5 days	Thu 5/26/16	Wed 6/1/16	127FS-1 day
129	Electrical at soffits	2 days	Tue 5/31/16	Wed 6/1/16	128FS-2 days
130	Vent soffits	5 days	Tue 5/31/16	Mon 6/6/16	129FS-2 days
131	Firecaulk soffits	2 days	Fri 6/3/16	Mon 6/6/16	130FS-2 days
132	HVAC/ Electrical inspection at soffits	1 day	Tue 6/7/16	Tue 6/7/16	131
133	Hang and tape soffits/Texture/PVA	7 days	Wed 6/8/16	Thu 6/16/16	132
134	Paint	4 days	Fri 6/17/16	Wed 6/22/16	133
135					
136	**L3 Zone 2 (301-331)**	**59 days**	**Tue 4/5/16**	**Fri 6/24/16**	
137	Sandblast	5 days	Tue 4/5/16	Mon 4/11/16	119
138	Install tubs	5 days	Tue 4/19/16	Mon 4/25/16	101
139	elec rough in	10 days	Tue 5/3/16	Mon 5/16/16	120
140	Elec, Plmb Inspections	1 day	Tue 5/17/16	Tue 5/17/16	139
141	Fire Caulk	2 days	Wed 5/18/16	Thu 5/19/16	140
142	Framing inspection	1 day	Fri 5/20/16	Fri 5/20/16	141
143	Insulation	4 days	Mon 5/23/16	Thu 5/26/16	142
144	Insulation Inspection	1 day	Fri 5/27/16	Fri 5/27/16	143

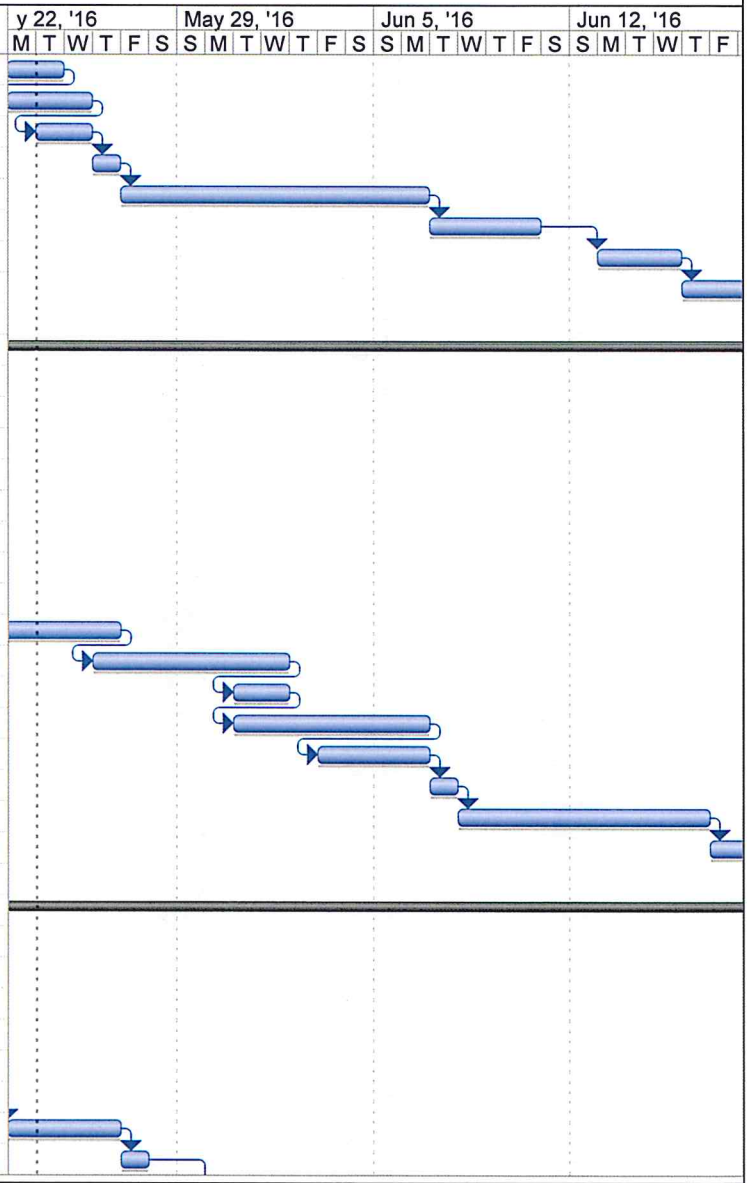

Project: MI Finish 5-23p
Date: Tue 5/24/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
5-23-2016

ID	Task Name	Duration	Start	Finish	Predecessors
145	Drywall Hang/Tape	5 days	Mon 5/30/16	Fri 6/3/16	144
146	Frame soffits	5 days	Fri 6/3/16	Thu 6/9/16	145FS-1 day
147	Electrical at soffits	2 days	Wed 6/8/16	Thu 6/9/16	146FS-2 days
148	Vent soffits	5 days	Wed 6/8/16	Tue 6/14/16	147FS-2 days
149	Firecaulk soffits	2 days	Mon 6/13/16	Tue 6/14/16	148FS-2 days
150	HVAC/ Electrical inspection at soffits	1 day	Wed 6/15/16	Wed 6/15/16	149
151	Hang and tape soffits/Texture/PVA	7 days	Thu 6/16/16	Fri 6/24/16	150

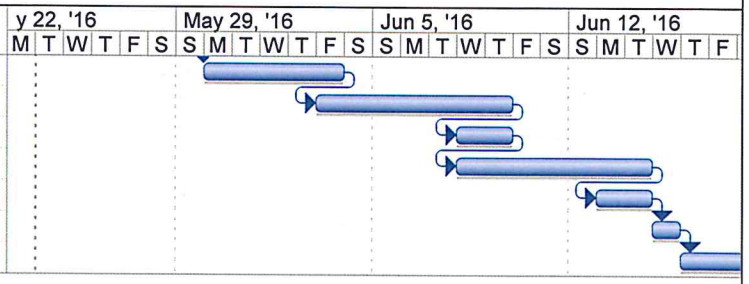

Project: MI Finish 5-23p
Date: Tue 5/24/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
