Hadley 3 Week Schedule (Interior)
6-13-2016

Interior Schedule

ID	Task Name	Duration	Start	Finish	Predecessors
1	**MEP Roof Down**	**43 days**	**Tue 5/31/16**	**Thu 7/28/16**	
2	**L5 Zone 1 (532-561)**	**24 days**	**Mon 6/13/16**	**Thu 7/14/16**	
3	Paint doors and millwork	8 days	Mon 6/13/16	Wed 6/22/16	
4	Closet Shelves	3 days	Thu 6/23/16	Mon 6/27/16	3
5	Deliver Appliances	3 days	Thu 6/23/16	Mon 6/27/16	3
6	Plumbing trim	2 days	Tue 6/28/16	Wed 6/29/16	5
7	Final Paint Walls	3 days	Thu 6/30/16	Mon 7/4/16	6
8	Window coverings	2 days	Tue 7/5/16	Wed 7/6/16	7
9	Final Clean	6 days	Thu 7/7/16	Thu 7/14/16	8
10					
11	**L4 Zone 1 (432-461)**	**33 days**	**Tue 5/31/16**	**Thu 7/14/16**	
12	Intsall Backsplash	5 days	Tue 5/31/16	Mon 6/6/16	
13	Doors and Millwork	5 days	Mon 6/6/16	Fri 6/10/16	
14	Drywall Repair ADA	6 days	Mon 6/13/16	Mon 6/20/16	13
15	Paint doors and millwork	6 days	Tue 6/21/16	Tue 6/28/16	14
16	Closet Shelves	3 days	Wed 6/29/16	Fri 7/1/16	15
17	Deliver Appliances	3 days	Wed 6/29/16	Fri 7/1/16	15
18	Plumbing trim	4 days	Mon 7/4/16	Thu 7/7/16	17
19	Final Paint Walls	3 days	Fri 7/8/16	Tue 7/12/16	18
20	Window coverings	2 days	Wed 7/13/16	Thu 7/14/16	19
21					
22	**L6 Zone 1 (632-661)**	**41 days**	**Thu 6/2/16**	**Thu 7/28/16**	
23	Intsall Backsplash	4 days	Thu 6/2/16	Tue 6/7/16	
24	Drywall Repair ADA	10 days	Mon 6/13/16	Fri 6/24/16	
25	Doors and Millwork	5 days	Mon 6/27/16	Fri 7/1/16	24
26	Paint doors and millwork	9 days	Mon 7/4/16	Thu 7/14/16	25
27	Closet Shelves	3 days	Fri 7/15/16	Tue 7/19/16	26
28	Deliver Appliances	3 days	Fri 7/15/16	Tue 7/19/16	26
29	Plumbing trim	4 days	Wed 7/20/16	Mon 7/25/16	28
30	Final Paint Walls	3 days	Tue 7/26/16	Thu 7/28/16	29
31					
32	**L3 Zone 1 (332-360)**	**34 days**	**Mon 6/6/16**	**Thu 7/21/16**	
33	Intsall Backsplash	5 days	Mon 6/6/16	Fri 6/10/16	
34	Drywall Repair ADA	15 days	Mon 6/13/16	Fri 7/1/16	33
35	Doors and Millwork	5 days	Mon 7/4/16	Fri 7/8/16	34
36	Paint doors and millwork	6 days	Mon 7/11/16	Mon 7/18/16	35

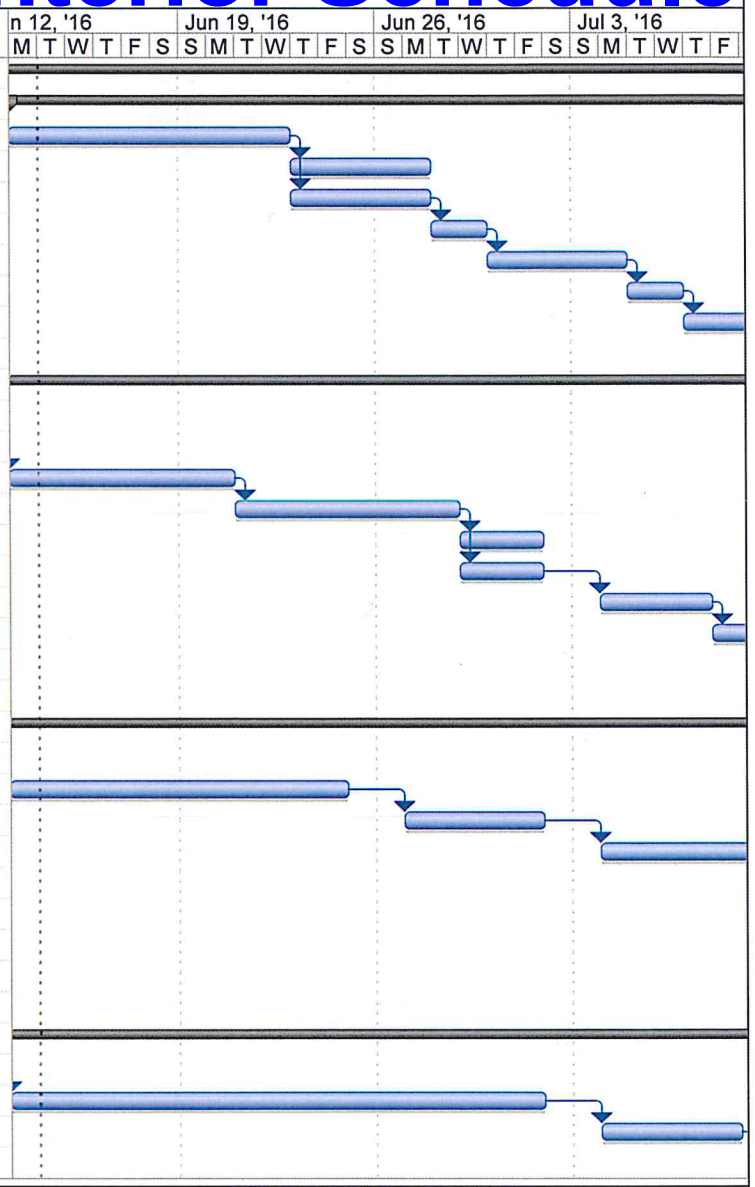

Project: MI Finish 6-13P
Date: Tue 6/14/16

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

Hadley 3 Week Schedule (Interior)
6-13-2016

ID	Task Name	Duration	Start	Finish	Predecessors
37	Closet Shelves	3 days	Tue 7/19/16	Thu 7/21/16	36
38	Deliver Appliances	3 days	Tue 7/19/16	Thu 7/21/16	36
39					
40	**L5 Zone 2 (501-531)**	**26 days**	**Thu 6/2/16**	**Thu 7/7/16**	
41	Gypcrete dry time	10 days	Thu 6/2/16	Wed 6/15/16	
42	Electrical trim	5 days	Thu 6/9/16	Wed 6/15/16	41FS-5 days
43	Fire/Sprinkler Trim	3 days	Thu 6/9/16	Mon 6/13/16	41FS-5 days
44	Install cabinets	10 days	Fri 6/10/16	Thu 6/23/16	41FS-4 days
45	Install Flooring	10 days	Fri 6/17/16	Thu 6/30/16	44FS-5 days
46	Install counter tops	6 days	Tue 6/28/16	Tue 7/5/16	45FS-3 days
47	Intsall Backsplash	6 days	Thu 6/30/16	Thu 7/7/16	46FS-4 days
48					
49	**L4 Zone 2 (401-431)**	**36 days**	**Thu 5/26/16**	**Thu 7/14/16**	
50	Hang and tape soffits/Texture/PVA	12 days	Thu 5/26/16	Fri 6/10/16	
51	Paint	4 days	Mon 6/13/16	Thu 6/16/16	50
52	Gypcrete	3 days	Fri 6/17/16	Tue 6/21/16	51
53	Gypcrete dry time	10 days	Wed 6/22/16	Tue 7/5/16	52
54	Electrical trim	5 days	Wed 6/29/16	Tue 7/5/16	53FS-5 days
55	Fire/Sprinkler Trim	3 days	Wed 6/29/16	Fri 7/1/16	53FS-5 days
56	Install cabinets	10 days	Fri 7/1/16	Thu 7/14/16	53FS-3 days
57					
58	**L6 Zone 2 (601-631)**	**38 days**	**Thu 6/2/16**	**Mon 7/25/16**	
59	Vent soffits	10 days	Thu 6/2/16	Wed 6/15/16	
60	Firecaulk soffits	2 days	Tue 6/14/16	Wed 6/15/16	59FS-2 days
61	HVAC/ Electrical inspection at soffits	1 day	Thu 6/16/16	Thu 6/16/16	60
62	Hang and tape soffits/Texture/PVA	10 days	Fri 6/17/16	Thu 6/30/16	61
63	Paint	4 days	Fri 7/1/16	Wed 7/6/16	62
64	Gypcrete	3 days	Thu 7/7/16	Mon 7/11/16	63
65	Gypcrete dry time	10 days	Tue 7/12/16	Mon 7/25/16	64
66					
67	**L3 Zone 2 (301-331)**	**32 days**	**Mon 5/30/16**	**Tue 7/12/16**	
68	Drywall Hang/Tape	15 days	Mon 5/30/16	Fri 6/17/16	
69	Frame soffits	5 days	Fri 6/17/16	Thu 6/23/16	68FS-1 day
70	Electrical at soffits	2 days	Wed 6/22/16	Thu 6/23/16	69FS-2 days
71	Vent soffits	5 days	Wed 6/22/16	Tue 6/28/16	70FS-2 days
72	Firecaulk soffits	2 days	Mon 6/27/16	Tue 6/28/16	71FS-2 days

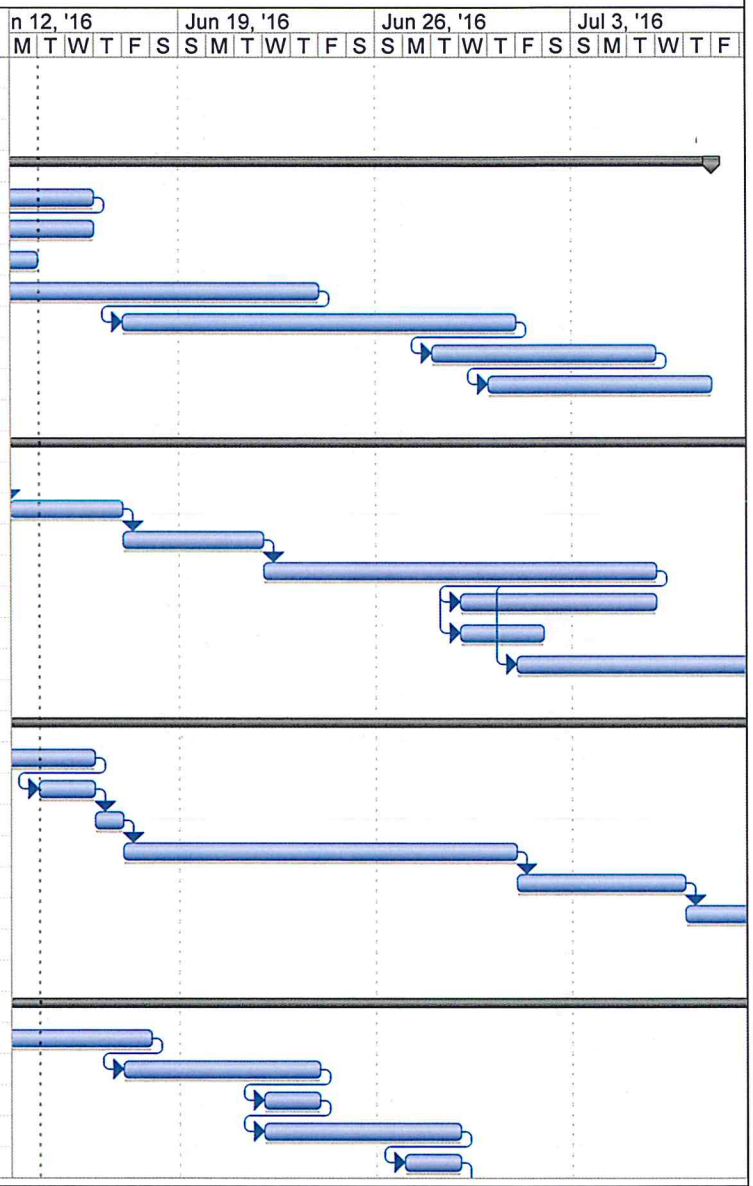

Project: MI Finish 6-13P
Date: Tue 6/14/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
6-13-2016

ID	Task Name	Duration	Start	Finish	Predecessors
73	HVAC/ Electrical inspection at soffits	1 day	Wed 6/29/16	Wed 6/29/16	72
74	Hang and tape soffits/Texture/PVA	9 days	Thu 6/30/16	Tue 7/12/16	73



Project: MI Finish 6-13P
Date: Tue 6/14/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
