CHINN
CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **01**

MEETING DATE: **02/24/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
Charlie Poggemann - CHINN
Lauren Bjorndahl – CHINN
Dan Schaeffer - CHINN
Dave – NW
Lincoln Boomars – LAB
Darryl McNamee - LAB

SAFETY:

1.01 Front end loader onsite, talk with crews about making eye contact with equipment operators

1.02 Dumpster will be located onsite along eastside of jobsite. No food trash is allowed in dumpster.

1.03 Crews to be wearing reflective t-shirts

SCHEDULE:

1.04 reviewed 3 wk look ahead schedule beginning 2/23/15

1.05 LAB to review CPM schedule

OLD BUSINESS: NONE

PERMIT STATUS:

RFIs:

1.06 LBJ RFIs need to show a date required back by and any cost impacts.

1.07 LBJ to address the concrete openings at Level P Stair 2

1.08 LAB discussed RFI to place footing and stem wall in lieu of thickened edge. CHINN to review

SUBMITTALS:

1.09 Transformer Vault rebar shop drawings have been reviewed, LBJ to send out.

NEW BUSINESS:

1.09 IEC to install conduit for placing boom and Elevator

1.10 LAB to send CP an email regarding placing boom staying after L1 deck is placed.

1.11 LAB to do a light and medium broom finish on top of a footing as a mock up.

1.12 MP will set up a whiteboard for scheduling deliveries.

1.13 MP make sure to clean up before the next trade comes through

NEXT MEETING: 03/03/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
2-23-2015

ID		Task Name	Duration	Start	Finish
1		**Mass Excavation**	**12 days**	**Mon 2/23/15**	**Tue 3/10/15**
2		Backfill/Grade NW	5 days	Mon 2/23/15	Fri 2/27/15
3		Export Cont. South	1 day	Wed 2/25/15	Wed 2/25/15
4		Pipe Trenching NW	5 days	Thu 2/26/15	Wed 3/4/15
5		Vapor Barrier/Cap Break NW	4 days	Thu 3/5/15	Tue 3/10/15
6		Backfill/Grade NE	5 days	Wed 3/4/15	Tue 3/10/15
7					
8		**CIP Concrete**	**14 days**	**Mon 2/23/15**	**Thu 3/12/15**
9		F&P Footings Northeast	4 days	Mon 2/23/15	Thu 2/26/15
10		F&P Walls/Columns Level P NE	5 days	Wed 2/25/15	Tue 3/3/15
11		SOG North El 98	1 day	Wed 3/11/15	Wed 3/11/15
12		SOG Ramp	1 day	Thu 3/12/15	Thu 3/12/15
13					
14		**Below Slab Utilities**	**10 days**	**Mon 3/2/15**	**Fri 3/13/15**
15		Sewer NW	4 days	Mon 3/2/15	Thu 3/5/15
16		Slab Drainage NW	4 days	Tue 3/3/15	Fri 3/6/15
17		Utilities NE	5 days	Mon 3/9/15	Fri 3/13/15
18					
19		**Temp Power**	**5 days**	**Mon 2/23/15**	**Fri 2/27/15**
20		Install Panels 5 line	5 days	Mon 2/23/15	Fri 2/27/15

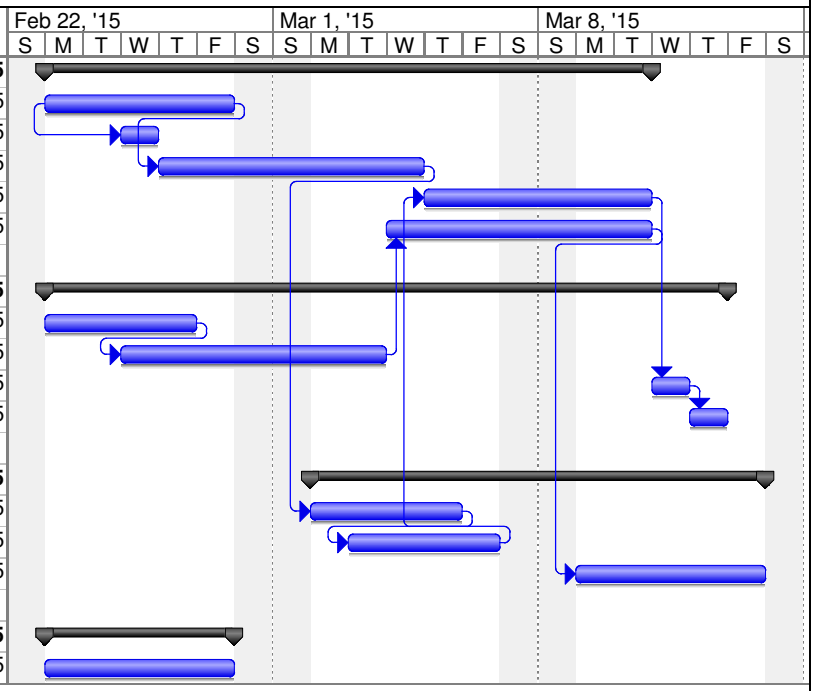

Project: 3wk Look ahead 2-23-15
Date: Fri 2/20/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
