CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **03**

MEETING DATE: **03/17/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
~~Charlie Poggemann – CHINN~~
Sim Mooers
Lauren Bjorndahl – CHINN
Dave Clark– NW
Lincoln Boomars – LAB
~~Darryl McNamee - LAB~~

John Studioso - IEC
Richard Donelson - OWP

SAFETY:

2.01 LNI will be onsite on 03/04 for a consultation
03/17/15: There was an incident with the crane rigger last week. He's ok and back to work. For consultation, do not drive equipment over cords and cover excavated holes.

3.01 Monday Safety meetings are going well. Be sure to remind your crews that the PT deck will be starting on Monday 03/23. Cable rails will be installed at the perimeter.

3.02 Be on the look out for water filled holes and footings from the recent rains.

3.03 Make sure to turn off 480 breaker when not in use. Signage to be placed on panels.

3.04 There needs to be 2 points of egress at all times on the L1 PT deck

SCHEDULE:

3.05 Reviewed 3 wk look ahead schedule beginning 3/16/15

3.06 Contaminted Soil to be hauled on Thursday 03/19/15

OLD BUSINESS:

2.06 Does COMI require a Post Tension precon?
03/17/15: Yes. The Preconstruction meeting is at 10:00 am on 03/24/15

2.07 LBJ briefly discussed IAQ Plan and CWM

PERMIT STATUS:

2.03 CHINN TI permit is with City for review.
03/17/15: TI permit has been issued.

RFIs:

SUBMITTALS:

NEW BUSINESS:

3.07 Can temp power run Clear Water equipment? IEC to look into it.

3.08 Recent rains are causing a lot of mud. Please make sure truck tires are being cleaned.

3.09 CHINN to send final decision on Depressurization System and venting**.**

3.10 PT precon is scheduled for Friday, at 1:30 to 3:00 PM at the CHINN construction office.

3.11 Subcontractors to layout and install cans through the deck. Gridlines will be snapped. Do not use wood screws.

NEXT MEETING: 03/24/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
3-16-2015

ID		Task Name	Duration	Start	Finish
1		**Excavation**	**12 days**	**Mon 3/16/15**	**Tue 3/31/15**
2		Cap Brake/Stego Rem Dock Slab	2 days	Mon 3/16/15	Tue 3/17/15
3		Excavate Footings SE LP	3 days	Mon 3/16/15	Wed 3/18/15
4		Backfill/Grade NE	5 days	Thu 3/19/15	Wed 3/25/15
5		Pipe Trenching NE	5 days	Fri 3/20/15	Thu 3/26/15
6		Vapor Barrier/Cap Break NE	5 days	Wed 3/25/15	Tue 3/31/15
7		Backfill 5 Line	7 days	Mon 3/23/15	Tue 3/31/15
8		Exc Srair 4 ftg	1 day	Wed 3/25/15	Wed 3/25/15
9					
10		**Waterproofing**	**4 days**	**Mon 3/16/15**	**Thu 3/19/15**
11		Clean/Prep Building Separation Walls	3 days	Mon 3/16/15	Wed 3/18/15
12		Apply Epro System B/7/H.5 Line	1 day	Thu 3/19/15	Thu 3/19/15
13					
14		**Utilities**	**1 day**	**Mon 3/16/15**	**Mon 3/16/15**
15		Water Main Sleeves	1 day	Mon 3/16/15	Mon 3/16/15
16					
17		**Underslab Piping**	**7 days**	**Mon 3/23/15**	**Tue 3/31/15**
18		Northeast Storm/Slab Drainage	7 days	Mon 3/23/15	Tue 3/31/15
19		Trench Drain NE Entry	2 days	Mon 3/30/15	Tue 3/31/15
20					
21		**CIP Concrete**	**22 days**	**Mon 3/16/15**	**Tue 4/14/15**
22		F&P Walls/Columns Level P NE	10 days	Mon 3/16/15	Fri 3/27/15
23		Shotcrete SW Corner	3 days	Mon 3/16/15	Wed 3/18/15
24		Form Perimeter for SOG El 98	2 days	Mon 3/16/15	Tue 3/17/15
25		Pour SOG Elev 98	1 day	Wed 3/18/15	Wed 3/18/15
26		Sawcut	1 day	Thu 3/19/15	Thu 3/19/15
27		Pour Stair 4 Ftg	3 days	Thu 3/26/15	Mon 3/30/15
28		Pour SOG NE	1 day	Wed 4/1/15	Wed 4/1/15
29		Sawcut	1 day	Thu 4/2/15	Thu 4/2/15
30		L1 Deck Shoring NW	10 days	Mon 3/16/15	Fri 3/27/15
31		Pour L1 PT NW	1 day	Tue 3/31/15	Tue 3/31/15
32		Stress/Strip	7 days	Mon 4/6/15	Tue 4/14/15

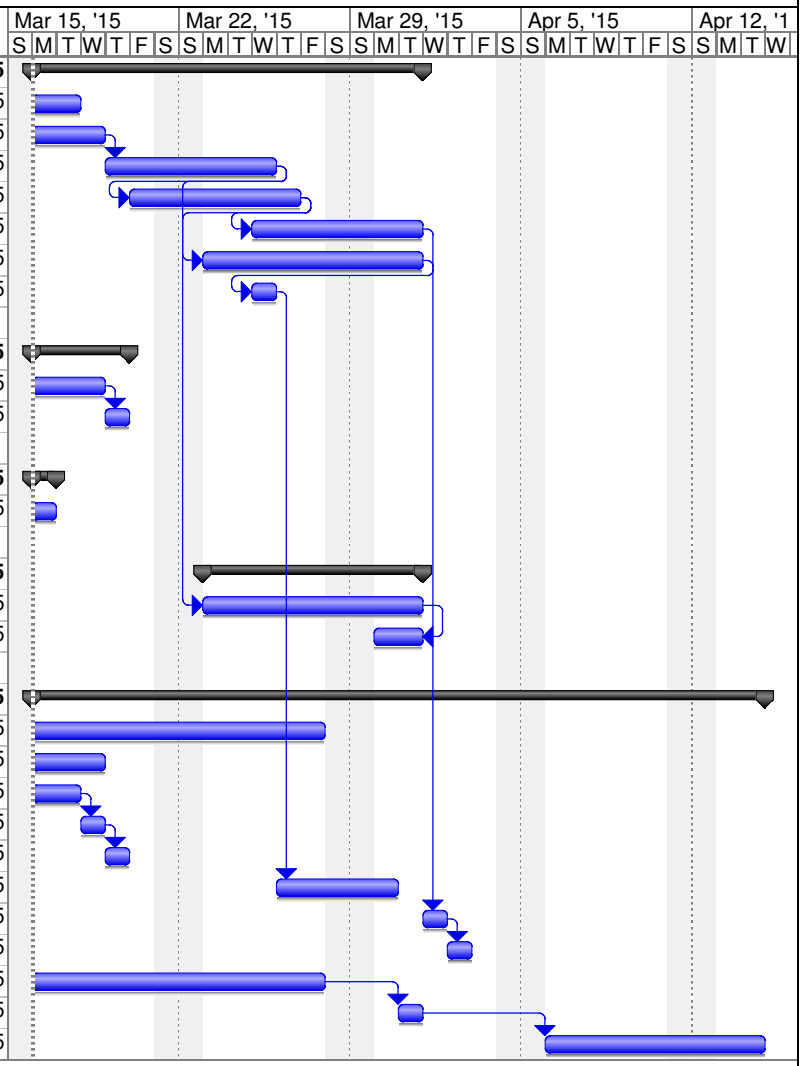

Project: 3wk look ahead 3-16-15
Date: Mon 3/16/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
