CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **04**

MEETING DATE: **03/24/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
Charlie Poggemann – CHINN
Sim Mooers
Lauren Bjorndahl – CHINN
Dave Clark– NW
Lincoln Boomars – LAB
Darryl McNamee - LAB

~~John Studioso - IEC~~
~~Richard Donelson - OWP~~

SAFETY:

3.03 Make sure to turn off 480 breaker when not in use. Signage to be placed on panels.
- 03/24/15: Signage has not been installed

4.01 PCI issued a report from 3rd party safety inspection

SCHEDULE:

4.02 Reviewed 3 wk look ahead schedule beginning 3/23/15
- There will be no work on 03/25/15 for crane repairs
- Placing boom is coming on Monday 03/30/15
- L1 Deck is pouring on 03/31/15 not on 03/27/15
- SOG NE to be placed on 04/09/15
- Lab confirmed PT ceretifications are onsite.

3.06 Contaminated soil to be hauled onThursday 03/19/15
- 03/24/15: Contaminated soil border keeps moving.

OLD BUSINESS:

2.07 LBJ briefly discussed IAQ Plan and CWM

3.07 Can temp power run Clear Water equipment? IEC to look into it.
03/24/15: IEC reviewing routing

3.08 Recent rains are causing a lot of mud. Please make sure truck tires are being cleaned.
03/23/15: All subcontractors must make sure they are cleaning truck tires off.

PERMIT STATUS:

RFIs:

4.03 Lagging walls move in and out, MP to get with LAB for RFI.
4.04 Submit RFI for waterproofing detail at the SW bracing
4.05 Relocate Shaft M33 RFI submitted

SUBMITTALS:

4.06 LBJ to run concrete curing product data by Epro waterproofing.

NEW BUSINESS:

4.07 LAB pulled back waterproofing at A line for concrete form. Axiom to repair.

4.08 PT pour on 03/31/15:

- Terracon will be inspecting as we go.
- The deck will be profiled the afternoon of the 03/26
- Structural Engineer will be onsite at 8:00 am on 03/30/15
- Call City for Monday Inspection

4.09 Does Elevator Lobby receive a troweled finish?

4.10 Island Crest Way off ramp will be closed on the weekend of 03/27.

NEXT MEETING: 03/31/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
3-23-2015

ID		Task Name	Duration	Start	Finish
1		**Excavation**	**13 days**	**Mon 3/23/15**	**Wed 4/8/15**
2		Backfill/Grade NE	5 days	Mon 3/23/15	Fri 3/27/15
3		Pipe Trenching NE	5 days	Thu 3/26/15	Wed 4/1/15
4		Vapor Barrier/Cap Break NE	5 days	Thu 4/2/15	Wed 4/8/15
5		Backfill 5, 7,H.5Line Walls	7 days	Mon 3/23/15	Tue 3/31/15
6		Exc Srair 4 ftg	1 day	Thu 3/26/15	Thu 3/26/15
7					
8		**Crane**	**1 day**	**Wed 3/25/15**	**Wed 3/25/15**
9		Demob 90 Ton	1 day	Wed 3/25/15	Wed 3/25/15
10		Repair Boom	1 day	Wed 3/25/15	Wed 3/25/15
11					
12		**Utilities**	**1 day**	**Wed 3/25/15**	**Wed 3/25/15**
13		Site Utility Precon	1 day	Wed 3/25/15	Wed 3/25/15
14					
15		**Underslab Piping**	**7 days?**	**Mon 3/23/15**	**Tue 3/31/15**
16		Northeast Storm/Slab Drainage	7 days	Mon 3/23/15	Tue 3/31/15
17		Trench Drain NE Entry	2 days	Mon 3/30/15	Tue 3/31/15
18		Run L1 to LP Drain Piping	1 day?	Fri 3/27/15	Fri 3/27/15
19					
20		**CIP Concrete**	**15 days**	**Mon 3/23/15**	**Fri 4/10/15**
21		F&P Walls/Columns Level P NE	6 days	Mon 3/23/15	Mon 3/30/15
22		Pour Stair 4 Ftg	3 days	Fri 3/27/15	Tue 3/31/15
23		Pour SOG NE	1 day	Thu 4/9/15	Thu 4/9/15
24		Sawcut	1 day	Fri 4/10/15	Fri 4/10/15
25		L1 Deck Shoring NW	1 day	Mon 3/23/15	Mon 3/23/15
26		Edgeform/Bottom mat	1 day	Mon 3/23/15	Mon 3/23/15
27		MEP Cans	0.5 days	Tue 3/24/15	Tue 3/24/15
28		Cables /Top mat	2 days	Tue 3/24/15	Wed 3/25/15
29		Smurf	0.5 days	Thu 3/26/15	Thu 3/26/15
30		Inspections	0.5 days	Thu 3/26/15	Thu 3/26/15
31		Pour L1 PT NW 03/31/15	1 day	~~Fri 3/27/15~~	~~Fri 3/27/15~~
32		Stress/Strip	7 days	Mon 3/30/15	Tue 4/7/15

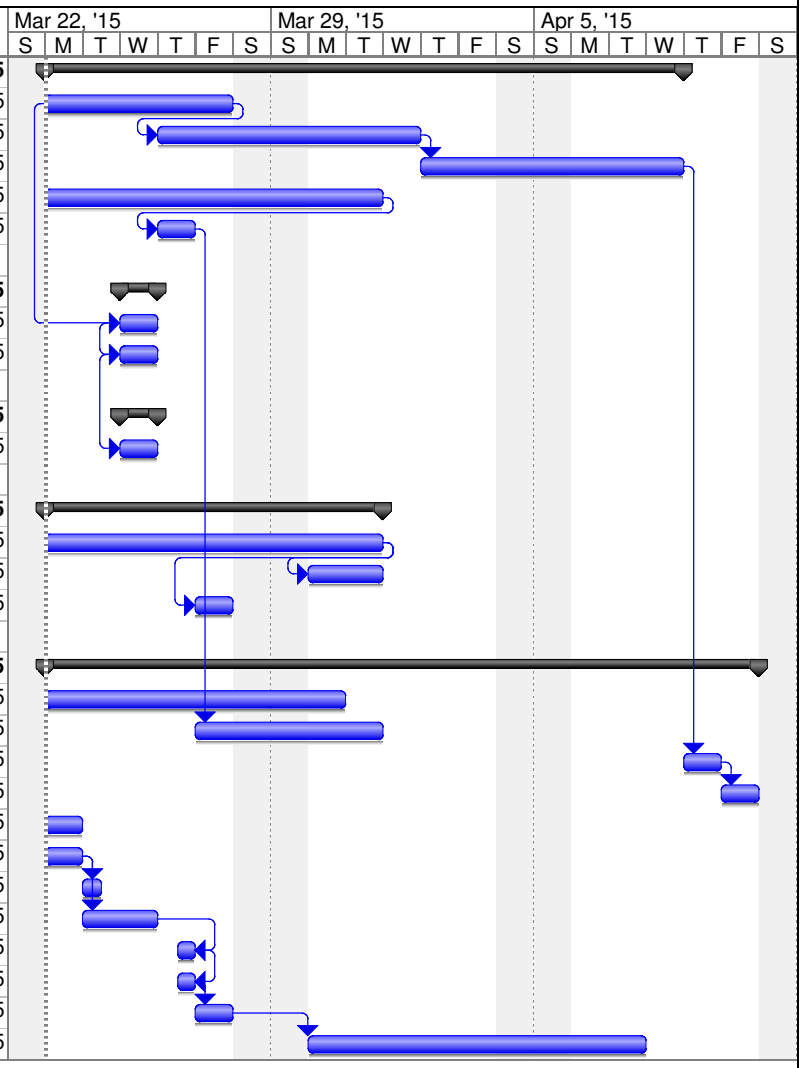

Project: 3wk look ahead 3-23-15
Date: Mon 3/23/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
