CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **08**

MEETING DATE: **04/20/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
~~Charlie Poggemann – CHINN~~
Sim Mooers - CHINN
Lauren Bjorndahl – CHINN
~~Dave Clark - NW~~
~~Lincoln Boomars – LAB~~
~~Darryl McNamee - LAB~~
John Studioso - IEC
Richard Donelson - OWP
~~Bill Huggins - Froula~~

SAFETY:

8.01 At Safety Meeting topics of discussion were

- People crossing between truck and trailer – not acceptable
- No handrails were installed at stairs and floor openings
- All crews using path, need to be mindful of surroundings, keep the volume down and no foul language.

SCHEDULE:

8.02 Reviewed 3 wk look ahead schedule beginning 04/20/15

- WP will be completed at Northside then back fill will begin
- Level 1 Deck NE pours 04/29/15
- Level 2 Deck NW pours 05/07/15

OLD BUSINESS:

7.04 CHINN to get compaction reports from Terracon to Panos where no geopiers were placed

7.07 OWP any shower depressions for Level 2?
04/22/14: No per OAC meeting

PERMIT STATUS:

RFIs:

SUBMITTALS:

7.08 **Please respond to the COMI comments on the deferred submittals. Each comment must have a response.

NEW BUSINESS:

8.03 CHINN to present proposed solution for conflicts at the Below Grade Exhaust Tunnel

8.04 Retail Gas routing to be confirmed

8.05 RD asked how much water is coming into the site from SW corner? Water treatment system can only clean 10 gpm. Basin and pumps are sized for 20 gpm. LBJ to bring up at OAC meeting.

NEXT MEETING: 04/28/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
4-20-2015

ID		Task Name	Duration	Start	Finish
1		**Excavation**	**11 days**	**Mon 4/20/15**	**Mon 5/4/15**
2		Backfill 5, 7,H.5Line Walls	5 days	Tue 4/28/15	Mon 5/4/15
3		Excavate Ftgs SW	3 days	Mon 4/20/15	Wed 4/22/15
4		Backfill 1 Line North	5 days	Thu 4/23/15	Wed 4/29/15
5					
6		**Underslab Piping**	**4 days**	**Thu 4/30/15**	**Tue 5/5/15**
7		Below Slab Drain Lines L1 SW	4 days	Thu 4/30/15	Tue 5/5/15
8					
9		**CIP Concrete**	**14 days**	**Mon 4/20/15**	**Thu 5/7/15**
10		F&P Ftgs SW	5 days	Tue 4/21/15	Mon 4/27/15
11		Shotcrete 10 Line ?	1 day	Tue 4/28/15	Tue 4/28/15
12					
13		**Level 1 PT NE**	**8 days**	**Mon 4/20/15**	**Wed 4/29/15**
14		MEP Layout	0.5 days	Mon 4/20/15	Mon 4/20/15
15		Bottom Mat	1 day	Mon 4/20/15	Mon 4/20/15
16		Profile PT	2 days	Tue 4/21/15	Wed 4/22/15
17		Smurf/Top Mat	2 days	Thu 4/23/15	Fri 4/24/15
18		Inspections	0.5 days	Fri 4/24/15	Fri 4/24/15
19		Pour	1 day	Wed 4/29/15	Wed 4/29/15
20					
21		**Level 2 PT NW**	**14 days**	**Mon 4/20/15**	**Thu 5/7/15**
22		Shore Deck	7 days	Mon 4/20/15	Tue 4/28/15
23		MEP Layout	0.5 days	Wed 4/29/15	Wed 4/29/15
24		Bottom Mat	1 day	Wed 4/29/15	Wed 4/29/15
25		Profile PT	2 days	Thu 4/30/15	Fri 5/1/15
26		Smurf/Top Mat	2 days	Mon 5/4/15	Tue 5/5/15
27		Inspections	0.5 days	Tue 5/5/15	Tue 5/5/15
28		Pour	1 day	Thu 5/7/15	Thu 5/7/15

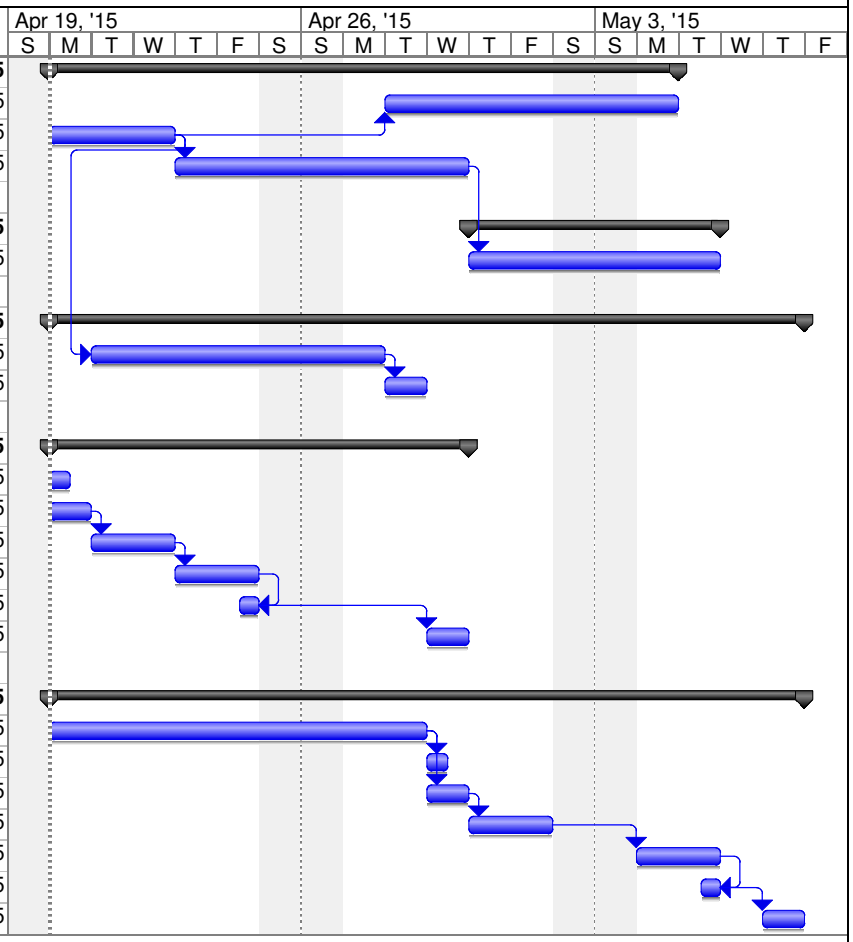

Project: 3wk look ahead 4-20-15
Date: Mon 4/20/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
