CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **13**

MEETING DATE: **05/26/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
~~Charlie Poggemann – CHINN~~
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
~~Darryl McNamee – LAB~~
John Studioso - IEC
Richard Donelson - OWP
~~Bill Huggins - Froula~~
Dave Clark– NW
Lincoln Boomars – LAB
Dave Hamacher

SAFETY:

13.01 Housekeeping

- CC to install temporary/permanent cable rails
- Reminder all subcontractors to be re-covering holes
- Always make sure toe boards are installed
- Remind crews – there is no smoking onsite
- Keep goat trails clear of debris
- Dumpster will be back Monday, 6/1

SCHEDULE:

13.02 Reviewed 3 wk look ahead schedule beginning 05/26/15

- SOG East to GL-G will be poured on 5/21
- Level 2 PT NE Pours 5/29, EOR is scheduled for 5/28 inspection
- Level 2 PT SW Pours 6/9
- Utilities to be complete in about a week and a half. (less gas and permanent power)

OLD BUSINESS:

7.04 CHINN to get compaction reports from Terracon to Panos where no geopiers were placed

8.04 Retail Gas routing to be confirmed

- 04/28/15: CHINN has a meeting with PSE and Infrasource today
- 05/05/15: There are two meters, (1) Residential (1) Commercial. One line will go to the retail space with T's. Install an extra sleeve.

9.03 Water Meter Vaults are under construction.

- Review Building has a 6"and 4"

- Review Vault has 4" and 3"
- 05/12/15: RFI has been issued to CPL
- 05/26/15: LBJ to follow up.

11.03 IEC needs approximately 2 days to get power to 2nd placing boom.

- 05/26/15 IEC will hook up power by the end of this week.

12.08 What are the irrigation needs at Level 3?

PERMIT STATUS:

RFIs:

12.04 CC to look up mat foundation at PSE Vault

SUBMITTALS:

NEW BUSINESS:

13.03 CHINN to talk with owner about getting PSE vault onsite to verify offsets. The lid is not centered on the vault.

13.04 New Clearwater system to be up and running by Thursday. 2nd baker tank to be removed 5/27.

13.05 Deck drains at L2 PT NE to be set at 5 ½" from top of step.

13.06 Stair 1 will have an energized standpipe for wood framing above the transfer deck

13.07 The perimeter drains need to get routed to underground drainage system and tested for pH and turbidity.

13.08 CHINN to follow up with updated CADs

NEXT MEETING: 06/02/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
5-26--2015

ID		Task Name	Duration	Start	Finish
1		**Excavation**	**5 days**	**Tue 5/26/15**	**Mon 6/1/15**
2		Excavate Rem. Ftgs South to Retail	2 days	Tue 5/26/15	Wed 5/27/15
3		Slab on Grade Prep South to GL-G	5 days	Tue 5/26/15	Mon 6/1/15
4					
5		**Instreet Utilities**	**5 days**	**Tue 5/26/15**	**Mon 6/1/15**
6		Rem Hydrants	2 days	Tue 5/26/15	Wed 5/27/15
7		Fire Line Taps	2 days	Thu 5/28/15	Fri 5/29/15
8		Set Water Vaults	2 days	Tue 5/26/15	Wed 5/27/15
9		Tap Water line	1 day	Mon 6/1/15	Mon 6/1/15
10					
11		**Underslab Piping**	**3 days**	**Tue 5/26/15**	**Thu 5/28/15**
12		Below Slab Drain Lines L1 SE	3 days	Tue 5/26/15	Thu 5/28/15
13					
14		**Stormwater Treatment**	**4 days**	**Mon 6/1/15**	**Thu 6/4/15**
15		Set Int System	2 days	Mon 6/1/15	Tue 6/2/15
16		Demob Equipment	2 days	Wed 6/3/15	Thu 6/4/15
17					
18		**CIP Concrete**	**19 days**	**Tue 5/26/15**	**Fri 6/19/15**
19		F&P Remaining L1 South Ftgs	2 days	Tue 5/26/15	Wed 5/27/15
20		Pour Stair 3 Walls	1 day	Tue 5/26/15	Tue 5/26/15
21		Shotcrete Rem South Wall	1 day	Mon 6/1/15	Mon 6/1/15
22		F&P Remaining Columns L1 South	3 days	Tue 5/26/15	Thu 5/28/15
23		SOG To Ret Step	1 day	Wed 5/27/15	Wed 5/27/15
24		Retail SOG	1 day	Tue 6/2/15	Tue 6/2/15
25					
26		**Level 2 PT NE**	**11 days**	**Tue 5/26/15**	**Tue 6/9/15**
27		MEP Cans	1 day	Tue 5/26/15	Tue 5/26/15
28		Profile PT	1 day	Tue 5/26/15	Tue 5/26/15
29		Top Mat/Smurf	2 days	Wed 5/27/15	Thu 5/28/15
30		Inspections	0.5 days	Wed 5/27/15	Wed 5/27/15
31		Pour	1 day	Fri 5/29/15	Fri 5/29/15
32		Stress/Strip	6 days	Tue 6/2/15	Tue 6/9/15
33					
34		**Level 2 PT NW**	**9 days**	**Tue 5/26/15**	**Fri 6/5/15**

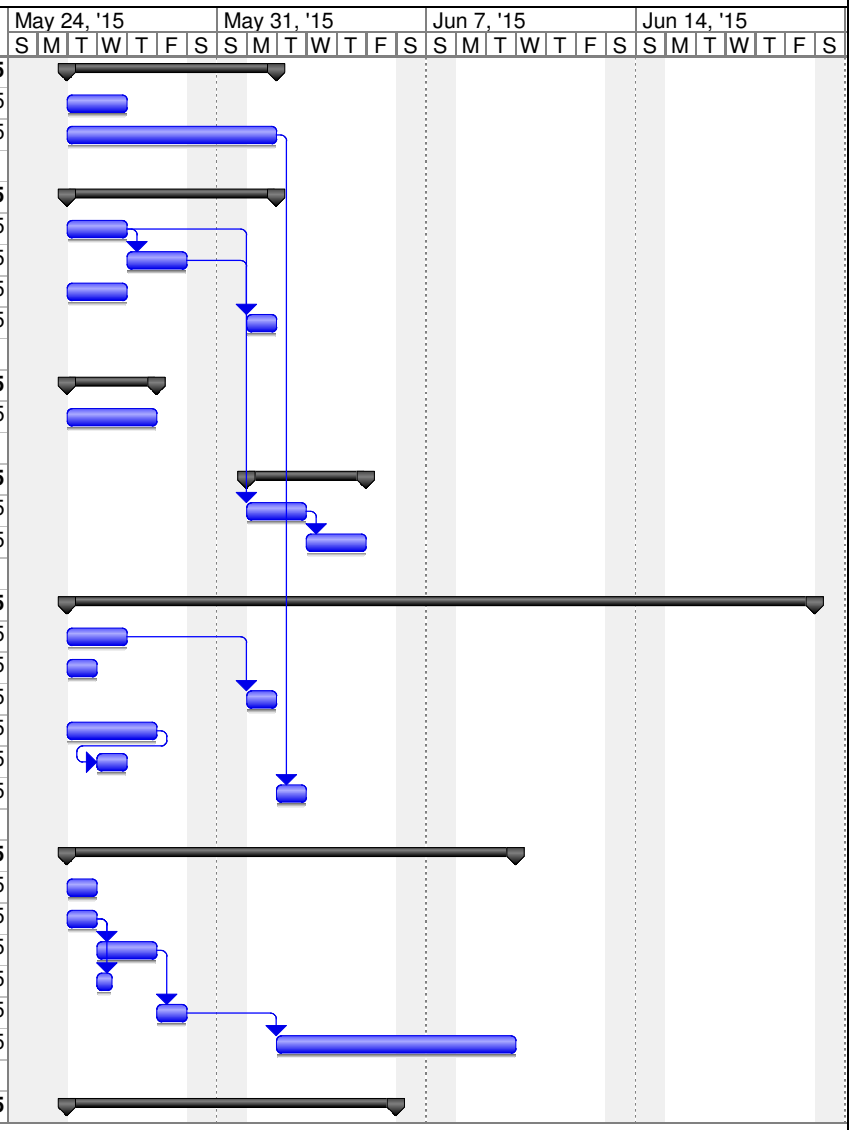

Project: 3wk look ahead 5-26-15
Date: Fri 5/22/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
5-26--2015

ID		Task Name	Duration	Start	Finish
35		Striip	2 days	Tue 5/26/15	Wed 5/27/15
36		Walls/Columns to L3	7 days	Thu 5/28/15	Fri 6/5/15
37					
38		**Level 2 PT SW**	**19 days**	**Tue 5/26/15**	**Fri 6/19/15**
39		Shore/Deck	6 days	Tue 5/26/15	Tue 6/2/15
40		Profile PT	2 days	Wed 6/3/15	Thu 6/4/15
41		Top Mat/Smurf	1 day	Fri 6/5/15	Fri 6/5/15
42		Inspections	0.5 days	Fri 6/5/15	Fri 6/5/15
43		Pour	1 day	Tue 6/9/15	Tue 6/9/15
44		Stress/Strip	6 days	Fri 6/12/15	Fri 6/19/15

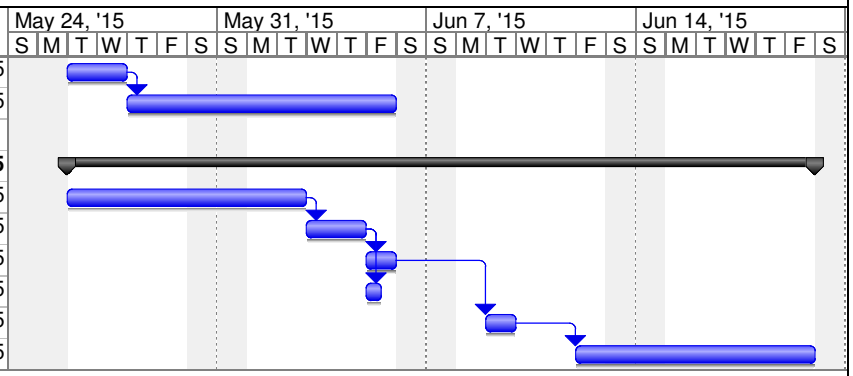

Project: 3wk look ahead 5-26-15
Date: Fri 5/22/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
