CHINN
CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **14**

MEETING DATE: **06/02/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
~~Charlie Poggemann – CHINN~~
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
Darryl McNamee – LAB-

~~John Studioso - IEC~~
Richard Donelson - OWP
~~Bill Huggins - Froula~~
Dave Clark– NW
~~Lincoln Boomars – LAB~~
~~Dave Hamacher~~

SAFETY:

14.01 Housekeeping

- Reminder all subcontractors to be re-covering holes
- Remind crews – there is no smoking onsite
- Keep goat trails clear of debris
- Sweep and clean up for the next trade
- Forklift operators – be on the look out for obstacles, (plumbing stub ups, FDCs etc.)

SCHEDULE:

14.02 Reviewed 3 wk look ahead schedule beginning 06/01/15

- 1 hydrant at SE to install
- SOG to Retail Slab 6/5
- Retail SOG pour 6/12
- Level 2 PT SW Pours 6/9
- Level 2 PT NE Stress/Strip 6/1-6/8
- Level 2 PT NW Walls/Columns to L3 6/1-6/8

OLD BUSINESS:

8.04 Retail Gas routing to be confirmed

- 04/28/15: CHINN has a meeting with PSE and Infrasource today
- 05/05/15: There are two meters, (1) Residential (1) Commercial. One line will go to the retail space with T's. Install an extra sleeve.
- 06/02/15: Routing being reviewed by ownership. Final meter location approval is with PSE/Infrasource

9.03 Water Meter Vaults are under construction.

- o Review Building has a 6"and 4"

    - Review Vault has 4" and 3"
- 05/12/15: RFI has been issued to CPL
- 05/26/15: LBJ to follow up.
- 06/02/15: RFI 74 response was issued.

12.08 What are the irrigation needs at Level 3?

13.03 CHINN to talk with owner about getting PSE vault onsite to verify offsets. The lid is not centered on the vault.

13.06 Stair 1 will have an energized standpipe for wood framing above the transfer deck
- **06/02/15: Correction, not energized**

PERMIT STATUS:

RFIs:

14.08 FDC Signage RFi

14.09 Backing at stairs with drywall

SUBMITTALS:

NEW BUSINESS:

14.03 NWC to provide cutsheet for sump pump adjacent to water vaults

14.04 NWC will be backfilling North wall to exhaust tunnel

14.05 Meeting request will be sent out for a Transfer Slab precon, to discuss penetrations, layout and panel drawings

14.06 CHINN to check into getting HM door for Fire Sprinkler room, OWP can get backflow preventers intalled

14.07 CHINN to schedule meeting with Fire Marshal before wood framing

NEXT MEETING: 06/09/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
6-1-2015

ID		Task Name	Duration	Start	Finish
1		**Excavation**	**7 days**	**Mon 6/1/15**	**Tue 6/9/15**
2		Slab on Grade Prep West to Retail	2 days	Mon 6/1/15	Tue 6/2/15
3		Backfill North Wall	5 days	Wed 6/3/15	Tue 6/9/15
4		Exc Retail Ftgs	2 days	Wed 6/3/15	Thu 6/4/15
5		SOG Prep SE Retail	2 days	Mon 6/1/15	Tue 6/2/15
6					
7		**Instreet Utilities**	**6 days?**	**Mon 6/1/15**	**Mon 6/8/15**
8		Rem Hydrants	2 days	Mon 6/1/15	Tue 6/2/15
9		Tap Domestic Water	2 days	Mon 6/1/15	Tue 6/2/15
10		Set Water Vaults	2 days	Wed 6/3/15	Thu 6/4/15
11		Set Meters/Tie to Structure	2 days	Fri 6/5/15	Mon 6/8/15
12			1 day?	Fri 6/5/15	Fri 6/5/15
13		**Underslab Piping**	**3 days**	**Mon 6/1/15**	**Wed 6/3/15**
14		Below Slab Drain Lines L1 SE	3 days	Mon 6/1/15	Wed 6/3/15
15					
16		**Stormwater Treatment**	**15 days**	**Mon 6/1/15**	**Fri 6/19/15**
17		Treat Contaminated Water & Discharge	15 days	Mon 6/1/15	Fri 6/19/15
18					
19		**CIP Concrete**	**15 days**	**Mon 6/1/15**	**Fri 6/19/15**
20		F&P Remaining L1 South Ftgs/Stair 1	3 days	Mon 6/1/15	Wed 6/3/15
21		Shotcrete Rem South Wall/Ramp	1 day	Mon 6/8/15	Mon 6/8/15
22		Columns L2 South	1 day	Wed 6/3/15	Wed 6/3/15
23		SOG To Ret Step	1 day	Fri 6/5/15	Fri 6/5/15
24		Retail SOG	1 day	Fri 6/5/15	Fri 6/5/15
25					
26		**Level 2 PT NE**	**6 days**	**Mon 6/1/15**	**Mon 6/8/15**
27		Stress/Strip	6 days	Mon 6/1/15	Mon 6/8/15
28					
29		**Level 2 PT NW**	**5 days**	**Mon 6/1/15**	**Fri 6/5/15**
30		Walls/Columns to L3	5 days	Mon 6/1/15	Fri 6/5/15
31					
32		**Level 2 PT SW**	**15 days**	**Mon 6/1/15**	**Fri 6/19/15**
33		Shore/Deck	2 days	Mon 6/1/15	Tue 6/2/15
34		Profile PT	2 days	Wed 6/3/15	Thu 6/4/15

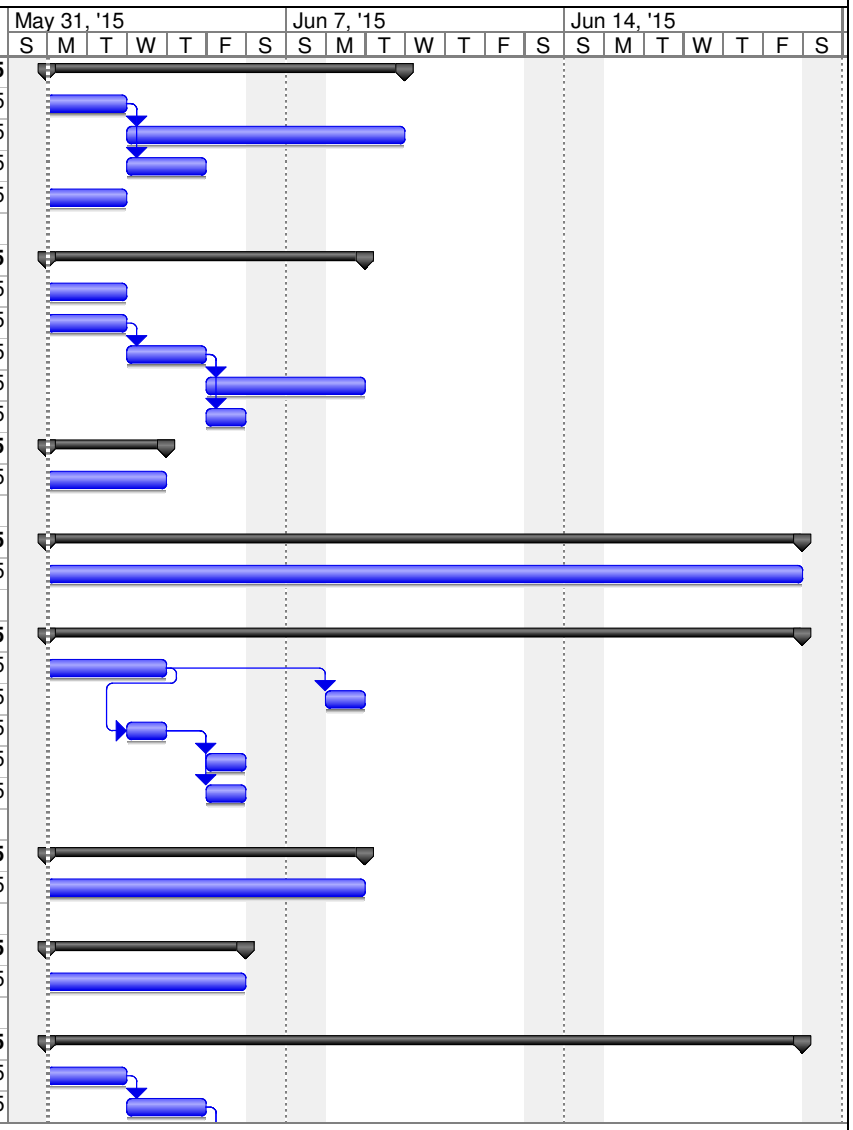

Project: 3wk look ahead 6-1-15
Date: Mon 6/1/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
6-1-2015

ID		Task Name	Duration	Start	Finish
35		Top Mat/Smurf	1 day	Fri 6/5/15	Fri 6/5/15
36		Inspections	0.5 days	Fri 6/5/15	Fri 6/5/15
37		Pour	1 day	Tue 6/9/15	Tue 6/9/15
38		Stress/Strip	6 days	Fri 6/12/15	Fri 6/19/15



Project: 3wk look ahead 6-1-15
Date: Mon 6/1/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
