CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **15**

MEETING DATE: **06/09/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
Charlie Poggemann – CHINN
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
~~Darryl McNamee – LAB~~

John Studioso - IEC
Richard Donelson - OWP
~~Bill Huggins - Froula~~

Lincoln Boomars – LAB
~~Dave Hamacher~~

SAFETY:

15.01 Housekeeping

- Remind crews – there is no smoking onsite
- Keep Parking lot clean
- Sweep and clean up for the next trade in work areas
- Forklift operators – be on the look out for obstacles, (plumbing stub ups, FDCs etc.)
- Crewman stepped on nail last Friday. No lost time
- Lunchrooms/Job shacks space is available in Parking garage
- Crews to stay hydrated

SCHEDULE:

14.02 Reviewed 3 wk look ahead schedule beginning 06/08/15

- Retail SOG pour 6/26
- Level 2 PT NE Strip/reshore 6/8-6/15
- Level 3 PT NW pours 7/8
- Level 2 PT SW pours 6/9 – today
- OWP/IEC pick out rooms for storage

OLD BUSINESS:

12.08 What are the irrigation needs at Level 3?

13.03 **CHINN to talk with owner about getting PSE vault onsite to verify offsets.** The lid is not centered on the vault.

14.03 **NWC to provide cutsheet for sump pump adjacent to water vaults**

14.06 **CHINN to check into getting HM door for Fire Sprinkler room, OWP can get backflow preventers installed**
06/09/15: LBJ to check on submittal review status

14.07 **CHINN to schedule Precon W/ COMI- Fire Marshal before wood framing**

PERMIT STATUS:

RFIs:

14.09 **Backing at stairs with drywall**

SUBMITTALS:

NEW BUSINESS:

15.01 Transfer Deck meeting is today at 10:30 am.

NEXT MEETING: 06/16/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
6-8-2015

ID		Task Name	Duration	Start	Finish
1		**Excavation**	**16 days**	**Mon 6/8/15**	**Mon 6/29/15**
2		Backfill North Wall	3 days	Mon 6/8/15	Wed 6/10/15
3		Stockpile West	4 days	Thu 6/11/15	Tue 6/16/15
4		Exc Retail Ftgs	3 days	Wed 6/10/15	Fri 6/12/15
5		Slab Drain Trenches	2 days	Wed 6/24/15	Thu 6/25/15
6		SOG Prep SE Retail	2 days	Fri 6/26/15	Mon 6/29/15
7					
8		**Instreet Utilities**	**3 days**	**Mon 6/8/15**	**Wed 6/10/15**
9		Complete /Backfill PIV/Water	2 days	Mon 6/8/15	Tue 6/9/15
10		Set Water Meters/Tie to Structure	3 days	Mon 6/8/15	Wed 6/10/15
11					
12		**Underslab Piping**	**3 days**	**Fri 6/26/15**	**Tue 6/30/15**
13		Below Slab Drain Lines L1 SE Retail	3 days	Fri 6/26/15	Tue 6/30/15
14					
15		**CIP Concrete**	**31 days**	**Mon 6/8/15**	**Mon 7/20/15**
16		F&P Remaining L1 South Ftgs Retail	2 days	Mon 6/15/15	Tue 6/16/15
17		Shotcrete West Wall to LE	3 days	Tue 6/16/15	Thu 6/18/15
18		Columns L2 South	4 days	Thu 6/18/15	Tue 6/23/15
19		Pour Retail SOG	1 day	Fri 6/26/15	Fri 6/26/15
20					
21		**Level 2 PT NE**	**6 days**	**Mon 6/8/15**	**Mon 6/15/15**
22		Strip/Reshore	6 days	Mon 6/8/15	Mon 6/15/15
23		F&P Walls/Columns	4 days	Mon 6/8/15	Thu 6/11/15
24					
25		**Level 3 PT NW**	**28 days**	**Thu 6/11/15**	**Mon 7/20/15**
26		Shore/Deck	7 days	Thu 6/11/15	Fri 6/19/15
27		Layout/Drains	2 days	Mon 6/22/15	Tue 6/23/15
28		Bottom Matt/Sleeve	2 days	Wed 6/24/15	Thu 6/25/15
29		Edgeform/Misc Steel	2 days	Thu 6/25/15	Fri 6/26/15
30		Profile Tendons	2 days	Mon 6/29/15	Tue 6/30/15
31		Top Matt/Smurf	2 days	Wed 7/1/15	Thu 7/2/15
32		Raised Slab Edge/Blockouts	3 days	Fri 7/3/15	Tue 7/7/15
33		Inspections	1 day	Tue 7/7/15	Tue 7/7/15
34		Pour	1 day	Wed 7/8/15	Wed 7/8/15

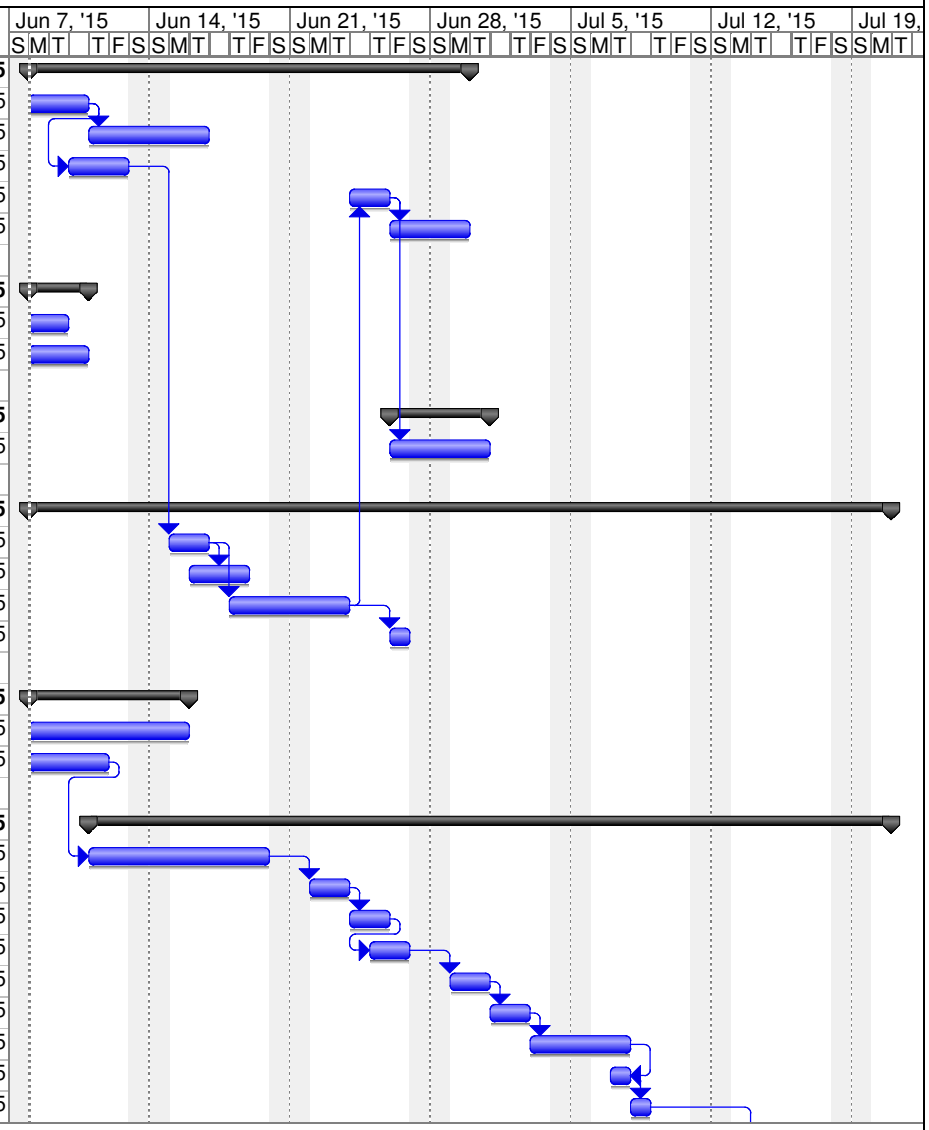

Project: 3wk look ahead 6-8-15
Date: Mon 6/8/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
6-8-2015

ID		Task Name	Duration	Start	Finish
35		Stress/Strip	5 days	Tue 7/14/15	Mon 7/20/15
36					
37		**Level 2 PT SW**	**11 days**	**Mon 6/8/15**	**Mon 6/22/15**
38		Inspections	1 day	Mon 6/8/15	Mon 6/8/15
39		Pour	1 day	Tue 6/9/15	Tue 6/9/15
40		Stress/Strip	6 days	Mon 6/15/15	Mon 6/22/15
41		F&P Walls/Columns	7 days	Wed 6/10/15	Thu 6/18/15

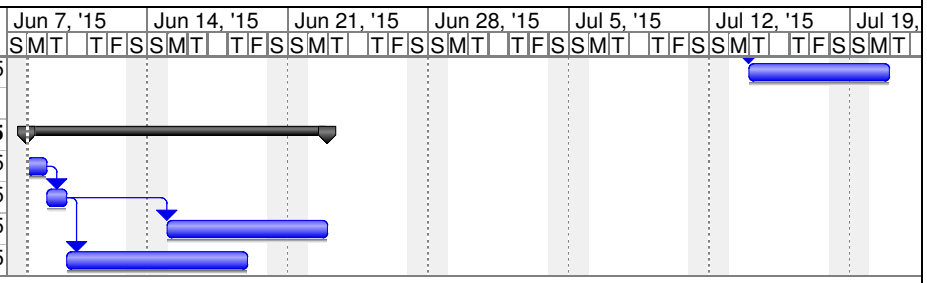

Project: 3wk look ahead 6-8-15
Date: Mon 6/8/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
