CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **18**

MEETING DATE: **07/01/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
~~Charlie Poggemann – CHINN~~
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
Darryl McNamee – LAB
Jesse Earle - Froula

~~John Studioso - IEC~~
Richard Donelson - OWP
~~Bill Huggins - Froula~~
~~Joe Barnhart - OWP~~
~~Lincoln Boomars – LAB~~
~~Dave Hamacher~~

SAFETY:

18.01 Housekeeping

- No smoking onsite
- Keep Parking lot clean
- Sweep and clean up for the next trade in work areas
- Forklift operators – be on the lookout for obstacles, (plumbing stub ups, FDCs etc.)
- Lunchrooms/Job shacks space is available in Parking garage
- Crews to stay hydrated
- There is no food allowed in the building when framing starts
- IEC to install Temp lighting in the garage
- No Mark or Sim onsite 7/2-76

SCHEDULE:

18.02 Reviewed **SITE** 3 wk look ahead schedule beginning 06/29/15

- Retail SOG pour 7/9
- Level 3 PT NW pours 7/8
  - EOR, Terracon, COMI inspections on 7/6
- Level 3 PT NE pours 7/23, Framer is snapping lines 7/9
- Level 3 PT SW pours 8/14, Framer snapping lines 8/5
- Wood Framing Layout Walls 8/3
- 07/06/15: BRH to layout GL 2, 4, F and J

XX.XX Reviewed **INTERIOR** 3wk look ahead schedule beginning xx/xx/xx

OLD BUSINESS:

12.08 What are the irrigation needs at Level 3?

- 07/01/15: Landscaper will be onsite later today.

13.03 **CHINN to talk with owner about getting PSE vault onsite to verify offsets.** The lid is not centered on the vault.

- 06/16/15: CC to discuss at owner's meeting for the layout for the underground vault and get vault installed and backfilled.
- 06/24/15: Owner is corresponding with PSE for vaults. Looking for vaults at the end of July

14.03 **NWC to provide cutsheet for sump pump adjacent to water vaults**

- 06/16/15: LBJ to follow up with NWC
- 07/01/15: LBJ to submit for approval

14.06 **CHINN to check into getting HM door for Fire Sprinkler room, OWP can get backflow preventers installed**
06/09/15: LBJ to check on submittal review status
06/16/15: Plumbing equipment Submittals were distributed 06/15
07/01/15: LBJ get doors ordered

17.03 Review kitchen electric outlets conflicts with collector studs at units 341, 347, 349 – Add furring wall

- 07/01/15: IEC to review

17.04 There is no hose bib on the roof

- 07/01/15: OWP to review

17.07 Still aiming to get rid of Clearwater system

- 07/01/15: OWP to look into what else is needed for final system. RD mentioned that a temp pump might want to be used. CHINN to get a schematic of the Final System by Glacier. Team to review system regarding volume and pressure.

PERMIT STATUS:

RFIs:

14.09 **Backing at stairs with drywall**

SUBMITTALS:

NEW BUSINESS:

18.03 Steel Stud Framer will be onsite on Tuesday. Start framing FACP room, Water treatment room

18.04 CHINN to send PSE Gas Meter Layout to OWP once received

18.05 OWP would like to order tubs/showers. LBJ needs final fixture submittal to submit.

18.06 OWP needs 2x6 walls in Units B3 and Unit G. Also there is plumbing conflict at RFI 66 Leasing Office Door and plumbing. LBJ to address at OAC Meeting.

18.07 SE Sanitary Sewer Conflict – alternative route goes to city for quick review.
7/1 CPL revising drawing
7/2 NWC patch back sawcut from original route
7/6 Sawcut new location

18.08 How much room does LAB need for the banded tendons on construction joint?
8' off of the edge

18.09 LAB to give Mark a list of Terracon inspections for next week.

18.10 LAB will be pouring Level 2 Closure strip on Monday

NEXT MEETING: 07/07/15**, time 10:00, at Jobsite office.**

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
6-29-2015

ID		Task Name	Duration	Start	Finish	Predecesso	R N
1		**Excavation**	**7 days**	**Mon 6/29/15**	**Wed 7/8/15**		
2		Exc Retail Ftgs	1 day	Mon 6/29/15	Mon 6/29/15		
3		Slab Drain Trenches	1 day	Mon 6/29/15	Mon 6/29/15		
4		SOG Prep SE Retail	2 days	Tue 7/7/15	Wed 7/8/15	3FS+4 days	
5		Backfill West	5 days	Mon 6/29/15	Mon 7/6/15		
6							
7		**Instreet Utilities**	**5 days**	**Mon 6/29/15**	**Mon 7/6/15**		
8		Sanitary South	5 days	Mon 6/29/15	Mon 7/6/15		
9							
10		**Underslab Piping**	**1 day**	**Mon 6/29/15**	**Mon 6/29/15**		
11		Below Slab Drain Lines L1 SE Retail	1 day	Mon 6/29/15	Mon 6/29/15		
12							
13		**CIP Concrete**	**43 days**	**Mon 6/29/15**	**Thu 8/27/15**		
14		F&P Remaining L1 South Ftgs/Col's Retail	2 days	Tue 6/30/15	Wed 7/1/15	2	
15		Stair 4/Columns	5 days	Tue 6/30/15	Tue 7/7/15	2	
16		Pour Retail SOG	1 day	Thu 7/9/15	Thu 7/9/15	15FS+1 day	
17							
18		**Level 3 PT NW**	**17 days**	**Mon 6/29/15**	**Wed 7/22/15**		
19		Profile Tendons	1 day	Mon 6/29/15	Mon 6/29/15		
20		Top Matt/Smurf	2 days	Tue 6/30/15	Wed 7/1/15	19	
21		Raised Slab Edge/Blockouts	3 days	Thu 7/2/15	Tue 7/7/15	20	
22		Inspections	1 day	Tue 7/7/15	Tue 7/7/15	21FF	
23		Pour	1 day	Wed 7/8/15	Wed 7/8/15	22	
24		Stress/Strip	7 days	Tue 7/14/15	Wed 7/22/15	23FS+3 day	
25							
26		**Level 3 PT NE**	**30 days**	**Mon 6/29/15**	**Mon 8/10/15**		
27		Shore/Deck	8 days	Mon 6/29/15	Thu 7/9/15		
28		Layout/Sleeves	2 days	Fri 7/10/15	Mon 7/13/15	27	
29		Bottom Mat/Sleeves	3 days	Tue 7/14/15	Thu 7/16/15	28	
30		Edgeform/Misc Sleeves	2 days	Fri 7/17/15	Mon 7/20/15	29	
31		Raised Slab Edge/Blockouts	2 days	Mon 7/20/15	Tue 7/21/15	30FS-1 day	
32		Inspections	1 day	Wed 7/22/15	Wed 7/22/15	31	
33		Pour	1 day	Thu 7/23/15	Thu 7/23/15	32	
34		Stress/Strip	7 days	Wed 7/29/15	Thu 8/6/15	33FS+3 day	

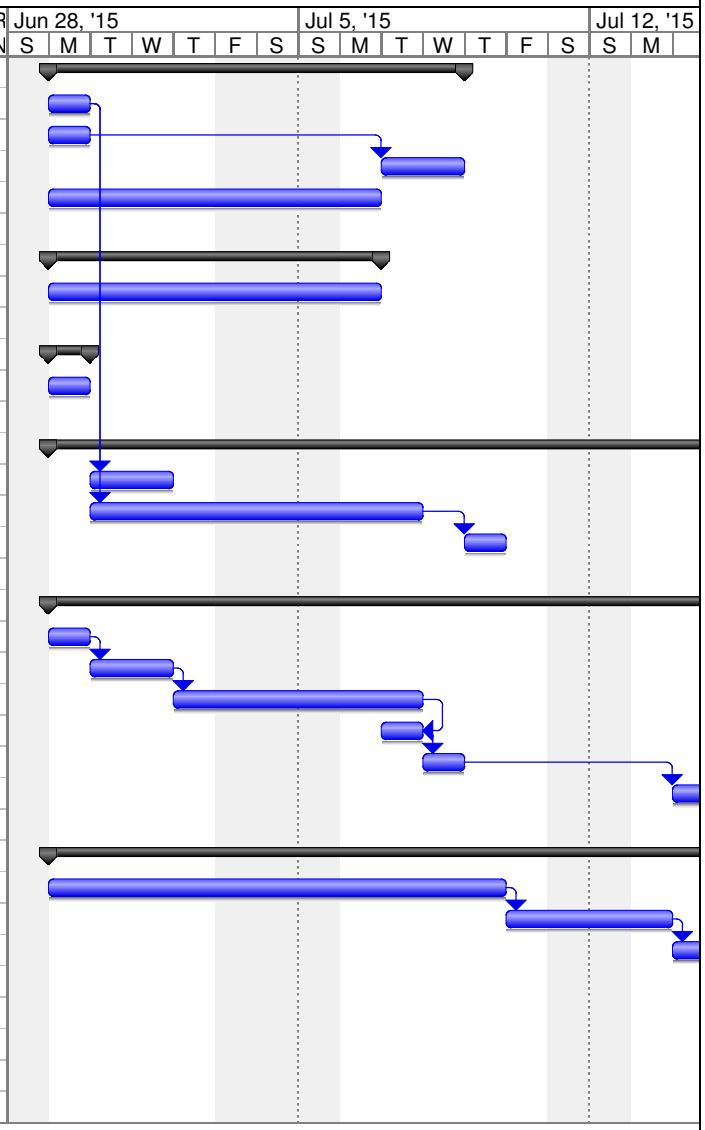

Project: 3wk look ahead 6-22-15
Date: Fri 6/26/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
6-29-2015

ID		Task Name	Duration	Start	Finish	Predecesso	R N
35		Remove Reshores North	2 days	Fri 8/7/15	Mon 8/10/15	34	
36							
37		**Level 3 PT SW**	**26 days**	**Thu 7/23/15**	**Thu 8/27/15**		
38		Shore/Deck	9 days	Thu 7/23/15	Tue 8/4/15	24	
39		Layout/Sleeves	2 days	Wed 8/5/15	Thu 8/6/15	38	
40		Bottom Mat/Sleeves	2 days	Fri 8/7/15	Mon 8/10/15	39	
41		Edgeform/Misc	2 days	Tue 8/11/15	Wed 8/12/15	40	
42		Raised Slab Edge	2 days	Thu 8/13/15	Fri 8/14/15	41	
43		Inspections	1 day	Thu 8/13/15	Thu 8/13/15	41	
44		Pour	1 day	Fri 8/14/15	Fri 8/14/15	43	
45		Stress/Strip	7 days	Wed 8/19/15	Thu 8/27/15	44FS+2 day	
46							
47		**Wood Framing NW**	**14 days**	**Mon 8/3/15**	**Thu 8/20/15**		
48		Layout Walls	1 day	Mon 8/3/15	Mon 8/3/15	33FS+6 day	
49		Frame	5 days	Tue 8/4/15	Mon 8/10/15	48	
50		TJI Joists	4 days	Tue 8/11/15	Fri 8/14/15	49	
51		Deck	4 days	Mon 8/17/15	Thu 8/20/15	50	

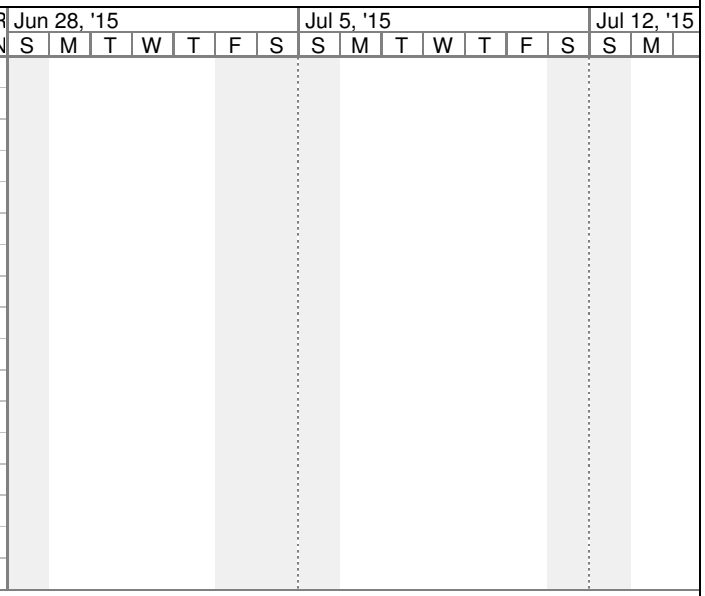

Project: 3wk look ahead 6-22-15
Date: Fri 6/26/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
6-29-2015

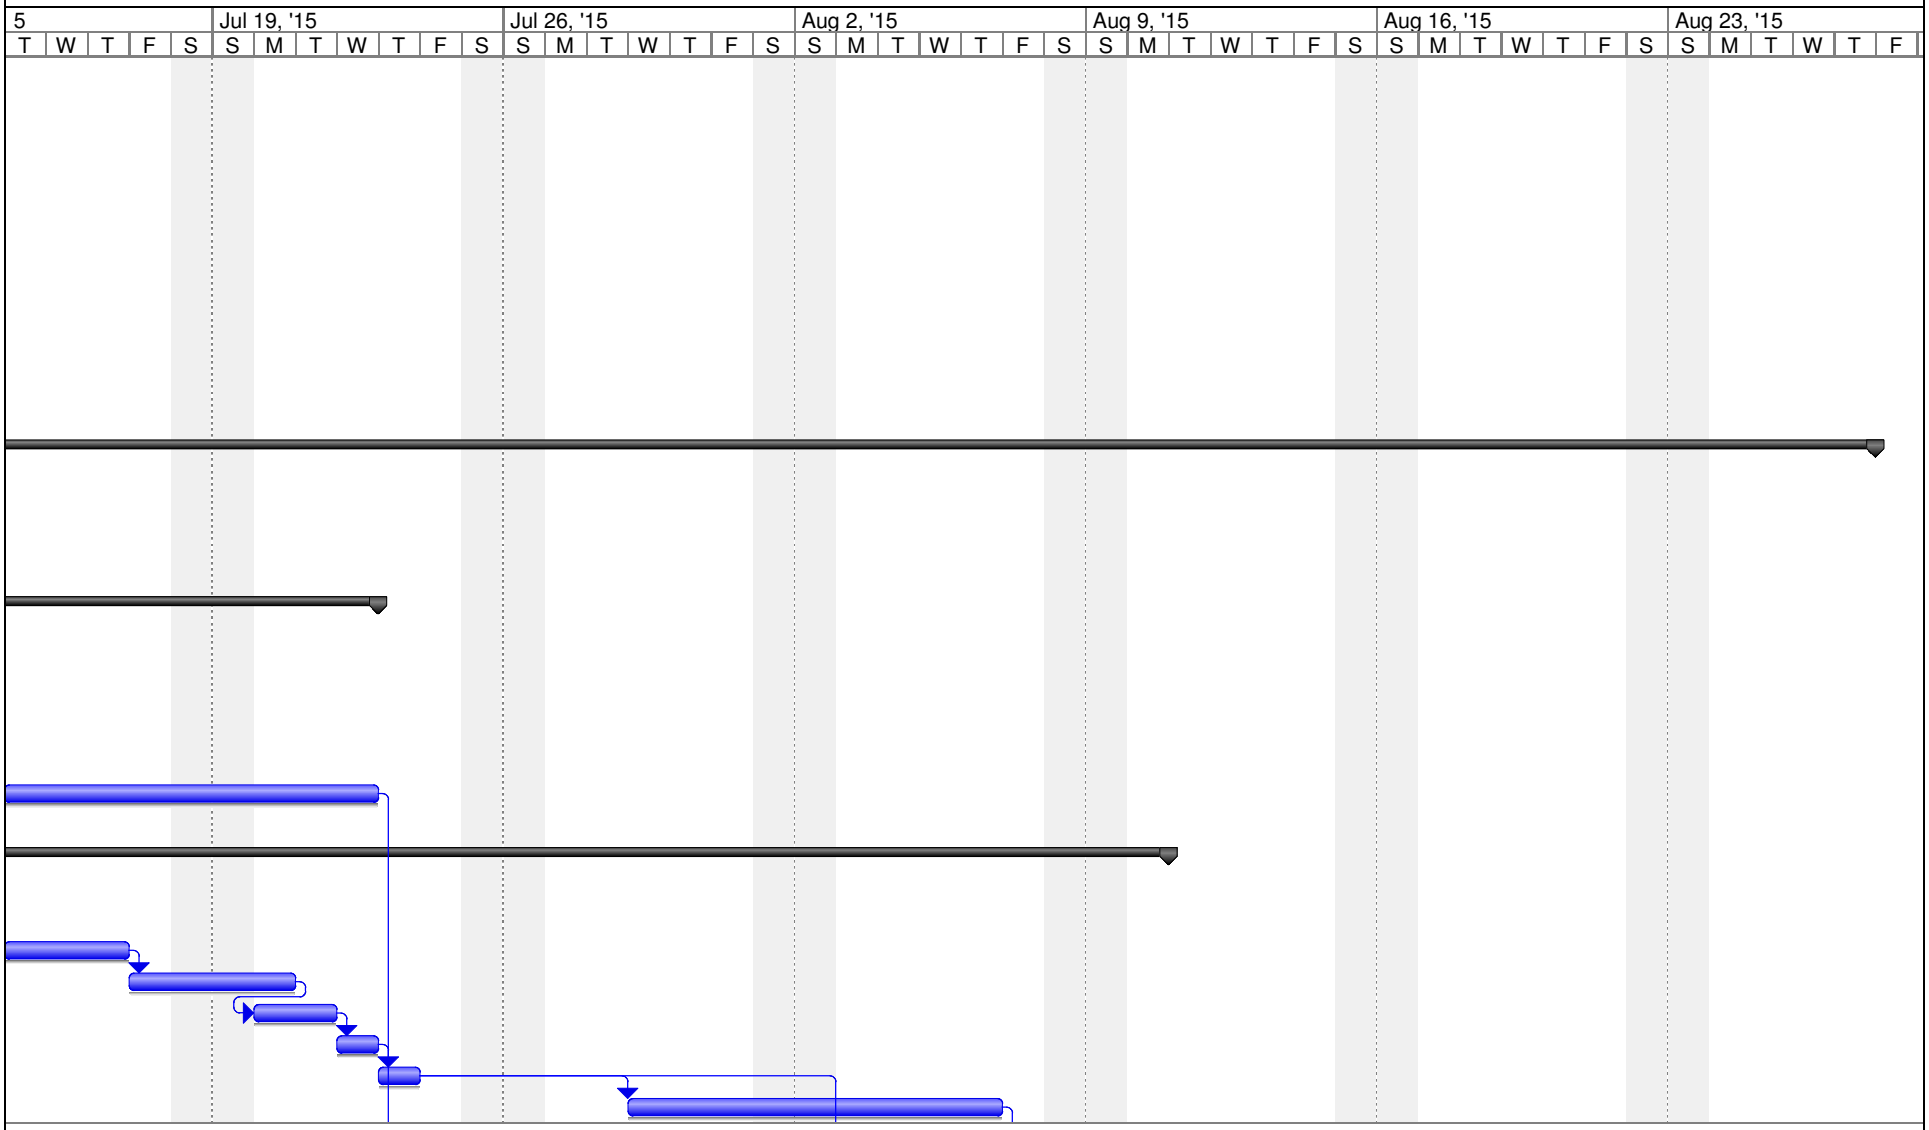

Project: 3wk look ahead 6-22-15
Date: Fri 6/26/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
6-29-2015

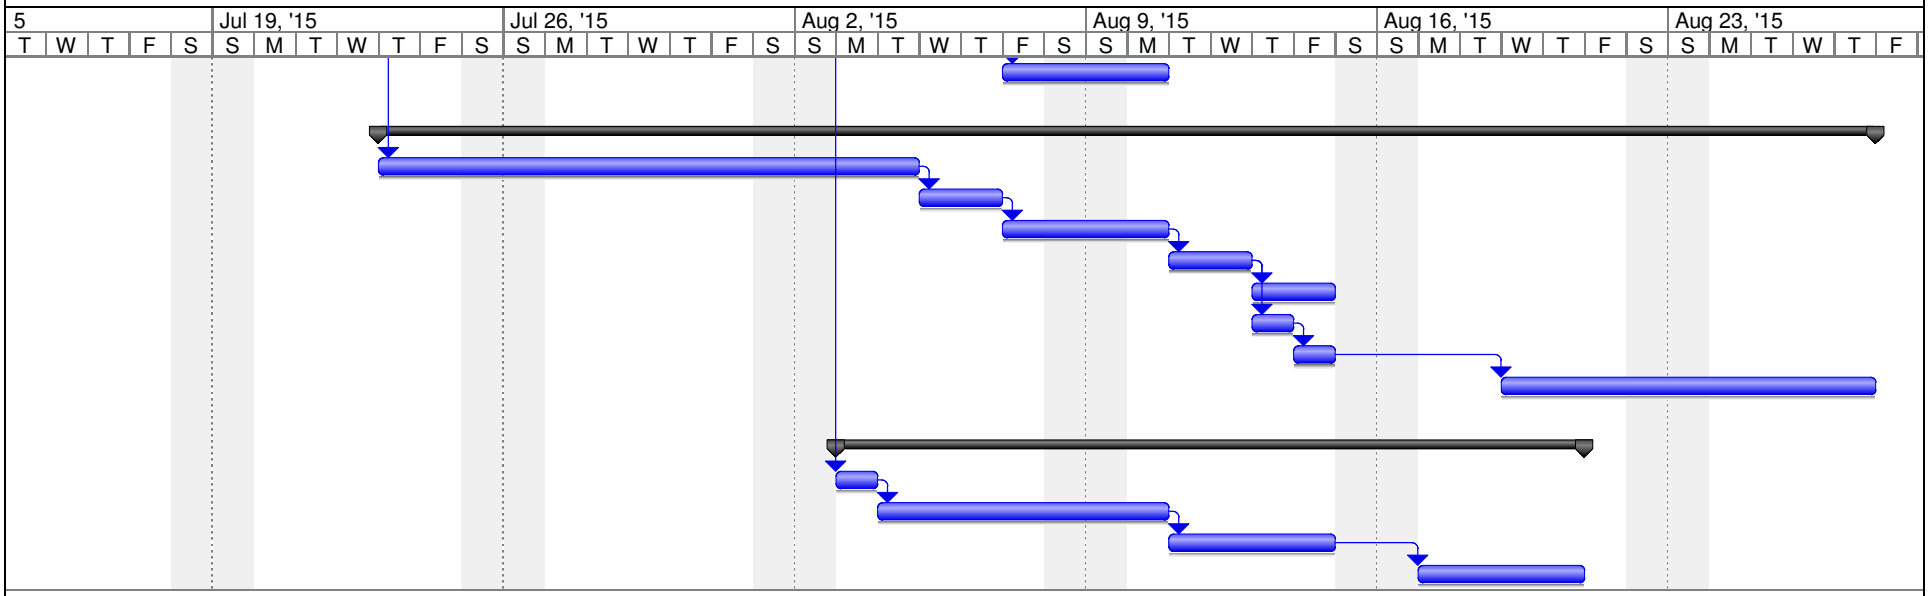

Project: 3wk look ahead 6-22-15
Date: Fri 6/26/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
