CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **20**

MEETING DATE: **07/14/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
~~Charlie Poggemann – CHINN~~
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
Darryl McNamee – LAB
~~Jesse Earle - Froula~~
~~John Studioso - IEC~~
~~Richard Donelson - OWP~~
~~Bill Huggins - Froula~~
Joe Barnhart - OWP
~~Lincoln Boomars – LAB~~
~~Dave Hamacher~~

SAFETY:

20.01 Housekeeping

- No smoking onsite
- Sweep and clean up for the next trade in work areas
- Forklift operators – be on the lookout for obstacles, (plumbing stub ups, FDCs etc.)
- There is no food allowed in the building when framing starts
- Framer will install handrail once LAB removes theirs.
- Big Equipment will be back in 2 weeks
- Security will be down at construction parking to monitor. If rules are violated there is a Verbal/Written/gone policy
- CHINN has new field personnel Eric Bull.
- As reshore is removed, more temp lighting in the garage is required.

SCHEDULE:

20.02 Reviewed **SITE** 3 wk look ahead schedule beginning 07/13/15

- Level 2 PT SE Layout/Sleeves 7/20
- Level 3 PT NW Stress and strip
- Level 3 PT NE pours 7/23, Inspections 7/22
- Level 3 PT SW pours 8/14, Shore/deck 7/21-7/31
- Wood Framing Layout Walls 8/3
- Once reshore is gone, CHINN will sweep the decks clean, then each trade is responsible for cleaning up,

XX.XX Reviewed **INTERIOR** 3wk look ahead schedule beginning xx/xx/xx

OLD BUSINESS:

12.08 What are the irrigation needs at Level 3?

- 07/01/15: Landscaper will be onsite later today.
- 07/07/15: Landscaper will be attending next OAC meeting

14.03 **NWC to provide cutsheet for sump pump adjacent to water vaults**

- 06/16/15: LBJ to follow up with NWC
- 07/01/15: LBJ to submit for approval

14.06 **CHINN to check into getting HM door for Fire Sprinkler room, OWP can get backflow preventers installed**
06/09/15: LBJ to check on submittal review status
06/16/15: Plumbing equipment Submittals were distributed 06/15
07/01/15: LBJ get doors ordered

17.04 There is no hose bib on the roof

- 07/01/15: OWP to review
- 07/07/15: Find a location in a warm wall for hose bib

17.07 Still aiming to get rid of Clearwater system

- 07/01/15: OWP to look into what else is needed for final system. RD mentioned that a temp pump might want to be used. CHINN to get a schematic of the Final System by Glacier. Team to review system regarding volume and pressure.
- 07/07/15: LBJ emailed Glacier for final schematic
- 07/14/15: Pending Schematic

PERMIT STATUS: Fire Sprinkler/Electrical/Fire Alarm

RFIs:

14.09 **Backing at stairs with drywall**

SUBMITTALS:

NEW BUSINESS:

20.03 7/27-8/7 NWC will be trenching from 27th street along east side of project for PSE conduits

20.04 LAB to leave hole covers in place. If they are removed by other trades, hole covers are to be replaced and fastened down.

20.05 Temporary FDC will run outside up the building to Level 3 at patio at gridline 3

20.06 OWP has a drain set outside the building at gl 3

20.07 CHINN to schedule BRH for tomorrow. Gridlines G/9

20.08 LBJ to look into equipment pads for HVAC/Plumbing

NEXT MEETING: 07/21/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
7-13-2015

ID		Task Name	Duration	Start	Finish
1		**Excavation**	**5 days**	**Thu 8/13/15**	**Wed 8/19/15**
2		Backfill West	5 days	Thu 8/13/15	Wed 8/19/15
3					
4		**Instreet Utilities**	**5 days**	**Tue 7/28/15**	**Mon 8/3/15**
5		Sanitary South	5 days	Tue 7/28/15	Mon 8/3/15
6		PSE In Street Conduit	5 days	Tue 7/28/15	Mon 8/3/15
7					
8		**CIP Concrete**	**7 days**	**Mon 7/13/15**	**Tue 7/21/15**
9		F&P Remaining L1 South Col's Retail	2 days	Mon 7/13/15	Tue 7/14/15
10		F&P NW Placing Boom Blockouts	5 days	Wed 7/15/15	Tue 7/21/15
11					
12		**Level 2 PT Southeast**	**31 days**	**Mon 7/13/15**	**Mon 8/24/15**
13		Shoring/Deck	5 days	Mon 7/13/15	Fri 7/17/15
14		Layout/Sleeves	1 day	Mon 7/20/15	Mon 7/20/15
15		Bottom Mat	1 day	Tue 7/21/15	Tue 7/21/15
16		Edgeform	1 day	Wed 7/22/15	Wed 7/22/15
17		Profile Tendons	2 days	Thu 7/23/15	Fri 7/24/15
18		Inspections	1 day	Mon 7/27/15	Mon 7/27/15
19		Pour	1 day	Wed 7/29/15	Wed 7/29/15
20		Strip/Reshore	5 days	Tue 8/4/15	Mon 8/10/15
21					
22		**Level 3 PT NE**	**21 days**	**Mon 7/13/15**	**Mon 8/10/15**
23		Shore/Deck	1 day	Mon 7/13/15	Mon 7/13/15
24		Layout/Sleeves	1 day	Tue 7/14/15	Tue 7/14/15
25		Bottom Mat/Sleeves	2 days	Wed 7/15/15	Thu 7/16/15
26		Edgeform/Misc Sleeves	2 days	Fri 7/17/15	Mon 7/20/15
27		Raised Slab Edge/Blockouts	2 days	Mon 7/20/15	Tue 7/21/15
28		Inspections	1 day	Wed 7/22/15	Wed 7/22/15
29		Pour	1 day	Thu 7/23/15	Thu 7/23/15
30		Stress/Strip	7 days	Wed 7/29/15	Thu 8/6/15
31		Remove Reshores North	2 days	Fri 8/7/15	Mon 8/10/15
32					
33		**Level 3 PT SW**	**25 days**	**Tue 7/21/15**	**Mon 8/24/15**
34		Shore/Deck	9 days	Tue 7/21/15	Fri 7/31/15

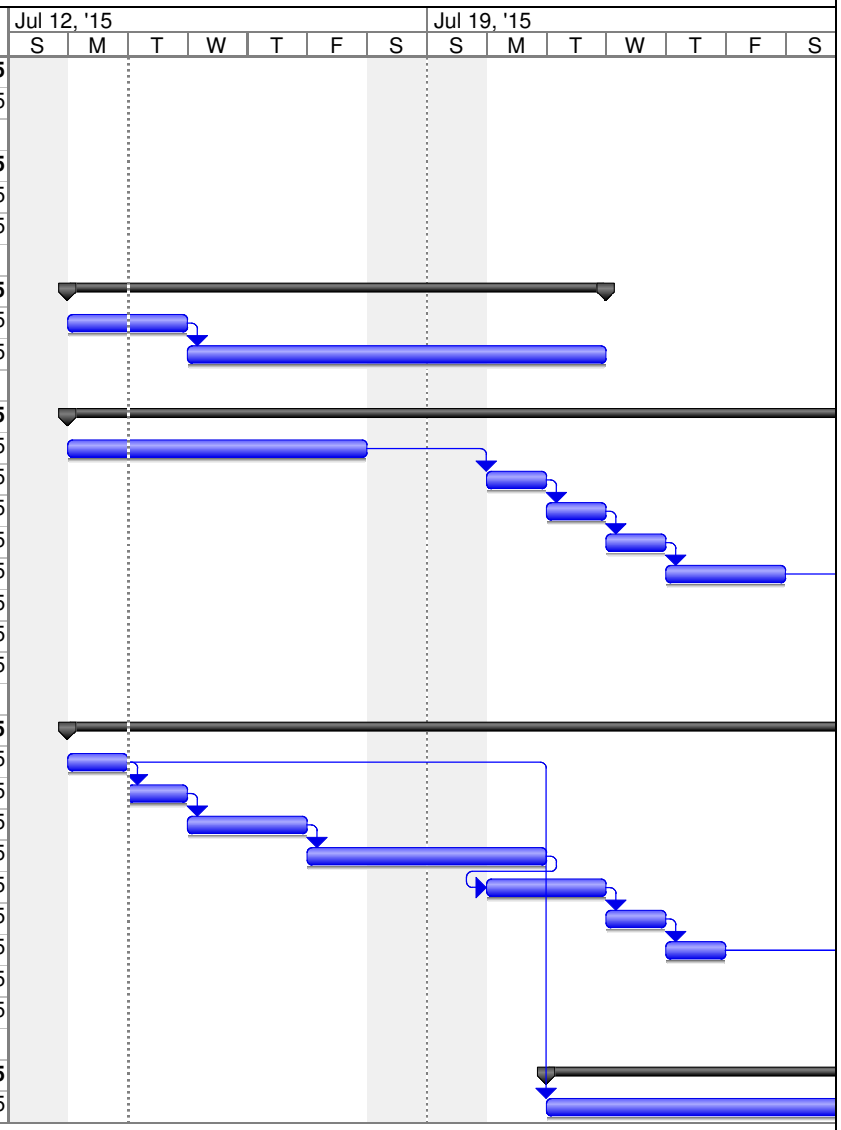

Project: 3wk look ahead 7-13-15
Date: Tue 7/14/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
7-13-2015

ID		Task Name	Duration	Start	Finish
35		Layout/Sleeves	2 days	Mon 8/3/15	Tue 8/4/15
36		Bottom Mat/Sleeves	2 days	Wed 8/5/15	Thu 8/6/15
37		Edgeform/Misc	2 days	Fri 8/7/15	Mon 8/10/15
38		Raised Slab Edge	2 days	Tue 8/11/15	Wed 8/12/15
39		Inspections	1 day	Tue 8/11/15	Tue 8/11/15
40		Pour	1 day	Wed 8/12/15	Wed 8/12/15
41		Stress/Strip	6 days	Mon 8/17/15	Mon 8/24/15
42					
43		**Wood Framing NW**	**14 days**	**Mon 8/3/15**	**Thu 8/20/15**
44		Layout Walls	1 day	Mon 8/3/15	Mon 8/3/15
45		Frame	5 days	Tue 8/4/15	Mon 8/10/15
46		TJI Joists	4 days	Tue 8/11/15	Fri 8/14/15
47		Deck	4 days	Mon 8/17/15	Thu 8/20/15

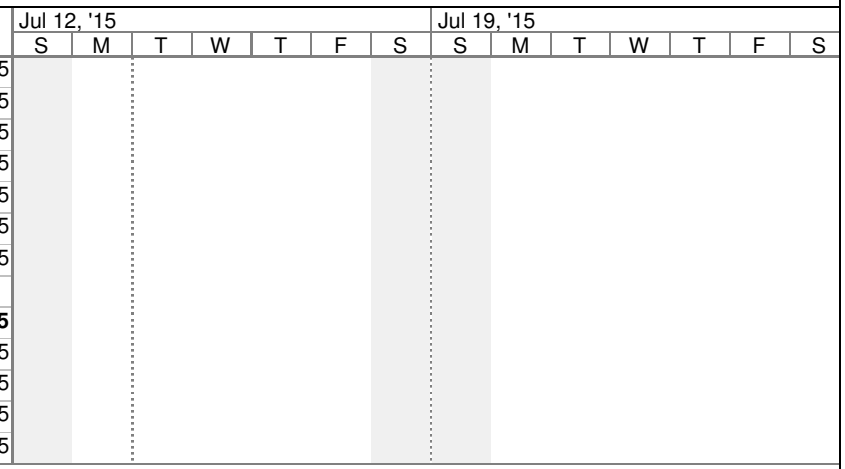

Project: 3wk look ahead 7-13-15
Date: Tue 7/14/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
7-13-2015

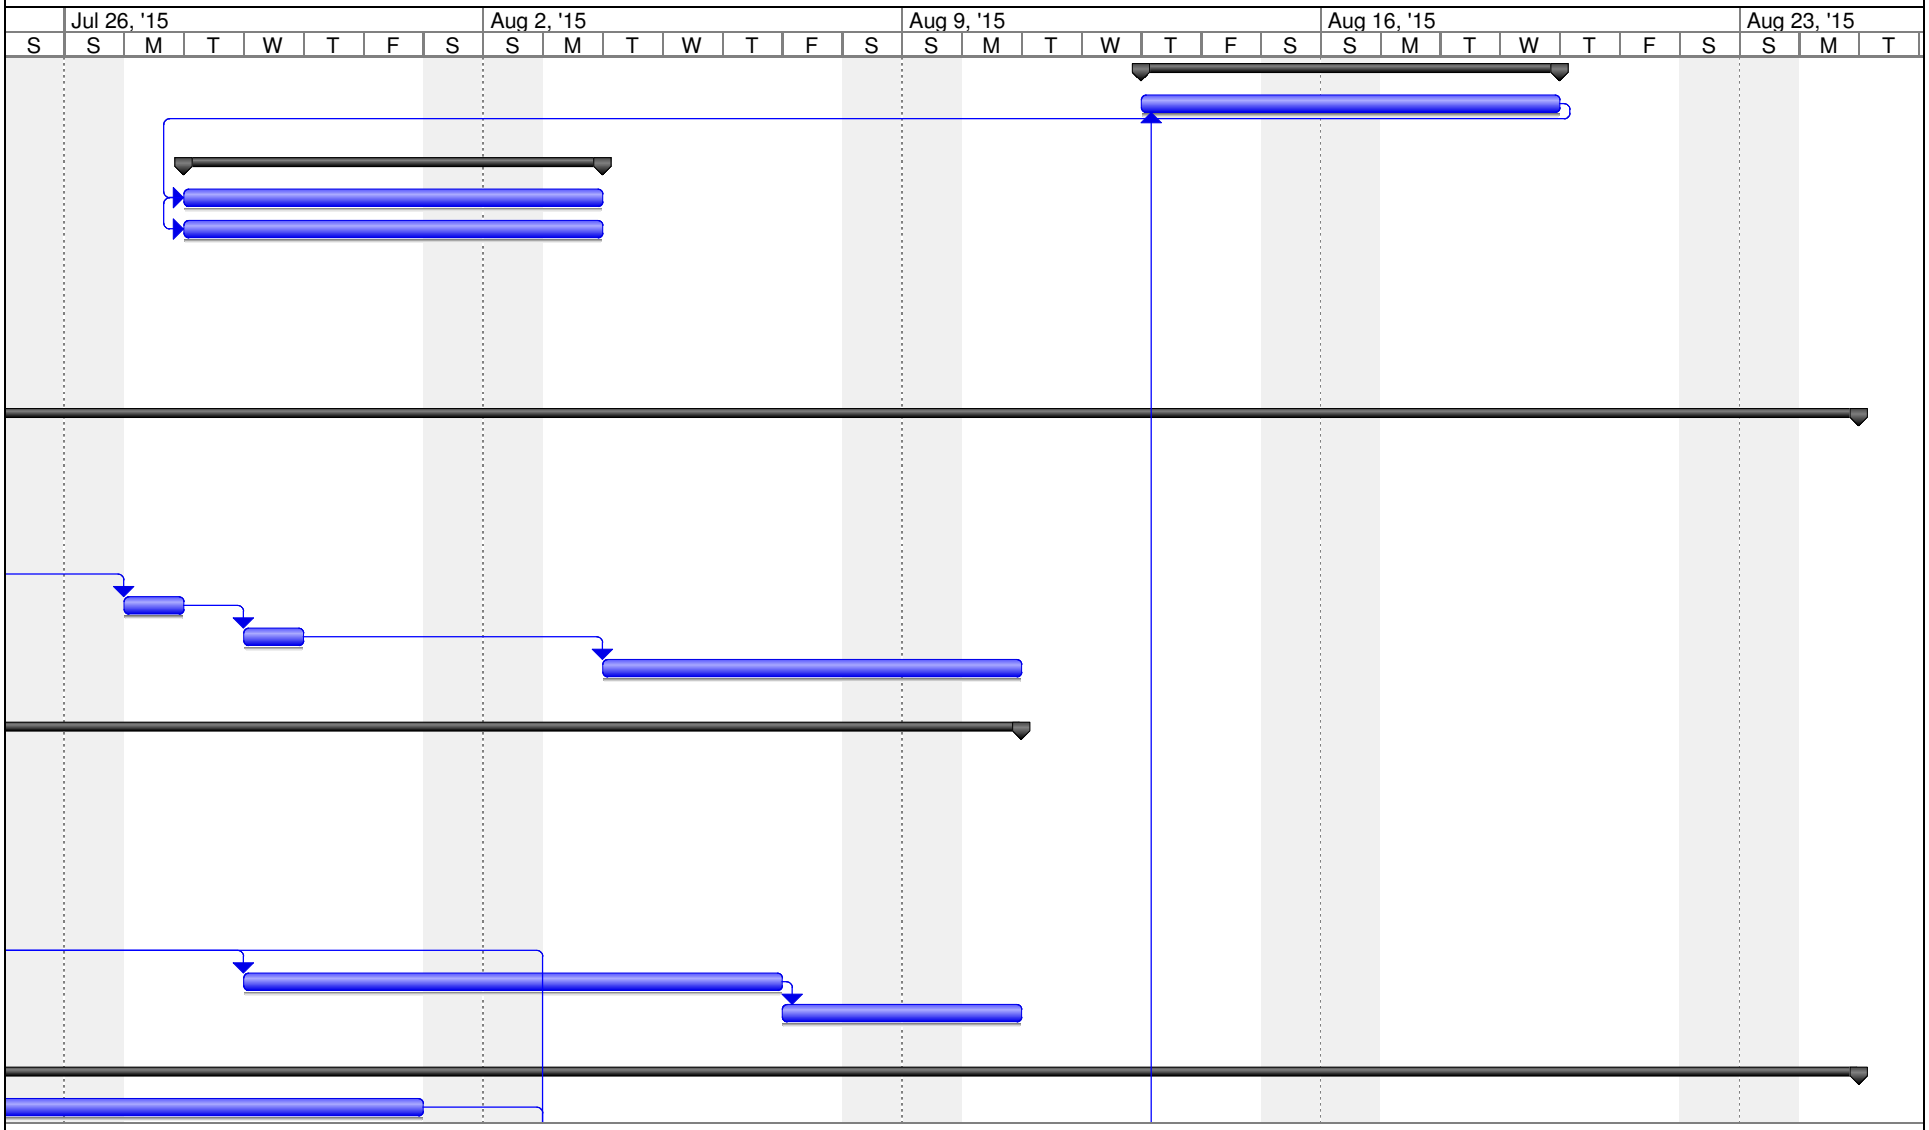

Project: 3wk look ahead 7-13-15
Date: Tue 7/14/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
7-13-2015

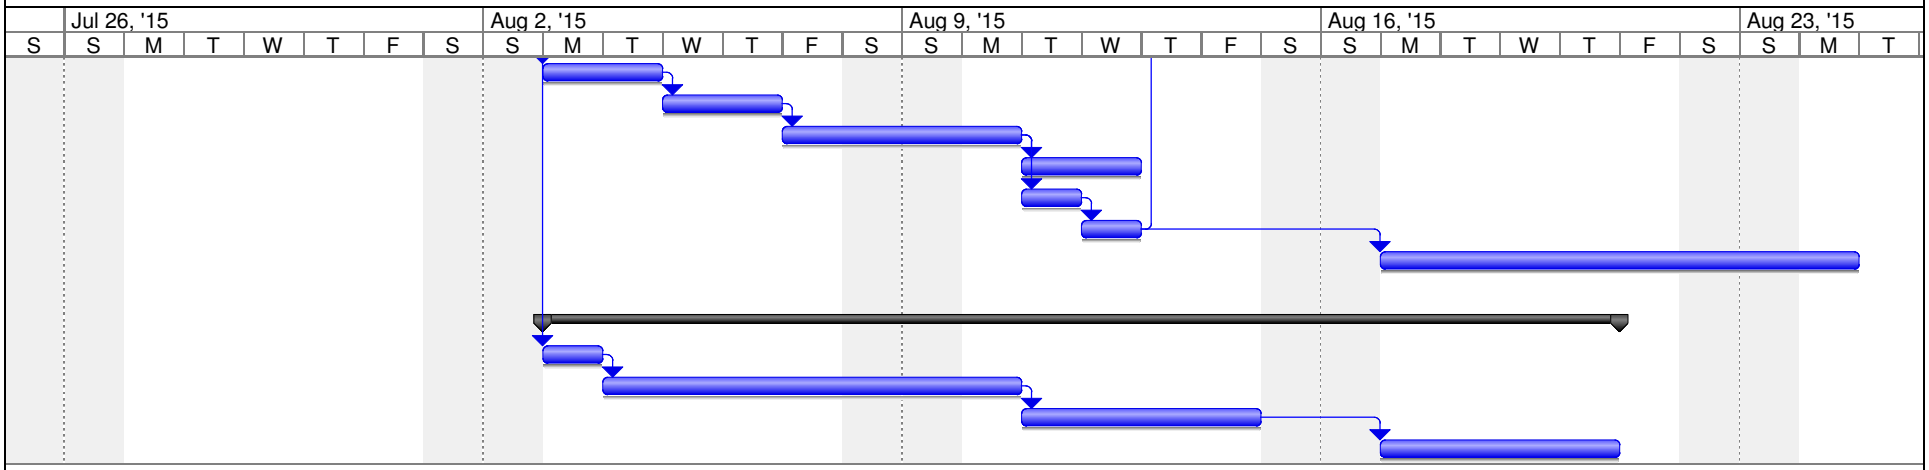

Project: 3wk look ahead 7-13-15
Date: Tue 7/14/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
