CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **21**

MEETING DATE: **07/21/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
~~Charlie Poggemann – CHINN~~
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
Darryl McNamee – LAB
~~Jesse Earle - Froula~~
~~John Studioso - IEC~~
~~Richard Donelson - OWP~~
~~Bill Huggins - Froula~~
Joe Barnhart - OWP
Lincoln Boomars – LAB
~~Dave Hamacher~~

SAFETY:

21.01 Housekeeping

- No smoking onsite
- Sweep and clean up for the next trade in work areas
- Forklift operators – be on the lookout for obstacles, (plumbing stub ups, FDCs etc.)
- There is no food allowed in the building when framing starts
- Big Equipment will be back in 2 weeks
- Verbal/Written/Gone Parking Policy
- As reshore is removed, more temp lighting in the garage is required.

SCHEDULE:

21.02 Reviewed **SITE** 3 wk look ahead schedule beginning 07/20/15

- Level 2 PT SE Pour 7/29
- Level 3 PT NE pours 7/23, Stress/Strip 7/29
- Level 3 PT SW pours 8/12
- Wood Framing Layout Walls 8/3
- Stair #1 will be onsite 7/29

XX.XX Reviewed **INTERIOR** 3wk look ahead schedule beginning xx/xx/xx

OLD BUSINESS:

12.08 What are the irrigation needs at Level 3?

- 07/01/15: Landscaper will be onsite later today.
- 07/07/15: Landscaper will be attending next OAC meeting
- 07/21/15: No POC at courtyard, however one is at the roof. Location will be addressed at the MEP Meeting 7/23

17.07 Still aiming to get rid of Clearwater system

- 07/01/15: OWP to look into what else is needed for final system. RD mentioned that a temp pump might want to be used. CHINN to get a schematic of the Final System by Glacier. Team to review system regarding volume and pressure.
- 07/07/15: LBJ emailed Glacier for final schematic
- 07/14/15: Pending Schematic
- 07/21/15: Pending Schematic

20.08 LBJ to look into equipment pads for HVAC/Plumbing

- **07/21/15:** Plumbing and Electrical do not require equipment pads, LBJ check with HVAC

PERMIT STATUS: Fire Sprinkler/Electrical/Fire Alarm

RFIs:

14.09 **Backing at stairs with drywall**

SUBMITTALS:

NEW BUSINESS:

21.03 West Shoring Wall Sequence – Backfill, bench, Place shoring wall, partial backfill, pull dirt back, shotcrete wall, then subgrade to final elevation and scaffold.

21.04 Warehouse forklift is coming to the site – to help demob shoring and for deliveries**.** It will be onsite for a limited time.

21.05 LAB to strip North end of Level 3 first for temp standpipe

21.06 There are two drains on the Civil drawings at (GL B.5, G.5 and South of 10 line) that stub into building. OWP does not have drains outside.

21.07 JB when can we bring out materials? – MP and JB to coordinate

21.08 ASI 07 – Concierge Lockers – do lockers sit on curbs? – LBJ to review during OAC meeting

NEXT MEETING: 07/28/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
7-20-2015

ID		Task Name	Duration	Start	Finish
1		**Instreet Utilities**	**9 days**	**Tue 7/28/15**	**Fri 8/7/15**
2		Sanitary South	5 days	Tue 7/28/15	Mon 8/3/15
3		PSE In Street Conduit	5 days	Mon 8/3/15	Fri 8/7/15
4					
5		**CIP Concrete**	**7 days**	**Mon 7/20/15**	**Tue 7/28/15**
6		F&P Remaining L1 South Col's Retail	2 days	Mon 7/20/15	Tue 7/21/15
7		F&P NW Placing Boom Blockouts	5 days	Wed 7/22/15	Tue 7/28/15
8					
9		**Level 2 PT Southeast**	**26 days**	**Mon 7/20/15**	**Mon 8/24/15**
10		Layout/Sleeves	1 day	Mon 7/20/15	Mon 7/20/15
11		Bottom Mat	1 day	Tue 7/21/15	Tue 7/21/15
12		Edgeform	1 day	Wed 7/22/15	Wed 7/22/15
13		Profile Tendons	2 days	Thu 7/23/15	Fri 7/24/15
14		Inspections	1 day	Mon 7/27/15	Mon 7/27/15
15		Pour	1 day	Wed 7/29/15	Wed 7/29/15
16		Strip/Reshore	5 days	Tue 8/4/15	Mon 8/10/15
17					
18		**Level 3 PT NE**	**16 days**	**Mon 7/20/15**	**Mon 8/10/15**
19		Raised Slab Edge/Blockouts	2 days	Mon 7/20/15	Tue 7/21/15
20		Inspections	1 day	Wed 7/22/15	Wed 7/22/15
21		Pour	1 day	Thu 7/23/15	Thu 7/23/15
22		Stress/Strip	7 days	Wed 7/29/15	Thu 8/6/15
23		Remove Reshores North	2 days	Fri 8/7/15	Mon 8/10/15
24					
25		**Level 3 PT SW**	**26 days**	**Mon 7/20/15**	**Mon 8/24/15**
26		Shore/Deck	10 days	Mon 7/20/15	Fri 7/31/15
27		Layout/Sleeves	2 days	Mon 8/3/15	Tue 8/4/15
28		Bottom Mat/Sleeves	2 days	Wed 8/5/15	Thu 8/6/15
29		Edgeform/Misc	2 days	Fri 8/7/15	Mon 8/10/15
30		Raised Slab Edge	2 days	Tue 8/11/15	Wed 8/12/15
31		Inspections	1 day	Tue 8/11/15	Tue 8/11/15
32		Pour	1 day	Wed 8/12/15	Wed 8/12/15
33		Stress/Strip	6 days	Mon 8/17/15	Mon 8/24/15
34					

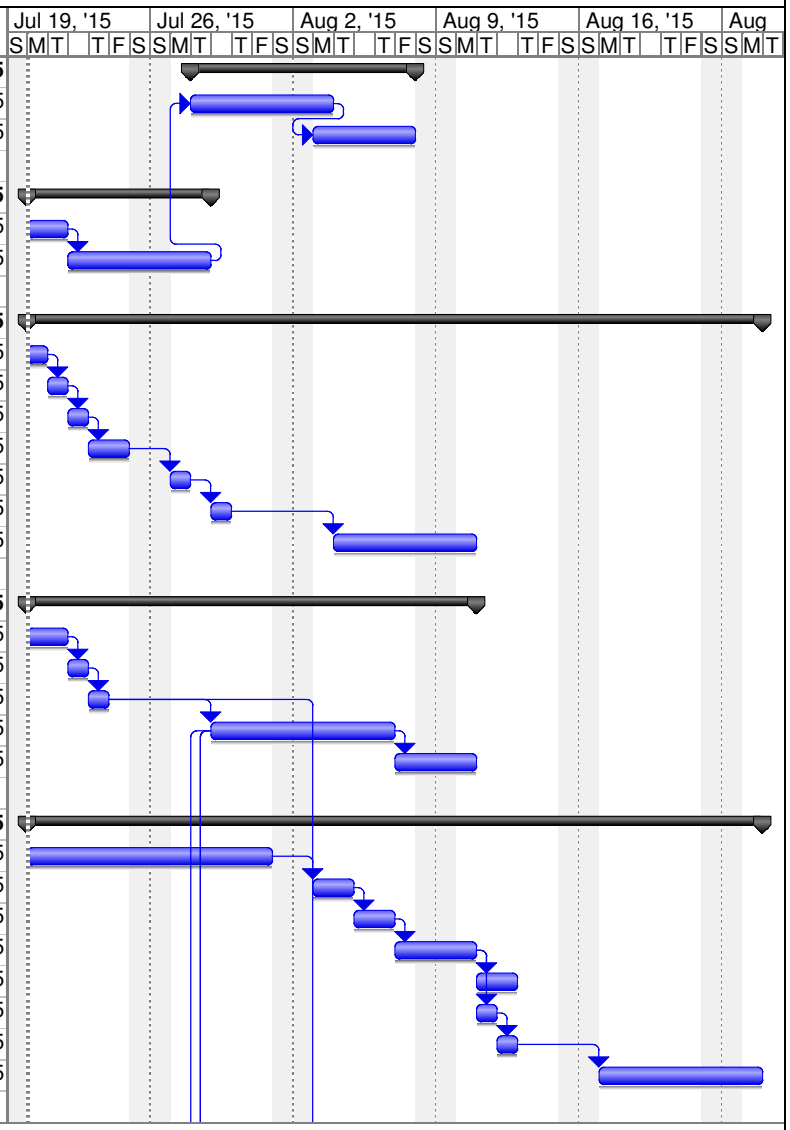

Project: 3wk look ahead 7-20-15
Date: Mon 7/20/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
7-20-2015

ID		Task Name	Duration	Start	Finish
35		**Wood Framing NW**	**14 days**	**Mon 8/3/15**	**Thu 8/20/15**
36		Layout Walls	1 day	Mon 8/3/15	Mon 8/3/15
37		Frame	5 days	Tue 8/4/15	Mon 8/10/15
38		TJI Joists	4 days	Tue 8/11/15	Fri 8/14/15
39		Deck	4 days	Mon 8/17/15	Thu 8/20/15
40					
41		**Struct Steel**	**3 days**	**Wed 7/29/15**	**Fri 7/31/15**
42		Set Stair 1 LP to L3	3 days	Wed 7/29/15	Fri 7/31/15
43					
44		**Fire Sprinkler**	**2 days**	**Fri 7/31/15**	**Mon 8/3/15**
45		FDC Standpipe to L3	2 days	Fri 7/31/15	Mon 8/3/15
46					
47		**Level P**	**5 days**	**Fri 7/31/15**	**Thu 8/6/15**
48		MEP RI LP	5 days	Fri 7/31/15	Thu 8/6/15

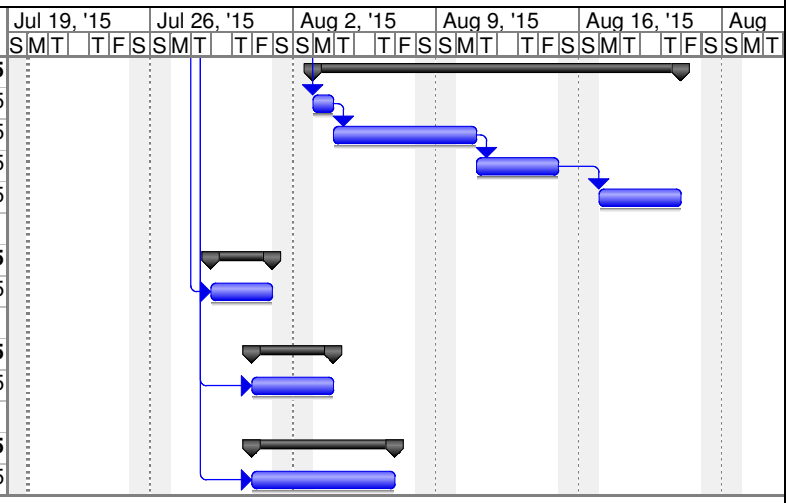

Project: 3wk look ahead 7-20-15
Date: Mon 7/20/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
