CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **22**

MEETING DATE: **07/28/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
~~Charlie Poggemann – CHINN~~
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
Darryl McNamee – LAB
~~Jesse Earle - Froula~~
~~John Studioso - IEC~~
Richard Donelson - OWP
~~Bill Huggins - Froula~~
~~Joe Barnhart - OWP~~
~~Lincoln Boomars – LAB~~
~~Dave Hamacher~~

SAFETY: Ron is the new Lift Director for crane.

22.01 Housekeeping

- No smoking onsite
- Sweep and clean up for the next trade in work areas
- There is no food allowed in the building when framing starts
- Verbal/Written/Gone Parking Policy
- IEC to install more temp lighting in garage

SCHEDULE:

22.02 Reviewed **SITE** 3 wk look ahead schedule beginning 07/27/15

- Level 2 PT SE Pour 7/29
- Level 3 PT NE Stress/Strip 7/29
- Level 3 PT SW pours 8/12
- Wood Framing Layout Walls 8/3
  - Walls, Decking, Terracon Inspections,
  - Subcontractors to mark up with wax pencils, no paint
- Stair #1 will be onsite 7/29, install starts 8/3

XX.XX Reviewed **INTERIOR** 3wk look ahead schedule beginning xx/xx/xx

OLD BUSINESS:

17.07 Still aiming to get rid of Clearwater system

- 07/01/15: OWP to look into what else is needed for final system. RD mentioned that a temp pump might want to be used. CHINN to get a schematic of the Final System by Glacier. Team to review system regarding volume and pressure.
- 07/07/15: LBJ emailed Glacier for final schematic
- 07/14/15: Pending Schematic
- 07/21/15: Pending Schematic

- 07/28/15: OWP was released to order pumps

20.08 LBJ to look into equipment pads for HVAC/Plumbing
- 07/21/15: Plumbing and Electrical do not require equipment pads, LBJ check with HVAC
- 07/28/15: No equipment pads are required

21.03 West Shoring Wall Sequence – Backfill, bench, Place shoring wall, partial backfill, pull dirt back, shotcrete wall, then subgrade to final elevation and scaffold.

21.06 There are two drains on the Civil drawings at (GL B.5, G.5 and South of 10 line) that stub into building. OWP does not have drains outside.
- 07/28/15: OWP has drains inside, NWC has drains outside

PERMIT STATUS: Fire Sprinkler/Electrical/Fire Alarm

RFIs:

14.09 **Backing at stairs with drywall**

SUBMITTALS:

NEW BUSINESS:

22.03 Asbuilt location of South Sanitary Sewer of where it steps out of the Building

22.04 LAB to schedule Air Place for mid to end September

22.05 A stair tower will be onsite (at North) for about 4 weeks for temporary fire sprinkler standpipe

22.06 CHINN to address WP with Envelope consultant with the horizontal PT slab and SOG.

NEXT MEETING: 08/04/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
7-20-2015

ID		Task Name	Duration	Start	Finish
1		**Instreet Utilities**	**5 days**	**Mon 8/3/15**	**Fri 8/7/15**
2		Sanitary South	2 days	Tue 8/4/15	Wed 8/5/15
3		PSE In Street Conduit	5 days	Mon 8/3/15	Fri 8/7/15
4					
5		**CIP Concrete**	**7 days**	**Mon 7/27/15**	**Tue 8/4/15**
6		F&P Remaining L1 South Col's Retail	2 days	Mon 7/27/15	Tue 7/28/15
7		F&P NW Placing Boom Blockouts	5 days	Wed 7/29/15	Tue 8/4/15
8					
9		**Level 2 PT Southeast**	**23 days**	**Mon 7/27/15**	**Wed 8/26/15**
10		Inspections	1 day	Mon 7/27/15	Mon 7/27/15
11		Pour	1 day	Wed 7/29/15	Wed 7/29/15
12		Strip/Reshore	5 days	Tue 8/4/15	Mon 8/10/15
13					
14		**Level 3 PT NE**	**9 days**	**Mon 7/27/15**	**Thu 8/6/15**
15		Stress/Strip	7 days	Mon 7/27/15	Tue 8/4/15
16		Remove Reshores North	2 days	Wed 8/5/15	Thu 8/6/15
17					
18		**Level 3 PT SW**	**23 days**	**Mon 7/27/15**	**Wed 8/26/15**
19		Shore/Deck	7 days	Mon 7/27/15	Tue 8/4/15
20		Layout/Sleeves	2 days	Wed 8/5/15	Thu 8/6/15
21		Bottom Mat/Sleeves	2 days	Fri 8/7/15	Mon 8/10/15
22		Edgeform/Misc	2 days	Tue 8/11/15	Wed 8/12/15
23		Raised Slab Edge	2 days	Thu 8/13/15	Fri 8/14/15
24		Inspections	1 day	Thu 8/13/15	Thu 8/13/15
25		Pour	1 day	Fri 8/14/15	Fri 8/14/15
26		Stress/Strip	6 days	Wed 8/19/15	Wed 8/26/15
27					
28		**Wood Framing NW**	**14 days**	**Mon 8/3/15**	**Thu 8/20/15**
29		Layout Walls	1 day	Mon 8/3/15	Mon 8/3/15
30		Frame	5 days	Tue 8/4/15	Mon 8/10/15
31		TJI Joists	4 days	Tue 8/11/15	Fri 8/14/15
32		Deck	4 days	Mon 8/17/15	Thu 8/20/15
33					
34		**Struct Steel**	**3 days**	**Mon 8/3/15**	**Wed 8/5/15**

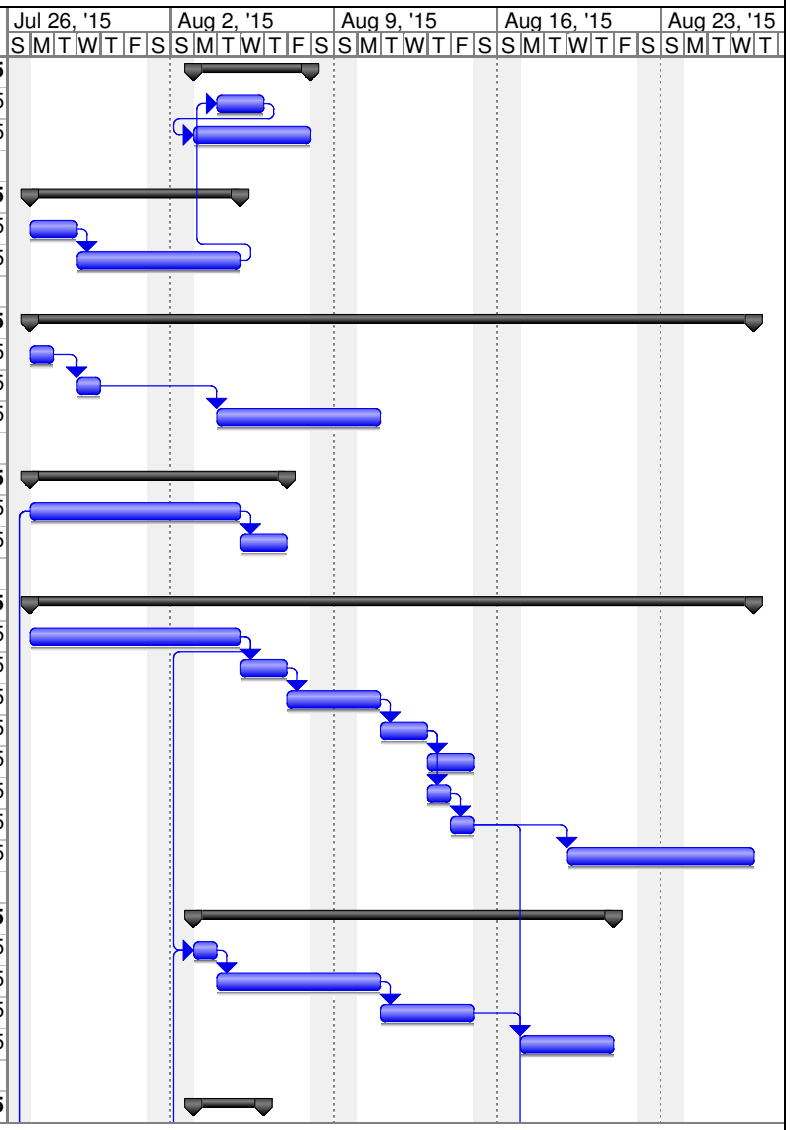

Project: 3wk look ahead 7-27-15
Date: Fri 7/24/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
7-20-2015

ID		Task Name	Duration	Start	Finish
35		Set Stair 1 LP to L3	3 days	Mon 8/3/15	Wed 8/5/15
36					
37		**Fire Sprinkler**	**2 days**	**Wed 7/29/15**	**Thu 7/30/15**
38		FDC Standpipe to L3	2 days	Wed 7/29/15	Thu 7/30/15
39					
40		**Level P**	**5 days**	**Fri 7/31/15**	**Thu 8/6/15**
41		MEP RI LP	5 days	Fri 7/31/15	Thu 8/6/15
42					
43		**Subgrade**	**4 days**	**Mon 8/17/15**	**Thu 8/20/15**
44		West exterior	4 days	Mon 8/17/15	Thu 8/20/15
45					
46		**Shoring**	**4 days**	**Fri 8/21/15**	**Wed 8/26/15**
47		Drill/Set Addl. Piles	4 days	Fri 8/21/15	Wed 8/26/15

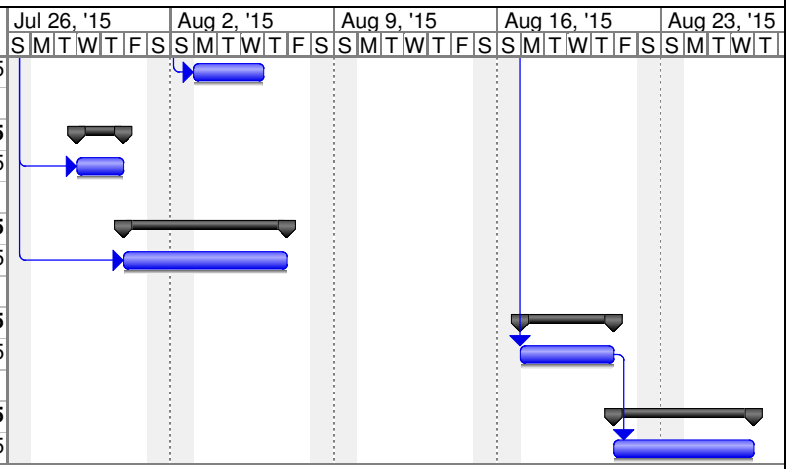

Project: 3wk look ahead 7-27-15
Date: Fri 7/24/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
