CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **24**

MEETING DATE: **08/11/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
~~Charlie Poggemann – CHINN~~
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
Darryl McNamee – LAB
Jesse Earle – Froula
~~John Studioso - IEC~~
~~Richard Donelson - OWP~~
Tim Hutchison - SS
Joe Barnhart - OWP
~~Lincoln Boomars – LAB~~
~~Eric Bull - CHINN~~
Ross Porterfield – IEC

SAFETY: Remind crews not to walk past Danger Tape. CHINN has placed 18 Fire extinguishers throughout site. Please do not relocate fire extinguishers.

24.01 Housekeeping

- No smoking onsite
- Sweep and clean up for the next trade in work areas
- There is no food allowed in the building when framing starts; framing crew to eat lunch in garage
- Verbal/Written/Gone Parking Policy
- IEC to install more temp lighting in Level P and Level1
- Crew will need to start carpooling
- Use the delivery board

SCHEDULE:

24.02 Reviewed **SITE** 3 wk look ahead schedule beginning 08/10/15

- Level 3 PT SW pours 8/14
- Level 3 PT SE 8/20 Layout/Sleeves, pours 9/4
- Wood Framing Layout Walls
  - NW frame walls 8/10-8/14
  - TJI Joists 6/17-6/21
  - NE Frame Walls 8/17-8/21
- Level P MEP Roughin 8/10-8/28
- Subgrade – West Exterior 8/17
- Shoring –Drill Set Additional Piles
- Stair #1 is installed

XX.XX Reviewed **INTERIOR** 3wk look ahead schedule beginning xx/xx/xx

OLD BUSINESS:

17.07 Still aiming to get rid of Clearwater system

- 07/01/15: OWP to look into what else is needed for final system. RD mentioned that a temp pump might want to be used. CHINN to get a schematic of the Final System by Glacier. Team to review system regarding volume and pressure.
- 07/07/15: LBJ emailed Glacier for final schematic
- 07/14/15: Pending Schematic
- 07/21/15: Pending Schematic
- 07/28/15: OWP was released to order pumps

23.05 Outlets at decks and locations

PERMIT STATUS: Fire Sprinkler/Electrical/Fire Alarm

RFIs:

14.09 **Backing at stairs with drywall**

SUBMITTALS:

NEW BUSINESS:

24.03 No personal vehicles are to be onsite

24.04 The Level 1 deck will need to be x-rayed for the sprinkler main. If something else needs to be x-rayed add it to the list on the white board in the construction office.

24.05 Per COMI Fire Marshal, lunchrooms may need fire treated plywood.

24.06 Lauren is out of the copy making business. Bring or make your own copies.

NEXT MEETING: 08/18/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
8-10-2015

ID		Task Name	Duration	Start	Finish
1		**Instreet Utilities**	**5 days**	**Mon 8/10/15**	**Fri 8/14/15**
2		PSE In Street Conduit	5 days	Mon 8/10/15	Fri 8/14/15
3					
4		**CIP Concrete**	**5 days**	**Mon 8/10/15**	**Fri 8/14/15**
5		F&P Remaining L1 South Col's Retail	2 days	Mon 8/10/15	Tue 8/11/15
6		F&P NW Placing Boom Blockouts	5 days	Mon 8/10/15	Fri 8/14/15
7					
8		**Level 2 PT Southeast**	**5 days**	**Mon 8/10/15**	**Fri 8/14/15**
9		Strip	5 days	Mon 8/10/15	Fri 8/14/15
10					
11		**Level 3 PT NE**	**2 days**	**Mon 8/10/15**	**Tue 8/11/15**
12		Strip	2 days	Mon 8/10/15	Tue 8/11/15
13		Remove Reshores North	2 days	Mon 8/10/15	Tue 8/11/15
14					
15		**Level 3 PT SW**	**11 days**	**Mon 8/10/15**	**Mon 8/24/15**
16		Edgeform/Misc	1 day	Mon 8/10/15	Mon 8/10/15
17		Raised Slab Edge	1 day	Tue 8/11/15	Tue 8/11/15
18		Inspections	2 days	Wed 8/12/15	Thu 8/13/15
19		Pour	1 day	Fri 8/14/15	Fri 8/14/15
20		Stress/Strip	6 days	Mon 8/17/15	Mon 8/24/15
21					
22		**Level 3 SE PT**	**29 days**	**Mon 8/10/15**	**Thu 9/17/15**
23		Shore/Deck	8 days	Mon 8/10/15	Wed 8/19/15
24		Layout/Sleeves	2 days	Thu 8/20/15	Fri 8/21/15
25		Rebar/PT	3 days	Mon 8/24/15	Wed 8/26/15
26		Edgeform/Misc	2 days	Thu 8/27/15	Fri 8/28/15
27		Raised Slab edge	2 days	Mon 8/31/15	Tue 9/1/15
28		Inspections	1 day	Wed 9/2/15	Wed 9/2/15
29		Pour	1 day	Fri 9/4/15	Fri 9/4/15
30		Stress/Strip	8 days	Tue 9/8/15	Thu 9/17/15
31					
32		**Wood Framing L3**	**16 days**	**Mon 8/10/15**	**Mon 8/31/15**
33		**Northwest**	**12 days**	**Mon 8/10/15**	**Tue 8/25/15**
34		Frame	5 days	Mon 8/10/15	Fri 8/14/15

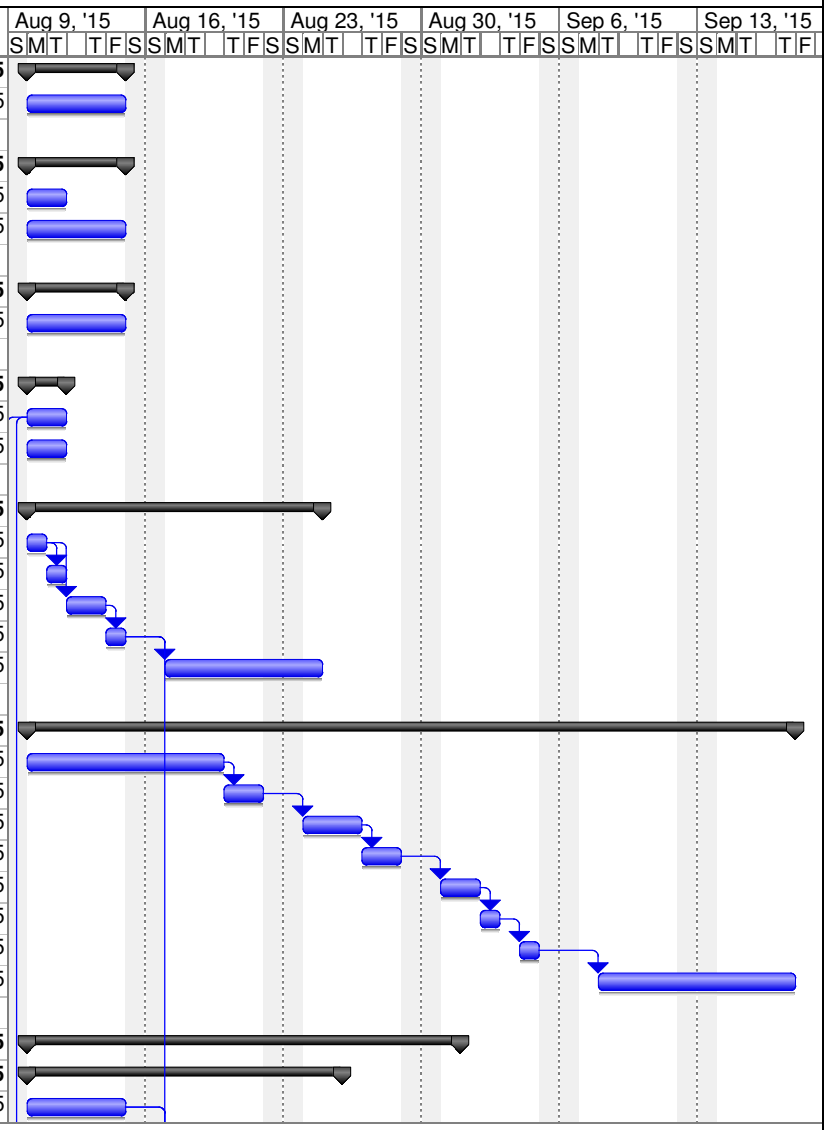

Project: 3wk look ahead 8-10-15
Date: Fri 8/7/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
8-10-2015

ID		Task Name	Duration	Start	Finish
35		TJI Joists	5 days	Mon 8/17/15	Fri 8/21/15
36		Deck	4 days	Thu 8/20/15	Tue 8/25/15
37		**Northeast**	**11 days**	**Mon 8/17/15**	**Mon 8/31/15**
38		Frame	5 days	Mon 8/17/15	Fri 8/21/15
39		TJI Joist	4 days	Mon 8/24/15	Thu 8/27/15
40		Deck	4 days	Wed 8/26/15	Mon 8/31/15
41					
42		**Fire Sprinkler**	**10 days**	**Tue 8/11/15**	**Mon 8/24/15**
43		Mains North Garage	10 days	Tue 8/11/15	Mon 8/24/15
44					
45		**Level P**	**15 days**	**Mon 8/10/15**	**Fri 8/28/15**
46		MEP RI LP/ 1	15 days	Mon 8/10/15	Fri 8/28/15
47					
48		**Subgrade**	**4 days**	**Mon 8/17/15**	**Thu 8/20/15**
49		West exterior	4 days	Mon 8/17/15	Thu 8/20/15
50					
51		**Shoring**	**5 days**	**Fri 8/21/15**	**Thu 8/27/15**
52		Drill/Set Addl. Piles	4 days	Fri 8/21/15	Wed 8/26/15
53		Lagging	2 days	Wed 8/26/15	Thu 8/27/15

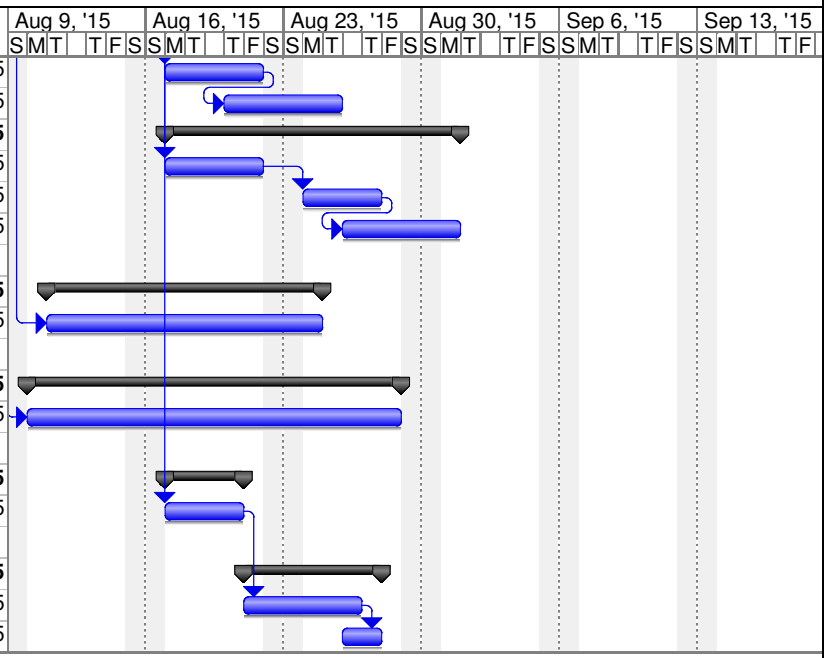

Project: 3wk look ahead 8-10-15
Date: Fri 8/7/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
