CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **25**

MEETING DATE: **08/18/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
~~Charlie Poggemann – CHINN~~
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
~~Darryl McNamee – LAB~~
~~Jesse Earle – Froula~~
~~John Studioso - IEC~~
Richard Donelson - OWP
Tim Hutchison - SS
~~Joe Barnhart - OWP~~
~~Lincoln Boomars – LAB~~
~~Eric Bull - CHINN~~
Ross Porterfield – IEC

SAFETY: Per PCI inspection, temporary lights must be hung from the eyelet at top of light fixture

25.01 Housekeeping

- No smoking onsite
- Sweep and clean up for the next trade in work areas
- There is no food allowed in the building when framing starts; framing crew to eat lunch in garage
- Verbal/Written/Gone Parking Policy
- IEC to install more temp lighting in Level P and Level1
- Crew will need to start carpooling
- Use the delivery board

SCHEDULE:

25.02 Reviewed **SITE** 3 wk look ahead schedule beginning 08/17/15

- Level 3 PT SW Stress/Strip 8/18- 8/27
- Level 3 PT SE 8/20 Layout/Sleeves, pours 9/4
- Wood Framing North L3
  - NE Frame Walls 8/17-8/21
  - TJI Joists 8/20-8/27
  - Deck 8/26-8/31
- Wood Framing South
  - Frame 8/20-8/27
  - TJI/Joist 8/28-9/3
  - Deck 9/2-9/7
- Wood Frame L4 North
  - Frame 8/28-9/10
- Fire Sprinkler Mains 8/17-8/28
- Level P MEP Roughin 8/17-9/4
- Subgrade – West Exterior 8/19-8/24
- Shoring –Drill Set Additional Piles 8/17-8/31

XX.XX Reviewed **INTERIOR** 3wk look ahead schedule beginning xx/xx/xx

OLD BUSINESS:

17.07 Still aiming to get rid of Clearwater system

- 07/01/15: OWP to look into what else is needed for final system. RD mentioned that a temp pump might want to be used. CHINN to get a schematic of the Final System by Glacier. Team to review system regarding volume and pressure.
- 07/07/15: LBJ emailed Glacier for final schematic
- 07/14/15: Pending Schematic
- 07/21/15: Pending Schematic
- 07/28/15: OWP was released to order pumps

23.05 Outlets at decks and locations

PERMIT STATUS: Fire Sprinkler/Electrical/Fire Alarm

RFIs:

25.03 LAB write RFI about closure strip

SUBMITTALS:

NEW BUSINESS:

25.04 OWP test water to Storm or Sanitary? – Per OAC Meeting 39, OWP plumbing to route test water into storm for now.

25.05 Kulchin will be out Wednesday to cut bracing and then waterproofing subcontractor will follow. NWC will have big equipment back.

25.06 LAB to schedule airplace for South

25.07 The construction set has been issued and the link has been emailed to the subcontractors

25.08 Please provide backing information to CHINN by 8/28/15

25.09 Subcontractors are responsible for their own task lighting.

NEXT MEETING: 08/25/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
8-17-2015

ID	Task Name	Duration	Start	Finish
1	**CIP Concrete**	**10 days**	**Mon 8/17/15**	**Fri 8/28/15**
2	F&P Remaining L1 South Col's Retail	2 days	Mon 8/17/15	Tue 8/18/15
3	F&P NW Placing Boom Blockouts	10 days	Mon 8/17/15	Fri 8/28/15
4	Shotcrete Southwest	1 day	Fri 8/28/15	Fri 8/28/15
5				
6	**Level 3 PT SW**	**9 days**	**Mon 8/17/15**	**Thu 8/27/15**
7	Strip Edgeform/Misc	1 day	Mon 8/17/15	Mon 8/17/15
8	Stress/Strip	8 days	Tue 8/18/15	Thu 8/27/15
9				
10	**Level 3 SE PT**	**24 days**	**Mon 8/17/15**	**Thu 9/17/15**
11	Shore/Deck	5 days	Mon 8/17/15	Fri 8/21/15
12	Layout/Sleeves	2 days	Mon 8/24/15	Tue 8/25/15
13	Rebar/PT	3 days	Wed 8/26/15	Fri 8/28/15
14	Edgeform/Misc	2 days	Mon 8/31/15	Tue 9/1/15
15	Raised Slab edge	2 days	Wed 9/2/15	Thu 9/3/15
16	Inspections	1 day	Thu 9/3/15	Thu 9/3/15
17	Pour	1 day	Fri 9/4/15	Fri 9/4/15
18	Stress/Strip	8 days	Tue 9/8/15	Thu 9/17/15
19				
20	**Wood Framing L3**	**16 days**	**Mon 8/17/15**	**Mon 9/7/15**
21	**North**	**11 days**	**Mon 8/17/15**	**Mon 8/31/15**
22	Frame	3 days	Mon 8/17/15	Wed 8/19/15
23	TJI Joists	6 days	Thu 8/20/15	Thu 8/27/15
24	Deck	4 days	Wed 8/26/15	Mon 8/31/15
25	**Southwest**	**13 days**	**Thu 8/20/15**	**Mon 9/7/15**
26	Frame	6 days	Thu 8/20/15	Thu 8/27/15
27	TJI/Joist	5 days	Fri 8/28/15	Thu 9/3/15
28	Deck	4 days	Wed 9/2/15	Mon 9/7/15
29				
30	**Level 4 North**	**10 days**	**Fri 8/28/15**	**Thu 9/10/15**
31	Frame	10 days	Fri 8/28/15	Thu 9/10/15
32				
33	**Fire Sprinkler**	**10 days**	**Mon 8/17/15**	**Fri 8/28/15**
34	Mains North Garage	10 days	Mon 8/17/15	Fri 8/28/15

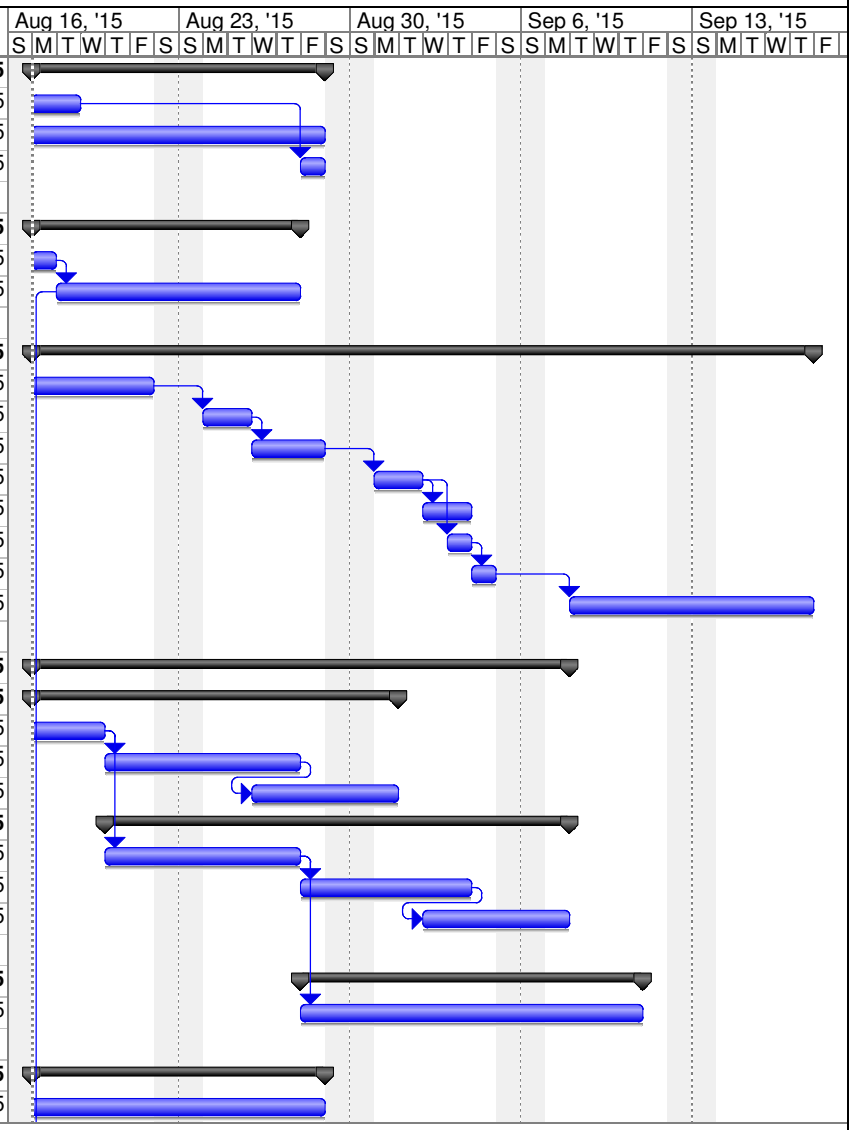

Project: 3wk look ahead 8-17-15
Date: Mon 8/17/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
8-17-2015

ID		Task Name	Duration	Start	Finish
35					
36		**Garage**	**15 days**	**Mon 8/17/15**	**Fri 9/4/15**
37		MEP RI LP/ 1	15 days	Mon 8/17/15	Fri 9/4/15
38					
39		**Waterproofing**	**4 days**	**Tue 8/18/15**	**Fri 8/21/15**
40		West wall	1 day	Tue 8/18/15	Tue 8/18/15
41		Blockouts/Tiebacks	3 days	Wed 8/19/15	Fri 8/21/15
42					
43		**Subgrade**	**4 days**	**Wed 8/19/15**	**Mon 8/24/15**
44		West exterior	4 days	Wed 8/19/15	Mon 8/24/15
45					
46		**Shoring**	**11 days**	**Mon 8/17/15**	**Mon 8/31/15**
47		Remove Horz Braces	1 day	Mon 8/17/15	Mon 8/17/15
48		Destress Tie-backs	2 days	Tue 8/18/15	Wed 8/19/15
49		Weld Shoring Plates	2 days	Thu 8/20/15	Fri 8/21/15
50		Drill/Set Additional Piles	4 days	Mon 8/24/15	Thu 8/27/15
51		Lagging	2 days	Fri 8/28/15	Mon 8/31/15

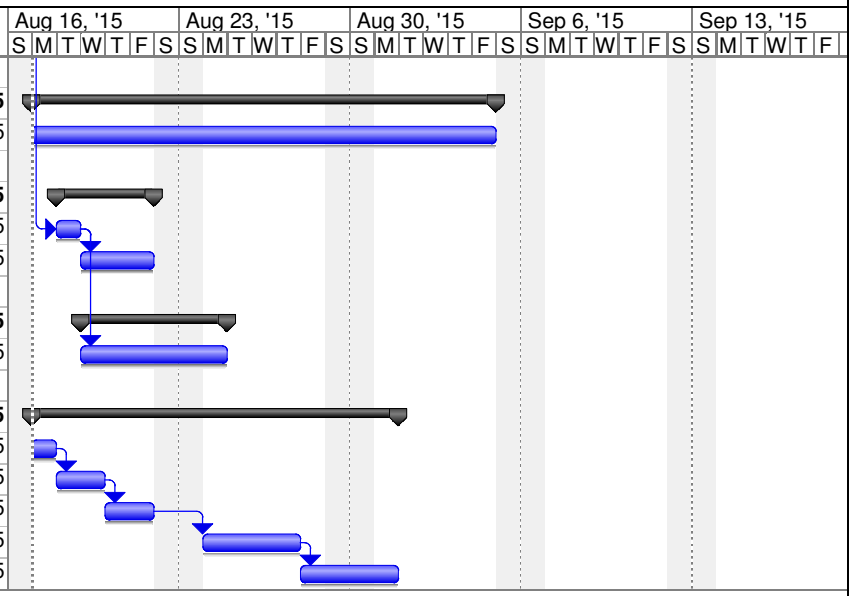

Project: 3wk look ahead 8-17-15
Date: Mon 8/17/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
