CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **26**

MEETING DATE: **08/25/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
Charlie Poggemann – CHINN
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
Darryl McNamee – LAB
~~Jesse Earle – Froula~~
Jason – CFM
~~John Studioso - IEC~~
~~Richard Donelson - OWP~~
Tim Hutchison - SS
Joe Barnhart - OWP
~~Lincoln Boomars – LAB~~
Eric Bull - CHINN
Ross Porterfield – IEC

SAFETY:

26.01 Housekeeping

- No smoking onsite
- Sweep and clean up for the next trade in work areas
- There is no food allowed in the building when framing starts; framing crew to eat lunch in garage
- Verbal/Written/Gone Parking Policy
- IEC to install more temp lighting in Level P and Level1
- Crew will need to start carpooling
- Use the delivery board – check crane box if you need crane

SCHEDULE:

26.02 Reviewed **SITE** 3 wk look ahead schedule beginning 08/24/15

- Level 3 PT SE Inspections 9/3, pours 9/4
- Wood Framing North L3
  - TJI Joists 8/24-8/26
  - Deck 8/25-8/26
- Wood Framing South
  - Frame 8/24-8/31
  - TJI/Joist 8/28-9/3
  - Deck 9/4-9/9
- Wood Frame L4 North
  - Frame 9/1-9/14
- Fire Sprinkler Mains 8/24-9/4
- Level P MEP Roughin 8/24-9/11
- Waterproofing 8/25-8/28
- Subgrade – West Exterior 8/24-8/28
- Shoring –Drill Set Additional Piles 8/24-9/2

XX.XX Reviewed **INTERIOR** 3wk look ahead schedule beginning xx/xx/xx

OLD BUSINESS:

23.05 Outlets at decks and locations

- 08/25/15: Owner/Architect to request variance with COMI.

PERMIT STATUS: Fire Sprinkler/Electrical/Fire Alarm

RFIs:

25.03 LAB write RFI about closure strip

SUBMITTALS:

NEW BUSINESS:

26.02 Clearwater will be demobilizing equipment on 8/31

26.03 Once SE deck is placed, IEC will layout spiderboxes and temp power. All trades to provide their own task lighting.

26.04 Xray for slab wil be onsite on 08/28, put xray needs on the white board in the construction office.

26.05 Unconditioned rooms currently show regular 5/8" drywall, should be blue board.

NEXT MEETING: 09/01/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
8-17-2015

ID		Task Name	Duration	Start	Finish
1		**CIP Concrete**	**10 days**	**Mon 8/24/15**	**Fri 9/4/15**
2		F&P NW Placing Boom Blockouts	10 days	Mon 8/24/15	Fri 9/4/15
3		Shotcrete Southwest	1 day	Mon 8/24/15	Mon 8/24/15
4					
5		**Level 3 PT SW**	**8 days**	**Mon 8/24/15**	**Wed 9/2/15**
6		Stress/Strip	8 days	Mon 8/24/15	Wed 9/2/15
7					
8		**Level 3 SE PT**	**19 days**	**Mon 8/24/15**	**Thu 9/17/15**
9		Layout/Sleeves	2 days	Mon 8/24/15	Tue 8/25/15
10		Rebar/PT	3 days	Wed 8/26/15	Fri 8/28/15
11		Edgeform/Misc	2 days	Mon 8/31/15	Tue 9/1/15
12		Raised Slab edge	2 days	Wed 9/2/15	Thu 9/3/15
13		Inspections	1 day	Thu 9/3/15	Thu 9/3/15
14		Pour	1 day	Fri 9/4/15	Fri 9/4/15
15		Stress/Strip	8 days	Tue 9/8/15	Thu 9/17/15
16					
17		**Wood Framing L3**	**13 days**	**Mon 8/24/15**	**Wed 9/9/15**
18		**North**	**3 days**	**Mon 8/24/15**	**Wed 8/26/15**
19		TJI Joists	3 days	Mon 8/24/15	Wed 8/26/15
20		Deck	2 days	Tue 8/25/15	Wed 8/26/15
21		**Southwest**	**13 days**	**Mon 8/24/15**	**Wed 9/9/15**
22		Frame	6 days	Mon 8/24/15	Mon 8/31/15
23		TJI/Joist	5 days	Tue 9/1/15	Mon 9/7/15
24		Deck	4 days	Fri 9/4/15	Wed 9/9/15
25					
26		**Level 4 North**	**10 days**	**Tue 9/1/15**	**Mon 9/14/15**
27		Frame	10 days	Tue 9/1/15	Mon 9/14/15
28					
29		**Fire Sprinkler**	**10 days**	**Mon 8/24/15**	**Fri 9/4/15**
30		Mains North Garage	10 days	Mon 8/24/15	Fri 9/4/15
31					
32		**Garage**	**15 days**	**Mon 8/24/15**	**Fri 9/11/15**
33		MEP RI LP/ 1	15 days	Mon 8/24/15	Fri 9/11/15
34					

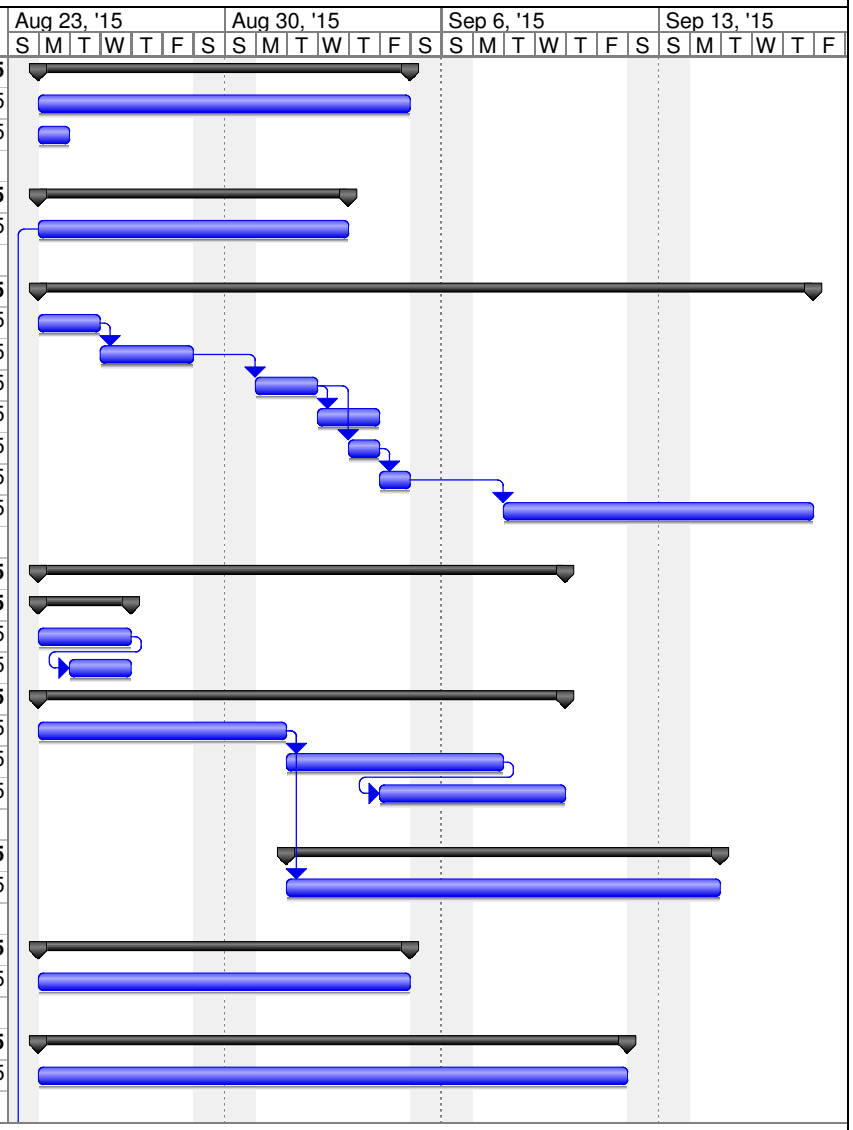

Project: 3wk look ahead 8-24-15
Date: Fri 8/21/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
8-17-2015

ID		Task Name	Duration	Start	Finish
35		**Mtl Stud Framing**	**14 days**	**Mon 8/24/15**	**Thu 9/10/15**
36		Level P	3 days	Mon 8/24/15	Wed 8/26/15
37		Stair 1 Exterior	4 days	Mon 8/24/15	Thu 8/27/15
38		Level 2 Units Etc. North	10 days	Fri 8/28/15	Thu 9/10/15
39					
40		**Waterproofing**	**4 days**	**Mon 8/24/15**	**Thu 8/27/15**
41		West wall	1 day	Mon 8/24/15	Mon 8/24/15
42		Blockouts/Tiebacks	3 days	Tue 8/25/15	Thu 8/27/15
43					
44		**Subgrade**	**4 days**	**Tue 8/25/15**	**Fri 8/28/15**
45		Shoring Support	4 days	Tue 8/25/15	Fri 8/28/15
46					
47		**Shoring**	**8 days**	**Mon 8/24/15**	**Wed 9/2/15**
48		Drill/Set Additional Piles	4 days	Wed 8/26/15	Mon 8/31/15
49		Lagging @ Corner	2 days	Mon 8/24/15	Tue 8/25/15
50		Additional Shoring Lagging	4 days	Fri 8/28/15	Wed 9/2/15
51					
52		**West Shoring walls**	**4 days**	**Tue 9/1/15**	**Fri 9/4/15**
53		Weld Nelson studs	1 day	Tue 9/1/15	Tue 9/1/15
54		Reinforcing	2 days	Wed 9/2/15	Thu 9/3/15
55		Shotcrete	1 day	Fri 9/4/15	Fri 9/4/15

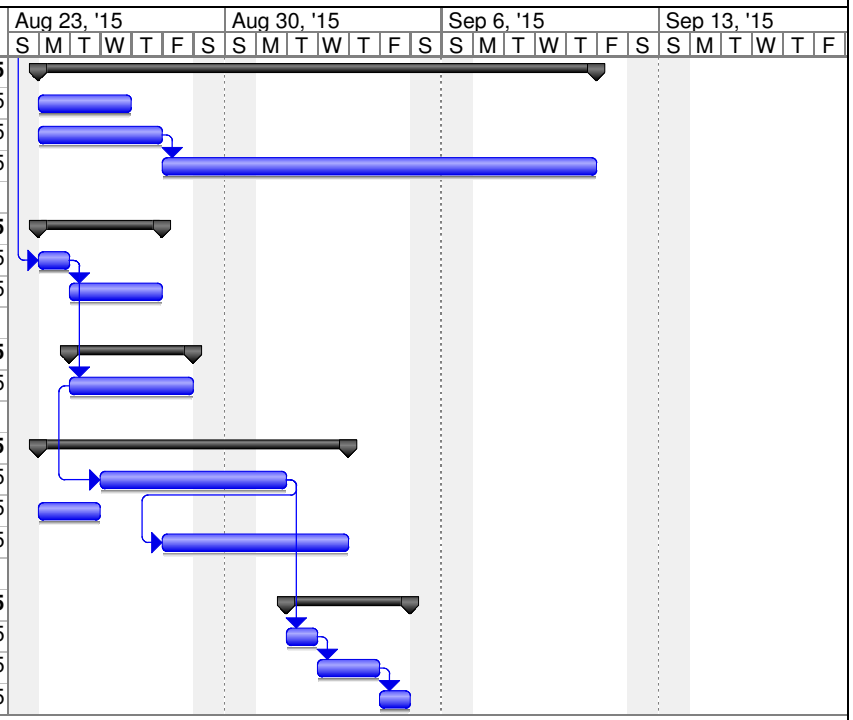

Project: 3wk look ahead 8-24-15
Date: Fri 8/21/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
