CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **28**

MEETING DATE: **09/08/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
~~Mark Pesanti – CHINN~~
Charlie Poggemann – CHINN
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
Darryl McNamee – LAB
~~Jesse Earle – Froula~~
Jason – CFM
~~John Studioso - IEC~~
~~Richard Donelson - OWP~~
Tim Hutchison - SS
Joe Barnhart - OWP
~~Lincoln Boomars – LAB~~
~~Eric Bull - CHINN~~
Ross Porterfield – IEC
Roger Rueda - WCP

SAFETY:

28.01 Housekeeping

- No smoking onsite
- Sweep and clean up for the next trade in work areas
- There is no food allowed in the building when framing starts; framing crew to eat lunch in garage
- Verbal/Written/Gone Parking Policy
- IEC is routing temp power for each floor
- Crew will need to start carpooling
- Use the delivery board – check crane box if you need crane

SCHEDULE:

28.02 Reviewed **SITE** 3 wk look ahead schedule beginning 08/24/15

- Level 3 PT SE Stress/Strip 9/8-9/17
- Wood Framing North L4
  - Frame, Roll Joists, Deck 9/8/9/17
- Wood Framing South L3
  - Frame, TJI Joist, Deck 9/8-9/28
- Fire Sprinkler Mains 9/8-9/21
- Level P MEP Roughin 9/8-9/28
- Mtl stud framing 9/8-9/25
- Hollow Metal 9/22-9/24
- Waterproofing 9/8-9/11
- Subgrade – West Exterior 9/8-9/15
- Shoring –Drill Set Additional Piles 9/14-9/17

XX.XX Reviewed **INTERIOR** 3wk look ahead schedule beginning xx/xx/xx

OLD BUSINESS:

23.05 Outlets at decks and locations

- 08/25/15: Owner/Architect to request variance with COMI.

26.05 Unconditioned rooms currently show regular 5/8" drywall, should be blue board.

- 09/08/15: With Owner for review

PERMIT STATUS: Electrical, HVAC

RFIs:

SUBMITTALS:

NEW BUSINESS:

28.03 OWP has the permanent pump for sub slab drainage system

28.04 Date of shotcrete for west wall be confirmed

28.05 Wood stairs will be starting at Level 3 at stair 1.

28.06 Electrical and subcontractors need cabinet shop drawings for layout

NEXT MEETING: 09/15/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
9-8-2015

ID		Task Name	Duration	Start	Finish
1		**Level 3 SE PT**	**8 days**	**Tue 9/8/15**	**Thu 9/17/15**
2		Stress/Strip	8 days	Tue 9/8/15	Thu 9/17/15
3					
4		**Wood Framing L3**	**15 days**	**Tue 9/8/15**	**Mon 9/28/15**
5		**Southwest**	**5 days**	**Tue 9/8/15**	**Mon 9/14/15**
6		Frame	2 days	Tue 9/8/15	Wed 9/9/15
7		Roll Joist	3 days	Thu 9/10/15	Mon 9/14/15
8		Sheath	2 days	Fri 9/11/15	Mon 9/14/15
9		**Southeast**	**13 days**	**Thu 9/10/15**	**Mon 9/28/15**
10		Frame	9 days	Thu 9/10/15	Tue 9/22/15
11		Roll Joist	6 days	Wed 9/16/15	Wed 9/23/15
12		Sheath	5 days	Tue 9/22/15	Mon 9/28/15
13					
14		**Level 4 North**	**8 days**	**Tue 9/8/15**	**Thu 9/17/15**
15		Frame	4 days	Tue 9/8/15	Fri 9/11/15
16		Roll Joist	3 days	Fri 9/11/15	Tue 9/15/15
17		Sheath	4 days	Mon 9/14/15	Thu 9/17/15
18					
19		**Fire Sprinkler**	**10 days**	**Tue 9/8/15**	**Mon 9/21/15**
20		Mains North Garage	10 days	Tue 9/8/15	Mon 9/21/15
21					
22		**Garage**	**15 days**	**Tue 9/8/15**	**Mon 9/28/15**
23		MEP RI LP/ 1	15 days	Tue 9/8/15	Mon 9/28/15
24					
25		**Mtl Stud Framing**	**14 days?**	**Tue 9/8/15**	**Fri 9/25/15**
26		Level P	3 days	Tue 9/8/15	Thu 9/10/15
27		Stair 1 Exterior	4 days	Tue 9/8/15	Fri 9/11/15
28		Level 2 Units Etc. North	10 days	Mon 9/14/15	Fri 9/25/15
29		Rock Ext walls	1 day?	Tue 9/8/15	Tue 9/8/15
30					
31		**Hollow metal**	**3 days**	**Tue 9/22/15**	**Thu 9/24/15**
32		Deliver	1 day	Tue 9/22/15	Tue 9/22/15
33		Set Frames	2 days	Wed 9/23/15	Thu 9/24/15
34					

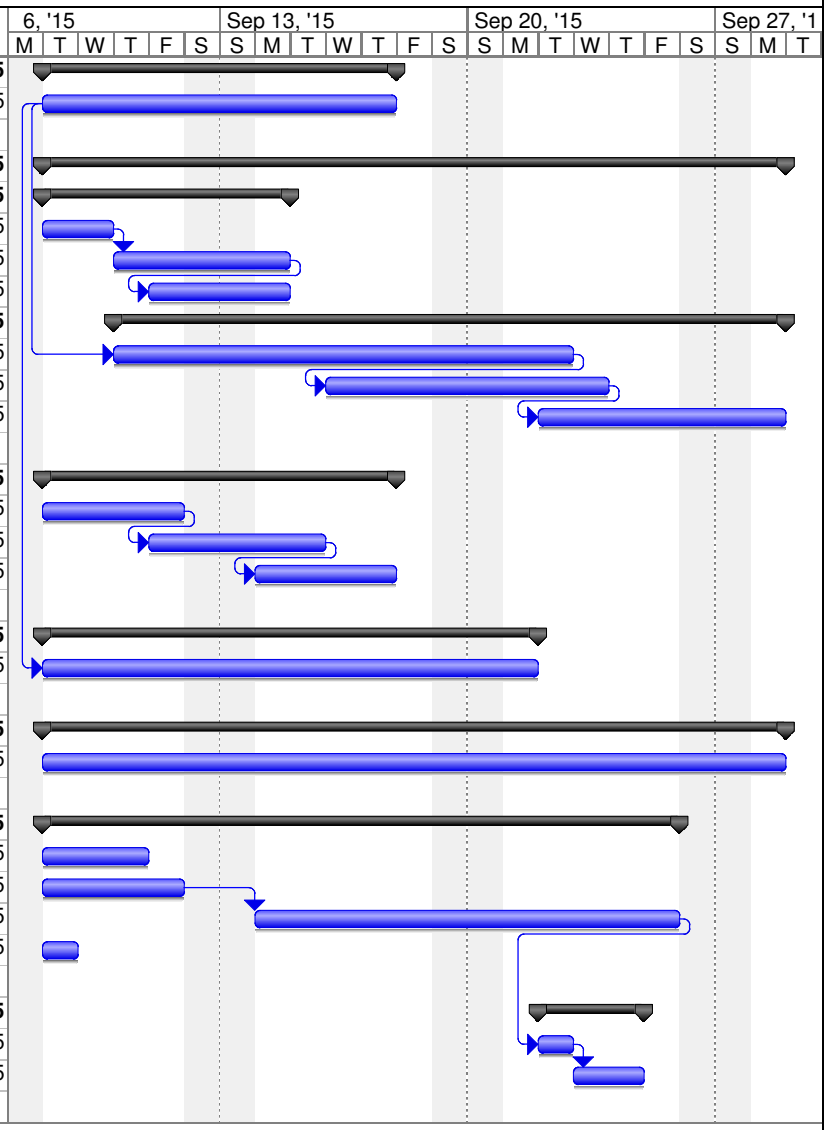

Project: 3wk look ahead 9-8-31 Rev 1
Date: Wed 9/2/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
9-8-2015

ID		Task Name	Duration	Start	Finish
35		**Waterproofing**	**4 days**	**Tue 9/8/15**	**Fri 9/11/15**
36		Blockouts/Tiebacks	4 days	Tue 9/8/15	Fri 9/11/15
37					
38		**Subgrade**	**6 days**	**Tue 9/8/15**	**Tue 9/15/15**
39		Grade West	4 days	Tue 9/8/15	Fri 9/11/15
40		West Drainage	4 days	Thu 9/10/15	Tue 9/15/15
41		Exc Wall Ftgs	2 days	Mon 9/14/15	Tue 9/15/15
42					
43		**West Shoring walls**	**4 days**	**Mon 9/14/15**	**Thu 9/17/15**
44		Weld Nelson studs	1 day	Mon 9/14/15	Mon 9/14/15
45		Reinforcing	2 days	Tue 9/15/15	Wed 9/16/15
46		Shotcrete	1 day	Thu 9/17/15	Thu 9/17/15

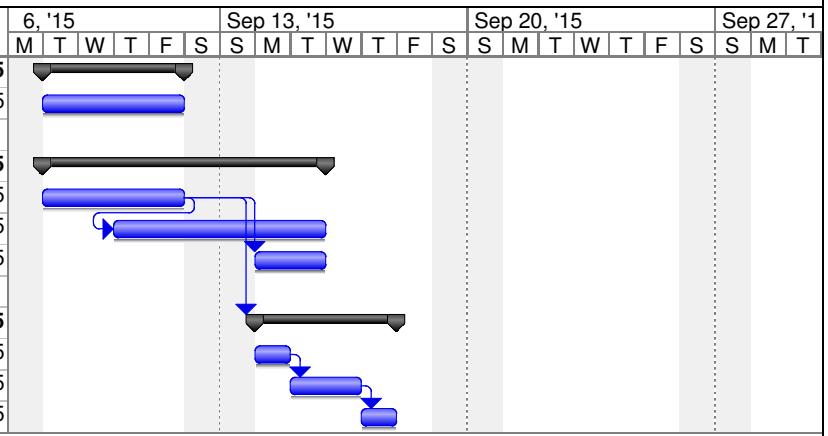

Project: 3wk look ahead 9-8-31 Rev 1
Date: Wed 9/2/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
