CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **29**

MEETING DATE: **09/15/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
~~Mark Pesanti – CHINN~~
Charlie Poggemann – CHINN
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
~~Darryl McNamee – LAB~~
~~Jesse Earle – Froula~~
~~Jason – CFM~~
Jose Mendina - Advanced
~~John Studioso - IEC~~
~~Richard Donelson - OWP~~
Tim Hutchison - SS
Joe Barnhart - OWP
Lincoln Boomars – LAB
Eric Bull - CHINN
Ross Porterfield – IEC
~~Roger Rueda – WCP~~

SAFETY:

29.01 Housekeeping

- No smoking onsite
- Sweep and clean up for the next trade in work areas
- There is no food allowed in the building when framing starts; framing crew to eat lunch in garage
- Verbal/Written/Gone Parking Policy
- IEC is routing temp power for each floor
    - More boloni cords are arriving today, additional bulbs are on order
- Crew will need to start carpooling
- Use the delivery board – check crane box if you need crane
- Music has been too loud in the parking lately. Keep the volume down
-

SCHEDULE:

29.02 Reviewed **SITE** 3 wk look ahead schedule beginning 09/15/15

- Level 3 PT SE – Strip, haulout 9/14-9/23
- Wood Framing North L4
    - Roll Joists, Deck 9/14-9/16
- Wood Framing North L5
    - Frame, Roll Joists, Sheath 10/7-10/14
- Wood Framing South L3
    - Frame, TJI Joist, Deck 9/14-9/30
- Fire Sprinkler Mains 9/14-9/25
- Level P MEP Roughin 9/14-10/2
- Mtl stud framing 9/14-9/29
- Hollow Metal 9/22-9/24

- Waterproofing 9/14-9/17
- Subgrade – Grade west, West Drainage, Exc Wall Ftgs, Set structures and tie in 9/24-9/25
- Shoring –Drill Set Additional Piles 9/14-9/17

XX.XX Reviewed **INTERIOR** 3wk look ahead schedule beginning xx/xx/xx

OLD BUSINESS:

23.05 Outlets at decks and locations
- 08/25/15: Owner/Architect to request variance with COMI.

26.05 Unconditioned rooms currently show regular 5/8" drywall, should be blue board.
- 09/08/15: With Owner for review
- 09/15/15: WCP approved to install blue board

28.04 Date of shotcrete for west wall be confirmed

28.06 Electrical and subcontractors need cabinet shop drawings for layout
- 09/15/15: Cabinet shops are in review.

PERMIT STATUS: Electrical, HVAC

RFIs:

SUBMITTALS:

NEW BUSINESS:

29.03 OWP to core drill for drainage at unit apron and courtyard apron

29.04 CHINN to coordinate with Advanced for more temporary standpipe

29.05 EB to measure for stair #3 and #4 as soon as reshores are removed

29.06 COMI will use inspection board at the back of the CHINN construction office.
Trades are welcome to use it to track inspections

29.07 EB to place unit numbers on the entry door rough framing.

29.08 IEC will need drop ceilings for feeders in Unassigned Utilities 371 and 380 stacks.

29.09 Owner, Low voltage, Plumbing and CHINN will need to schedule a box walk.

29.10 WCP will start framing Level 2 once reshores are gone (less the Elevator Lobby)

29.11 CHINN and WCP to coordinate scrap out dumpster location

29.12 IEC to verify size of switch gear to get gear in the room.

29.13 Review puddy pad and fire rated assemblies on sheet A/0930

NEXT MEETING: 09/22/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
9-14-2015

ID		Task Name	Duration	Start	Finish
1		**Concrete**	**16 days**	**Mon 9/14/15**	**Mon 10/5/15**
2		**Site/Structure**	**16 days**	**Mon 9/14/15**	**Mon 10/5/15**
3		Shotcrete West	4 days	Fri 9/18/15	Wed 9/23/15
4		West Retaing walls	8 days	Thu 9/24/15	Mon 10/5/15
5		Grind/Sack Exterior	15 days	Mon 9/14/15	Fri 10/2/15
6		Pourback Closure	1 day	Thu 9/24/15	Thu 9/24/15
7					
8		**Level 3 SE PT**	**8 days**	**Mon 9/14/15**	**Wed 9/23/15**
9		Strip/Haulout	8 days	Mon 9/14/15	Wed 9/23/15
10					
11		**Wood Framing L3**	**13 days**	**Mon 9/14/15**	**Wed 9/30/15**
12		**Southwest**	**3 days**	**Mon 9/14/15**	**Wed 9/16/15**
13		Roll Joist	3 days	Mon 9/14/15	Wed 9/16/15
14		Sheath	2 days	Tue 9/15/15	Wed 9/16/15
15		**Southeast**	**13 days**	**Mon 9/14/15**	**Wed 9/30/15**
16		Frame	7 days	Mon 9/14/15	Tue 9/22/15
17		Roll Joist	6 days	Fri 9/18/15	Fri 9/25/15
18		Sheath	6 days	Wed 9/23/15	Wed 9/30/15
19					
20		**Level 4 North**	**3 days**	**Mon 9/14/15**	**Wed 9/16/15**
21		Roll Joist	2 days	Mon 9/14/15	Tue 9/15/15
22		Sheath	2 days	Tue 9/15/15	Wed 9/16/15
23					
24		**Level 5 North**	**16 days**	**Wed 9/23/15**	**Wed 10/14/15**
25		Frame	12 days	Wed 9/23/15	Thu 10/8/15
26		Roll Joist	6 days	Fri 10/2/15	Fri 10/9/15
27		Sheath	6 days	Wed 10/7/15	Wed 10/14/15
28					
29		**Fire Sprinkler**	**10 days**	**Mon 9/14/15**	**Fri 9/25/15**
30		Mains North Garage	10 days	Mon 9/14/15	Fri 9/25/15
31					
32		**MEP**	**15 days**	**Mon 9/14/15**	**Fri 10/2/15**
33		MEP RI LP- 1-2	15 days	Mon 9/14/15	Fri 10/2/15
34		L2 South	10 days	Mon 9/21/15	Fri 10/2/15

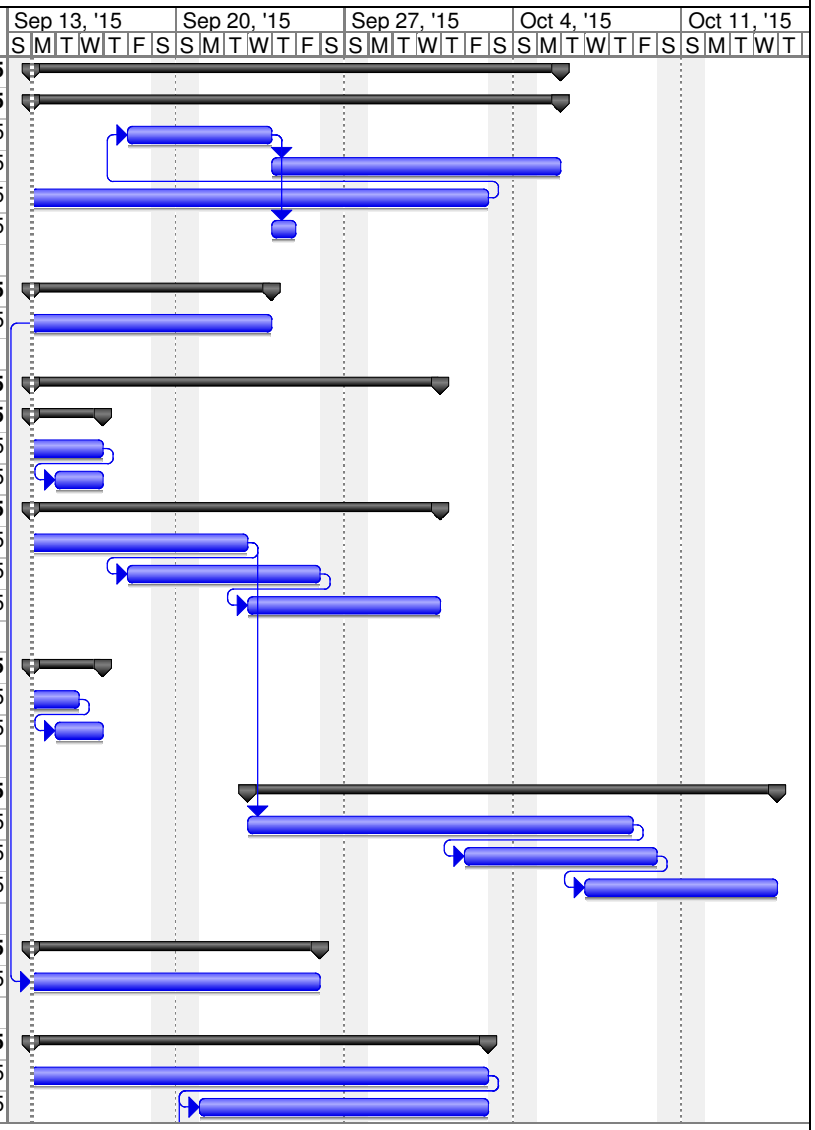

Project: 3wk look ahead 9-14-31 Rev
Date: Mon 9/14/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
9-14-2015

ID		Task Name	Duration	Start	Finish
35		Level 3 North	10 days	Mon 9/21/15	Fri 10/2/15
36					
37		**Mtl Stud Framing**	**12 days**	**Mon 9/14/15**	**Tue 9/29/15**
38		Level 2 Units Etc. North	4 days	Mon 9/14/15	Thu 9/17/15
39		Rock Ext walls	8 days	Fri 9/18/15	Tue 9/29/15
40		Level 1-2 South walls	6 days	Fri 9/18/15	Fri 9/25/15
41					
42		**Hollow metal**	**3 days**	**Tue 9/22/15**	**Thu 9/24/15**
43		Deliver	1 day	Tue 9/22/15	Tue 9/22/15
44		Set Frames	2 days	Wed 9/23/15	Thu 9/24/15
45					
46		**Waterproofing**	**4 days**	**Mon 9/14/15**	**Thu 9/17/15**
47		Blockouts/Tiebacks	4 days	Mon 9/14/15	Thu 9/17/15
48					
49		**Subgrade**	**10 days**	**Mon 9/14/15**	**Fri 9/25/15**
50		Grade West	3 days	Mon 9/14/15	Wed 9/16/15
51		West Drainage	2 days	Tue 9/15/15	Wed 9/16/15
52		Exc Wall Ftgs	4 days	Thu 9/17/15	Tue 9/22/15
53		Set Structures/Tie-in	3 days	Wed 9/23/15	Fri 9/25/15

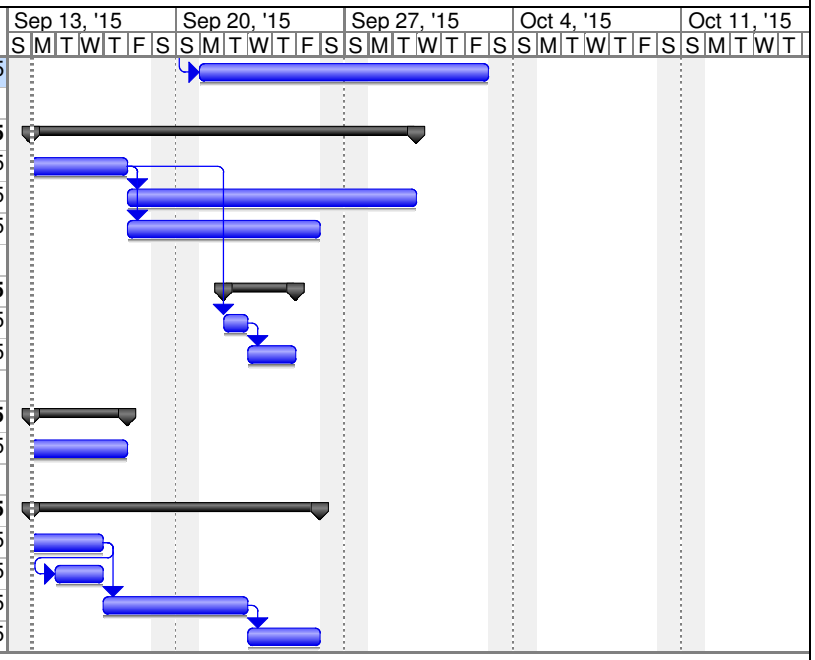

Project: 3wk look ahead 9-14-31 Rev
Date: Mon 9/14/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
