CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **30**

MEETING DATE: **09/22/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
~~Mark Pesanti – CHINN~~
~~Charlie Poggemann – CHINN~~
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
~~Darryl McNamee – LAB~~
~~Jesse Earle – Froula~~
~~Jason – CFM~~
~~Jose Mendina - Advanced~~
~~John Studioso - IEC~~
~~Richard Donelson - OWP~~
Tim Hutchison - SS
Joe Barnhart - OWP
~~Lincoln Boomars – LAB~~
Eric Bull - CHINN
Ross Porterfield – IEC
~~Roger Rueda – WCP~~

SAFETY: **Fire Extinguishers have been placed on each floor in case of emergency. It was noted on a weekly safety inspection that boloni cord was hung by wire. Framers be sure to tie off around shafts.**

30.01 Housekeeping

- No smoking onsite
- Sweep and clean up for the next trade in work areas
- There is no food allowed in the building when framing starts
- Verbal/Written/Gone Parking Policy
- IEC is routing temp power for each floor
  - More boloni cords are required for the 5th floor
- Use the delivery board – check crane box if you need crane

SCHEDULE:

30.02 Reviewed **SITE** 3 wk look ahead schedule beginning 09/21/15

- Site Structure – Shotcrete West 9/23, West retaining walls 9/28-10/7, Grind/Sack Exterior, Pour back closure 9/21-10/9
- Wood Framing Level 4 South – Roll Joists, sheath 9/21-9/28
- Wood Framing Level 5 North/South – Frame, Roll Joists, Sheath 9/21-10/13
- Fire Sprinkler – Mains North Garage 9/21-10/2
- Level P/1 – MEP RI LP, 1 and 2 – 9/21-10/9
- Metal Stud Framing – Level 2 Units 9/21-9/24, Sheet rock ext walls 9/25-10/6, Level 1-2 south walls 9/25-10/2
- Hollow Metal – 9/29-10/1
- Waterproofing – West Wall and Tiebacks 10/1
- Subgrade – Grade West 9/21-9/23, West Drainage 9/23-9/25, Exc Wall Footings 9/24-9/29, Set Structures/Tie-in 9/23-9/25

- Shoring – Weld Nelson Studs, Reinforcing, Shotcrete 9/28-9/30
- Shoring –Drill Set Additional Piles 9/14-9/17

XX.XX Reviewed **INTERIOR** 3wk look ahead schedule beginning xx/xx/xx

OLD BUSINESS:

23.05 Outlets at decks and locations

- 08/25/15: Owner/Architect to request variance with COMI.

28.06 Electrical and subcontractors need cabinet shop drawings for layout

- 09/15/15: Cabinet shops are in review.
- 09/22/15: CHINN is expecting revised shops today

29.09 Owner, Low voltage, Plumbing and CHINN will need to schedule a box walk.

- 09/22/15: Add IEC to box walk

29.11 CHINN and WCP to coordinate scrap out dumpster location

PERMIT STATUS: Electrical, HVAC

RFIs:

SUBMITTALS:

NEW BUSINESS:

30.03 We will have visitors on 10/1 to tour the project

30.04 Advanced to advise sprinkler testing

30.05 WCP will be installing densglass on the exterior of Stair 1

30.06 Shotcrete at the West is schedule for 9/23, then site walls and the access road to the west and north will closed.

30.07 A building envelope precon meeting invite will be sent out to the subs including but not limited to: fire ratings, putty packs, fire safing, siding, WRB etc…

30.08 OWP furnishes and installs shower valve backing

30.09 OWP and CHINN to coordinate rain runnel location.

NEXT MEETING: 09/29/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
9-21-2015

ID		Task Name	Duration	Start	Finish
1		**Concrete**	**15 days**	**Mon 9/21/15**	**Fri 10/9/15**
2		**Site/Structure**	**15 days**	**Mon 9/21/15**	**Fri 10/9/15**
3		Shotcrete West	3 days	Mon 9/21/15	Wed 9/23/15
4		West Retaing walls	8 days	Mon 9/28/15	Wed 10/7/15
5		Grind/Sack Exterior	15 days	Mon 9/21/15	Fri 10/9/15
6		Pourback Closure	1 day	Mon 9/21/15	Mon 9/21/15
7					
8		**Level 3 SE PT**	**3 days**	**Mon 9/21/15**	**Wed 9/23/15**
9		Strip/Haulout	3 days	Mon 9/21/15	Wed 9/23/15
10					
11		**Wood Framing**	**21 days**	**Mon 9/21/15**	**Mon 10/19/15**
12		**Level 4 SW**	**6 days**	**Mon 9/21/15**	**Mon 9/28/15**
13		Joist	2 days	Mon 9/21/15	Tue 9/22/15
14		Sheath	1 day	Wed 9/23/15	Wed 9/23/15
15					
16		**Level 3 SE**	**6 days**	**Mon 9/21/15**	**Mon 9/28/15**
17		Roll Joist	5 days	Mon 9/21/15	Fri 9/25/15
18		Sheath	4 days	Wed 9/23/15	Mon 9/28/15
19					
20		**Level 5 North**	**16 days**	**Mon 9/21/15**	**Mon 10/12/15**
21		Frame	10 days	Mon 9/21/15	Fri 10/2/15
22		Roll Joist	8 days	Mon 9/28/15	Wed 10/7/15
23		Sheath	6 days	Mon 10/5/15	Mon 10/12/15
24					
25		**Level 5 SW**	**14 days**	**Thu 9/24/15**	**Tue 10/13/15**
26		Frame	8 days	Thu 9/24/15	Mon 10/5/15
27		Roll Joist	6 days	Thu 10/1/15	Thu 10/8/15
28		Sheath	5 days	Wed 10/7/15	Tue 10/13/15
29					
30		**Level 4 SE**	**15 days**	**Tue 9/29/15**	**Mon 10/19/15**
31		Frame	8 days	Tue 9/29/15	Thu 10/8/15
32		Roll Joist	7 days	Tue 10/6/15	Wed 10/14/15
33		Sheath	5 days	Tue 10/13/15	Mon 10/19/15
34					

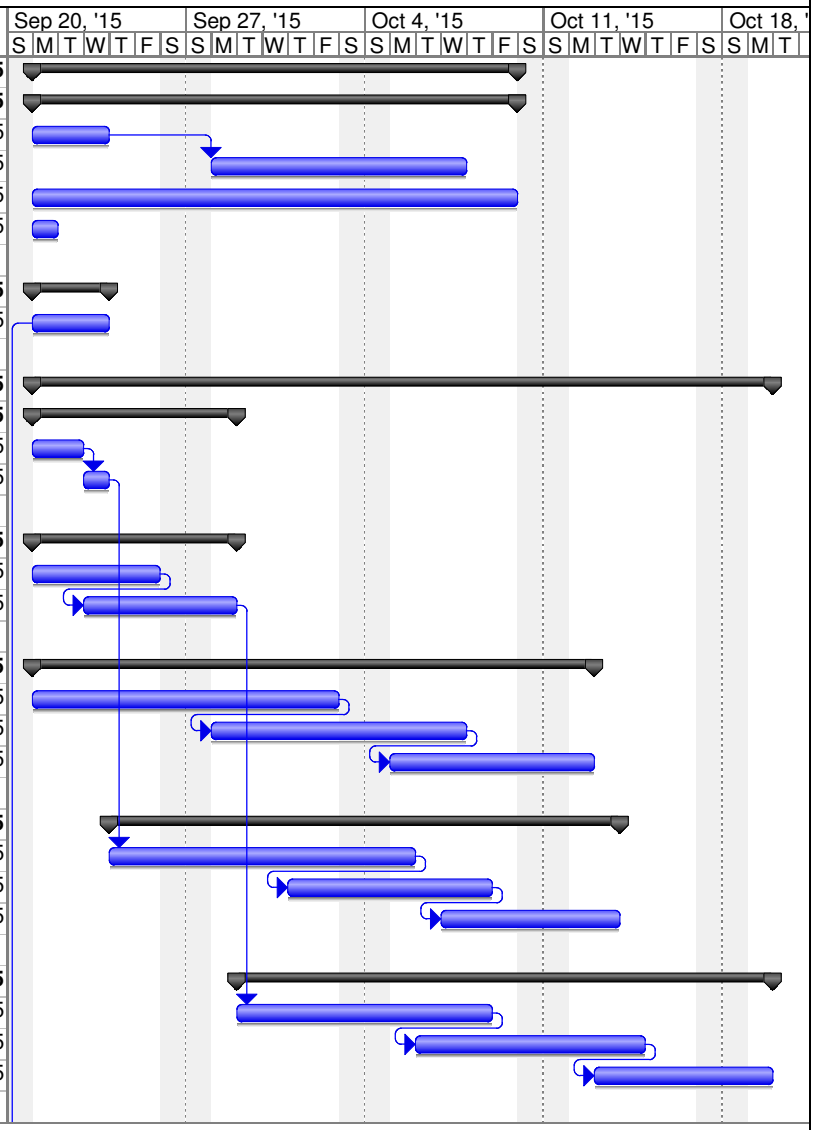

Project: 3wk look ahead 9-21-31 Rev
Date: Fri 9/18/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
9-21-2015

ID	Task Name	Duration	Start	Finish
35	**Fire Sprinkler**	**10 days**	**Mon 9/21/15**	**Fri 10/2/15**
36	Mains North Garage	10 days	Mon 9/21/15	Fri 10/2/15
37				
38	**MEP**	**15 days**	**Mon 9/21/15**	**Fri 10/9/15**
39	MEP RI LP- 1-2	15 days	Mon 9/21/15	Fri 10/9/15
40	L2 South	10 days	Mon 9/28/15	Fri 10/9/15
41	Level 3 North	10 days	Mon 9/28/15	Fri 10/9/15
42				
43	**Mtl Stud Framing**	**12 days**	**Mon 9/21/15**	**Tue 10/6/15**
44	Level 2 Units Ext. North	4 days	Mon 9/21/15	Thu 9/24/15
45	Rock Ext walls	8 days	Fri 9/25/15	Tue 10/6/15
46	Level 1-2 South walls	6 days	Fri 9/25/15	Fri 10/2/15
47				
48	**Hollow metal**	**3 days**	**Tue 9/29/15**	**Thu 10/1/15**
49	Deliver	1 day	Tue 9/29/15	Tue 9/29/15
50	Set Frames	2 days	Wed 9/30/15	Thu 10/1/15
51				
52	**Waterproofing**	**4 days**	**Mon 9/21/15**	**Thu 9/24/15**
53	Blockouts/Tiebacks	4 days	Mon 9/21/15	Thu 9/24/15
54				
55	**Subgrade**	**8 days**	**Mon 9/21/15**	**Wed 9/30/15**
56	Grade West	3 days	Mon 9/21/15	Wed 9/23/15
57	West Drainage	4 days	Tue 9/22/15	Fri 9/25/15
58	Exc Wall Ftgs	4 days	Thu 9/24/15	Tue 9/29/15
59	Set Structures/Tie-in	3 days	Mon 9/28/15	Wed 9/30/15

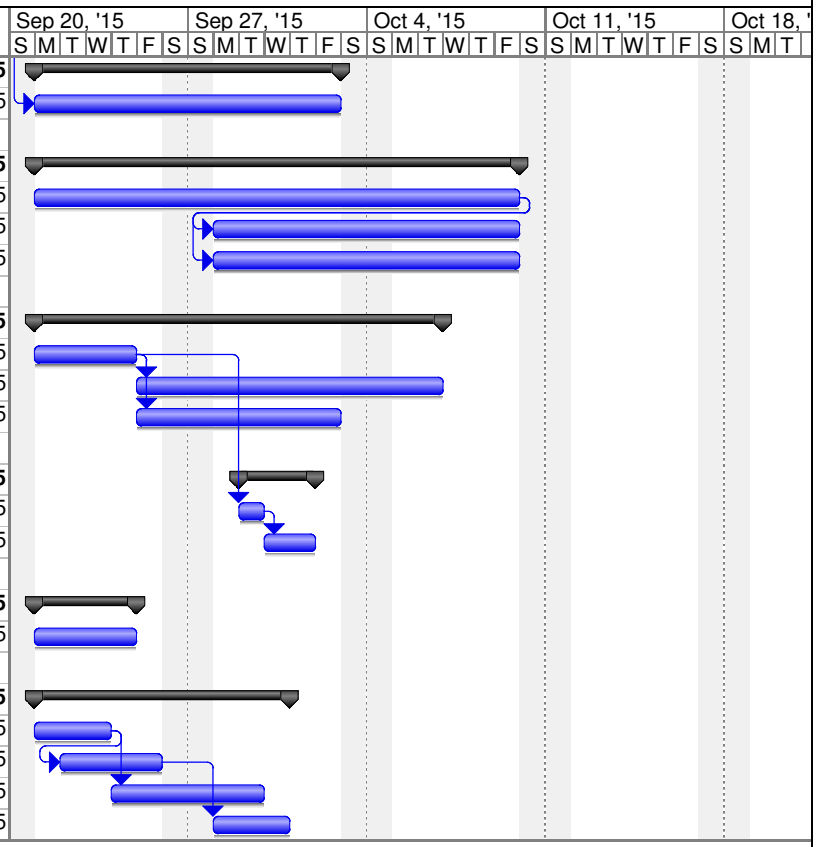

Project: 3wk look ahead 9-21-31 Rev
Date: Fri 9/18/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
