CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **39**

MEETING DATE: **11/24/15**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
~~Charlie Poggemann – CHINN~~
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
Eric Bull – CHINN
~~Jesse Earle – Froula~~
~~Jason – CFM~~
Joe Barnhart - OWP
George Faler - CHINN
Casey Hutchison - SS
Richard Donelson - OWP
Jose Mendina – Advanced
Gary – Prec. Wall
~~Ross Porterfield – IEC~~
Roger Rueda – WCP

SAFETY: Be mindful of slippery surfaces and the cold weather. Review JHA for using 10 yard container to hoist materials.

39.01 Housekeeping

- No smoking onsite
- Sweep and clean up for the next trade in work areas
  - All subs need to clean up all areas everyday
- There is no food allowed above Level 2
- IEC is routing temp power for each floor
- Use the delivery board – check crane box if you need crane
- Do not remove temporary screens in the deck drains
- Do not plug cords into the string lights
- Do not flip spider boxes on their sides
- Windows are being stocked in the units. Do Not lean material against them and do not open them if they are tacked up in the units.
- Please coordinate with CHINN on where you are stocking the building, how long material will sit in the building…etc
- Level 6 spider box needs repairs, only two outlets work.
- Subcontractors to provide crews with task lighting

SCHEDULE:

39.02 Reviewed **SITE** 3 wk look ahead schedule beginning 11/23/15

- Site Grading/Utilities – West Exc and Backfill 11/23, North 11/23-12/3, Exc Secondary Trench 11/23, Excavate Transformer room.
- Site Structure – North Retaining Walls 11/23-12/7, East Storefront Topping slab 11/23
- Wood Framing Roof North Soutwest – Roof 11/23-12/8
- Wood framing Roof Southeast – Complete Framing 12/7-12/8, set walkway stanchions 12/7-12/11, Cricket/Screen walls 12/14-12/18, Roofing 12/21-1/1
- Penthouse/Mezzanine – Frame, Joist/Sheath 11/23-12/4

- Exterior – Bonnet Scaffold 11/23-11/25, wrap/set door pans and windows west 11/30-12/7, Deliver windows complete 11/23-12/2, Target Wall Stubs 11/23-11/30, Set rim scaffold, Tyvek and siding 12/8-1/1
- Metal Stud Framing – Rock storefronts, rock ext level 1-2 south 11/23-12/4
- Temp Heat – Temp Gas Meter, Deliver/Set Equipment, Heat West 12/7-12/9
- Waterproofing – Bentonite shaft/N wall 11/23

39.03 Reviewed **INTERIOR** 3wk look ahead schedule beginning 11/23/15

- 11/23/15: OWP to have waste and water inspected by 12/9 in Zone 3

OLD BUSINESS:

36.05 Roof – make sure your curbs have been laid out, vent pipes, screen walls, and HVAC equipment disconnects.

- 11/24/15: OWP had vents stubbed though the roof and were directed to remove them. OWP and Premier Roofing to discuss sequencing. LB to send roofer's contact information to RD

37.04 Crane dismantle is scheduled for 01/09/16

37.09 Sprinkler sub wants to know if he can set the head heights now as opposed to coming back later and cutting them.

- 11/17/15: Pending

38.06 Temporary gas is being prepped at the SW side of the building. IEC has all of the required information for temp heating.

- 11/24/15: The temp gas line should be installed the 1st week of December. OWP and CHINN to review temp gas manifold layout. MP Temp heat should be turned on the 2nd or 3rd week of December.

38.08 SSI to start flushing out nails on the interior courtyard side and to schedule holdown personnel to be onsite.

- 11/24/15: CH this work is completed.

38.09 Advanced and IEC to coordinate lights and sprinklers at storefront alcoves

38.10 Concrete punch – MEP subs to cut any nails from slab can outs, so the garage concrete can be punched.

- 11/24/15: OWP completed.

PERMIT STATUS: **HVAC** – Jason (CFM) Corrections were submitted 10/09 or 10/12, Met with Architect on 11/16 to discuss Louvers at the storefront

RFIs:

SUBMITTALS:

NEW BUSINESS:

39.04 CHINN to review scupper size.

39.05 OWP needs enough room at the roof top BBQ to install a regulator next to the gas line stub up.

39.06 OWP confirmed 1st tub delivery on 12/2

39.07 Loading and unloading units are x07 stack and x60 stack

39.08 OWP would like to run the gas line and penetrate the North elevation wall as opposed to the eas.

39.09 Gypcrete under tubs is scheduled for 12/14/15.

39.10 The sub slab depressurization system blower will be installed next week

39.11 CHINN to submit RFI on the storefront alcove framing at storefronts.

NEXT MEETING: 12/02/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
11-23-2015

ID		Task Name	Duration	Start	Finish
1		**Site Grading/Utilities**	**7 days**	**Mon 11/23/15**	**Thu 12/3/15**
2		**West**	**1 day**	**Mon 11/23/15**	**Mon 11/23/15**
3		Exc/Backfill Rem Sitewall	1 day	Mon 11/23/15	Mon 11/23/15
4		**North**	**7 days**	**Mon 11/23/15**	**Thu 12/3/15**
5		Backfill Ret Wall	1 day	Mon 11/23/15	Mon 11/23/15
6		Exc Secondary Trench	1 day	Mon 11/23/15	Mon 11/23/15
7		Excavate Transformer room	1 day	Thu 12/3/15	Thu 12/3/15
8					
9		**Site/Structure**	**9 days**	**Mon 11/23/15**	**Mon 12/7/15**
10		**North**	**9 days**	**Mon 11/23/15**	**Mon 12/7/15**
11		Retaining Walls	7 days	Mon 11/23/15	Mon 12/7/15
12		**East**	**1 day**	**Mon 11/23/15**	**Mon 11/23/15**
13		Storefront Topping slab	1 day	Mon 11/23/15	Mon 11/23/15
14					
15					
16		**Wood Framing/Roofing**	**10 days**	**Mon 11/23/15**	**Tue 12/8/15**
17		**North/Southwest**	**10 days**	**Mon 11/23/15**	**Tue 12/8/15**
18		Roof	10 days	Mon 11/23/15	Tue 12/8/15
19		**Penthouse SE**	**8 days**	**Mon 11/23/15**	**Fri 12/4/15**
20		Frame	7 days	Mon 11/23/15	Thu 12/3/15
21		Joist/Sheath	3 days	Wed 12/2/15	Fri 12/4/15
22		**Southeast**	**21 days**	**Wed 12/2/15**	**Fri 1/1/16**
23		Complete Framing	5 days	Wed 12/2/15	Tue 12/8/15
24		Walkway Stanchions	5 days	Mon 12/7/15	Fri 12/11/15
25		Crickets	5 days	Mon 12/14/15	Fri 12/18/15
26		Roofing	8 days	Mon 12/21/15	Fri 1/1/16
27					
28		**Exterior**	**26 days**	**Mon 11/23/15**	**Fri 1/1/16**
29		Bonnet Scaffolds	3 days	Mon 11/23/15	Wed 11/25/15
30		Wrap/Set Door Pans/ Windows West/North	6 days	Mon 11/30/15	Mon 12/7/15
31		Deliver Windows Complete	11 days	Mon 11/23/15	Wed 12/9/15
32		Target Wall Stubs	4 days	Mon 11/23/15	Mon 11/30/15
33		Set Rm North Scaffold	2 days	Fri 12/4/15	Mon 12/7/15
34		Tyvek	2 days	Tue 12/8/15	Wed 12/9/15

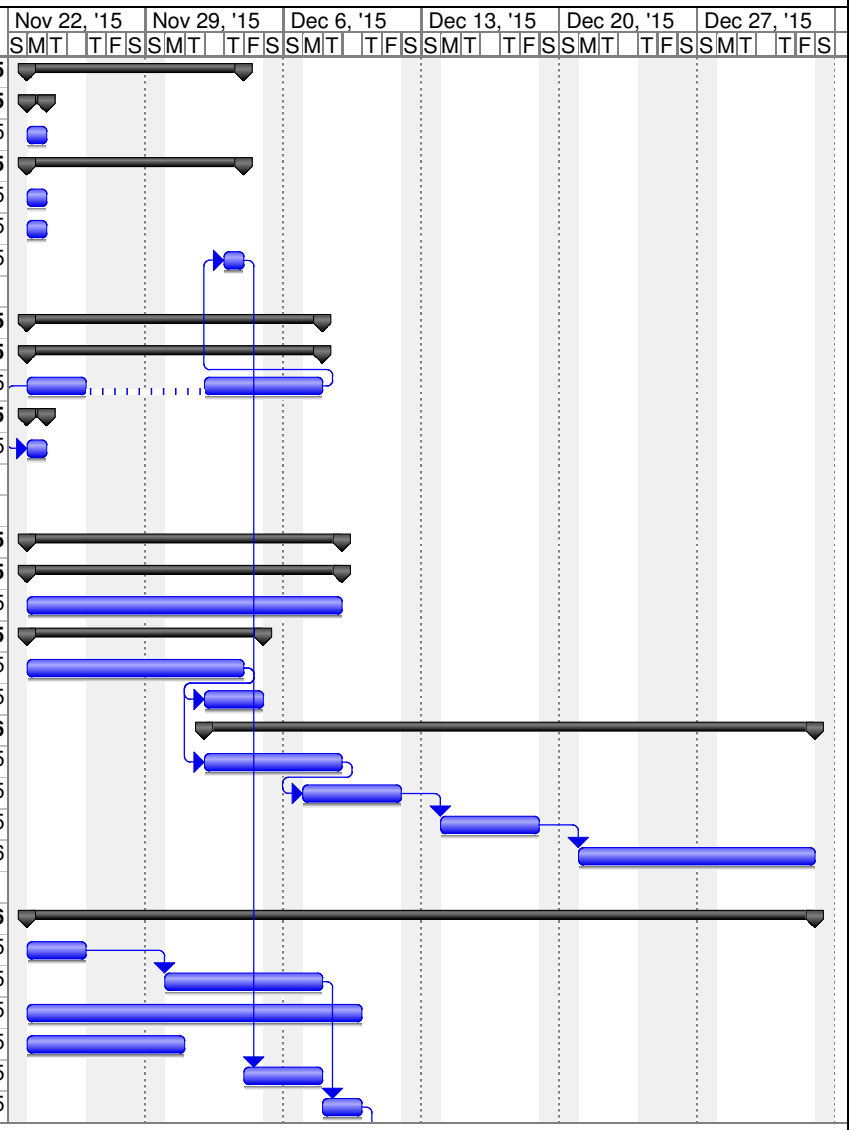

Project: 3wk 11-23-2015
Date: Fri 11/20/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
11-23-2015

ID		Task Name	Duration	Start	Finish
35		Siding	15 days	Thu 12/10/15	Fri 1/1/16
36					
37		**Mtl Stud Framing**	**8 days**	**Mon 11/23/15**	**Fri 12/4/15**
38		Rock Storefronts	4 days	Mon 11/23/15	Mon 11/30/15
39		Rock Ext Level 1-2 South	4 days	Tue 12/1/15	Fri 12/4/15
40					
41		**Temp Heat**	**3 days?**	**Mon 12/7/15**	**Wed 12/9/15**
42		Temp Gas to Meter	1 day?	Mon 12/7/15	Mon 12/7/15
43		Deliver/Set Equipment	1 day?	Tue 12/8/15	Tue 12/8/15
44		Heat West	1 day?	Wed 12/9/15	Wed 12/9/15
45					
46		**Waterproofing**	**1 day**	**Mon 11/23/15**	**Mon 11/23/15**
47		Bentonine Exhaust Shaft/N Wall	1 day	Mon 11/23/15	Mon 11/23/15

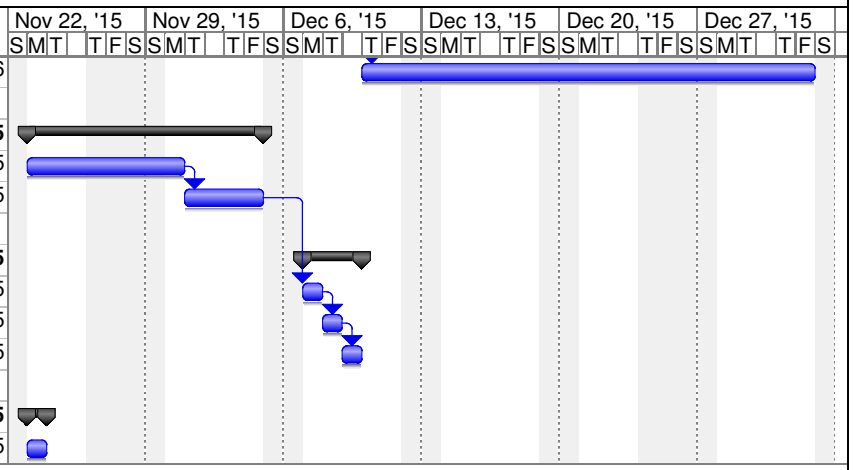

Project: 3wk 11-23-2015
Date: Fri 11/20/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID		Task Name	Duration	Start	Finish
1		**Interiors Schedule MP&E**	**63 days**	**Fri 10/2/15**	**Tue 12/29/15**
2					
3		**L3 Zone 1**	**10 days**	**Fri 10/2/15**	**Thu 10/15/15**
4		Framing Pick Up	4 days	Fri 10/2/15	Wed 10/7/15
5		Plumbing RI Drain Waste and Vent	3 days	Thu 10/8/15	Mon 10/12/15
6		Plumbing RI Water Supply	2 days	Tue 10/13/15	Wed 10/14/15
7		Fire Sprinkler Rough In	3 days	Thu 10/8/15	Mon 10/12/15
8		Electrical Box And Drill	3 days	Tue 10/13/15	Thu 10/15/15
9		Low Volt Box and Drill	1 day	Thu 10/15/15	Thu 10/15/15
10		HVAC Exhaust/AC Port Drill	2 days	Tue 10/13/15	Wed 10/14/15
11					
12		**L3 Zone 2**	**10 days**	**Thu 10/8/15**	**Wed 10/21/15**
13		Framing Pick Up	4 days	Thu 10/8/15	Tue 10/13/15
14		Plumbing RI Drain Waste and Vent	3 days	Wed 10/14/15	Fri 10/16/15
15		Plumbing RI Water Supply	2 days	Mon 10/19/15	Tue 10/20/15
16		Fire Sprinkler Rough In	3 days	Wed 10/14/15	Fri 10/16/15
17		Electrical Box And Drill	3 days	Mon 10/19/15	Wed 10/21/15
18		Low Volt Box and Drill	1 day	Wed 10/21/15	Wed 10/21/15
19		HVAC Exhaust/AC Port Drill	2 days	Mon 10/19/15	Tue 10/20/15
20					
21		**L3 Zone 3**	**10 days**	**Wed 10/14/15**	**Tue 10/27/15**
22		Framing Pick Up	4 days	Wed 10/14/15	Mon 10/19/15
23		Plumbing RI Drain Waste and Vent	3 days	Tue 10/20/15	Thu 10/22/15
24		Plumbing RI Water Supply	2 days	Fri 10/23/15	Mon 10/26/15
25		Fire Sprinkler Rough In	3 days	Tue 10/20/15	Thu 10/22/15
26		Electrical Box And Drill	3 days	Fri 10/23/15	Tue 10/27/15
27		Low Volt Box and Drill	1 day	Tue 10/27/15	Tue 10/27/15
28		HVAC Exhaust/AC Port Drill	2 days	Fri 10/23/15	Mon 10/26/15
29					
30		**L3 Zone 4**	**10 days**	**Mon 10/19/15**	**Fri 10/30/15**
31		Framing Pick Up	4 days	Mon 10/19/15	Thu 10/22/15
32		Plumbing RI Drain Waste and Vent	3 days	Fri 10/23/15	Tue 10/27/15
33		Plumbing RI Water Supply	2 days	Wed 10/28/15	Thu 10/29/15
34		Fire Sprinkler Rough In	3 days	Fri 10/23/15	Tue 10/27/15

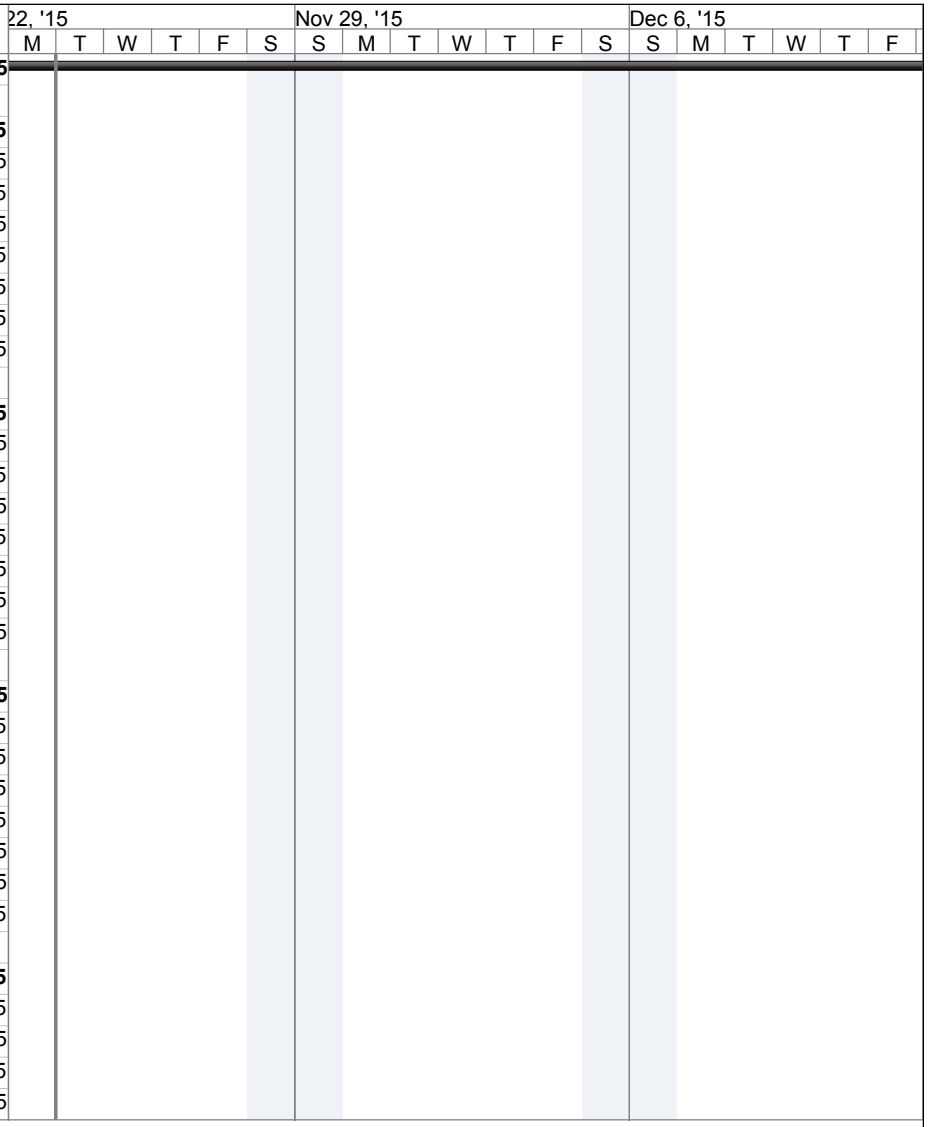

Project: MI MPE RI 11-19
Date: Tue 11/24/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

ID		Task Name	Duration	Start	Finish
35		Electrical Box And Drill	3 days	Wed 10/28/15	Fri 10/30/15
36		Low Volt Box and Drill	1 day	Fri 10/30/15	Fri 10/30/15
37		HVAC Exhaust/AC Port Drill	2 days	Wed 10/28/15	Thu 10/29/15
38					
39		Plumbing RI Levels P-L3 Test	3 days	Fri 10/30/15	Tue 11/3/15
40		Plumbing RI Levels P-L3 Inspect	1 day	Wed 11/4/15	Wed 11/4/15
41					
42					
43		**L4 Zone 1**	**10 days**	**Thu 10/22/15**	**Wed 11/4/15**
44		Framing Pick Up	4 days	Thu 10/22/15	Tue 10/27/15
45		Plumbing RI Drain Waste and Vent	3 days	Wed 10/28/15	Fri 10/30/15
46		Plumbing RI Water Supply	2 days	Mon 11/2/15	Tue 11/3/15
47		Fire Sprinkler Rough In	3 days	Wed 10/28/15	Fri 10/30/15
48		Electrical Box And Drill	3 days	Mon 11/2/15	Wed 11/4/15
49		Low Volt Box and Drill	1 day	Wed 11/4/15	Wed 11/4/15
50		HVAC Exhaust/AC Port Drill	2 days	Mon 11/2/15	Tue 11/3/15
51					
52		**L4 Zone 2**	**10 days**	**Tue 10/27/15**	**Mon 11/9/15**
53		Framing Pick Up	4 days	Tue 10/27/15	Fri 10/30/15
54		Plumbing RI Drain Waste and Vent	3 days	Mon 11/2/15	Wed 11/4/15
55		Plumbing RI Water Supply	2 days	Thu 11/5/15	Fri 11/6/15
56		Fire Sprinkler Rough In	3 days	Mon 11/2/15	Wed 11/4/15
57		Electrical Box And Drill	3 days	Thu 11/5/15	Mon 11/9/15
58		Low Volt Box and Drill	1 day	Mon 11/9/15	Mon 11/9/15
59		HVAC Exhaust/AC Port Drill	2 days	Thu 11/5/15	Fri 11/6/15
60					
61		**L4 Zone 3**	**10 days**	**Fri 10/30/15**	**Thu 11/12/15**
62		Framing Pick Up	4 days	Fri 10/30/15	Wed 11/4/15
63		Plumbing RI Drain Waste and Vent	3 days	Thu 11/5/15	Mon 11/9/15
64		Plumbing RI Water Supply	2 days	Tue 11/10/15	Wed 11/11/15
65		Fire Sprinkler Rough In	3 days	Thu 11/5/15	Mon 11/9/15
66		Electrical Box And Drill	3 days	Tue 11/10/15	Thu 11/12/15
67		Low Volt Box and Drill	1 day	Thu 11/12/15	Thu 11/12/15
68		HVAC Exhaust/AC Port Drill	2 days	Tue 11/10/15	Wed 11/11/15

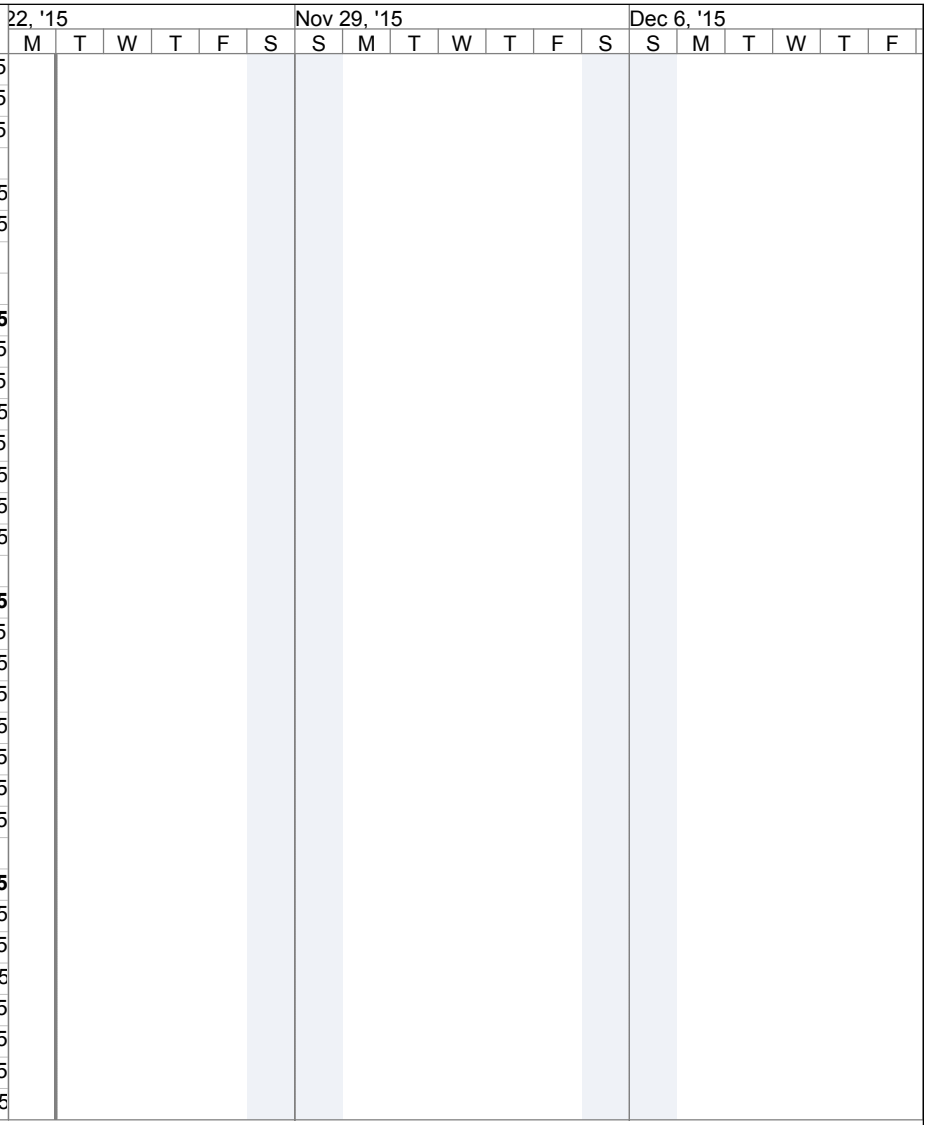

Project: MI MPE RI 11-19
Date: Tue 11/24/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

ID	Task Name	Duration	Start	Finish
69				
70	**L5 Zone 3**	**10 days**	**Wed 11/4/15**	**Tue 11/17/15**
71	Framing Pick Up	4 days	Wed 11/4/15	Mon 11/9/15
72	Plumbing RI Drain Waste and Vent	3 days	Tue 11/10/15	Thu 11/12/15
73	Plumbing RI Water Supply	2 days	Fri 11/13/15	Mon 11/16/15
74	Fire Sprinkler Rough In	3 days	Tue 11/10/15	Thu 11/12/15
75	Electrical Box And Drill	3 days	Fri 11/13/15	Tue 11/17/15
76	Low Volt Box and Drill	1 day	Tue 11/17/15	Tue 11/17/15
77	HVAC Exhaust/AC Port Drill	2 days	Fri 11/13/15	Mon 11/16/15
78				
79	**L6 Zone 3**	**13 days**	**Mon 11/9/15**	**Wed 11/25/15**
80	Framing Pick Up	4 days	Mon 11/9/15	Thu 11/12/15
81	Plumbing RI Drain Waste and Vent	6 days	Fri 11/13/15	Fri 11/20/15
82	Plumbing RI Water Supply	2 days	Mon 11/23/15	Tue 11/24/15
83	Fire Sprinkler Rough In	3 days	Fri 11/13/15	Tue 11/17/15
84	Electrical Box And Drill	3 days	Mon 11/23/15	Wed 11/25/15
85	Low Volt Box and Drill	1 day	Wed 11/25/15	Wed 11/25/15
86	HVAC Exhaust/AC Port Drill	2 days	Mon 11/23/15	Tue 11/24/15
87				
88	**L5 Zone 1**	**13 days**	**Thu 11/12/15**	**Mon 11/30/15**
89	Framing Pick Up	4 days	Thu 11/12/15	Tue 11/17/15
90	Plumbing RI Drain Waste and Vent	6 days	Wed 11/18/15	Wed 11/25/15
91	Plumbing RI Water Supply	2 days	Thu 11/26/15	Fri 11/27/15
92	Fire Sprinkler Rough In	3 days	Wed 11/18/15	Fri 11/20/15
93	Electrical Box And Drill	3 days	Thu 11/26/15	Mon 11/30/15
94	Low Volt Box and Drill	1 day	Mon 11/30/15	Mon 11/30/15
95	HVAC Exhaust/AC Port Drill	2 days	Thu 11/26/15	Fri 11/27/15
96				
97	**L6 Zone 1**	**13 days**	**Tue 11/17/15**	**Thu 12/3/15**
98	Framing Pick Up	4 days	Tue 11/17/15	Fri 11/20/15
99	Plumbing RI Drain Waste and Vent	6 days	Mon 11/23/15	Mon 11/30/15
100	Plumbing RI Water Supply	2 days	Tue 12/1/15	Wed 12/2/15
101	Fire Sprinkler Rough In	3 days	Mon 11/23/15	Wed 11/25/15
102	Electrical Box And Drill	3 days	Tue 12/1/15	Thu 12/3/15

Project: MI MPE RI 11-19
Date: Tue 11/24/15

Task	External Milestone	Manual Summary Rollup	
Split	Inactive Task	Manual Summary	
Milestone	Inactive Milestone	Start-only	
Summary	Inactive Summary	Finish-only	
Project Summary	Manual Task	Progress	
External Tasks	Duration-only	Deadline	

ID	Task Name	Duration	Start	Finish
103	Low Volt Box and Drill	1 day	Thu 12/3/15	Thu 12/3/15
104	HVAC Exhaust/AC Port Drill	2 days	Tue 12/1/15	Wed 12/2/15
105				
106	**L3-L6 Zones 1 and 3**	**10 days**	**Thu 11/26/15**	**Wed 12/9/15**
107	Fire Sprinkler Test	3 days	Thu 11/26/15	Mon 11/30/15
108	Fire Sprinkler Inspection	2 days	Tue 12/1/15	Wed 12/2/15
109	Plumbing RI Levels L3-L6 Test	3 days	Thu 12/3/15	Mon 12/7/15
110	Plumbing RI Levels L3-L6 Inspect	2 days	Tue 12/8/15	Wed 12/9/15
111				
112	**L5 Zone 2**	**12 days**	**Fri 11/20/15**	**Mon 12/7/15**
113	Framing Pick Up	4 days	Fri 11/20/15	Wed 11/25/15
114	Plumbing RI Drain Waste and Vent	5 days	Thu 11/26/15	Wed 12/2/15
115	Plumbing RI Water Supply	2 days	Thu 12/3/15	Fri 12/4/15
116	Fire Sprinkler Rough In	3 days	Thu 11/26/15	Mon 11/30/15
117	Electrical Box And Drill	3 days	Thu 12/3/15	Mon 12/7/15
118	Low Volt Box and Drill	1 day	Mon 12/7/15	Mon 12/7/15
119	HVAC Exhaust/AC Port Drill	2 days	Thu 12/3/15	Fri 12/4/15
120				
121	**L6 Zone 2**	**12 days**	**Wed 11/25/15**	**Thu 12/10/15**
122	Framing Pick Up	4 days	Wed 11/25/15	Mon 11/30/15
123	Plumbing RI Drain Waste and Vent	5 days	Tue 12/1/15	Mon 12/7/15
124	Plumbing RI Water Supply	2 days	Tue 12/8/15	Wed 12/9/15
125	Fire Sprinkler Rough In	3 days	Tue 12/1/15	Thu 12/3/15
126	Electrical Box And Drill	3 days	Tue 12/8/15	Thu 12/10/15
127	Low Volt Box and Drill	1 day	Thu 12/10/15	Thu 12/10/15
128	HVAC Exhaust/AC Port Drill	2 days	Tue 12/8/15	Wed 12/9/15
129				
130	**L4 Zone 4**	**12 days**	**Mon 11/30/15**	**Tue 12/15/15**
131	Framing Pick Up	4 days	Mon 11/30/15	Thu 12/3/15
132	Plumbing RI Drain Waste and Vent	5 days	Fri 12/4/15	Thu 12/10/15
133	Plumbing RI Water Supply	2 days	Fri 12/11/15	Mon 12/14/15
134	Fire Sprinkler Rough In	3 days	Fri 12/4/15	Tue 12/8/15
135	Electrical Box And Drill	3 days	Fri 12/11/15	Tue 12/15/15
136	Low Volt Box and Drill	1 day	Tue 12/15/15	Tue 12/15/15

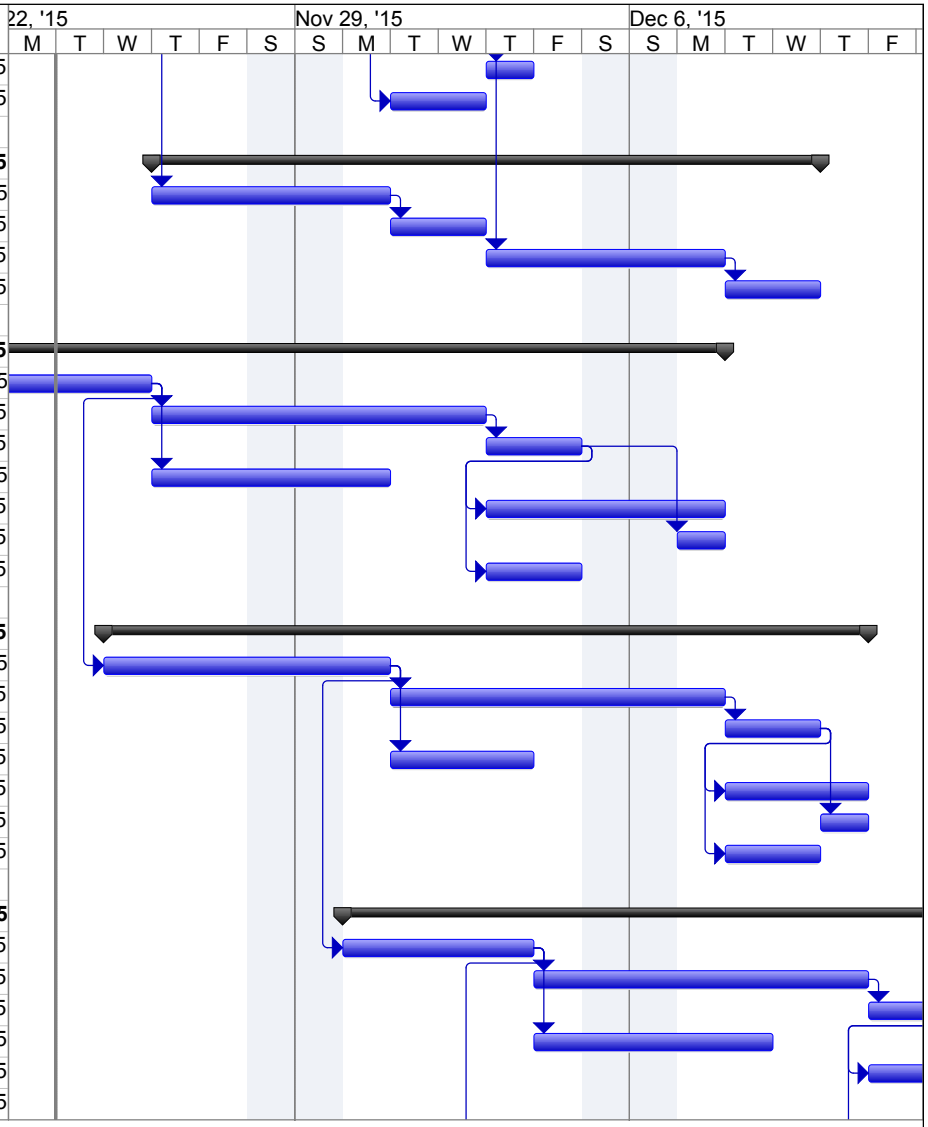

Project: MI MPE RI 11-19
Date: Tue 11/24/15

Task	External Milestone	Manual Summary Rollup	
Split	Inactive Task	Manual Summary	
Milestone	Inactive Milestone	Start-only	
Summary	Inactive Summary	Finish-only	
Project Summary	Manual Task	Progress	
External Tasks	Duration-only	Deadline	

ID	Task Name	Duration	Start	Finish
137	HVAC Exhaust/AC Port Drill	2 days	Fri 12/11/15	Mon 12/14/15
138				
139	**L5 Zone 4**	**12 days**	**Thu 12/3/15**	**Fri 12/18/15**
140	Framing Pick Up	4 days	Thu 12/3/15	Tue 12/8/15
141	Plumbing RI Drain Waste and Vent	5 days	Wed 12/9/15	Tue 12/15/15
142	Plumbing RI Water Supply	2 days	Wed 12/16/15	Thu 12/17/15
143	Fire Sprinkler Rough In	3 days	Wed 12/9/15	Fri 12/11/15
144	Electrical Box And Drill	3 days	Wed 12/16/15	Fri 12/18/15
145	Low Volt Box and Drill	1 day	Fri 12/18/15	Fri 12/18/15
146	HVAC Exhaust/AC Port Drill	2 days	Wed 12/16/15	Thu 12/17/15
147				
148	**L6 Zone 4**	**12 days**	**Tue 12/8/15**	**Wed 12/23/15**
149	Framing Pick Up	4 days	Tue 12/8/15	Fri 12/11/15
150	Plumbing RI Drain Waste and Vent	5 days	Mon 12/14/15	Fri 12/18/15
151	Plumbing RI Water Supply	2 days	Mon 12/21/15	Tue 12/22/15
152	Fire Sprinkler Rough In	3 days	Mon 12/14/15	Wed 12/16/15
153	Electrical Box And Drill	3 days	Mon 12/21/15	Wed 12/23/15
154	Low Volt Box and Drill	1 day	Wed 12/23/15	Wed 12/23/15
155	HVAC Exhaust/AC Port Drill	2 days	Mon 12/21/15	Tue 12/22/15
156				
157	**L3-L6 Zones 2 and 4**	**9 days**	**Thu 12/17/15**	**Tue 12/29/15**
158	Fire Sprinkler Test	3 days	Thu 12/17/15	Mon 12/21/15
159	Fire Sprinkler Inspection	2 days	Tue 12/22/15	Wed 12/23/15
160	Plumbing RI Levels P-L3 Test	3 days	Wed 12/23/15	Fri 12/25/15
161	Plumbing RI Levels P-L3 Inspect	2 days	Mon 12/28/15	Tue 12/29/15
162				
163	**MEP Roof Down**	**120 days**	**Mon 11/23/15**	**Fri 5/6/16**
164	**L6 Zone 1 (West Side)**	**66 days**	**Mon 11/23/15**	**Mon 2/22/16**
165	Roofing Installed	10 days	Mon 11/23/15	Fri 12/4/15
166	Electrical RI	10 days	Mon 12/7/15	Fri 12/18/15
167	Low volt RI	4 days	Thu 12/17/15	Tue 12/22/15
168	Plumbing/Electrical/Lowvolt Inspectio	4 days	Wed 12/23/15	Mon 12/28/15
169	Framing inspection	1 day	Tue 12/29/15	Tue 12/29/15
170	Insulation	4 days	Wed 12/30/15	Mon 1/4/16

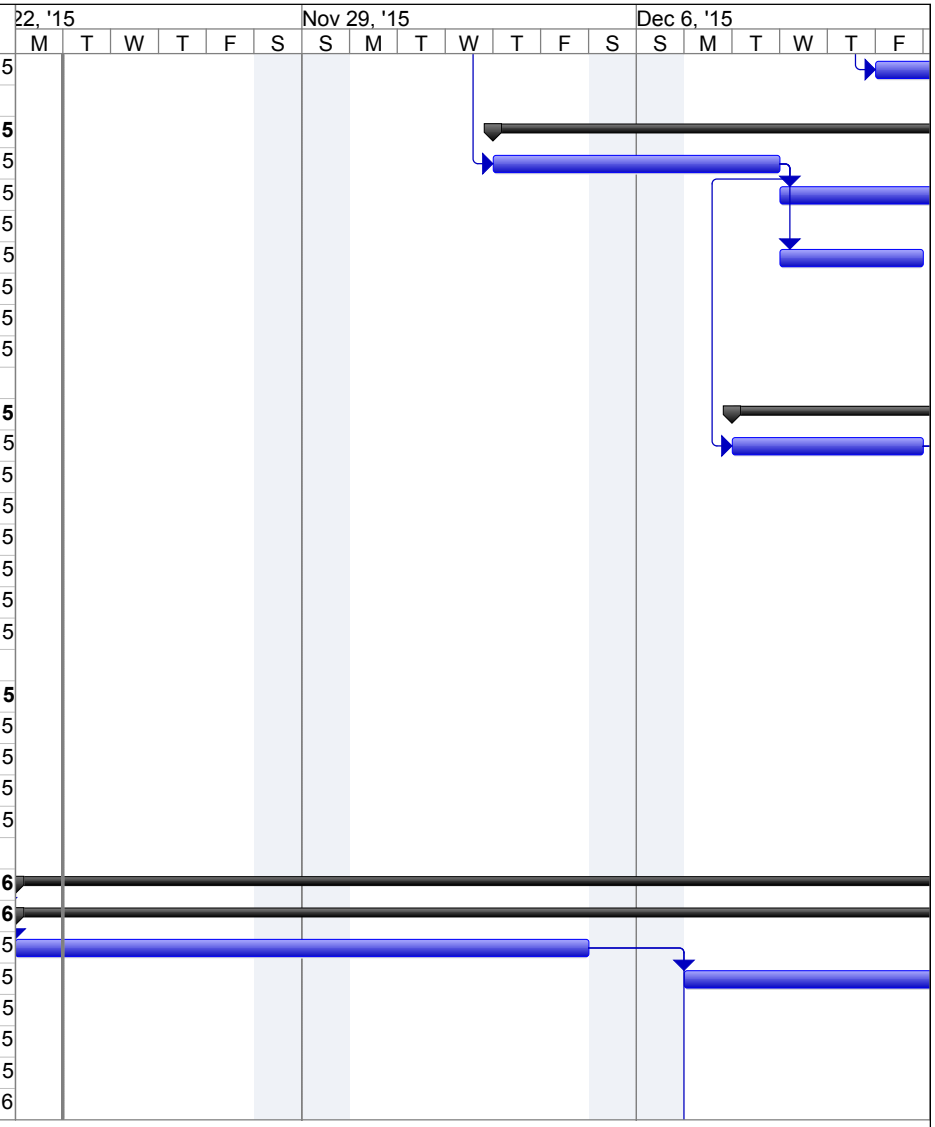

Project: MI MPE RI 11-19
Date: Tue 11/24/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

ID		Task Name	Duration	Start	Finish
171		Insulation Inspection	1 day	Tue 1/5/16	Tue 1/5/16
172		Drywall Hang/Tape/Texture/PVA	15 days	Wed 1/6/16	Tue 1/26/16
173		Frame soffits	4 days	Wed 1/13/16	Mon 1/18/16
174		Vent soffits	4 days	Tue 1/19/16	Fri 1/22/16
175		Electrical at soffits	2 days	Mon 1/25/16	Tue 1/26/16
176		HVAC/ Electrical inspection at soffits	1 day	Wed 1/27/16	Wed 1/27/16
177		Hang and tape soffits	5 days	Thu 1/28/16	Wed 2/3/16
178		Paint	5 days	Thu 2/4/16	Wed 2/10/16
179		Gypcrete	3 days	Thu 2/4/16	Mon 2/8/16
180		Gypcrete dry time	10 days	Tue 2/9/16	Mon 2/22/16
181		Electrical trim	5 days	Tue 2/2/16	Mon 2/8/16
182		Install cabinets	5 days	Tue 2/9/16	Mon 2/15/16
183					
184		Zone 1 Electrical Unit Feeders, L 3-6	10 days	Mon 12/7/15	Fri 12/18/15
185					
186		**L6-3 Zone 1 Tubs**	**11 days**	**Mon 12/14/15**	**Mon 12/28/15**
187		Gypcrete at Tubs All Levels All Zo	3 days	Mon 12/14/15	Wed 12/16/15
188		Insulate at Tubs	2 days	Thu 12/17/15	Fri 12/18/15
189		Pre Rock at Tubs	2 days	Mon 12/21/15	Tue 12/22/15
190		Install Tubs	4 days	Wed 12/23/15	Mon 12/28/15
191					
192		**L6 Zone 2 (East Side)**	**91 days**	**Mon 11/23/15**	**Mon 3/28/16**
193		Roof framing complete	20 days	Mon 11/23/15	Fri 12/18/15
194		Roofing installed	10 days	Mon 12/21/15	Fri 1/1/16
195		Electrical RI	10 days	Mon 1/4/16	Fri 1/15/16
196		Low volt RI	4 days	Thu 1/14/16	Tue 1/19/16
197		Plumbing/Electrical/Lowvolt Inspectio	4 days	Wed 1/20/16	Mon 1/25/16
198		Framing inspection	1 day	Tue 1/26/16	Tue 1/26/16
199		Insulation	4 days	Wed 1/27/16	Mon 2/1/16
200		Insulation Inspection	1 day	Tue 2/2/16	Tue 2/2/16
201		Drywall Hang/Tape/Texture/PVA	15 days	Wed 2/3/16	Tue 2/23/16
202		Frame soffits	4 days	Wed 2/10/16	Mon 2/15/16
203		Vent soffits	4 days	Tue 2/16/16	Fri 2/19/16
204		Electrical at soffits	2 days	Mon 2/22/16	Tue 2/23/16

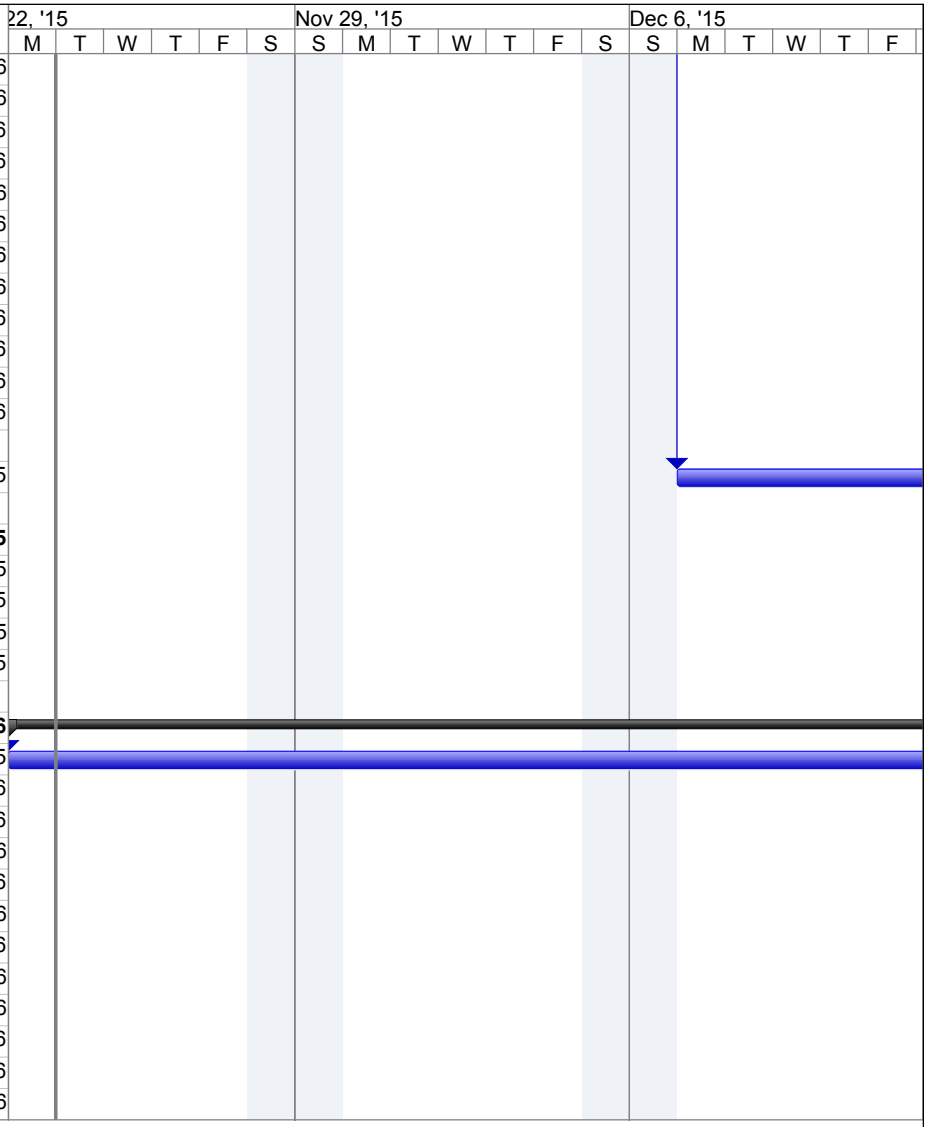

Project: MI MPE RI 11-19
Date: Tue 11/24/15

Task	External Milestone	Manual Summary Rollup
Split	Inactive Task	Manual Summary
Milestone	Inactive Milestone	Start-only
Summary	Inactive Summary	Finish-only
Project Summary	Manual Task	Progress
External Tasks	Duration-only	Deadline

ID	Task Name	Duration	Start	Finish
205	HVAC/ Electrical inspection at soffits	1 day	Wed 2/24/16	Wed 2/24/16
206	Hang and tape soffits	5 days	Thu 2/25/16	Wed 3/2/16
207	Paint	5 days	Thu 3/3/16	Wed 3/9/16
208	Gypcrete	3 days	Thu 3/10/16	Mon 3/14/16
209	Gypcrete dry time	10 days	Tue 3/15/16	Mon 3/28/16
210	Electrical trim	5 days	Tue 3/8/16	Mon 3/14/16
211	Install cabinets	5 days	Tue 3/15/16	Mon 3/21/16
212				
213				
214	Electrical Unit Feeders Zone 2, L 3-6	8 days	Mon 1/4/16	Wed 1/13/16
215				
216	**L6-3 Zone 2 Tubs**	**8 days**	**Thu 12/17/15**	**Mon 12/28/15**
217	Insulate at Tubs	2 days	Thu 12/17/15	Fri 12/18/15
218	Pre Rock at Tubs	2 days	Mon 12/21/15	Tue 12/22/15
219	Install Tubs	4 days	Wed 12/23/15	Mon 12/28/15
220				
221	**L5 Zone 1 (West Side)**	**56 days**	**Mon 12/21/15**	**Mon 3/7/16**
222	Electrical RI	10 days	Mon 12/21/15	Fri 1/1/16
223	Low volt RI	4 days	Thu 12/31/15	Tue 1/5/16
224	Plumbing/Electrical/Lowvolt Inspectio	4 days	Wed 1/6/16	Mon 1/11/16
225	Framing inspection	1 day	Tue 1/12/16	Tue 1/12/16
226	Insulation	4 days	Wed 1/13/16	Mon 1/18/16
227	Insulation Inspection	1 day	Tue 1/19/16	Tue 1/19/16
228	Drywall Hang/Tape/Texture/PVA	15 days	Wed 1/20/16	Tue 2/9/16
229	Frame soffits	4 days	Wed 1/27/16	Mon 2/1/16
230	Vent soffits	4 days	Tue 2/2/16	Fri 2/5/16
231	Electrical at soffits	2 days	Mon 2/8/16	Tue 2/9/16
232	HVAC/ Electrical inspection at soffits	1 day	Wed 2/10/16	Wed 2/10/16
233	Hang and tape soffits	5 days	Thu 2/11/16	Wed 2/17/16
234	Paint	5 days	Thu 2/18/16	Wed 2/24/16
235	Gypcrete	3 days	Thu 2/18/16	Mon 2/22/16
236	Gypcrete dry time	10 days	Tue 2/23/16	Mon 3/7/16
237	Electrical trim	5 days	Tue 2/16/16	Mon 2/22/16
238	Install cabinets	5 days	Tue 2/23/16	Mon 2/29/16

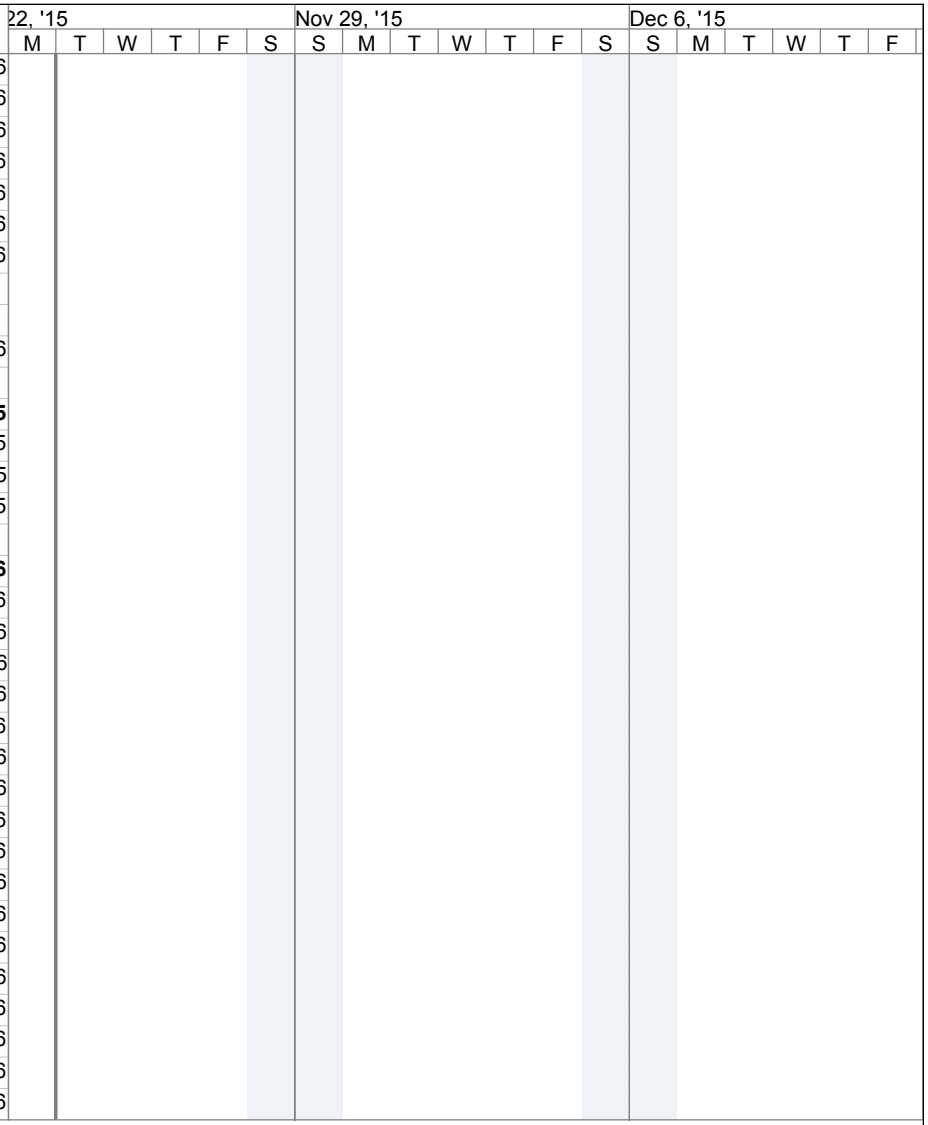

Project: MI MPE RI 11-19
Date: Tue 11/24/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

ID		Task Name	Duration	Start	Finish
239					
240		**L5 Zone 2 (East Side)**	**56 days**	**Mon 1/18/16**	**Mon 4/4/16**
241		Electrical RI	10 days	Mon 1/18/16	Fri 1/29/16
242		Low volt RI	4 days	Thu 1/28/16	Tue 2/2/16
243		Plumbing/Electrical/Lowvolt Inspectio	4 days	Wed 2/3/16	Mon 2/8/16
244		Framing inspection	1 day	Tue 2/9/16	Tue 2/9/16
245		Insulation	4 days	Wed 2/10/16	Mon 2/15/16
246		Insulation Inspection	1 day	Tue 2/16/16	Tue 2/16/16
247		Drywall Hang/Tape/Texture/PVA	15 days	Wed 2/17/16	Tue 3/8/16
248		Frame soffits	4 days	Wed 2/24/16	Mon 2/29/16
249		Vent soffits	4 days	Tue 3/1/16	Fri 3/4/16
250		Electrical at soffits	2 days	Mon 3/7/16	Tue 3/8/16
251		HVAC/ Electrical inspection at soffits	1 day	Wed 3/9/16	Wed 3/9/16
252		Hang and tape soffits	5 days	Thu 3/10/16	Wed 3/16/16
253		Paint	5 days	Thu 3/17/16	Wed 3/23/16
254		Gypcrete	3 days	Thu 3/17/16	Mon 3/21/16
255		Gypcrete dry time	10 days	Tue 3/22/16	Mon 4/4/16
256		Electrical trim	5 days	Tue 3/15/16	Mon 3/21/16
257		Install cabinets	5 days	Tue 3/22/16	Mon 3/28/16
258					
259		**L4 Zone 1 (West Side)**	**56 days**	**Mon 1/4/16**	**Mon 3/21/16**
260		Electrical RI	10 days	Mon 1/4/16	Fri 1/15/16
261		Low volt RI	4 days	Thu 1/14/16	Tue 1/19/16
262		Plumbing/Electrical/Lowvolt Inspectio	4 days	Wed 1/20/16	Mon 1/25/16
263		Framing inspection	1 day	Tue 1/26/16	Tue 1/26/16
264		Insulation	4 days	Wed 1/27/16	Mon 2/1/16
265		Insulation Inspection	1 day	Tue 2/2/16	Tue 2/2/16
266		Drywall Hang/Tape/Texture/PVA	15 days	Wed 2/3/16	Tue 2/23/16
267		Frame soffits	4 days	Wed 2/10/16	Mon 2/15/16
268		Vent soffits	4 days	Tue 2/16/16	Fri 2/19/16
269		Electrical at soffits	2 days	Mon 2/22/16	Tue 2/23/16
270		HVAC/ Electrical inspection at soffits	1 day	Wed 2/24/16	Wed 2/24/16
271		Hang and tape soffits	5 days	Thu 2/25/16	Wed 3/2/16
272		Paint	5 days	Thu 3/3/16	Wed 3/9/16

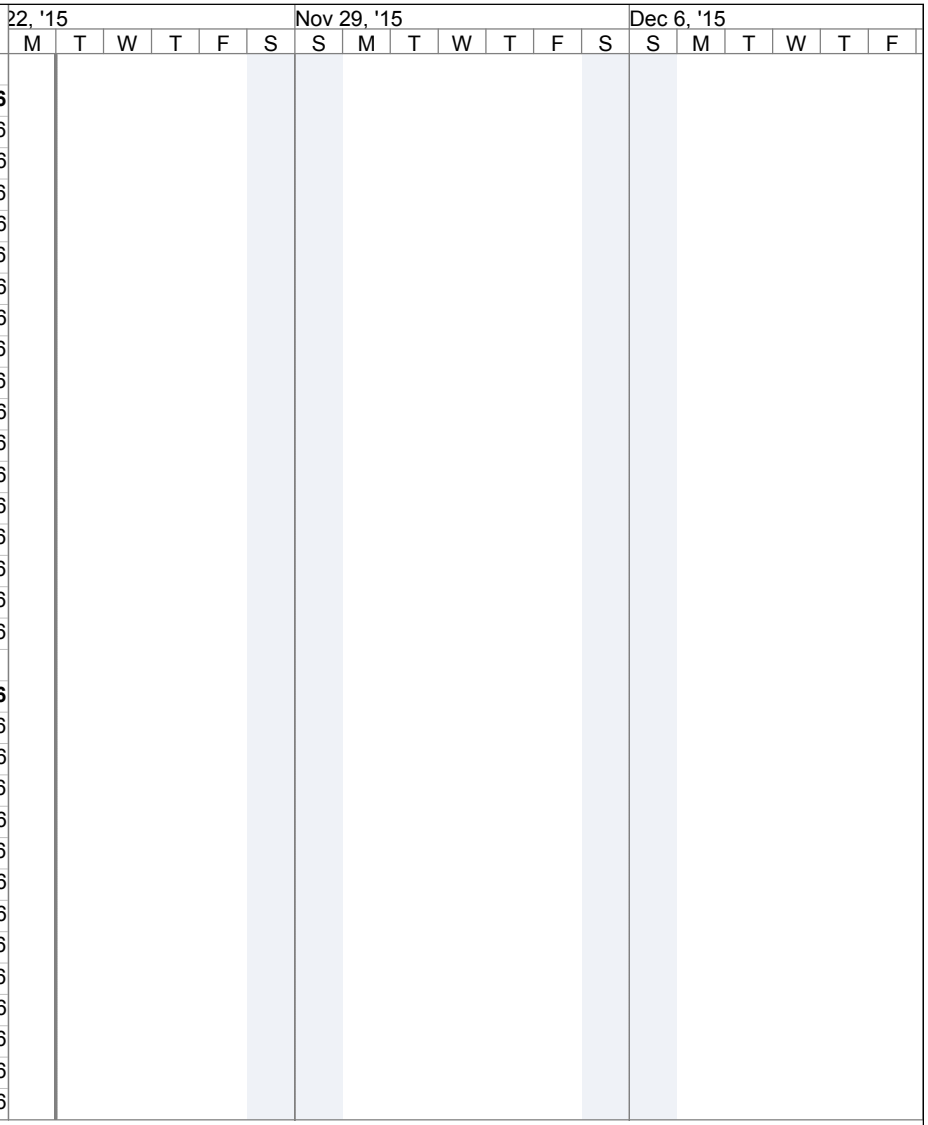

Project: MI MPE RI 11-19
Date: Tue 11/24/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

ID		Task Name	Duration	Start	Finish
273		Gypcrete	3 days	Thu 3/3/16	Mon 3/7/16
274		Gypcrete dry time	10 days	Tue 3/8/16	Mon 3/21/16
275		Electrical trim	5 days	Tue 3/1/16	Mon 3/7/16
276		Install cabinets	5 days	Tue 3/8/16	Mon 3/14/16
277					
278		**L4 Zone 2 (East side)**	**56 days**	**Mon 2/1/16**	**Mon 4/18/16**
279		Electrical RI	10 days	Mon 2/1/16	Fri 2/12/16
280		Low volt RI	4 days	Thu 2/11/16	Tue 2/16/16
281		Plumbing/Electrical/Lowvolt Inspectio	4 days	Wed 2/17/16	Mon 2/22/16
282		Framing inspection	1 day	Tue 2/23/16	Tue 2/23/16
283		Insulation	4 days	Wed 2/24/16	Mon 2/29/16
284		Insulation Inspection	1 day	Tue 3/1/16	Tue 3/1/16
285		Drywall Hang/Tape/Texture/PVA	15 days	Wed 3/2/16	Tue 3/22/16
286		Frame soffits	4 days	Wed 3/9/16	Mon 3/14/16
287		Vent soffits	4 days	Tue 3/15/16	Fri 3/18/16
288		Electrical at soffits	2 days	Mon 3/21/16	Tue 3/22/16
289		HVAC/ Electrical inspection at soffits	1 day	Wed 3/23/16	Wed 3/23/16
290		Hang and tape soffits	5 days	Thu 3/24/16	Wed 3/30/16
291		Paint	5 days	Thu 3/31/16	Wed 4/6/16
292		Gypcrete	3 days	Thu 3/31/16	Mon 4/4/16
293		Gypcrete dry time	10 days	Tue 4/5/16	Mon 4/18/16
294		Electrical trim	5 days	Tue 3/29/16	Mon 4/4/16
295		Install cabinets	5 days	Tue 4/5/16	Mon 4/11/16
296					
297		**L3 Zone 1 (West Side)**	**60 days**	**Mon 1/18/16**	**Fri 4/8/16**
298		Electrical RI	10 days	Mon 1/18/16	Fri 1/29/16
299		Low volt RI	4 days	Thu 1/28/16	Tue 2/2/16
300		Plumbing/Electrical/Lowvolt Inspectio	4 days	Wed 2/3/16	Mon 2/8/16
301		Framing inspection	1 day	Tue 2/9/16	Tue 2/9/16
302		Insulation	4 days	Wed 2/10/16	Mon 2/15/16
303		Insulation Inspection	1 day	Tue 2/16/16	Tue 2/16/16
304		Drywall Hang/Tape/Texture/PVA	15 days	Wed 2/17/16	Tue 3/8/16
305		Frame soffits	4 days	Wed 2/24/16	Mon 2/29/16
306		Vent soffits	4 days	Tue 3/1/16	Fri 3/4/16

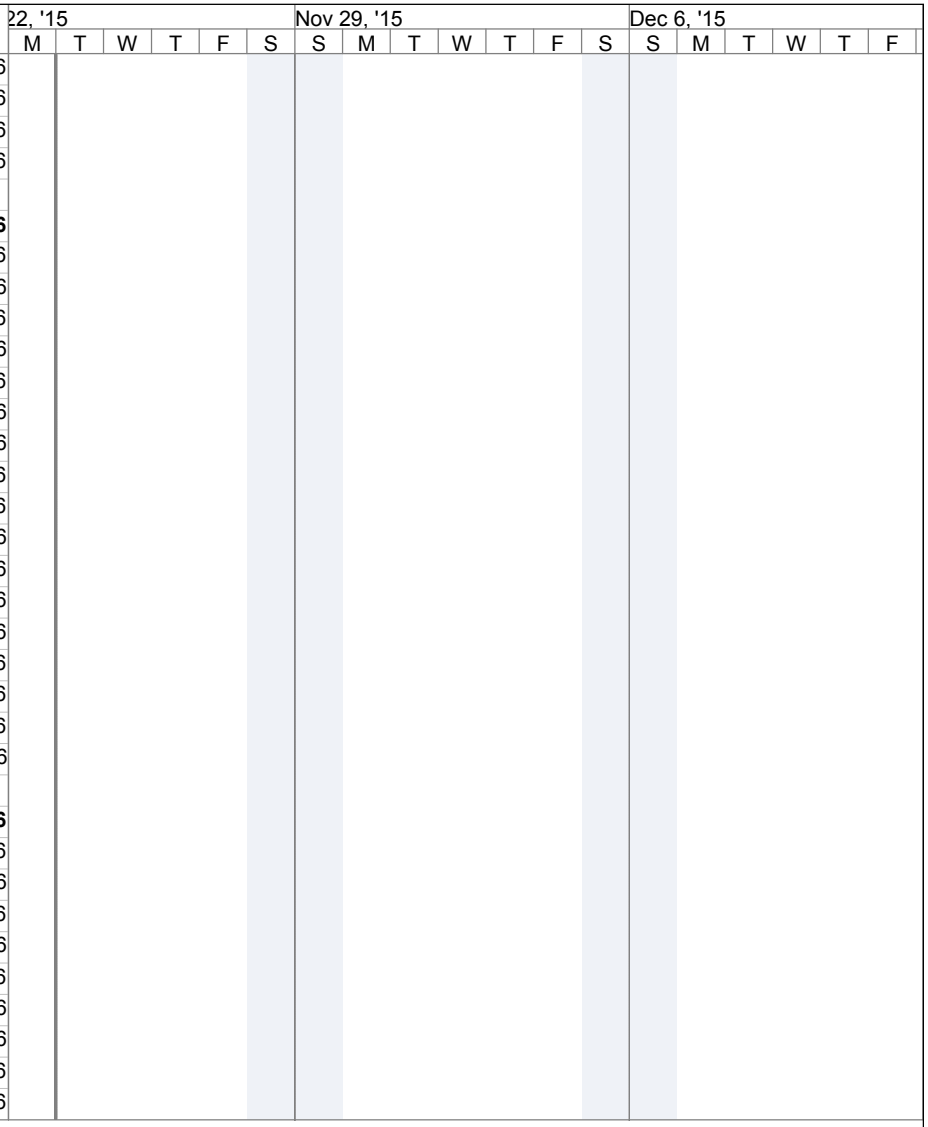

Project: MI MPE RI 11-19
Date: Tue 11/24/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

ID		Task Name	Duration	Start	Finish
307		Electrical at soffits	2 days	Mon 3/7/16	Tue 3/8/16
308		HVAC/ Electrical inspection at soffits	1 day	Wed 3/9/16	Wed 3/9/16
309		Hang and tape soffits	5 days	Thu 3/10/16	Wed 3/16/16
310		Paint	5 days	Thu 3/17/16	Wed 3/23/16
311		Electrical trim	5 days	Thu 3/24/16	Wed 3/30/16
312		Install flooring	7 days	Thu 3/24/16	Fri 4/1/16
313		Install cabinets	5 days	Mon 4/4/16	Fri 4/8/16
314					
315		**L3 Zone 2 (East Side)**	**60 days**	**Mon 2/15/16**	**Fri 5/6/16**
316		Electrical RI	10 days	Mon 2/15/16	Fri 2/26/16
317		Low volt RI	4 days	Thu 2/25/16	Tue 3/1/16
318		Plumbing/Electrical/Lowvolt Inspectio	4 days	Wed 3/2/16	Mon 3/7/16
319		Framing inspection	1 day	Tue 3/8/16	Tue 3/8/16
320		Insulation	4 days	Wed 3/9/16	Mon 3/14/16
321		Insulation Inspection	1 day	Tue 3/15/16	Tue 3/15/16
322		Drywall Hang/Tape/Texture/PVA	15 days	Wed 3/16/16	Tue 4/5/16
323		Frame soffits	4 days	Wed 3/23/16	Mon 3/28/16
324		Vent soffits	4 days	Tue 3/29/16	Fri 4/1/16
325		Electrical at soffits	2 days	Mon 4/4/16	Tue 4/5/16
326		HVAC/ Electrical inspection at soffits	1 day	Wed 4/6/16	Wed 4/6/16
327		Hang and tape soffits	5 days	Thu 4/7/16	Wed 4/13/16
328		Paint	5 days	Thu 4/14/16	Wed 4/20/16
329		Electrical trim	5 days	Thu 4/21/16	Wed 4/27/16
330		Install flooring	7 days	Thu 4/21/16	Fri 4/29/16
331		Install cabinets	5 days	Mon 5/2/16	Fri 5/6/16

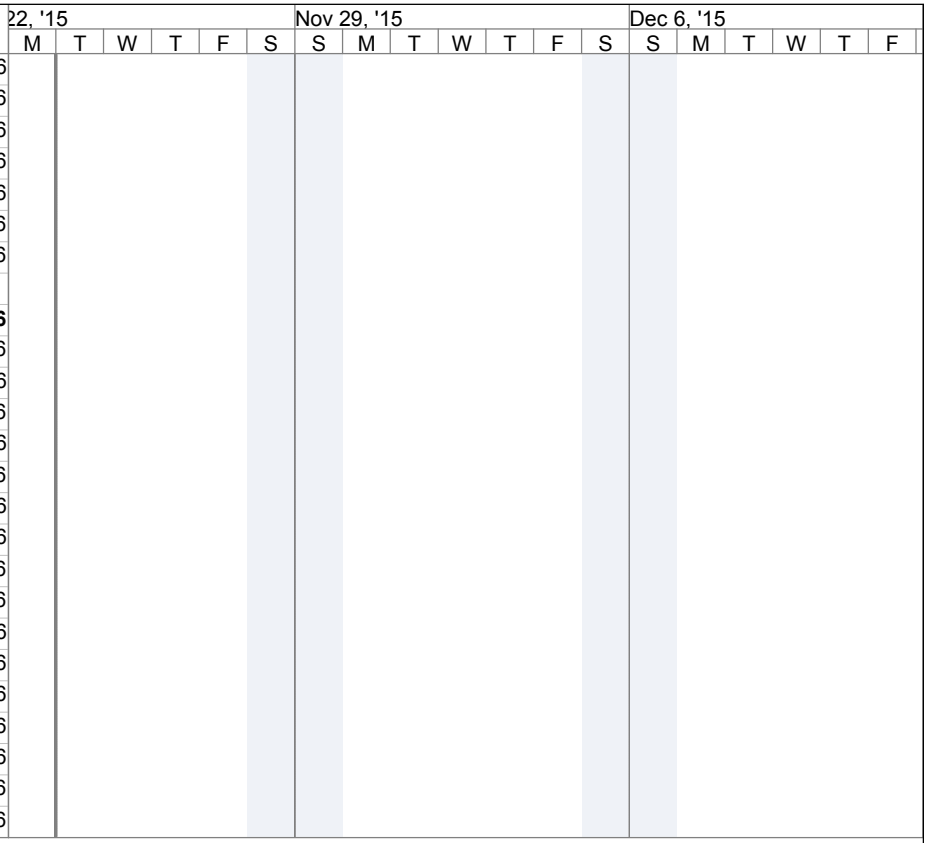

Project: MI MPE RI 11-19
Date: Tue 11/24/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	
