CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **41**

MEETING DATE: **12/08/15**

ATTENDEES:

Mike Kalvelage – CHINN-
Mark Pesanti – CHINN
Charlie Poggemann – CHINN
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
~~Eric Bull – CHINN~~
~~Jesse Earle – Froula~~
Jason – CFM
Joe Barnhart - OWP
~~George Faler - CHINN~~
Casey Hutchison - SS
Chad Likkel - Axiom
Jose Mendina – Advanced
~~Gary – Prec. Wall~~
Ross Porterfield – IEC
Roger Rueda – WCP

SAFETY: All trades that are using the scaffold must sign off on the inspection tag daily. All crews must have task lighting. LNI does not consider head lamps task lighting.

41.01 Housekeeping

- **CRANE DISMANTLE is scheduled for 1/9/16.**
- **Stocking and Unloading stacks are x07 and x60**
- No smoking onsite
- Sweep and clean up for the next trade in work areas
  - All subs need to clean up all areas everyday
- There is no food allowed above Level 2
- Use the delivery board – check crane box if you need crane
- Do not remove temporary screens in the deck drains
- Do not plug cords into the string lights, Do not flip spider boxes on their sides
- Windows are being stocked in the units. Do not lean material against them and do not open them if they are tacked up in the units.

SCHEDULE:

41.02 Reviewed **SITE** 3 wk look ahead schedule beginning 12/07/15

- Site Grading/Utilities – North – Backfill NW, Backfill NE retaining wall 12/7-12/21, Excavate stair footings 12/9, Grade/Excavate Transformer Vault 12/18-12/21
- PSE Gas – Temp Service South 12/22, Permanent service North 1/8-1/11
- Site Structure – North Retaining Stair Footings and Walls 12/7-12/10, F&P Transformer footings/SOG 12/22-12/28, F&P Transformer Walls 12/29-1/7
- Wood Framing Roof North Southwest – Roof 12/7-12/18
- Wood framing Roof Southeast – Frame Trellis Walls 12/7-12/9, set walkway stanchions 12/16-12/22, Cricket 12/23-12/31, Roofing 1/1-1/12
- Penthouse/Mezzanine – Frame, Joist/Sheath 12/7-`12/15
- Exterior – Bonnet Scaffold 12/7-12/9, wrap/set door pans and windows west 12/7-12/10, Tyvek West 12/11-12/14, Siding/Flashing mock up west 12/15-12/21, North Set scaffold

12/11-12/14, prep densglass/Trim Openings 12/17, wrap openings, set windows 12/18-12/31, Courtyard West prep densglass, wrap openings, set windows 12/8-1/8.

- Metal Stud Framing – Rock storefronts, rock ext level 1-2 south 12/7-12/18
- Temp Heat – Temp Gas Meter, Deliver/Set Equipment, Heat West 12/23-12/30

41.03 Reviewed **INTERIOR** 3wk look ahead schedule beginning 12/07/15

- 12/07/15: Zone 3 plumbing inspection is scheduled for 12/09/15, shooting for next inspection in Zone 1 around 12/14/15.

OLD BUSINESS:

38.09 Advanced and IEC to coordinate lights and sprinklers at storefront alcoves

39.04 CHINN to review scupper size.

- 12/08/15 – Detail 17/A0905 shows 8" wide by 6" tall

39.08 OWP would like to run the gas line and penetrate the North elevation wall as opposed to the east.

- 12/08/15: Ownership would like to see a drawing.

40.04 Does WCP will need to install construction trash chute before crane dismantle?

40.05 General SF to asbuilt framing at the Level 1 storefront after RCP Entry and alcove framing are addressed

- 12/08/15: WCP storefronts will be ready for asbuilt on 12/14. CHINN to schedule General Storefronts.

PERMIT STATUS: **HVAC** – Jason (CFM) Corrections were submitted 10/09 or 10/12, Met with Architect on 11/16 to discuss Louvers at the storefront, 12/08 – revisions have been submitted for review with COMI.

RFIs: 41.09 Flashing RFI's have been submitted. Axiom to bring sample flashings to the site to review the inside corner interfaces.

SUBMITTALS:

NEW BUSINESS:

41.04 MP asked framing subcontractors were removing scaffolding tiebacks from wall? CH replied no.

41.05 CHINN to layout roof walkway stanchions.

41.06 IEC to install any lighting roughin at the north wall

41.07 CHINN to discuss lighting in the SW stair at the next OAC meeting.

41.08 LB to get dimensions for louver above loading dock.

41.10 Interiors to start focusing on shafts

41.11 Gypcrete is scheduled for 12/14. SS to complete second sided shear walls.

41.12 CHINN to schedule a handrail mock up. WCP, SS, and CHINN to attend for backing purposes.

41.13 IEC needs smart panels installed to locate their outlet.

41.14 LB to send SS Box walk notes for furring walls.

41.15 OWP needs centerline of sink at Sky lounge

41.16 OWP has vent pipe that must exhaust 10' from the walkway. Is it acceptable for OWP to drill a 4" hole through beam or is a soffit acceptable?

NEXT MEETING: 12/15/15, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
12-7-2015

ID		Task Name	Duration	Start	Finish
1		**Site Grading/Utilities**	**24 days**	**Mon 12/7/15**	**Mon 1/11/16**
2		**North**	**11 days**	**Mon 12/7/15**	**Mon 12/21/15**
3		Backfill NE Ret wall	2 days	Mon 12/7/15	Tue 12/8/15
4		Exc. Stair Wall Ftgs	1 day	Wed 12/9/15	Wed 12/9/15
5		Grade/Excavate Transformer Vault	2 days	Fri 12/18/15	Mon 12/21/15
6					
7		**PSE/Gas**	**13 days**	**Tue 12/22/15**	**Mon 1/11/16**
8		Temp Service South	1 day	Tue 12/22/15	Tue 12/22/15
9		Permanent Service North	2 days	Fri 1/8/16	Mon 1/11/16
10					
11		**Site/Structure**	**22 days**	**Mon 12/7/15**	**Thu 1/7/16**
12		**North**	**22 days**	**Mon 12/7/15**	**Thu 1/7/16**
13		Stair Ftgs/Walls	4 days	Mon 12/7/15	Thu 12/10/15
14		F&P Transformer Rm Ftgs/SOG	3 days	Tue 12/22/15	Mon 12/28/15
15		F&P Transformer Walls	8 days	Tue 12/29/15	Thu 1/7/16
16					
17		**South**	**3 days**	**Mon 12/7/15**	**Wed 12/9/15**
18		F&P Planters	3 days	Mon 12/7/15	Wed 12/9/15
19					
20		**Wood Framing/Roofing**	**29 days**	**Mon 12/7/15**	**Mon 1/18/16**
21		**North/Southwest**	**10 days**	**Mon 12/7/15**	**Fri 12/18/15**
22		Roof	10 days	Mon 12/7/15	Fri 12/18/15
23		**Penthouse SE**	**7 days**	**Mon 12/7/15**	**Tue 12/15/15**
24		Frame	7 days	Mon 12/7/15	Tue 12/15/15
25		Joist/Sheath	3 days	Fri 12/11/15	Tue 12/15/15
26		**Southeast**	**22 days**	**Wed 12/16/15**	**Mon 1/18/16**
27		Frame Trellis Walls	5 days	Tue 1/12/16	Mon 1/18/16
28		Walkway Stanchions	5 days	Wed 12/16/15	Tue 12/22/15
29		Crickets	5 days	Wed 12/23/15	Thu 12/31/15
30		Roofing	8 days	Fri 1/1/16	Tue 1/12/16
31					
32		**Exterior**	**17 days**	**Mon 12/7/15**	**Thu 12/31/15**
33		**West**	**11 days**	**Mon 12/7/15**	**Mon 12/21/15**
34		Bonnet Scaffold West wing	3 days	Mon 12/7/15	Wed 12/9/15

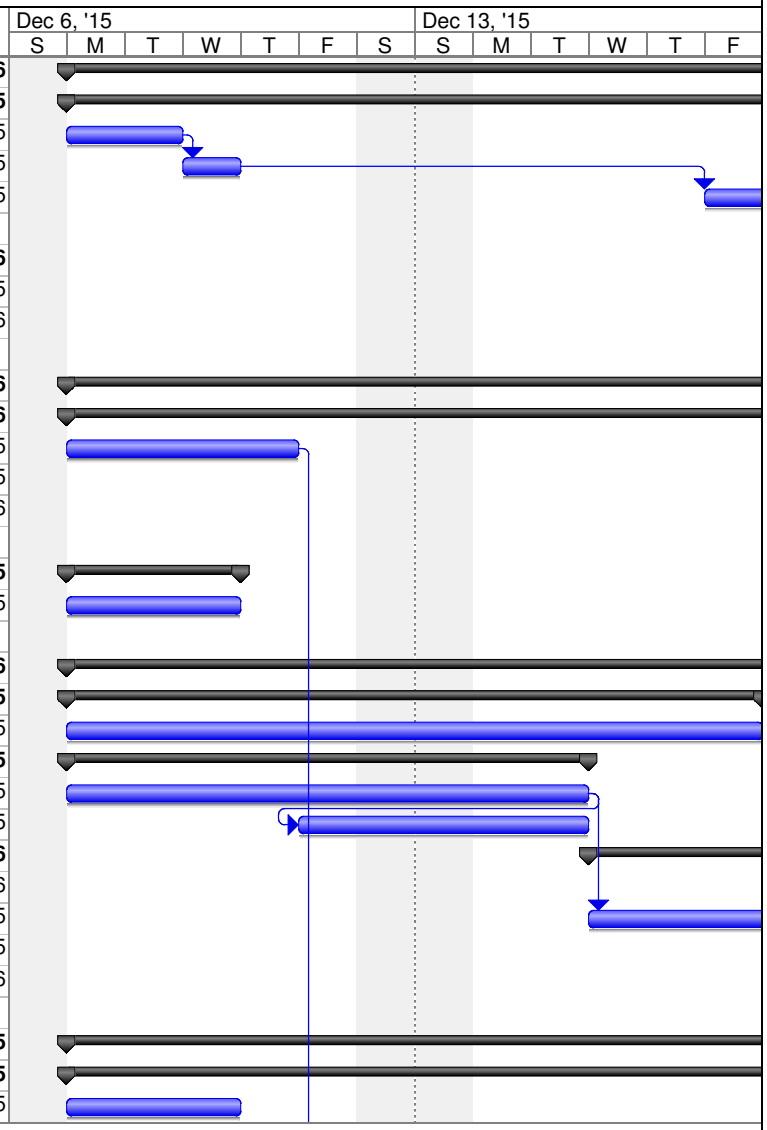

Project: 3wk 12-7-2015
Date: Fri 12/4/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
12-7-2015

ID		Task Name	Duration	Start	Finish
35		Wrap/Set Door Pans/ Windows West	4 days	Mon 12/7/15	Thu 12/10/15
36		Tyvek West	2 days	Fri 12/11/15	Mon 12/14/15
37		Siding/Flashing Mock-up West	5 days	Tue 12/15/15	Mon 12/21/15
38					
39		**North**	**13 days**	**Fri 12/11/15**	**Thu 12/31/15**
40		Set Rem Scaffold	2 days	Fri 12/11/15	Mon 12/14/15
41		Prep Densglass/Trim Openings	3 days	Tue 12/15/15	Thu 12/17/15
42		Wrap Openings/Set Windows	8 days	Fri 12/18/15	Thu 12/31/15
43					
44		**Courtyard**	**10 days**	**Mon 12/7/15**	**Fri 12/18/15**
45		**West**	**10 days**	**Mon 12/7/15**	**Fri 12/18/15**
46		Prep D-Glass/Openings	2 days	Mon 12/7/15	Tue 12/8/15
47		Wrap/Set Windows	6 days	Fri 12/11/15	Fri 12/18/15
48					
49		**Mtl Stud Framing**	**6 days**	**Mon 12/7/15**	**Mon 12/14/15**
50		Frame/Rock Storefronts	6 days	Mon 12/7/15	Mon 12/14/15
51					
52		**Temp Heat**	**4 days**	**Wed 12/23/15**	**Wed 12/30/15**
53		Deliver/Set Equipment	3 days	Wed 12/23/15	Tue 12/29/15
54		Temp Heat West	1 day	Wed 12/30/15	Wed 12/30/15

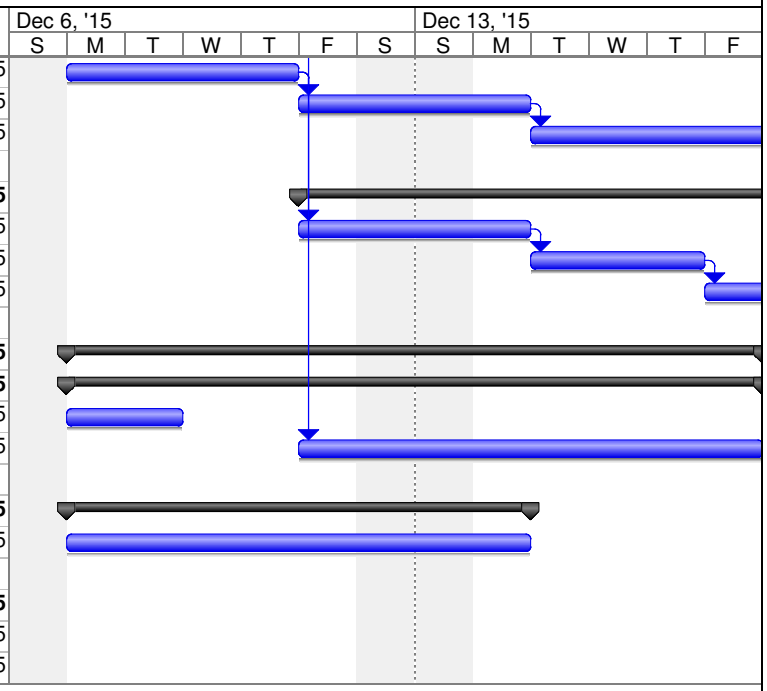

Project: 3wk 12-7-2015
Date: Fri 12/4/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
12-7-2015

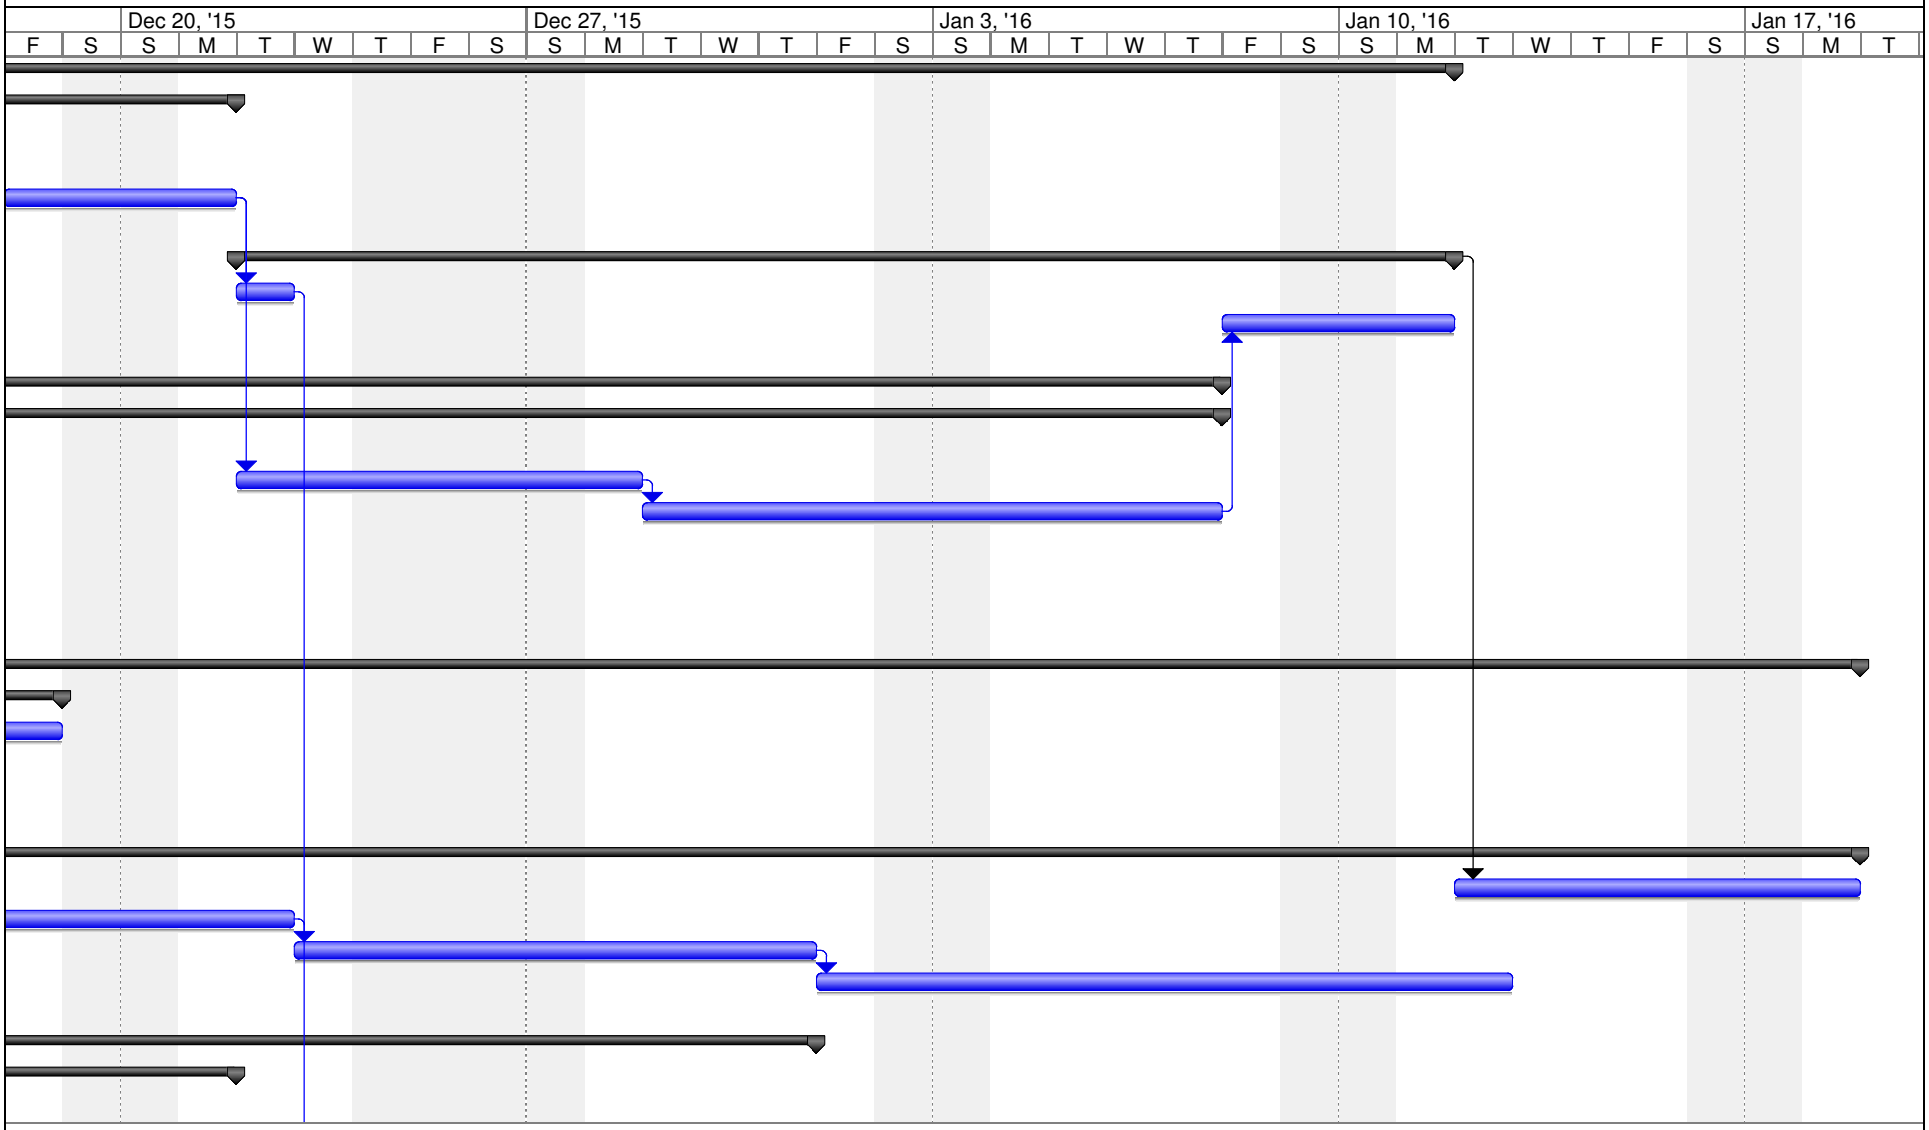

Project: 3wk 12-7-2015
Date: Fri 12/4/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
12-7-2015

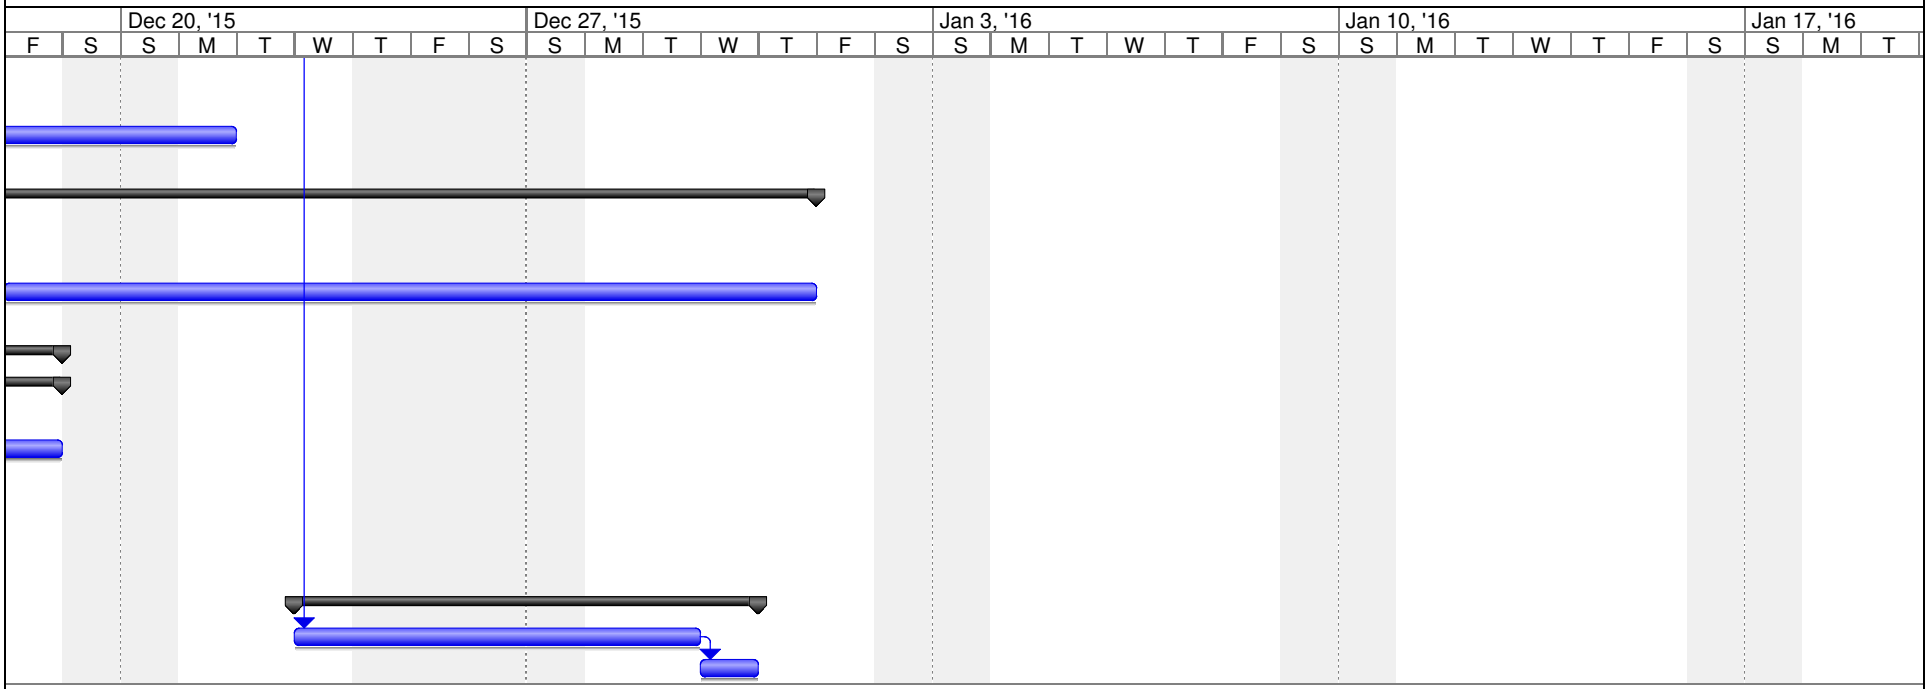

Project: 3wk 12-7-2015
Date: Fri 12/4/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish
77	HVAC Exhaust/AC Port Drill	2 days	Fri 11/13/15	Mon 11/16/15
78				
79	**L6 Zone 3**	**13 days**	**Mon 11/9/15**	**Wed 11/25/15**
80	Framing Pick Up	4 days	Mon 11/9/15	Thu 11/12/15
81	Plumbing RI Drain Waste and Vent	6 days	Fri 11/13/15	Fri 11/20/15
82	Plumbing RI Water Supply	2 days	Mon 11/23/15	Tue 11/24/15
83	Fire Sprinkler Rough In	3 days	Fri 11/13/15	Tue 11/17/15
84	Electrical Box And Drill	3 days	Mon 11/23/15	Wed 11/25/15
85	Low Volt Box and Drill	1 day	Wed 11/25/15	Wed 11/25/15
86	HVAC Exhaust/AC Port Drill	2 days	Mon 11/23/15	Tue 11/24/15
87				
88	**L5 Zone 1**	**13 days**	**Thu 11/12/15**	**Mon 11/30/15**
89	Framing Pick Up	4 days	Thu 11/12/15	Tue 11/17/15
90	Plumbing RI Drain Waste and Vent	6 days	Wed 11/18/15	Wed 11/25/15
91	Plumbing RI Water Supply	2 days	Thu 11/26/15	Fri 11/27/15
92	Fire Sprinkler Rough In	3 days	Wed 11/18/15	Fri 11/20/15
93	Electrical Box And Drill	3 days	Thu 11/26/15	Mon 11/30/15
94	Low Volt Box and Drill	1 day	Mon 11/30/15	Mon 11/30/15
95	HVAC Exhaust/AC Port Drill	2 days	Thu 11/26/15	Fri 11/27/15
96				
97	**L6 Zone 1**	**15 days**	**Tue 11/17/15**	**Mon 12/7/15**
98	Framing Pick Up	4 days	Tue 11/17/15	Fri 11/20/15
99	Plumbing RI Drain Waste and Vent	6 days	Mon 11/23/15	Mon 11/30/15
100	Plumbing RI Water Supply	4 days	Tue 12/1/15	Fri 12/4/15
101	Fire Sprinkler Rough In	3 days	Mon 11/23/15	Wed 11/25/15
102	Electrical Box And Drill	3 days	Thu 12/3/15	Mon 12/7/15
103	Low Volt Box and Drill	1 day	Mon 12/7/15	Mon 12/7/15
104	HVAC Exhaust/AC Port Drill	2 days	Thu 12/3/15	Fri 12/4/15
105				
106	**L3-L6 Zones 1 and 3**	**17 days**	**Thu 11/26/15**	**Fri 12/18/15**
107	Fire Sprinkler Test	3 days	Thu 11/26/15	Mon 11/30/15
108	Fire Sprinkler Inspection	2 days	Tue 12/1/15	Wed 12/2/15
109	Plumbing RI Levels L3-L6 Test Z1	3 days	Mon 12/7/15	Wed 12/9/15
110	Plumbing RI Levels L3-L6 Inspect	2 days	Thu 12/10/15	Fri 12/11/15
111	Plumbing RI Levels P-L3 Test Z3	3 days	Mon 12/14/15	Wed 12/16/15
112	Plumbing RI Levels P-L3 Inspect	2 days	Thu 12/17/15	Fri 12/18/15
113				
114	**L5 Zone 2**	**15 days**	**Fri 11/20/15**	**Thu 12/10/15**

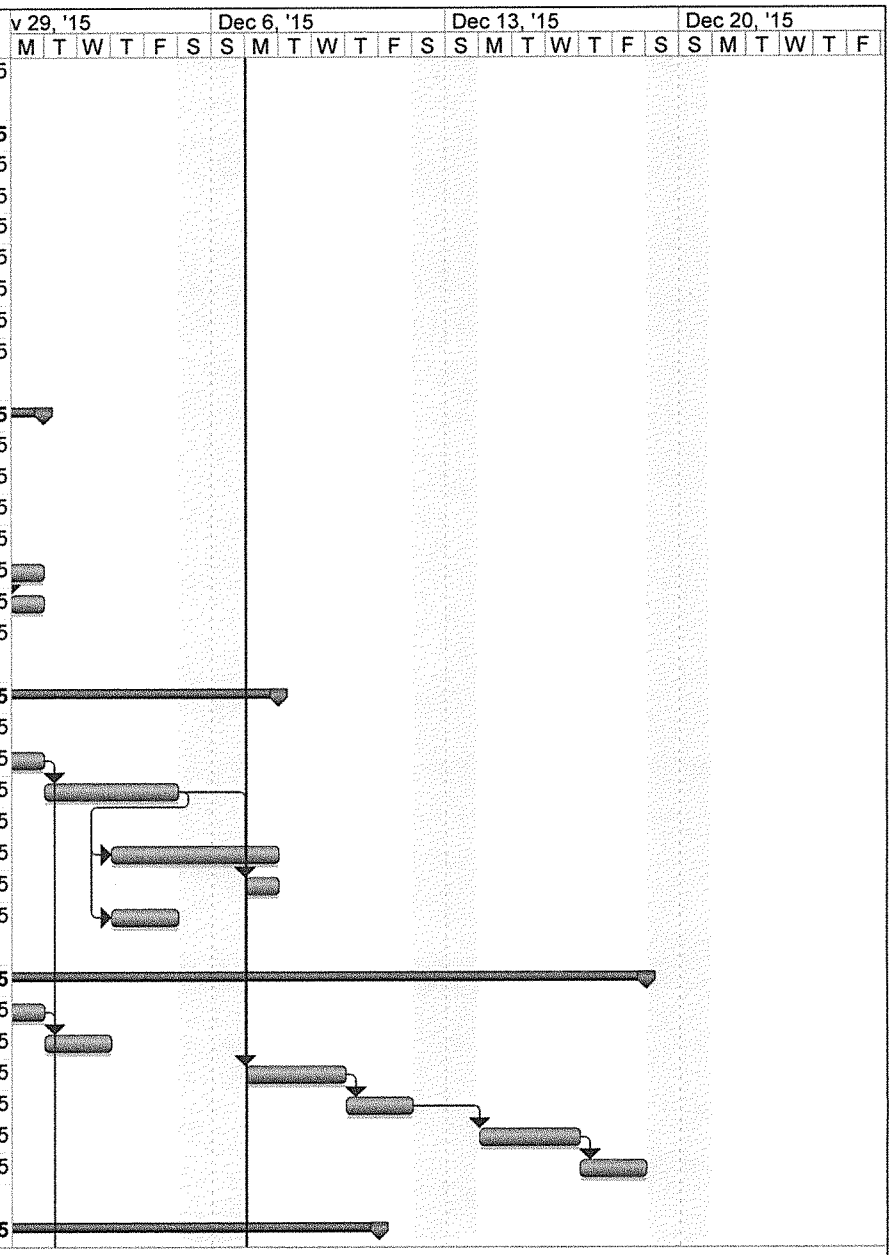

Project: MI MPE RI 12-7
Date: Mon 12/7/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish
115	Framing Pick Up	4 days	Fri 11/20/15	Wed 11/25/15
116	Plumbing RI Drain Waste and Vent	5 days	Tue 12/1/15	Mon 12/7/15
117	Plumbing RI Water Supply	2 days	Tue 12/8/15	Wed 12/9/15
118	Fire Sprinkler Rough In	3 days	Thu 11/26/15	Mon 11/30/15
119	Electrical Box And Drill	3 days	Tue 12/8/15	Thu 12/10/15
120	Low Volt Box and Drill	1 day	Thu 12/10/15	Thu 12/10/15
121	HVAC Exhaust/AC Port Drill	2 days	Tue 12/8/15	Wed 12/9/15
122				
123	**L6 Zone 2**	**17 days**	**Wed 11/25/15**	**Thu 12/17/15**
124	Framing Pick Up	4 days	Wed 11/25/15	Mon 11/30/15
125	Plumbing RI Drain Waste and Vent	5 days	Tue 12/8/15	Mon 12/14/15
126	Plumbing RI Water Supply	2 days	Tue 12/15/15	Wed 12/16/15
127	Fire Sprinkler Rough In	3 days	Tue 12/1/15	Thu 12/3/15
128	Electrical Box And Drill	3 days	Tue 12/15/15	Thu 12/17/15
129	Low Volt Box and Drill	1 day	Thu 12/17/15	Thu 12/17/15
130	HVAC Exhaust/AC Port Drill	2 days	Tue 12/15/15	Wed 12/16/15
131				
132	**L4 Zone 4**	**14 days**	**Mon 11/30/15**	**Thu 12/17/15**
133	Framing Pick Up	4 days	Mon 11/30/15	Thu 12/3/15
134	Plumbing RI Drain Waste and Vent	5 days	Tue 12/8/15	Mon 12/14/15
135	Plumbing RI Water Supply	2 days	Tue 12/15/15	Wed 12/16/15
136	Fire Sprinkler Rough In	3 days	Fri 12/4/15	Tue 12/8/15
137	Electrical Box And Drill	3 days	Tue 12/15/15	Thu 12/17/15
138	Low Volt Box and Drill	1 day	Thu 12/17/15	Thu 12/17/15
139	HVAC Exhaust/AC Port Drill	2 days	Tue 12/15/15	Wed 12/16/15
140				
141	**L5 Zone 4**	**16 days**	**Thu 12/3/15**	**Thu 12/24/15**
142	Framing Pick Up	4 days	Thu 12/3/15	Tue 12/8/15
143	Plumbing RI Drain Waste and Vent	5 days	Tue 12/15/15	Mon 12/21/15
144	Plumbing RI Water Supply	2 days	Tue 12/22/15	Wed 12/23/15
145	Fire Sprinkler Rough In	3 days	Wed 12/9/15	Fri 12/11/15
146	Electrical Box And Drill	3 days	Tue 12/22/15	Thu 12/24/15
147	Low Volt Box and Drill	1 day	Thu 12/24/15	Thu 12/24/15
148	HVAC Exhaust/AC Port Drill	2 days	Tue 12/22/15	Wed 12/23/15
149				
150	**L6 Zone 4**	**18 days**	**Tue 12/8/15**	**Thu 12/31/15**
151	Framing Pick Up	4 days	Tue 12/8/15	Fri 12/11/15
152	Plumbing RI Drain Waste and Vent	5 days	Tue 12/22/15	Mon 12/28/15

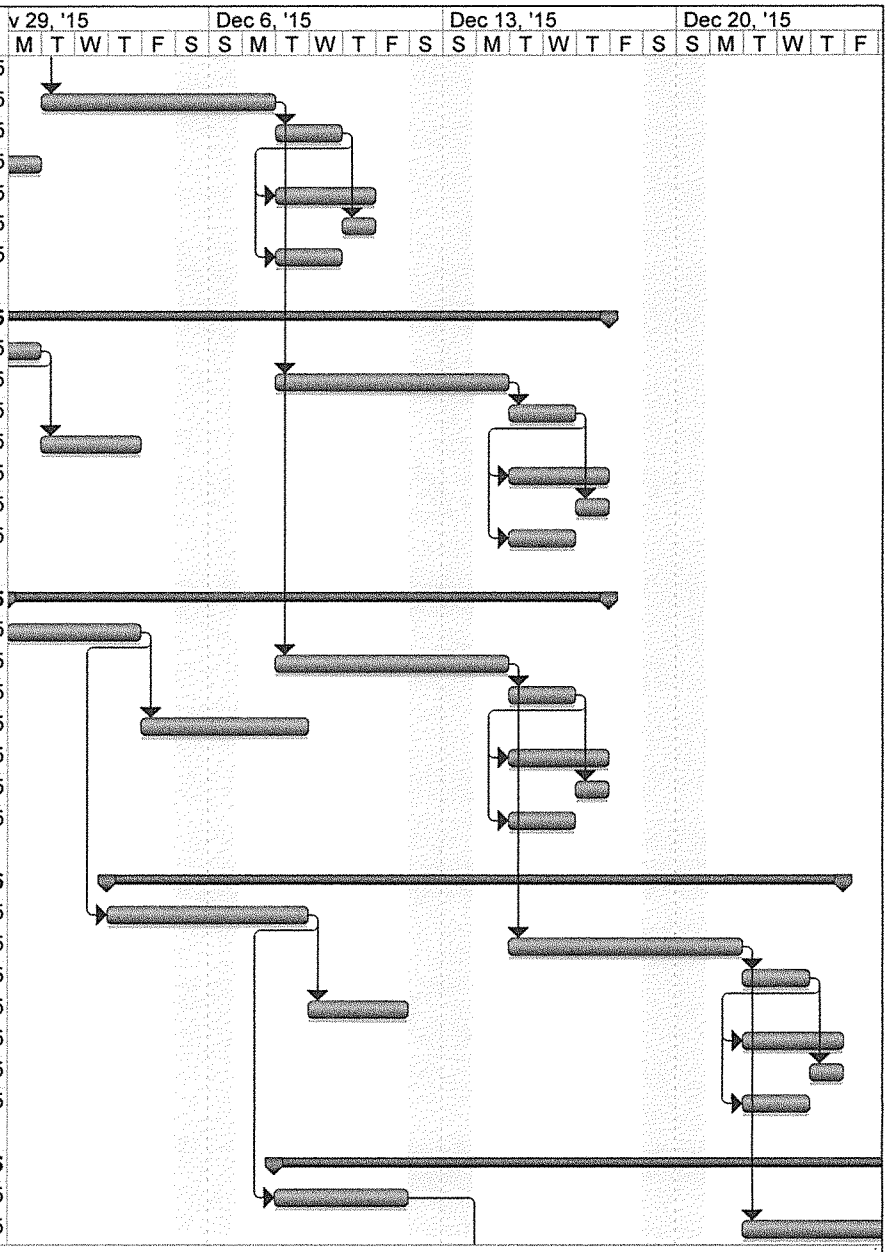

Project: MI MPE RI 12-7
Date: Mon 12/7/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish
153	Plumbing RI Water Supply	2 days	Tue 12/29/15	Wed 12/30/15
154	Fire Sprinkler Rough In	3 days	Mon 12/14/15	Wed 12/16/15
155	Electrical Box And Drill	3 days	Tue 12/29/15	Thu 12/31/15
156	Low Volt Box and Drill	1 day	Thu 12/31/15	Thu 12/31/15
157	HVAC Exhaust/AC Port Drill	2 days	Tue 12/29/15	Wed 12/30/15
158				
159	**L3-L6 Zones 2 and 4**	**20 days**	**Thu 12/17/15**	**Wed 1/13/16**
160	Fire Sprinkler Test	3 days	Thu 12/17/15	Mon 12/21/15
161	Fire Sprinkler Inspection	2 days	Tue 12/22/15	Wed 12/23/15
162	Plumbing RI Levels P-L3 Test	3 days	Thu 12/31/15	Mon 1/4/16
163	Plumbing RI Levels P-L3 Inspect Z2	2 days	Tue 1/5/16	Wed 1/6/16
164	Plumbing RI Levels P-L3 Test	3 days	Thu 1/7/16	Mon 1/11/16
165	Plumbing RI Levels P-L3 Inspect Z4	2 days	Tue 1/12/16	Wed 1/13/16
166				
167	**MEP Roof Down**	**161 days**	**Fri 10/2/15**	**Fri 5/13/16**
168	**L6 Zone 1 (West Side)**	**71 days**	**Mon 11/23/15**	**Mon 2/29/16**
169	Roofing Installed	15 days	Mon 11/23/15	Fri 12/11/15
170	Electrical RI	10 days	Mon 12/14/15	Fri 12/25/15
171	Low volt RI	4 days	Thu 12/24/15	Tue 12/29/15
172	Plumbing/Electrical/Lowvolt Inspectior	4 days	Wed 12/30/15	Mon 1/4/16
173	Framing inspection	1 day	Tue 1/5/16	Tue 1/5/16
174	Insulation	4 days	Wed 1/6/16	Mon 1/11/16
175	Insulation Inspection	1 day	Tue 1/12/16	Tue 1/12/16
176	Drywall Hang/Tape/Texture/PVA	15 days	Wed 1/13/16	Tue 2/2/16
177	Frame soffits	4 days	Wed 1/20/16	Mon 1/25/16
178	Vent soffits	4 days	Tue 1/26/16	Fri 1/29/16
179	Electrical at soffits	2 days	Mon 2/1/16	Tue 2/2/16
180	HVAC/ Electrical inspection at soffits	1 day	Wed 2/3/16	Wed 2/3/16
181	Hang and tape soffits	5 days	Thu 2/4/16	Wed 2/10/16
182	Paint	5 days	Thu 2/11/16	Wed 2/17/16
183	Gypcrete	3 days	Thu 2/11/16	Mon 2/15/16
184	Gypcrete dry time	10 days	Tue 2/16/16	Mon 2/29/16
185	Electrical trim	5 days	Tue 2/9/16	Mon 2/15/16
186	Install cabinets	5 days	Tue 2/16/16	Mon 2/22/16
187				
188	Zone 1 Electrical Unit Feeders, L 3-6	10 days	Mon 12/14/15	Fri 12/25/15
189				
190	**L6-3 Zone 1 Tubs**	**11 days**	**Mon 12/7/15**	**Mon 12/21/15**

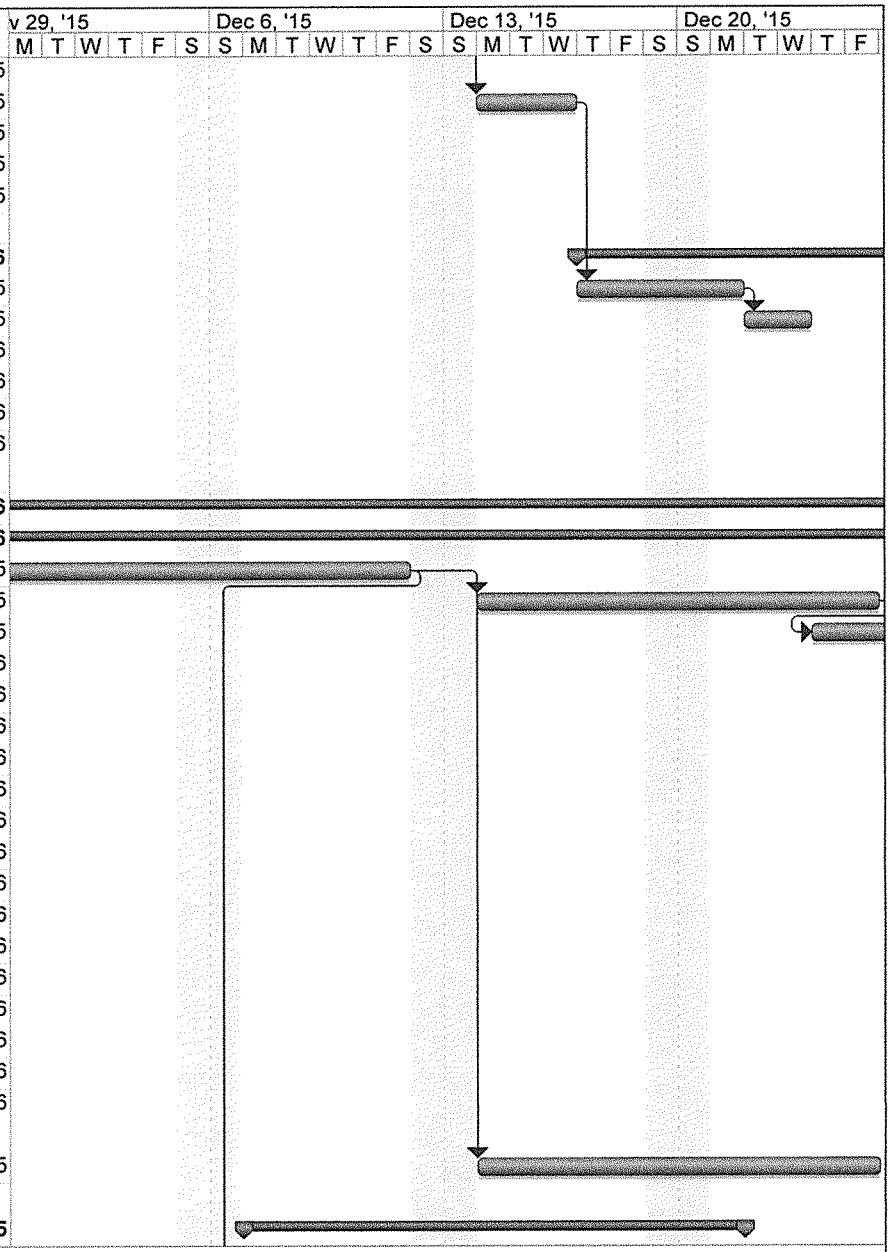

Project: MI MPE RI 12-7
Date: Mon 12/7/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish
191	Insulate at Tubs	2 days	Mon 12/7/15	Tue 12/8/15
192	Pre Rock at Tubs	2 days	Wed 12/9/15	Thu 12/10/15
193	Gypcrete at Tubs	3 days	Fri 12/11/15	Tue 12/15/15
194	Install Tubs	4 days	Wed 12/16/15	Mon 12/21/15
195				
196	**L6 Zone 2 (East Side)**	**132 days**	**Fri 10/2/15**	**Mon 4/4/16**
197	Roof framing complete	25 days	Mon 11/23/15	Fri 12/25/15
198	Roofing installed	10 days	Mon 12/28/15	Fri 1/8/16
199	Electrical RI	10 days	Mon 1/11/16	Fri 1/22/16
200	Low volt RI	4 days	Thu 1/21/16	Tue 1/26/16
201	Plumbing/Electrical/Lowvolt Inspectior	4 days	Wed 1/27/16	Mon 2/1/16
202	Framing inspection	1 day	Tue 2/2/16	Tue 2/2/16
203	Insulation	4 days	Wed 2/3/16	Mon 2/8/16
204	Insulation Inspection	1 day	Tue 2/9/16	Tue 2/9/16
205	Drywall Hang/Tape/Texture/PVA	15 days	Wed 2/10/16	Tue 3/1/16
206	Frame soffits	4 days	Wed 2/17/16	Mon 2/22/16
207	Vent soffits	4 days	Tue 2/23/16	Fri 2/26/16
208	Electrical at soffits	2 days	Mon 2/29/16	Tue 3/1/16
209	HVAC/ Electrical inspection at soffits	1 day	Wed 3/2/16	Wed 3/2/16
210	Hang and tape soffits	5 days	Thu 3/3/16	Wed 3/9/16
211	Paint	5 days	Thu 3/10/16	Wed 3/16/16
212	Gypcrete	3 days	Thu 3/17/16	Mon 3/21/16
213	Gypcrete dry time	10 days	Tue 3/22/16	Mon 4/4/16
214	Electrical trim	5 days	Tue 3/15/16	Mon 3/21/16
215	Install cabinets	5 days	Tue 3/22/16	Mon 3/28/16
216				
217				
218	Electrical Unit Feeders Zone 2, L 3-6	8 days	Mon 1/11/16	Wed 1/20/16
219				
220	**L6-3 Zone 2 Tubs**	**8 days**	**Fri 10/2/15**	**Tue 10/13/15**
221	Insulate at Tubs	2 days	Fri 10/2/15	Mon 10/5/15
222	Pre Rock at Tubs	2 days	Tue 10/6/15	Wed 10/7/15
223	Install Tubs	4 days	Thu 10/8/15	Tue 10/13/15
224				
225	**L5 Zone 1 (West Side)**	**56 days**	**Mon 12/28/15**	**Mon 3/14/16**
226	Electrical RI	10 days	Mon 12/28/15	Fri 1/8/16
227	Low volt RI	4 days	Thu 1/7/16	Tue 1/12/16
228	Plumbing/Electrical/Lowvolt Inspectior	4 days	Wed 1/13/16	Mon 1/18/16

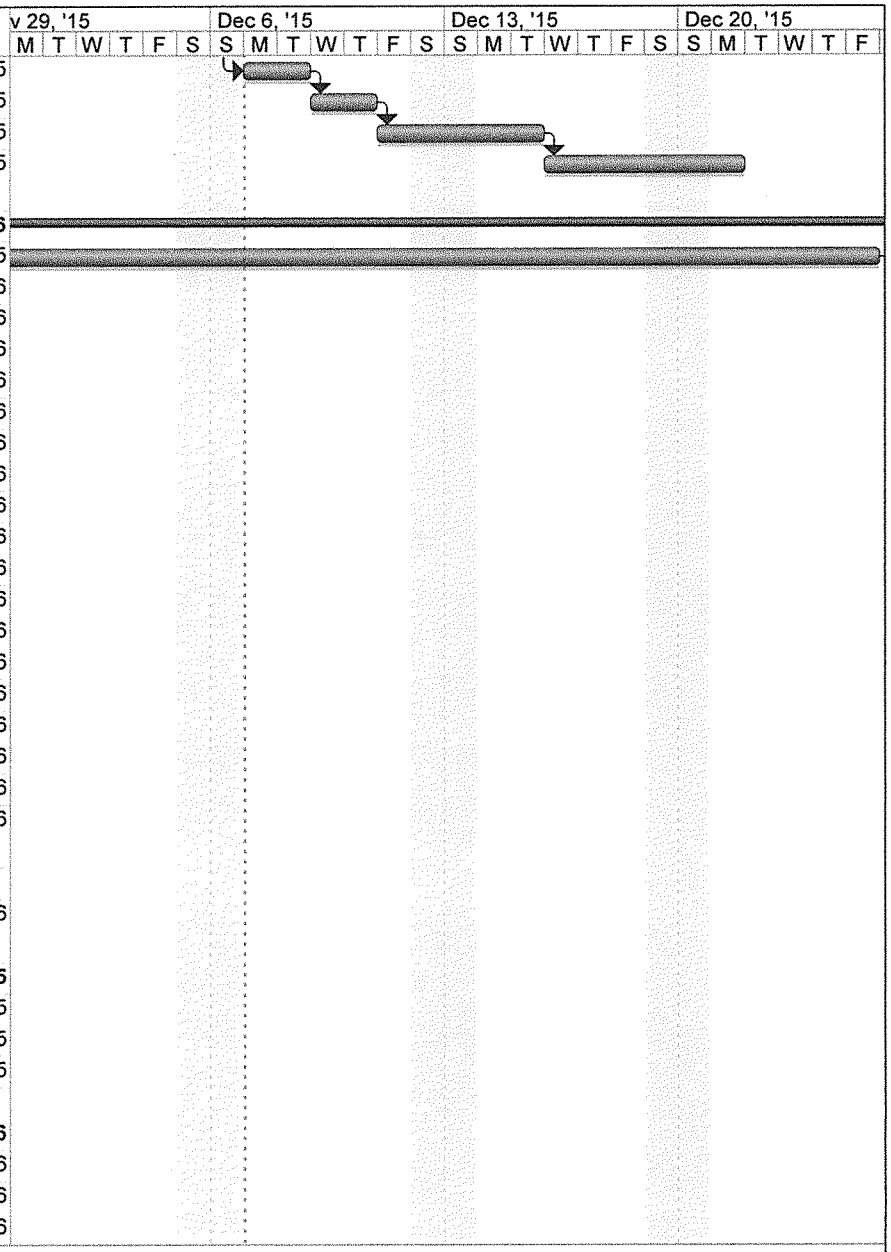

Project: MI MPE RI 12-7
Date: Mon 12/7/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
