CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **46**

MEETING DATE: **01/12/16**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
Charlie Poggemann – CHINN
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
Eric Bull – CHINN
Kyle – Froula
~~Jason – CFM~~
Richard Donelson - OWP
~~George Faler - CHINN~~
Casey Hutchison - SS
Kenny - Axiom
Jose Mendina – Advanced
Gary – Prec. Wall
Ross Porterfield – IEC
John Perillo – WCP

SAFETY: Temp heating has been turned on at the 5th and 6th floors. Only authorized personnel are to turn off/on temp heating.

46.01 Housekeeping

- **CRANE DISMANTLE 02/13/16**
- No smoking onsite
- Roof needs tobe cleaned of screws, nails, Plmbg fittings, and all construction debris
- There is no food allowed above Level 2
- Use the delivery board – check crane box if you need crane
- Do not remove temporary screens in the deck drains
- Do not plug cords into the string lights, Do not flip spider boxes on their sides
- See Site Superindent for parking passes.

SCHEDULE:

46.02 Reviewed **SITE** 3 wk look ahead schedule beginning 1/4/16

- Site Grading – North – Drain line/Backfill NE Retaining Wall 1/11-1/12, Backfill NW, Excavate Transformer enclosure 1/14-1/18
- Utilities – PSE Gas – Permanent Service North 1/25-1/27
- Site Structure – North – Strip Stair Walls 1/11-1/13, F&P Transformer Rm Ftgs/SOG 1/19-1/22, F&P Transformer Walls 1/25-2/2
  - East – Set Comm Sleeves 1/11-1/12, Set Scaffold 1/11-1/14
- Wood Framing/Roofing North Southwest – Parapet Cap 1/12-1/18, Set Mechanical Equipment 1/11
- Wood framing Roof Southeast – Frame Trellis Walls1/13-1/18, Crickets 1/11-1/12, Roofing 1/13-1/22, Parapet Caps 1/25-11/29
- Exterior – Siding/Flashing Mock up West 1/11-1/12, Production Siding 1/13-1/26
  - North – Set Rem Scaffold 1/13-1/14, Prep Densglass/Trim Openings 1/15-1/19, Wrap Windows/Set windows 1/20-1/29
  - Courtyard – East Prep Densglass openings1/11-1/15, Wrap/Set windows1/18-1/27

- East Face – Set Scaffold/Bonnet/Greenscreen 1/11-1/27, Fix Dens Glass 1/13 1/19, Wrap/Set Windows 1/18-1/27

46.03 Reviewed **INTERIOR** 3wk look ahead schedule beginning 1/4/16

- 01/12/16: Temp heat is on
  - IEC needs corridor ventilation shafts framed
  - CHINN to provide best estimate on drywall install for 5th and 6th floors

OLD BUSINESS:

38.09 Advanced and IEC to coordinate lights and sprinklers at storefront alcoves

41.08 LB to get dimensions for louver above loading dock.

41.12 CHINN to schedule a handrail mock up. WCP, SS, and CHINN to attend for backing purposes.
12/29/15: Wood handrail mock up is installed. CHINN to check on metal handrail.

44.04 Crane Operator and Rigger will not be onsite full time. All subcontractors need to forecast deliveries.

44.06 Froula needs to know what is being pulled to each unit for franchise utilities
01/12/16: CHINN printed out COP for Kyle

44.07 IEC needs the corridor ventilation shafts framed to rough in electrical.

44.08 GF mechanical curb needs coping metal

44.09 OWP presented BBQ and Fireplace ½" gas pipe routing. LB to present at next OAC meeting on 1/5.

PERMIT STATUS: **HVAC** – Jason (CFM) Corrections were submitted 10/09 or 10/12, Met with Architect on 11/16 to discuss Louvers at the storefront, 12/08 – revisions have been submitted for review with COMI.

RFIs: 44.10 RFI 217 – Patio Light Fixture Location – A couple of locations that are listed C4, C3, J, and G will not work. LB to email Architect.

SUBMITTALS:

NEW BUSINESS:

46.03 Roof drains need screens installed

46.04 Wave or CenturyLink dropped off a vault onsite. Froula to layout MDF equipment so we can see what the franchise utilities require.

46.05 The final TWF mock up is today.

46.06 SS stated the Earthbound System is complete.

46.07 Lighting needs to be installed at the East scaffolding.

NEXT MEETING: 01/12/16, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
1-11-2016

ID		Task Name	Duration	Start	Finish
1		**Site Grading/Utilities**	**13 days**	**Mon 1/11/16**	**Wed 1/27/16**
2		**North**	**6 days**	**Mon 1/11/16**	**Mon 1/18/16**
3		Drainline/Backfill NE Ret wall	2 days	Mon 1/11/16	Tue 1/12/16
4		Grade/Excavate Transformer Vault	3 days	Thu 1/14/16	Mon 1/18/16
5					
6		**PSE/Gas**	**2 days**	**Tue 1/26/16**	**Wed 1/27/16**
7		Permanent Service North	2 days	Tue 1/26/16	Wed 1/27/16
8		**Site/Structure**	**17 days**	**Mon 1/11/16**	**Tue 2/2/16**
9		**North**	**17 days**	**Mon 1/11/16**	**Tue 2/2/16**
10		Strip Stair Walls	3 days	Mon 1/11/16	Wed 1/13/16
11		F&P Transformer Rm Ftgs/SOG	4 days	Tue 1/19/16	Fri 1/22/16
12		F&P Transformer Walls	7 days	Mon 1/25/16	Tue 2/2/16
13					
14		**East**	**4 days**	**Mon 1/11/16**	**Thu 1/14/16**
15		Set Com Sleeves	2 days	Mon 1/11/16	Tue 1/12/16
16		Set Scaffold	4 days	Mon 1/11/16	Thu 1/14/16
17					
18		**Wood Framing/Roofing**	**15 days**	**Mon 1/11/16**	**Fri 1/29/16**
19		**North/Southwest**	**6 days**	**Mon 1/11/16**	**Mon 1/18/16**
20		Parapet Cap	5 days	Tue 1/12/16	Mon 1/18/16
21		Set Mech Equipment	1 day	Mon 1/11/16	Mon 1/11/16
22		**Southeast**	**15 days**	**Mon 1/11/16**	**Fri 1/29/16**
23		Frame Trellis Walls	4 days	Wed 1/13/16	Mon 1/18/16
24		Crickets	2 days	Mon 1/11/16	Tue 1/12/16
25		Roofing	8 days	Wed 1/13/16	Fri 1/22/16
26		Parapet Caps	5 days	Mon 1/25/16	Fri 1/29/16
27					
28		**Exterior**	**15 days**	**Mon 1/11/16**	**Fri 1/29/16**
29		**West**	**12 days**	**Mon 1/11/16**	**Tue 1/26/16**
30		Flashing Mock-up	2 days	Mon 1/11/16	Tue 1/12/16
31		Production Siding	10 days	Wed 1/13/16	Tue 1/26/16
32		**North**	**13 days**	**Wed 1/13/16**	**Fri 1/29/16**
33		Set Rem Scaffold	2 days	Wed 1/13/16	Thu 1/14/16
34		Prep Densglass/Trim Openings	3 days	Fri 1/15/16	Tue 1/19/16

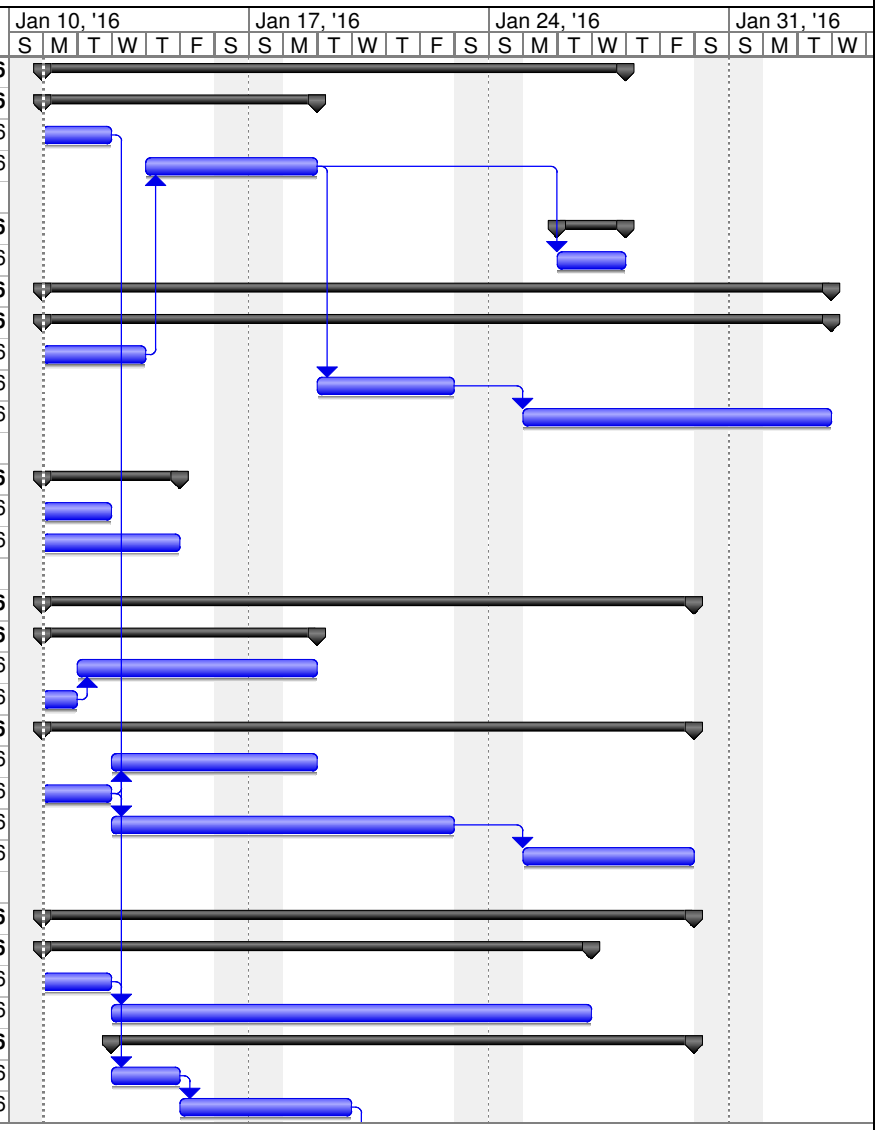

Project: 3wk 1-11-2016
Date: Mon 1/11/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
1-11-2016

ID		Task Name	Duration	Start	Finish
35		Wrap Openings/Set Windows	8 days	Wed 1/20/16	Fri 1/29/16
36					
37		**Courtyard**	**13 days**	**Mon 1/11/16**	**Wed 1/27/16**
38		**East**	**13 days**	**Mon 1/11/16**	**Wed 1/27/16**
39		Prep D-Glass/Openings	5 days	Mon 1/11/16	Fri 1/15/16
40		Wrap/Set Windows	8 days	Mon 1/18/16	Wed 1/27/16
41		**East Face**	**13 days**	**Mon 1/11/16**	**Wed 1/27/16**
42		Set Scaffold/Bonnet /Greenscreen	4 days	Mon 1/11/16	Thu 1/14/16
43		Fix Dens-Glass	5 days	Wed 1/13/16	Tue 1/19/16
44		Wrap/Set Windows	8 days	Mon 1/18/16	Wed 1/27/16

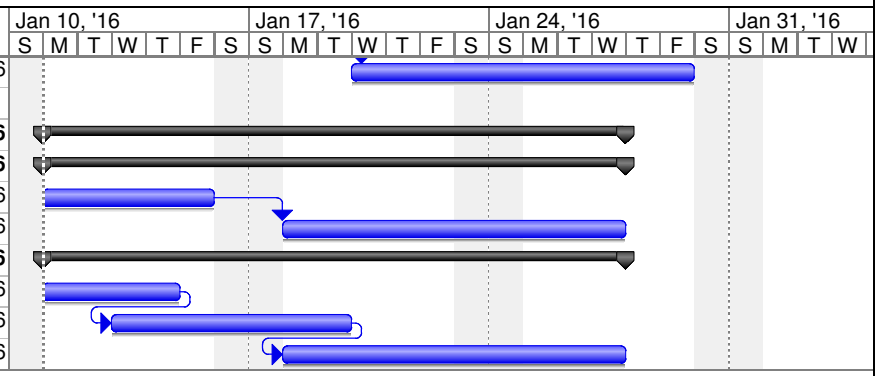

Project: 3wk 1-11-2016
Date: Mon 1/11/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
