CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **49**

MEETING DATE: **01/26/16**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
Charlie Poggemann – CHINN
Sim Mooers – CHINN
Lauren Bjorndahl – CHINN
Eric Bull – CHINN
Kyle – Froula
~~Jason – CFM~~
Richard Donelson - OWP
~~George Faler - CHINN~~
Casey Hutchison - SS
Kenny - Axiom
Jose Mendina – Advanced
Gary – Prec. Wall
Ross Porterfield – IEC
John Perillo – WCP

SAFETY: Stair Tower NE will be dismantled and replaced with Scaffold to prepare for Windows and Siding.

46.01 Housekeeping

- **CRANE DISMANTLE 02/13/16 Make sue to coordinate you deliveries to the site and make sure the Site, Roof and Courtyard are free of unneeded material and Trash.**
- No smoking onsite
- Roof needs tobe cleaned of screws, nails, Plmbg fittings, and all construction debris
- There is no food allowed above Level 2
- Use the delivery board for all deliveries after the demobilization of the crane.
- Do not remove temporary screens in the deck drains
- Do not plug cords into the string lights, Do not flip spider boxes on their sides
- See Site Superindent for parking passes.
- All personel to be masked in areas of sandblasting West or remain out of the area.

SCHEDULE:

46.02 Reviewed **SITE** 3 wk look ahead schedule beginning 2 8/16

- Site Grading – Exc. Gas and Comm Vaults after Trans. Walls.
- Utilities – PSE Gas – Permanent Service North 2-1-16
- Site Structure –
  - Remainder East Scaffold, Green screen/Bonnet
- Wood Framing/ Remaing Roofing North Southwest – Parapet Cap complete, Set Mechanical Equipment 2/11
- Sheath Trellis Walls2/8—2/11, , Parapet Caps 2/8—2/11- Need all framing at Mezz and Amenities including Stairs 2/17
- Exterior – Siding/Flashing, Production Siding ??? 2/1
  - North --, Wrap Windows/Set windows 2/1???
  - Courtyard – Complete Scaffold at Access units/ Repair Dens Glass Wrap/Set windows/ Man doors 1-19/1-29 @/8 – 2/11
  - East Face – Fix Dens Glass 2/1 to 2/5 Wrap/Set Windows 2/4

46.03 Reviewed **INTERIOR** 3wk look ahead schedule beginning 1/4/16

- 01/12/16: Temp heat is on
  - IEC needs corridor ventilation shafts framed
  - CHINN to provide best estimate on drywall install for 5th and 6th floors
  - Level 4 West signed of by Rose

OLD BUSINESS:

38.09 Advanced and IEC to coordinate lights and sprinklers at storefront alcoves

41.08 EB to get dimensions for louver above loading dock.

41.12 CHINN to schedule a handrail mock up. WCP, SS, and CHINN to attend for backing purposes.
12/29/15: Wood handrail mock up is installed. CHINN to check on metal handrail.

44.04 Crane Operator and Rigger will not be onsite after Friday 2/13 All subcontractors need to forecast deliveries.

44.06 Froula needs to know what is being pulled to each unit for franchise utilities
01/12/16: CHINN printed out COP for Kyle

44.07 IEC needs the corridor ventilation shafts framed to rough in electrical.

44.08 CFM to supply Mech curbs for all rooftop equipment

PERMIT STATUS: **HVAC** – Jason /Jeremy met with Chinn, Legacy, Via and the COMI on Friday 1-22-16 to discuss and resolve permit issues between CFM drawings and the City,s comments. Nine out of eleven issues were resolved and CFM will make corrections and resubmit and the plans examiner stated they will approve the drawings and allow acquisition of the permit by this Friday

Update Via/ CFM to redesign Garage Exhaust due to code issues with existing. This is holding up permit until new plan is reviewed.

RFIs: 44.09 RFI 217 – Patio Light Fixture Location – A couple of locations that are listed C4, C3, J, and G will not work. LB to email Architect.

NEW BUSINESS:

46.04 Wave and CenturyLink dropped off a vaults onsite. Location was provided by CPL and NW will set vaults

46.05 The Roof top Mech units need to have flashing and isolation from the TPO. The fan for Stair 1 also needs relocation. Complete

46.06 SS stated the Earthbound System is complete.

46.07 Power from the Crane will be used for the Elevator

NEXT MEETING: 01/26/16, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley 3 Week Schedule (Interior)
2-8-2016

ID	Task Name	Duration	Start	Finish
1	**MEP Roof Down**	**87 days**	**Tue 1/12/16**	**Wed 5/11/16**
2	**L5 Zone 1 (South half)**	**39 days**	**Tue 1/12/16**	**Fri 3/4/16**
3	Electrical RI	5 days	Tue 1/12/16	Mon 1/18/16
4	Low volt RI	4 days	Wed 1/13/16	Mon 1/18/16
5	Plumbing/Electrical/Lowvolt Inspe	1 day	Tue 1/19/16	Tue 1/19/16
6	Fire Caulk	2 days	Wed 1/20/16	Thu 1/21/16
7	Insulate for pre rock at tubs	1 day	Fri 1/22/16	Fri 1/22/16
8	Pre rock for tubs/ accoustic	1 day	Mon 1/25/16	Mon 1/25/16
9	Framing inspection	1 day	Tue 1/26/16	Tue 1/26/16
10	Insulation	3 days	Wed 1/27/16	Fri 1/29/16
11	Insulation Inspection	1 day	Mon 2/1/16	Mon 2/1/16
12	Drywall Hang/Tape/Texture/PVA	15 days	Tue 2/2/16	Mon 2/22/16
13	Frame soffits	4 days	Tue 2/9/16	Fri 2/12/16
14	Vent soffits	4 days	Mon 2/15/16	Thu 2/18/16
15	Electrical at soffits	2 days	Fri 2/19/16	Mon 2/22/16
16	HVAC/ Electrical inspection at sof	1 day	Tue 2/23/16	Tue 2/23/16
17	Hang and tape soffits	5 days	Wed 2/24/16	Tue 3/1/16
18	Paint	3 days	Wed 3/2/16	Fri 3/4/16
19				
20	**L5 Zone 1 (North half)**	**39 days**	**Tue 1/19/16**	**Fri 3/11/16**
21	Electrical RI	5 days	Tue 1/19/16	Mon 1/25/16
22	Low volt RI	4 days	Wed 1/20/16	Mon 1/25/16
23	Plumbing/Electrical/Lowvolt Inspe	1 day	Tue 1/26/16	Tue 1/26/16
24	Fire Caulk	2 days	Wed 1/27/16	Thu 1/28/16
25	Insulate for pre rock at tubs	1 day	Fri 1/29/16	Fri 1/29/16
26	Pre rock for tubs/ accoustic	1 day	Mon 2/1/16	Mon 2/1/16
27	Framing inspection	1 day	Tue 2/2/16	Tue 2/2/16
28	Insulation	3 days	Wed 2/3/16	Fri 2/5/16
29	Insulation Inspection	1 day	Mon 2/8/16	Mon 2/8/16
30	Drywall Hang/Tape/Texture/PVA	15 days	Tue 2/9/16	Mon 2/29/16
31	Frame soffits	4 days	Tue 2/16/16	Fri 2/19/16
32	Vent soffits	4 days	Mon 2/22/16	Thu 2/25/16
33	Electrical at soffits	2 days	Fri 2/26/16	Mon 2/29/16
34	HVAC/ Electrical inspection at sof	1 day	Tue 3/1/16	Tue 3/1/16
35	Hang and tape soffits	5 days	Wed 3/2/16	Tue 3/8/16
36	Paint	3 days	Wed 3/9/16	Fri 3/11/16

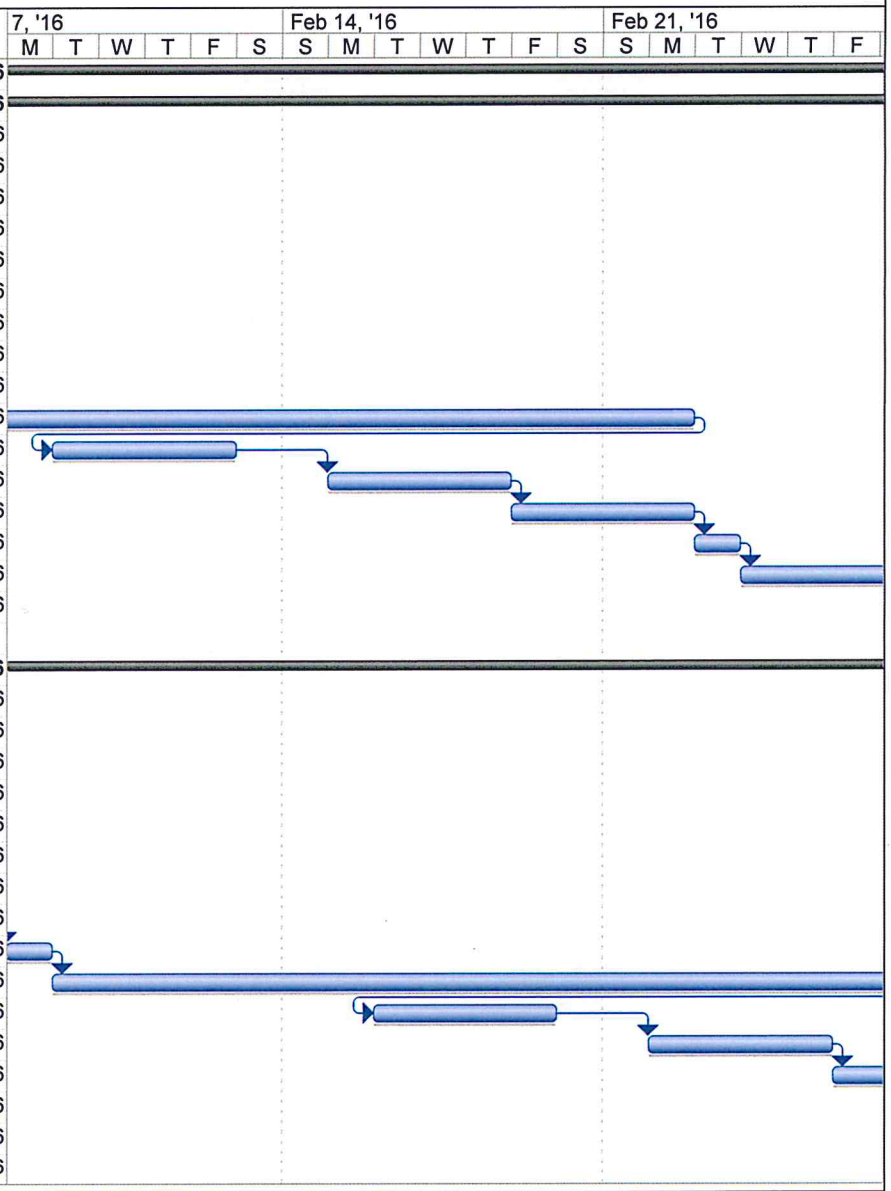

Project: MI MPE RI 2-8
Date: Mon 2/8/16

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

Hadley 3 Week Schedule (Interior)
2-8-2016

ID	Task Name	Duration	Start	Finish
37				
38	**L5 Zone 1 (West side)**	**77 days**	**Tue 1/26/16**	**Wed 5/11/16**
39	Gypcrete	3 days	Mon 3/14/16	Wed 3/16/16
40	Gypcrete dry time	10 days	Thu 3/17/16	Wed 3/30/16
41	Electrical trim	5 days	Thu 3/24/16	Wed 3/30/16
42	Install cabinets	5 days	Thu 3/31/16	Wed 4/6/16
43				
44	**L4 Zone 1 (South half)**	**39 days**	**Tue 1/26/16**	**Fri 3/18/16**
45	Electrical RI	5 days	Tue 1/26/16	Mon 2/1/16
46	Low volt RI	4 days	Wed 1/27/16	Mon 2/1/16
47	Plumbing/Electrical/Lowvolt I	1 day	Tue 2/2/16	Tue 2/2/16
48	Fire Caulk	2 days	Wed 2/3/16	Thu 2/4/16
49	Insulate for pre rock at tubs	1 day	Fri 2/5/16	Fri 2/5/16
50	Pre rock for tubs/ accoustic	1 day	Mon 2/8/16	Mon 2/8/16
51	Framing inspection	1 day	Tue 2/9/16	Tue 2/9/16
52	Insulation	3 days	Wed 2/10/16	Fri 2/12/16
53	Insulation Inspection	1 day	Mon 2/15/16	Mon 2/15/16
54	Drywall Hang/Tape/Texture/F	15 days	Tue 2/16/16	Mon 3/7/16
55	Frame soffits	4 days	Tue 2/23/16	Fri 2/26/16
56	Vent soffits	4 days	Mon 2/29/16	Thu 3/3/16
57	Electrical at soffits	2 days	Fri 3/4/16	Mon 3/7/16
58	HVAC/ Electrical inspection a	1 day	Tue 3/8/16	Tue 3/8/16
59	Hang and tape soffits	5 days	Wed 3/9/16	Tue 3/15/16
60	Paint	3 days	Wed 3/16/16	Fri 3/18/16
61				
62	**L4 Zone 1 (North half)**	**39 days**	**Tue 2/2/16**	**Fri 3/25/16**
63	Electrical RI	5 days	Tue 2/2/16	Mon 2/8/16
64	Low volt RI	4 days	Wed 2/3/16	Mon 2/8/16
65	Plumbing/Electrical/Lowvolt I	1 day	Tue 2/9/16	Tue 2/9/16
66	Fire Caulk	2 days	Wed 2/10/16	Thu 2/11/16
67	Insulate for pre rock at tubs	1 day	Fri 2/12/16	Fri 2/12/16
68	Pre rock for tubs/ accoustic	1 day	Mon 2/15/16	Mon 2/15/16
69	Framing inspection	1 day	Tue 2/16/16	Tue 2/16/16
70	Insulation	3 days	Wed 2/17/16	Fri 2/19/16
71	Insulation Inspection	1 day	Mon 2/22/16	Mon 2/22/16
72	Drywall Hang/Tape/Texture/F	15 days	Tue 2/23/16	Mon 3/14/16

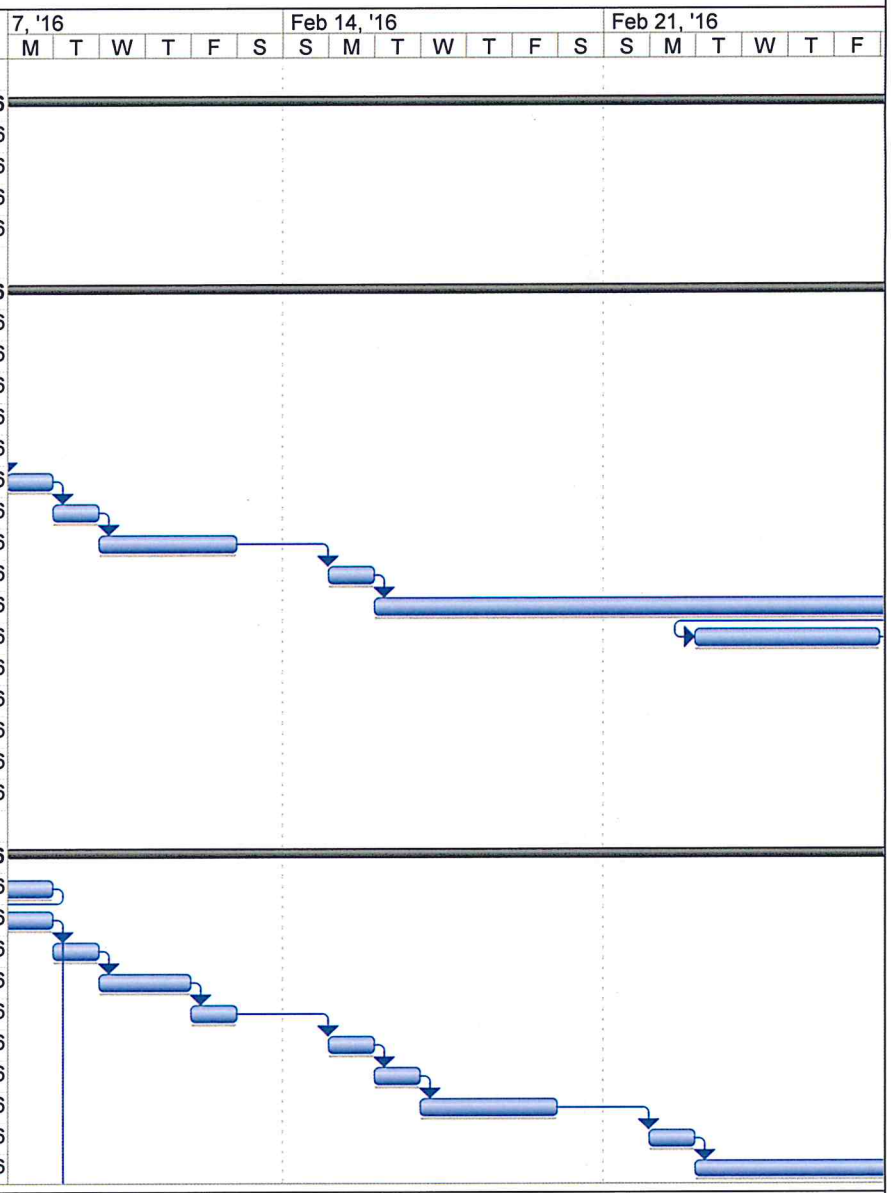

Project: MI MPE RI 2-8
Date: Mon 2/8/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
2-8-2016

ID	Task Name	Duration	Start	Finish
73	Frame soffits	4 days	Tue 3/1/16	Fri 3/4/16
74	Vent soffits	4 days	Mon 3/7/16	Thu 3/10/16
75	Electrical at soffits	2 days	Fri 3/11/16	Mon 3/14/16
76	HVAC/ Electrical inspection a	1 day	Tue 3/15/16	Tue 3/15/16
77	Hang and tape soffits	5 days	Wed 3/16/16	Tue 3/22/16
78	Paint	3 days	Wed 3/23/16	Fri 3/25/16
79				
80	**L4 Zone 1 (West side)**	**67 days**	**Tue 2/9/16**	**Wed 5/11/16**
81	Gypcrete	3 days	Mon 3/28/16	Wed 3/30/16
82	Gypcrete dry time	10 days	Thu 3/31/16	Wed 4/13/16
83	Electrical trim	5 days	Thu 4/7/16	Wed 4/13/16
84	Install cabinets	5 days	Thu 4/14/16	Wed 4/20/16
85				
86	**L3 Zone 1 (South half)**	**39 days**	**Tue 2/9/16**	**Fri 4/1/16**
87	Electrical RI	5 days	Tue 2/9/16	Mon 2/15/16
88	Low volt RI	4 days	Wed 2/10/16	Mon 2/15/16
89	Plumbing/Electrical/Low	1 day	Tue 2/16/16	Tue 2/16/16
90	Fire Caulk	2 days	Wed 2/17/16	Thu 2/18/16
91	Insulate for pre rock at t	1 day	Fri 2/19/16	Fri 2/19/16
92	Pre rock for tubs/ accou	1 day	Mon 2/22/16	Mon 2/22/16
93	Framing inspection	1 day	Tue 2/23/16	Tue 2/23/16
94	Insulation	3 days	Wed 2/24/16	Fri 2/26/16
95	Insulation Inspection	1 day	Mon 2/29/16	Mon 2/29/16
96	Drywall Hang/Tape/Text	15 days	Tue 3/1/16	Mon 3/21/16
97	Frame soffits	4 days	Tue 3/8/16	Fri 3/11/16
98	Vent soffits	4 days	Mon 3/14/16	Thu 3/17/16
99	Electrical at soffits	2 days	Fri 3/18/16	Mon 3/21/16
100	HVAC/ Electrical inspect	1 day	Tue 3/22/16	Tue 3/22/16
101	Hang and tape soffits	5 days	Wed 3/23/16	Tue 3/29/16
102	Paint	3 days	Wed 3/30/16	Fri 4/1/16
103				
104	**L3 Zone 1 (North half)**	**62 days**	**Tue 2/16/16**	**Wed 5/11/16**
105	Electrical RI	5 days	Tue 2/16/16	Mon 2/22/16
106	Low volt RI	4 days	Wed 2/17/16	Mon 2/22/16
107	Plumbing/Electrical/Low	1 day	Tue 2/23/16	Tue 2/23/16
108	Fire Caulk	2 days	Wed 2/24/16	Thu 2/25/16

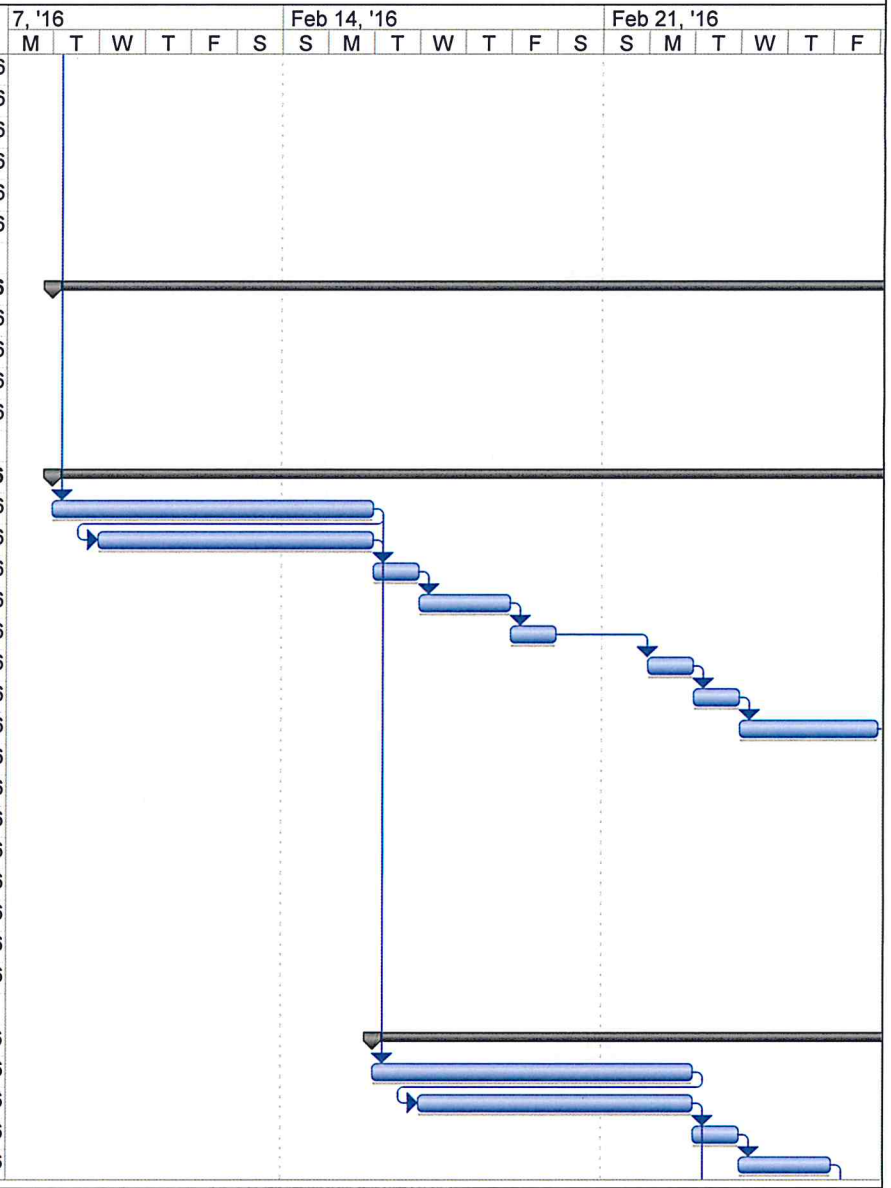

Project: MI MPE RI 2-8
Date: Mon 2/8/16

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

Hadley 3 Week Schedule (Interior)
2-8-2016

ID	Task Name	Duration	Start	Finish
109	Insulate for pre rock at t	1 day	Fri 2/26/16	Fri 2/26/16
110	Pre rock for tubs/ accou	1 day	Mon 2/29/16	Mon 2/29/16
111	Framing inspection	1 day	Tue 3/1/16	Tue 3/1/16
112	Insulation	3 days	Wed 3/2/16	Fri 3/4/16
113	Insulation Inspection	1 day	Mon 3/7/16	Mon 3/7/16
114	Drywall Hang/Tape/Text	15 days	Tue 3/8/16	Mon 3/28/16
115	Frame soffits	4 days	Tue 3/15/16	Fri 3/18/16
116	Vent soffits	4 days	Mon 3/21/16	Thu 3/24/16
117	Electrical at soffits	2 days	Fri 3/25/16	Mon 3/28/16
118	HVAC/ Electrical inspect	1 day	Tue 3/29/16	Tue 3/29/16
119	Hang and tape soffits	5 days	Wed 3/30/16	Tue 4/5/16
120	Paint	3 days	Wed 4/6/16	Fri 4/8/16
121				
122	**L6 Zone 1 (South half)**	**34 days**	**Tue 2/23/16**	**Fri 4/8/16**
123	Electrical RI	5 days	Tue 2/23/16	Mon 2/29/16
124	Low volt RI	4 days	Wed 2/24/16	Mon 2/29/16
125	Plumbing/Electrical	1 day	Tue 2/23/16	Tue 2/23/16
126	Fire Caulk	2 days	Wed 2/24/16	Thu 2/25/16
127	Insulate for pre rock	1 day	Fri 2/26/16	Fri 2/26/16
128	Pre rock for tubs/ a	1 day	Mon 2/29/16	Mon 2/29/16
129	Framing inspection	1 day	Tue 3/1/16	Tue 3/1/16
130	Insulation	3 days	Wed 3/2/16	Fri 3/4/16
131	Insulation Inspectio	1 day	Mon 3/7/16	Mon 3/7/16
132	Drywall Hang/Tape/	15 days	Tue 3/8/16	Mon 3/28/16
133	Frame soffits	4 days	Tue 3/15/16	Fri 3/18/16
134	Vent soffits	4 days	Mon 3/21/16	Thu 3/24/16
135	Electrical at soffits	2 days	Fri 3/25/16	Mon 3/28/16
136	HVAC/ Electrical in	1 day	Tue 3/29/16	Tue 3/29/16
137	Hang and tape soffi	5 days	Wed 3/30/16	Tue 4/5/16
138	Paint	3 days	Wed 4/6/16	Fri 4/8/16
139				
140	**L6 Zone 1 (North half)**	**34 days**	**Tue 3/1/16**	**Fri 4/15/16**
141	Electrical RI	5 days	Tue 3/1/16	Mon 3/7/16
142	Low volt RI	4 days	Wed 3/2/16	Mon 3/7/16
143	Plumbing/Electrical	1 day	Tue 3/1/16	Tue 3/1/16
144	Fire Caulk	2 days	Wed 3/2/16	Thu 3/3/16

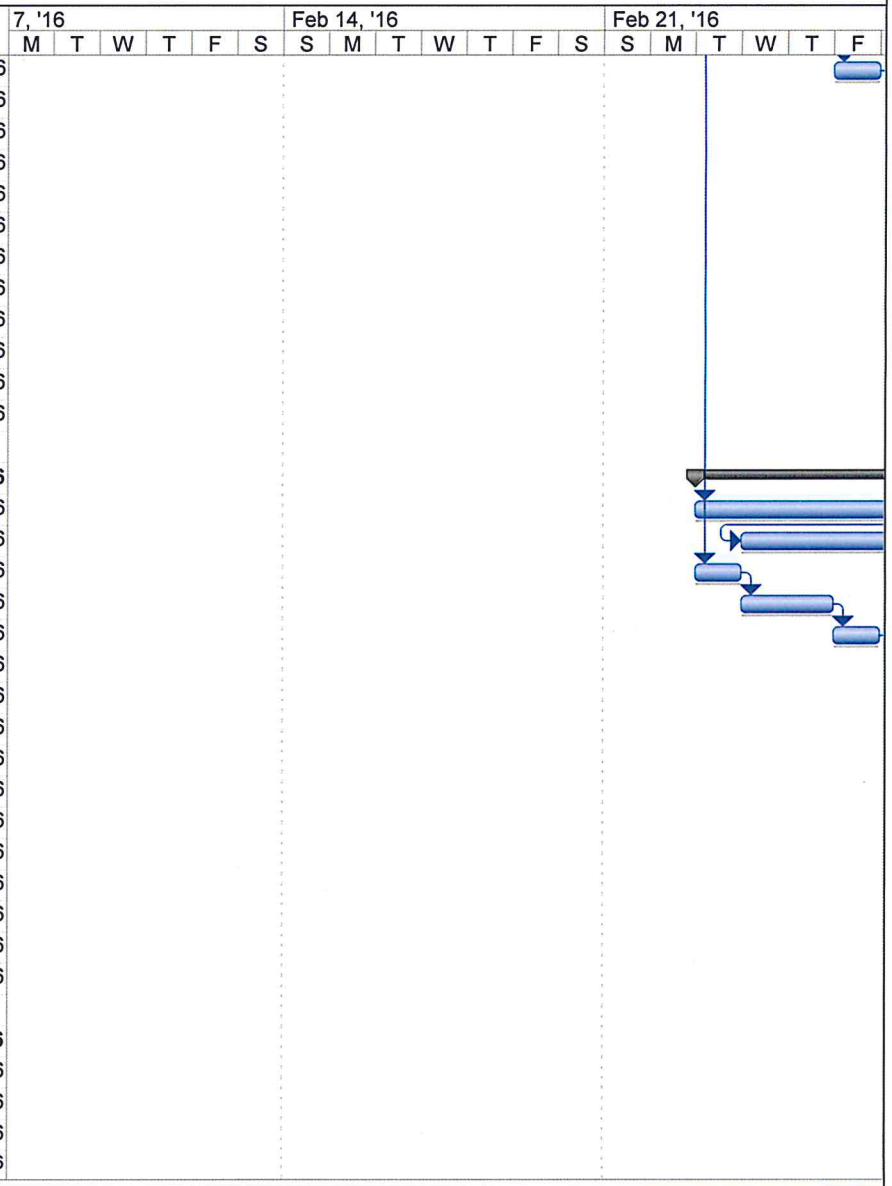

Project: MI MPE RI 2-8
Date: Mon 2/8/16

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

Hadley Mixed use
Legacy
3 wk Look ahead
2-8-2016

ID		Task Name	Duration	Start	Finish
1		**Site Grading/Utilities**	**5 days**	**Tue 2/9/16**	**Mon 2/15/16**
2		**North**	**5 days**	**Tue 2/9/16**	**Mon 2/15/16**
3		Install Gas Sleeve	2 days	Wed 2/10/16	Thu 2/11/16
4		Demob Crane	2 days	Fri 2/12/16	Mon 2/15/16
5		Install Vista Switch/Primary's	3 days	Tue 2/9/16	Thu 2/11/16
6					
7		**Site/Structure**	**7 days**	**Mon 2/8/16**	**Tue 2/16/16**
8		**North**	**7 days**	**Mon 2/8/16**	**Tue 2/16/16**
9		F&P Transformer Walls	7 days	Mon 2/8/16	Tue 2/16/16
10					
11		**Wood Framing/Roofing**	**3 days**	**Mon 2/8/16**	**Wed 2/10/16**
12		**North/Southwest**	**3 days**	**Mon 2/8/16**	**Wed 2/10/16**
13		Parapet Cap	3 days	Mon 2/8/16	Wed 2/10/16
14		Set Mech Equipment	3 days	Mon 2/8/16	Wed 2/10/16
15					
16		**Southeast**	**12 days**	**Mon 2/8/16**	**Tue 2/23/16**
21		Roof	3 days	Mon 2/8/16	Wed 2/10/16
22		Paper Penthouses	2 days	Thu 2/11/16	Fri 2/12/16
23		Set Windows	1 day	Mon 2/15/16	Mon 2/15/16
24					
25		**Exterior**	**10 days**	**Mon 2/8/16**	**Fri 2/19/16**
26		**West**	**10 days**	**Mon 2/8/16**	**Fri 2/19/16**
27		Window Test West L5/6	1 day	Mon 2/8/16	Mon 2/8/16
28		Battons/Siding West	10 days	Mon 2/8/16	Fri 2/19/16
29		**South**	**2 days**	**Mon 2/8/16**	**Tue 2/9/16**
30		Set Windows	2 days	Mon 2/8/16	Tue 2/9/16
31		**North**	**6 days**	**Mon 2/8/16**	**Mon 2/15/16**
32		Tyvek	3 days	Mon 2/8/16	Wed 2/10/16
33		Wrap Openings/Set Windows	5 days	Tue 2/9/16	Mon 2/15/16
34					
35		**Courtyard**	**4 days**	**Mon 2/8/16**	**Thu 2/11/16**
36		**North**	**4 days**	**Mon 2/8/16**	**Thu 2/11/16**
37		Set Windows	4 days	Mon 2/8/16	Thu 2/11/16
38		**East Perimeter**	**17 days**	**Mon 2/8/16**	**Tue 3/1/16**

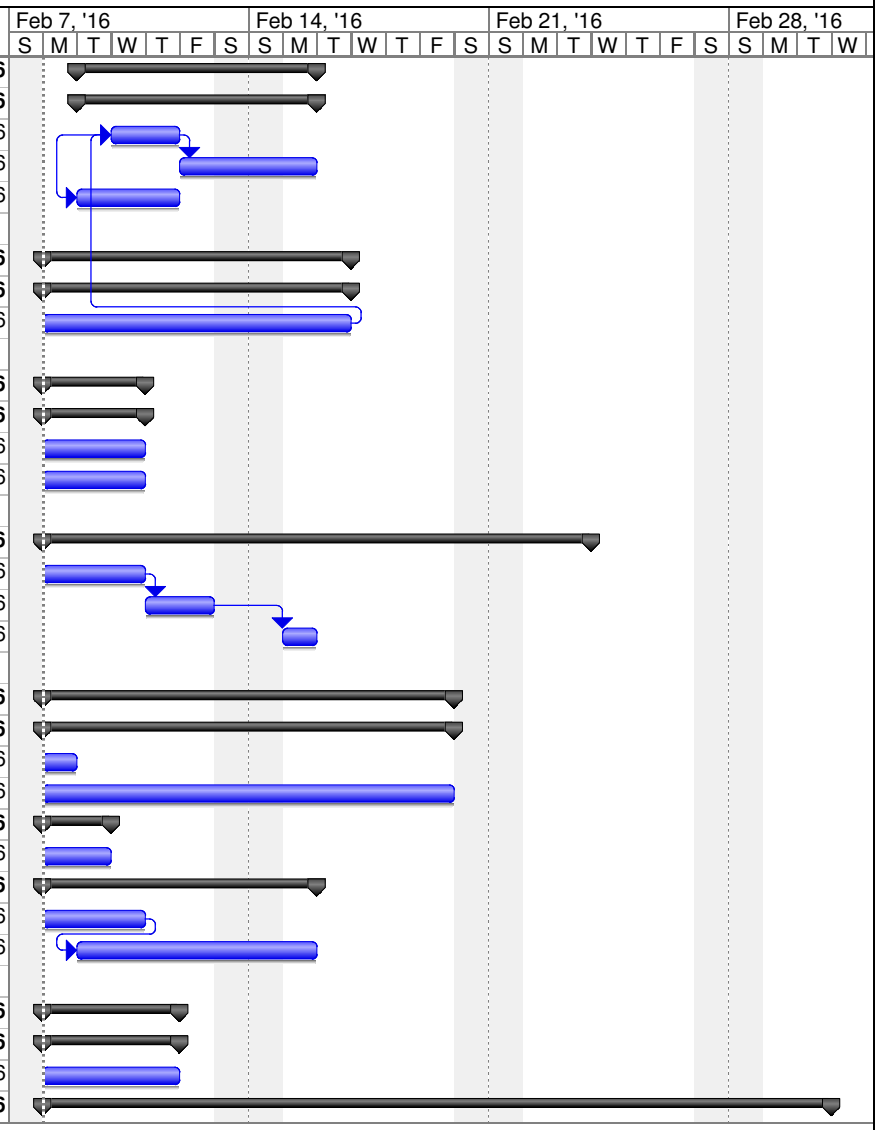

Project: 3wk 2-8-16
Date: Mon 2/8/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
2-8-2016

ID		Task Name	Duration	Start	Finish
39		Scaffold/Bonnet /Greenscreen	2 days	Mon 2/8/16	Tue 2/9/16
40		Fix Dens-Glass	6 days	Mon 2/8/16	Mon 2/15/16
41		Tyvek	3 days	Tue 2/16/16	Thu 2/18/16
42		Wrap/Set Windows	8 days	Fri 2/19/16	Tue 3/1/16



Project: 3wk 2-8-16
Date: Mon 2/8/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
