CHINN CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **53**

MEETING DATE: **3/1/16**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
Charlie Poggemann – CHINN
Sim Mooers – CHINN
Eric Bull – CHINN
Kyle – Froula
~~Jason – CFM~~
John Perillo – WCP

~~George Faler – CHINN Richard Donelson - OWP~~
~~Casey Hutchison – SS~~
Kevin – SS
Kenny - Axiom
Jose Mendina – Advanced
Gary – Prec. Wall
Ross Porterfield – IEC

SAFETY: **TRASH CHUTE**

- **Do not enter dumpster to rearrange trash without marking gates prior to.**
- **Make sure debris is small enough to fit in chute.**
- **Keep arms and head out of chute.**
- **Glass Sliders have been installed and protected at chutes Please be carefull not to damage frame.**

46.01 Housekeeping

- No smoking onsite
- Roof is cleaned and punched. Do not place material on it without protection.
- There is no food allowed above Level 2
- Use the delivery board for all deliveries after the demobilization of the crane.
- Do not remove temporary screens in the deck drains
- Do not plug cords into the string lights, Do not flip spider boxes on their sides
- See Site Superindent for parking passes.
- All personel to be masked in areas of sandblasting West or remain out of the area.
- Chinn provided a reach Forklift that will better service loads to the Courtyard etc. Be certain that your operator is got their credentials..

SCHEDULE:

46.02 Reviewed **SITE** 3 wk look ahead schedule beginning 2/22/16

- Gas Sleeve complete/Gas Main anticipated in 3 weeks
- Switchgear delivery Monday 3/7
- Site Structure –
  Window test move to Friday 3/11
- Parapet Cap needs completion @ roof
- B and BB Windows need RO 6” smaller to complete install
- Need AC ports and Stucco Backing Completed
- Exterior – Precision adding to crew for production siding to start.
  - North --,Complete ready for siding/stucco L 3,4,5
  - Window testing will complete end of week 3/11

46.03 Reviewed **INTERIOR** 3wk look ahead schedule beginning 3/7/16

- 01/12/16: Temp heat is on
  - All shafts are in need of rock as not to delay power etc.
  - CHINN to provide best estimate on drywall install for 3rd and 4th floors
  - Stair ¼ Sandblast next
  - Heat close for East Tower
  - Elevators arrived 3/3---3/4/16 Awaiting permit to begin installation
  - Switchgear arrives 3/7/16. IEC to set an d pull secondaries.

OLD BUSINESS:

38.09 Unit venting in for permit

41.08 New direction on garage exhaust in for plan review

41.12 CHINN to schedule a handrail mock up. WCP, SS, and CHINN to attend for backing purposes.
12/29/15: Wood handrail mock up is installed. CHINN to check on metal handrail.

44.04 Northwest gone until scaffold demob East

44.06 Froula needs to know what is being pulled to each unit for franchise utilities
01/12/16: CHINN printed out COP for Kyle

44.07 IEC needs the corridor ventilation shafts framed to rough in electrical.

44.08 CFM to complete Roof equip etc.

44.09 Crane openings will be formed and poured by 3/4/16 Done

44.10 Hollow metal leafs arrived 2/29

44.11 Additional Temp heat for East this week

PERMIT STATUS: **HVAC** – Jason /Jeremy met with Chinn, Legacy, Via and the COMI on Friday 1-22-16 to discuss and resolve permit issues between CFM drawings and the City,s comments. Nine out of eleven issues were resolved and CFM will make corrections and resubmit and the plans examiner stated they will approve the drawings and allow acquisition of the permit by this Friday

Update Via/ CFM to redesign Garage Exhaust due to code issues with existing. This is holding up permit until new plan is reviewed.

Latest **CFM submittal questions answed now Legacy in line for missing info.**

RFIs: 44.09 RFI 217 – Patio Light Fixture Location – A couple of locations that are listed C4, C3, J, and G will not work. LB to email Architect.

NEW BUSINESS:

46.04 Wave and CenturyLink, Comcast Vaults/Conduit complete

46.05 The Roof top Mech units need to have flashing and isolation from the TPO. The fan for Stair 1 also needs relocation. Complete

46.06 SS stated the Earthbound System is complete.

46.07 Power from the Crane will be used for the Elevator

46.08 BCRA to Window test 3/1116. Inspect and approve all elevations for siding.

NEXT MEETING: 3/8/16, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
3-7-2016

ID		Task Name	Duration	Start	Finish
1		**Garage**	**27 days**	**Mon 3/7/16**	**Tue 4/12/16**
2		**Level P**	**23 days**	**Mon 3/7/16**	**Wed 4/6/16**
3		Set Switchgear	10 days	Mon 3/7/16	Fri 3/18/16
4		Pull Secondary's	5 days	Mon 3/14/16	Fri 3/18/16
5		Set Transformer/Pull main	3 days	Mon 4/4/16	Wed 4/6/16
6		FT Plywood Comm Rm.	3 days	Mon 3/21/16	Wed 3/23/16
7		Swing needed HM doors	2 days	Thu 3/24/16	Fri 3/25/16
8		Light Fixtures	5 days	Mon 3/7/16	Fri 3/11/16
9					
10		**Level 1**	**17 days**	**Mon 3/7/16**	**Tue 3/29/16**
11		Replace Rock	5 days	Mon 3/7/16	Fri 3/11/16
12		Swing HM	2 days	Mon 3/14/16	Tue 3/15/16
13		Garage Light Fixtures	10 days	Mon 3/14/16	Fri 3/25/16
14		Insulate Lid	7 days	Mon 3/21/16	Tue 3/29/16
15					
16		**Level 2**	**27 days**	**Mon 3/7/16**	**Tue 4/12/16**
17		Z-Girts/Rigid@ Ext.	5 days	Mon 3/7/16	Fri 3/11/16
18		Dens-Glass Ext	4 days	Thu 3/10/16	Tue 3/15/16
19		Tyvek Wrap	2 days	Wed 3/16/16	Thu 3/17/16
20		Set Doors/Windows	3 days	Fri 3/18/16	Tue 3/22/16
21		Garage Lighting	7 days	Mon 3/28/16	Tue 4/5/16
22		Insulate Lids	10 days	Wed 3/30/16	Tue 4/12/16
23					
24		**Site/Structure**	**20 days**	**Mon 3/7/16**	**Fri 4/1/16**
25		**North**	**20 days**	**Mon 3/7/16**	**Fri 4/1/16**
26		F&P Planters Transformer	5 days	Mon 3/7/16	Fri 3/11/16
27		Gas Main/Manifold	5 days	Mon 3/14/16	Fri 3/18/16
28		Install Gas Branch lines	3 days	Mon 3/21/16	Wed 3/23/16
29		Install Vault Grating and Gate	4 days	Thu 3/24/16	Tue 3/29/16
30		Set Transformer/Pull Mains	3 days	Wed 3/30/16	Fri 4/1/16
31					
32		**/Roofing**	**4 days**	**Mon 3/7/16**	**Thu 3/10/16**
33		**North/Southwest**	**4 days**	**Mon 3/7/16**	**Thu 3/10/16**
34		Scuppers	1 day	Mon 3/7/16	Mon 3/7/16

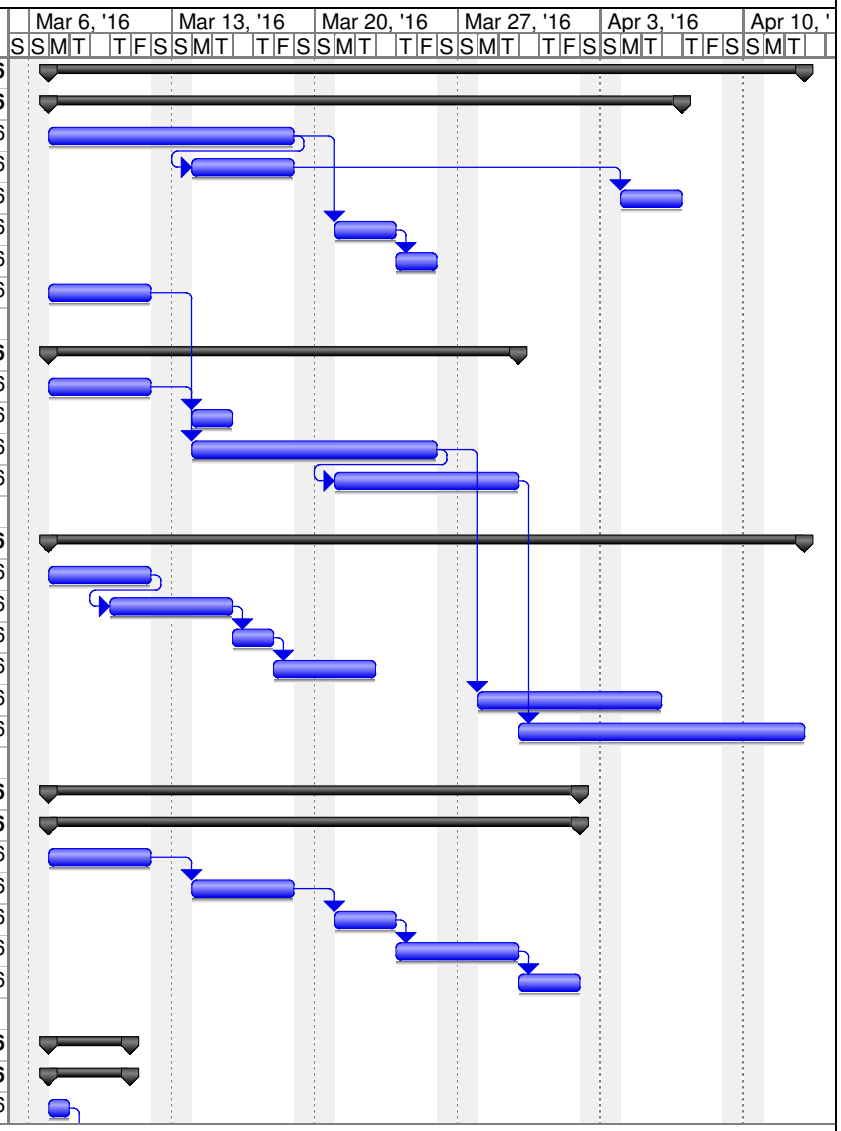

Project: 3wk 3-7-16
Date: Fri 3/4/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
3-7-2016

ID		Task Name	Duration	Start	Finish
35		Walk Mats	3 days	Tue 3/8/16	Thu 3/10/16
36		Carlisle Inspection	1 day	Mon 3/7/16	Mon 3/7/16
37		BCRA Inspection	1 day	Mon 3/7/16	Mon 3/7/16
38					
39		**Penthouses**	**12 days**	**Mon 3/7/16**	**Tue 3/22/16**
44		Tyvek	1 day	Mon 3/7/16	Mon 3/7/16
45		Battons/Siding	10 days	Tue 3/8/16	Mon 3/21/16
46		Joist Walkway	4 days	Tue 3/22/16	Fri 3/25/16
47					
48		**Exterior**	**13 days**	**Mon 3/7/16**	**Wed 3/23/16**
49		Rem Window Tests North,South Courtyard	1 day	Thu 3/10/16	Thu 3/10/16
50		**West**	**13 days**	**Mon 3/7/16**	**Wed 3/23/16**
51		Battons/Siding West, Courtyard,	10 days	Mon 3/7/16	Fri 3/18/16
52		Stucco	5 days	Mon 3/7/16	Fri 3/11/16
53		Caulking	6 days	Wed 3/16/16	Wed 3/23/16
54		Paint Mock-up	2 days	Mon 3/21/16	Tue 3/22/16
55		**North**	**13 days**	**Mon 3/7/16**	**Wed 3/23/16**
56		Battons	3 days	Mon 3/7/16	Wed 3/9/16
57		Stucco Prep	5 days	Thu 3/10/16	Wed 3/16/16
58		Siding	10 days	Thu 3/10/16	Wed 3/23/16
59		**Courtyard**	**18 days**	**Mon 3/7/16**	**Wed 3/30/16**
60		**North**	**18 days**	**Mon 3/7/16**	**Wed 3/30/16**
61		Battons	3 days	Mon 3/7/16	Wed 3/9/16
62		Siding	15 days	Thu 3/10/16	Wed 3/30/16
63		**East Perimeter**	**4 days**	**Mon 3/7/16**	**Thu 3/10/16**
64		Flashing	4 days	Mon 3/7/16	Thu 3/10/16
65		**South**	**12 days**	**Mon 3/7/16**	**Tue 3/22/16**
66		Stucco	2 days	Mon 3/7/16	Tue 3/8/16
67		Siding	10 days	Wed 3/9/16	Tue 3/22/16

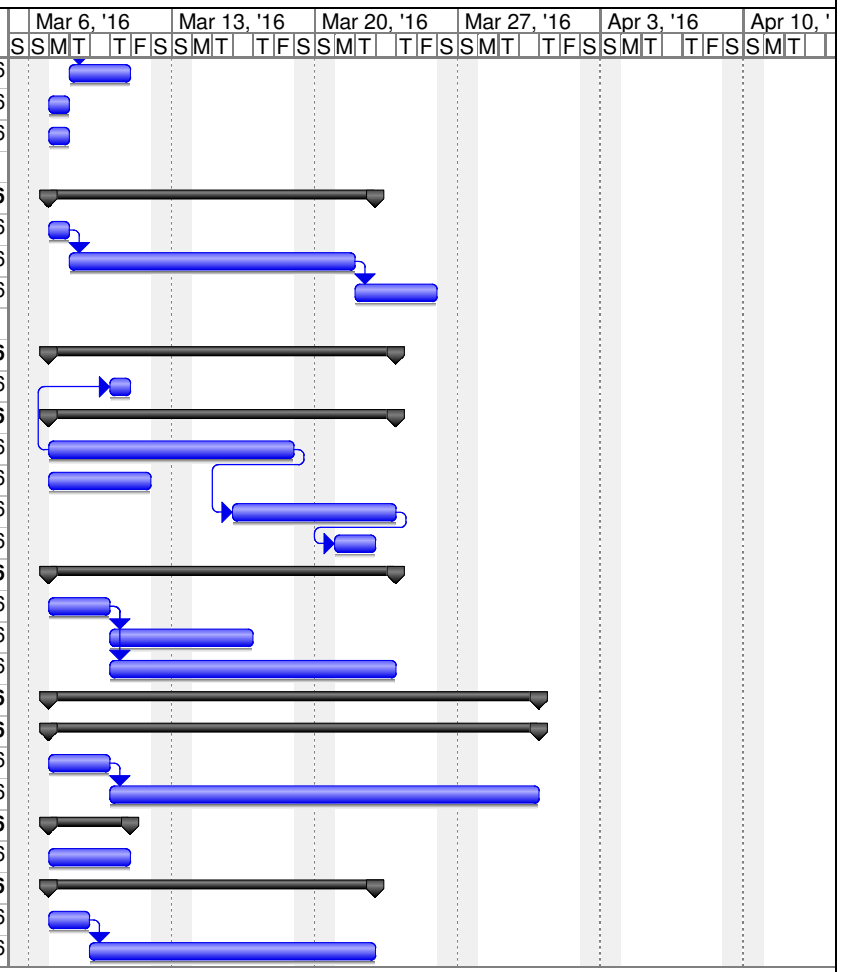

Project: 3wk 3-7-16
Date: Fri 3/4/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
3-7-2016

ID	Task Name	Duration	Start	Finish
1	**MEP Roof Down**	**76 days**	**Tue 1/12/16**	**Tue 4/26/16**
2	**L5 Zone 1 (South half)**	**34 days**	**Tue 1/12/16**	**Fri 2/26/16**
3	Electrical RI	5 days	Tue 1/12/16	Mon 1/18/16
4	Low volt RI	4 days	Wed 1/13/16	Mon 1/18/16
5	Plumbing/Electrical/Lowvolt Inspe	1 day	Tue 1/19/16	Tue 1/19/16
6	Fire Caulk	2 days	Wed 1/20/16	Thu 1/21/16
7	Insulate for pre rock at tubs	1 day	Fri 1/22/16	Fri 1/22/16
8	Pre rock for tubs/ accoustic	1 day	Mon 1/25/16	Mon 1/25/16
9	Framing inspection	1 day	Tue 1/26/16	Tue 1/26/16
10	Insulation	3 days	Wed 1/27/16	Fri 1/29/16
11	Insulation Inspection	1 day	Mon 2/1/16	Mon 2/1/16
12	Drywall Hang/Tape	10 days	Tue 2/2/16	Mon 2/15/16
13	Frame soffits	2 days	Tue 2/9/16	Wed 2/10/16
14	Electrical at soffits	1 day	Thu 2/11/16	Thu 2/11/16
15	Vent soffits	2 days	Fri 2/12/16	Mon 2/15/16
16	HVAC/ Electrical inspection at sof	1 day	Tue 2/16/16	Tue 2/16/16
17	Hang and tape soffits/Texture/PV/	5 days	Wed 2/17/16	Tue 2/23/16
18	Paint	3 days	Wed 2/24/16	Fri 2/26/16
19				
20	**L5 Zone 1 (North half)**	**43.5 days**	**Tue 1/19/16**	**Fri 3/18/16**
21	Electrical RI	5 days	Tue 1/19/16	Mon 1/25/16
22	Low volt RI	4 days	Wed 1/20/16	Mon 1/25/16
23	Plumbing/Electrical/Lowvolt Inspe	1 day	Tue 1/26/16	Tue 1/26/16
24	Fire Caulk	2 days	Wed 1/27/16	Thu 1/28/16
25	Insulate for pre rock at tubs	1 day	Fri 1/29/16	Fri 1/29/16
26	Pre rock for tubs/ accoustic	1 day	Mon 2/1/16	Mon 2/1/16
27	Framing inspection	1 day	Tue 2/2/16	Tue 2/2/16
28	Insulation	3 days	Wed 2/3/16	Fri 2/5/16
29	Insulation Inspection	1 day	Mon 2/8/16	Mon 2/8/16
30	Drywall Hang/Tape	10 days	Tue 2/9/16	Mon 2/22/16
31	Frame soffits	4 days	Tue 2/16/16	Fri 2/19/16
32	Electrical at soffits	1 day	Mon 2/22/16	Mon 2/22/16
33	Vent soffits	2 days	Tue 2/23/16	Wed 2/24/16
34	HVAC/ Electrical inspection at sof	4.5 days	Thu 2/25/16	Wed 3/2/16
35	Hang and tape soffits/Texture/PV/	10 days	Wed 3/2/16	Wed 3/16/16
36	Paint	2 days	Wed 3/16/16	Fri 3/18/16

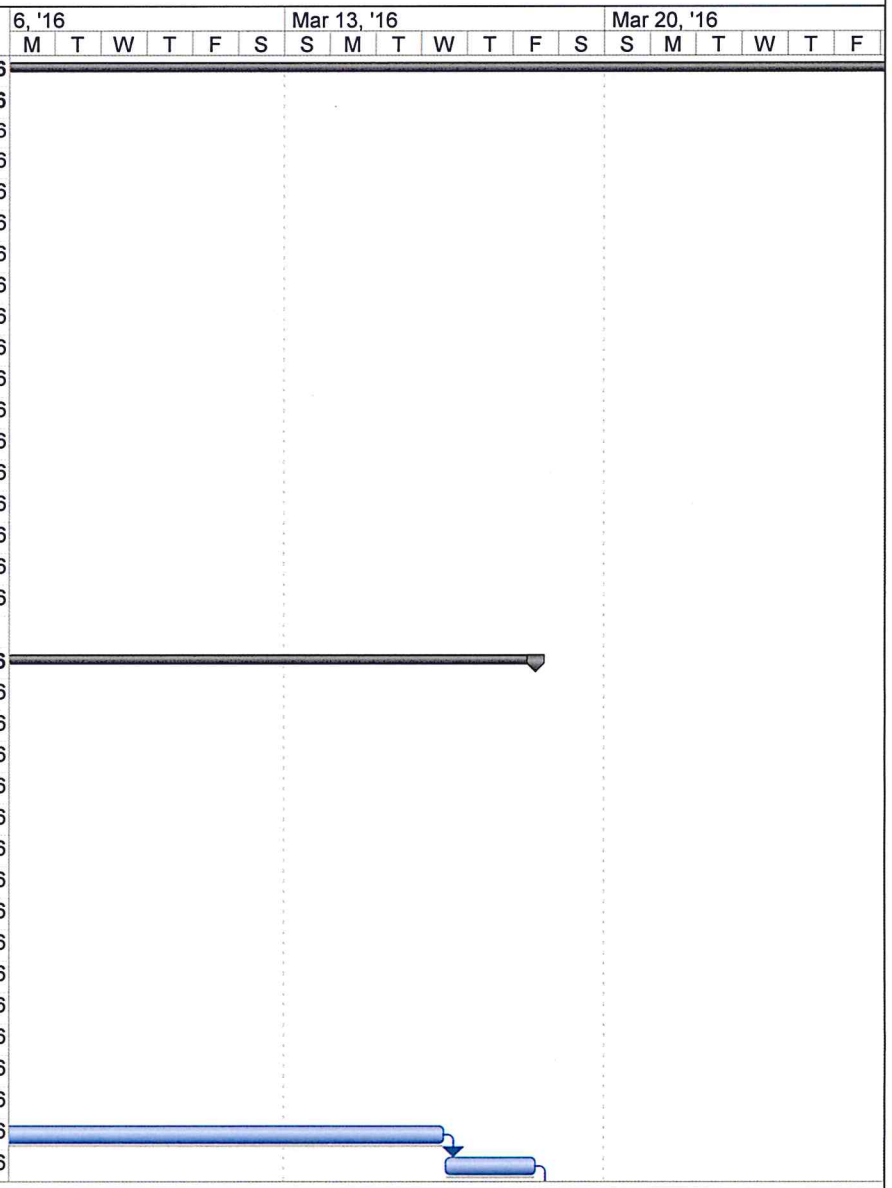

Project: MI MPE RI 3-7
Date: Mon 3/7/16

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

Hadley 3 Week Schedule (Interior)
3-7-2016

ID	Task Name	Duration	Start	Finish
37				
38	**L5 Zone 1 (West side)**	**66 days**	**Tue 1/26/16**	**Tue 4/26/16**
39	Gypcrete	3 days	Fri 3/18/16	Wed 3/23/16
40	Gypcrete dry time	10 days	Wed 3/23/16	Wed 4/6/16
41	Electrical trim	5 days	Wed 3/30/16	Wed 4/6/16
42	Install cabinets	5 days	Wed 4/6/16	Wed 4/13/16
43				
44	**L4 Zone 1 (South half)**	**34 days**	**Tue 1/26/16**	**Fri 3/11/16**
45	Electrical RI	5 days	Tue 1/26/16	Mon 2/1/16
46	Low volt RI	4 days	Wed 1/27/16	Mon 2/1/16
47	Plumbing/Electrical/Lowvolt I	1 day	Tue 2/2/16	Tue 2/2/16
48	Fire Caulk	2 days	Wed 2/3/16	Thu 2/4/16
49	Insulate for pre rock at tubs	1 day	Fri 2/5/16	Fri 2/5/16
50	Pre rock for tubs/ accoustic	1 day	Mon 2/8/16	Mon 2/8/16
51	Framing inspection	1 day	Tue 2/9/16	Tue 2/9/16
52	Insulation	3 days	Wed 2/10/16	Fri 2/12/16
53	Insulation Inspection	1 day	Mon 2/15/16	Mon 2/15/16
54	Drywall Hang/Tape	10 days	Tue 2/16/16	Mon 2/29/16
55	Frame soffits	2 days	Tue 2/23/16	Wed 2/24/16
56	Electrical at soffits	1 day	Thu 2/25/16	Thu 2/25/16
57	Vent soffits	2 days	Fri 2/26/16	Mon 2/29/16
58	HVAC/ Electrical inspection a	1 day	Tue 3/1/16	Tue 3/1/16
59	Hang and tape soffits/Texture	5 days	Wed 3/2/16	Tue 3/8/16
60	Paint	3 days	Wed 3/9/16	Fri 3/11/16
61				
62	**L4 Zone 1 (North half)**	**38 days**	**Tue 2/2/16**	**Thu 3/24/16**
63	Electrical RI	5 days	Tue 2/2/16	Mon 2/8/16
64	Low volt RI	4 days	Wed 2/3/16	Mon 2/8/16
65	Plumbing/Electrical/Lowvolt I	1 day	Tue 2/9/16	Tue 2/9/16
66	Fire Caulk	2 days	Wed 2/10/16	Thu 2/11/16
67	Insulate for pre rock at tubs	1 day	Fri 2/12/16	Fri 2/12/16
68	Pre rock for tubs/ accoustic	1 day	Mon 2/15/16	Mon 2/15/16
69	Framing inspection	1 day	Tue 2/16/16	Tue 2/16/16
70	Insulation	3 days	Wed 2/17/16	Fri 2/19/16
71	Insulation Inspection	3 days	Mon 2/22/16	Wed 2/24/16
72	Drywall Hang/Tape	10 days	Thu 2/25/16	Wed 3/9/16

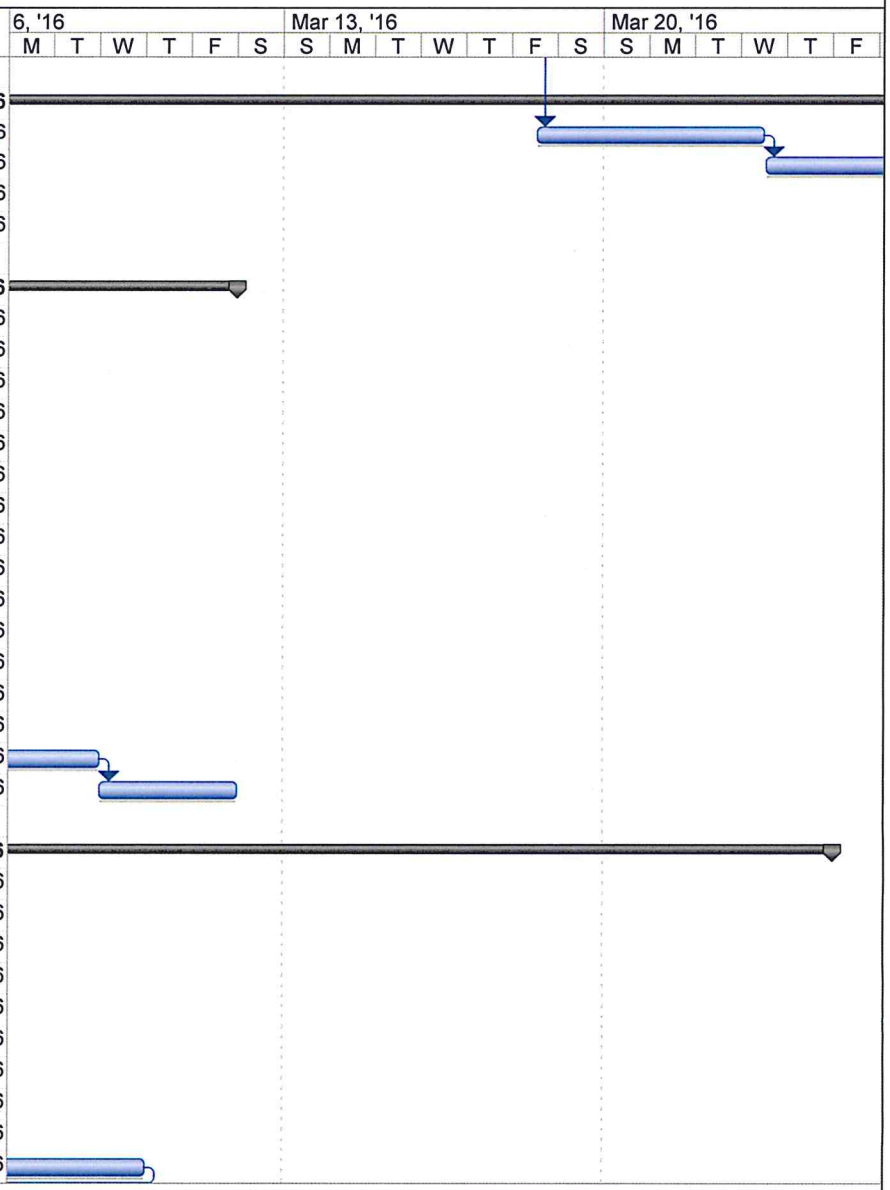

Project: MI MPE RI 3-7
Date: Mon 3/7/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
3-7-2016

ID	Task Name	Duration	Start	Finish
73	Frame soffits	2 days	Thu 3/3/16	Fri 3/4/16
74	Electrical at soffits	1 day	Mon 3/7/16	Mon 3/7/16
75	Vent soffits	2 days	Tue 3/8/16	Wed 3/9/16
76	HVAC/ Electrical inspection a	1 day	Thu 3/10/16	Thu 3/10/16
77	Hang and tape soffits/Texture	7 days	Fri 3/11/16	Mon 3/21/16
78	Paint	3 days	Tue 3/22/16	Thu 3/24/16
79				
80	**L4 Zone 1 (West side)**	**56 days**	**Tue 2/9/16**	**Tue 4/26/16**
81	Gypcrete	3 days	Fri 3/25/16	Tue 3/29/16
82	Gypcrete dry time	10 days	Wed 3/30/16	Tue 4/12/16
83	Electrical trim	5 days	Wed 4/6/16	Tue 4/12/16
84	Install cabinets	5 days	Wed 4/13/16	Tue 4/19/16
85				
86	**L3 Zone 1 (South half)**	**35 days**	**Tue 2/9/16**	**Mon 3/28/16**
87	Electrical RI	5 days	Tue 2/9/16	Mon 2/15/16
88	Low volt RI	4 days	Wed 2/10/16	Mon 2/15/16
89	Plumbing/Electrical/Low	1 day	Tue 2/16/16	Tue 2/16/16
90	Fire Caulk	2 days	Wed 2/17/16	Thu 2/18/16
91	Insulate for pre rock at tu	1 day	Fri 2/19/16	Fri 2/19/16
92	Pre rock for tubs/ accou:	2 days	Mon 2/22/16	Tue 2/23/16
93	Framing inspection	1 day	Wed 2/24/16	Wed 2/24/16
94	Insulation	3 days	Thu 2/25/16	Mon 2/29/16
95	Insulation Inspection	1 day	Tue 3/1/16	Tue 3/1/16
96	Drywall Hang/Tape	10 days	Wed 3/2/16	Tue 3/15/16
97	Frame soffits	2 days	Wed 3/9/16	Thu 3/10/16
98	Electrical at soffits	1 day	Fri 3/11/16	Fri 3/11/16
99	Vent soffits	2 days	Mon 3/14/16	Tue 3/15/16
100	HVAC/ Electrical inspect	1 day	Wed 3/16/16	Wed 3/16/16
101	Hang and tape soffits/Te	5 days	Thu 3/17/16	Wed 3/23/16
102	Paint	3 days	Thu 3/24/16	Mon 3/28/16
103				
104	**L3 Zone 1 (North half)**	**56 days**	**Tue 2/9/16**	**Tue 4/26/16**
105	Electrical RI	5 days	Tue 2/16/16	Mon 2/22/16
106	Low volt RI	3 days	Wed 2/17/16	Fri 2/19/16
107	Plumbing/Electrical/Low	1 day	Mon 2/22/16	Mon 2/22/16
108	Fire Caulk	1 day	Tue 2/23/16	Tue 2/23/16

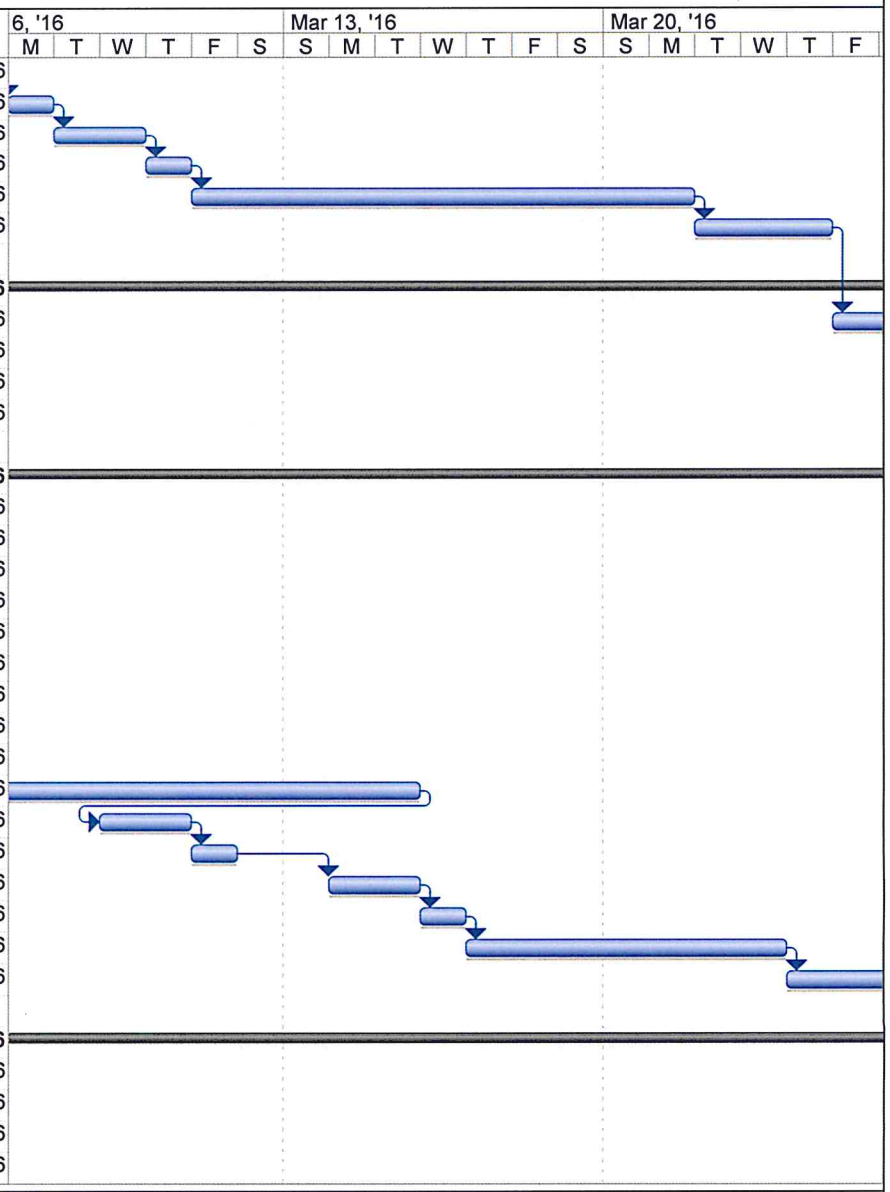

Project: MI MPE RI 3-7
Date: Mon 3/7/16

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

Hadley 3 Week Schedule (Interior)
3-7-2016

ID	Task Name	Duration	Start	Finish
109	Insulate for pre rock at tı	1 day	Wed 2/24/16	Wed 2/24/16
110	Pre rock for tubs/ accou:	1 day	Thu 2/25/16	Thu 2/25/16
111	Framing inspection	1 day	Fri 2/26/16	Fri 2/26/16
112	Insulation	5 days	Mon 2/29/16	Fri 3/4/16
113	Insulation Inspection	1 day	Mon 3/7/16	Mon 3/7/16
114	Drywall Hang/Tape	10 days	Tue 3/8/16	Mon 3/21/16
115	Frame soffits	2 days	Tue 3/15/16	Wed 3/16/16
116	Electrical at soffits	1 day	Thu 3/17/16	Thu 3/17/16
117	Vent soffits	2 days	Fri 3/18/16	Mon 3/21/16
118	HVAC/ Electrical inspecl	1 day	Tue 3/22/16	Tue 3/22/16
119	Hang and tape soffits/Te	5 days	Wed 3/23/16	Tue 3/29/16
120	Paint	3 days	Wed 3/30/16	Fri 4/1/16
121				
122	**L6 Zone 1 (South half)**	**32 days**	**Tue 2/9/16**	**Wed 3/23/16**
123	Electrical RI	5 days	Tue 2/9/16	Mon 2/15/16
124	Low volt RI	4 days	Wed 2/10/16	Mon 2/15/16
125	Plumbing/Electrical.	1 day	Tue 2/16/16	Tue 2/16/16
126	Fire Caulk	2 days	Wed 2/17/16	Thu 2/18/16
127	Insulate for pre rock	1 day	Fri 2/19/16	Fri 2/19/16
128	Pre rock for tubs/ a	1 day	Mon 2/22/16	Mon 2/22/16
129	Framing inspection	1 day	Tue 2/23/16	Tue 2/23/16
130	Insulation	1 day	Wed 2/24/16	Wed 2/24/16
131	Insulation Inspectio	1 day	Thu 2/25/16	Thu 2/25/16
132	Drywall Hang/Tape	10 days	Fri 2/26/16	Thu 3/10/16
133	Frame soffits	2 days	Fri 3/4/16	Mon 3/7/16
134	Electrical at soffits	1 day	Tue 3/8/16	Tue 3/8/16
135	Vent soffits	2 days	Wed 3/9/16	Thu 3/10/16
136	HVAC/ Electrical in:	1 day	Fri 3/11/16	Fri 3/11/16
137	Hang and tape soffi	5 days	Mon 3/14/16	Fri 3/18/16
138	Paint	3 days	Mon 3/21/16	Wed 3/23/16
139				
140	**L6 Zone 1 (North half)**	**38 days**	**Tue 2/9/16**	**Thu 3/31/16**
141	Electrical RI	5 days	Tue 2/9/16	Mon 2/15/16
142	Low volt RI	4 days	Wed 2/10/16	Mon 2/15/16
143	Plumbing/Electrical.	1 day	Tue 2/16/16	Tue 2/16/16
144	Fire Caulk	2 days	Wed 2/17/16	Thu 2/18/16

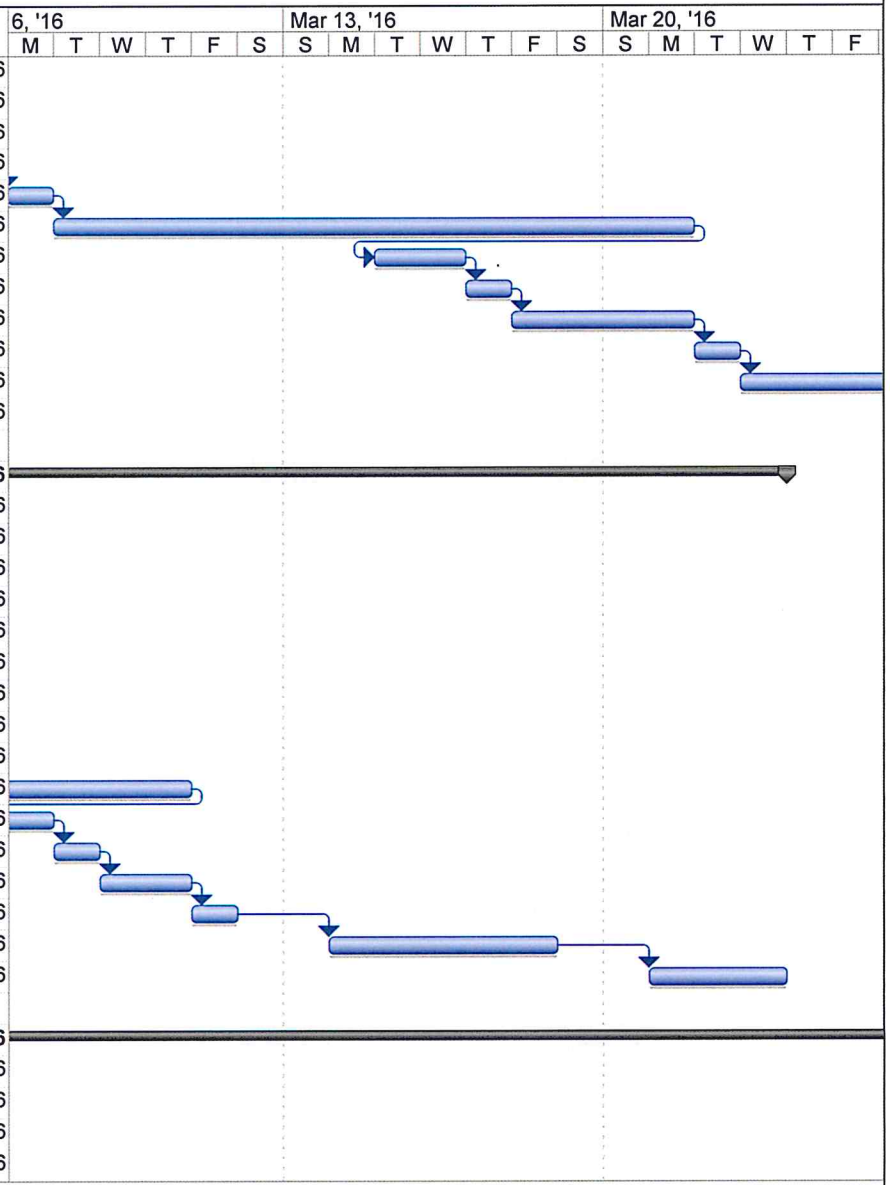

Project: MI MPE RI 3-7
Date: Mon 3/7/16

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

Hadley 3 Week Schedule (Interior)
3-7-2016

ID	Task Name	Duration	Start	Finish
145	Insulate for pre rock	1 day	Fri 2/19/16	Fri 2/19/16
146	Pre rock for tubs/ a	1 day	Mon 2/22/16	Mon 2/22/16
147	Framing inspection	1 day	Tue 2/23/16	Tue 2/23/16
148	Insulation	3 days	Wed 2/24/16	Fri 2/26/16
149	Insulation Inspectio	5 days	Mon 2/29/16	Fri 3/4/16
150	Drywall Hang/Tape	10 days	Mon 3/7/16	Fri 3/18/16
151	Frame soffits	2 days	Mon 3/14/16	Tue 3/15/16
152	Electrical at soffits	1 day	Wed 3/16/16	Wed 3/16/16
153	Vent soffits	2 days	Thu 3/17/16	Fri 3/18/16
154	HVAC/ Electrical in	1 day	Mon 3/21/16	Mon 3/21/16
155	Hang and tape soffi	5 days	Tue 3/22/16	Mon 3/28/16
156	Paint	3 days	Tue 3/29/16	Thu 3/31/16
157				
158	**L6 Zone 1 (West side)**	**18 days**	**Fri 4/1/16**	**Tue 4/26/16**
159	Gypcrete	3 days	Fri 4/1/16	Tue 4/5/16
160	Gypcrete dry time	10 days	Wed 4/6/16	Tue 4/19/16
161	Electrical trim	5 days	Wed 4/13/16	Tue 4/19/16
162	Install cabinets	5 days	Wed 4/20/16	Tue 4/26/16

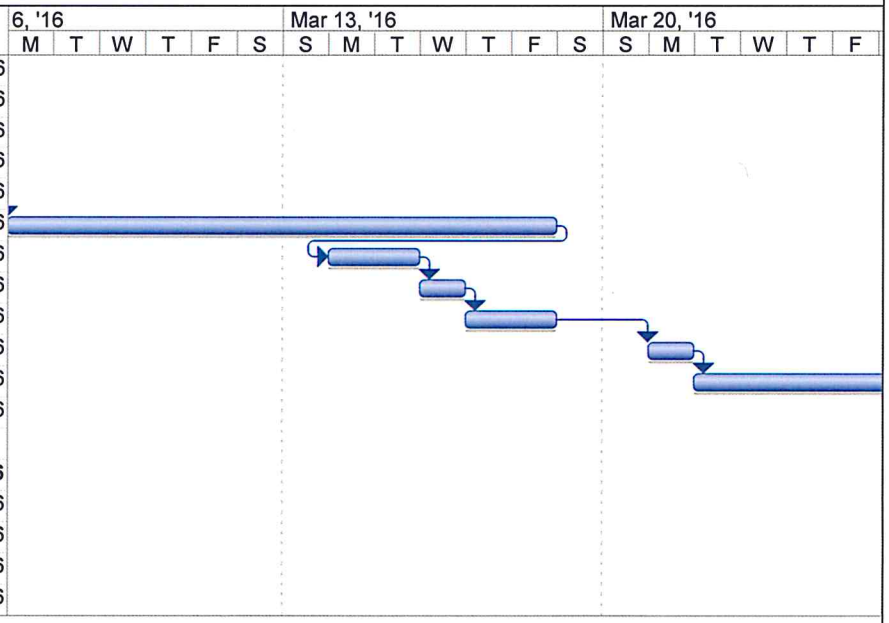

Project: MI MPE RI 3-7
Date: Mon 3/7/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
