CHINN
CONSTRUCTION, LLC

CONSTRUCTION SUBCONTRACTOR MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Jobsite Office**

MEETING #: **57**

MEETING DATE: **04/5/16**

ATTENDEES:

~~Mike Kalvelage – CHINN~~
Mark Pesanti – CHINN
Charlie Poggemann – CHINN
Sim Mooers – CHINN
~~Lauren Bjorndahl – CHINN~~
Eric Bull – CHINN
Kyle – Froula
~~Jason – CFM~~
Richard Donelson - OWP
~~George Falor - CHINN~~
~~Casey Hutchison - SS~~
Kenny - Axiom
Jose Mendina – Advanced
Gary – Prec. Wall
Ross Porterfield – IEC
John Perillo – WCP

SAFETY: **TRASH CHUTE**

- **Do not enter dumpster to rearrange trash without marking gates prior to.**
- **Make sure debris is small enough to fit in chute.**
- **Keep arms and head out of chute.**
- **Glass Sliders have been installed and protected at chutes Please be carefull not to damage frame.**
- **Donot throw shovels full of floor sweeping down the chute as they make a dust cloud that drifts through the neighborhood.**

General

- **Safety meetings have been moved to Monday's at 12:45 due to lack of personel showing up at the 7:00 AM meeting time. It is a contractual requirement that all employees attend these and sign-in.**

- **Observations have been made onsite of numerous employees not wearing reflective Vests and Hard hats in and around the site. The requirements for both the vests and hats have been relaxed while working in the interior of the units and corridors. Any Exterior work and Access/Egress to and from still requires reflective vest and hard hats at all times.**

Deliveries

- **With the increasing amount of work on the interior and exterior our deliveries have greatly increased in number and will get even more difficult to manage in the future. It is imperative that these are coordinated on the board and reviewed by each sub as to not overlap with others. In order to do this Chinn asks that each sub pick their day, overall time and location for each and show that on the board.**

- **Soon there will be Scaffold removal and Civil/Sitework subs onboard in which deliveries to certain elevations will need to be scheduled off hours unless they can be accommodated during normal business hours.**

46.01 Housekeeping

- No smoking onsite
- Roof is cleaned and punched. Do not place material on it without protection.
- There is no food allowed above Level 2
- Use the delivery board for all deliveries.
- Do not remove temporary screens in the deck drains
- Do not plug cords into the string lights, Do not flip spider boxes on their sides
- See Site Superindent for parking passes.
- All personel to be masked in areas of sandblasting East or remain out of the area.
- Chinn provided a reach Forklift that will better service loads to the Courtyard etc. Be certain that your operator is got their credentials..

SCHEDULE:

46.02 Reviewed **SITE** 3 wk look ahead schedule beginning 4/4/16

- Gas Sleeve complete/Gas Main anticipated in 2 weeks
- Switchgear set Need to close wall and plywood for Comm boxes
- Site Structure –

- Comcast, Wave, Direct TV, Century Link and Froula met with Chinn onsite to review and mark-up space for their equipment in Comm and Electrical Rooms.
- Set Remainder of Doors.windows Level 2 4/6/16 and remove all extra stock from units
- Paint will resume West followed by Courtyard next week
- Exterior – Precision adding to crew for production siding to start.
  - North --,Complete ready for siding/stucco L 3,4,5
    East Stucco started as well as Hardie

46.03 Reviewed **INTERIOR** 3wk look ahead schedule beginning 3/7/16

- 01/12/16: Temp heat is on
  - All shafts are in need of rock as not to delay power, HVAC etc.
  - Gypcrete Continues West and North
-
  - Elevator Permit acquired and work is ongoing by Otis

OLD BUSINESS:

38.09 Unit venting in for permit. No new news?

41.08 New direction on garage exhaust in for plan review No word yet as of 4/4/16

41.12 CHINN to schedule a handrail mock up. WCP, SS, and CHINN to attend for backing

purposes.
12/29/15: Wood handrail mock up is installed. CHINN to check on metal handrail.

44.04 Northwest gone until scaffold demob East

44.07 IEC needs the corridor ventilation shafts framed to rough in electrical.

44.08 CFM to complete Roof equip etc.

44.09 Need repairs/conpleteion siding to continue painting

44.10 Hollow metal leafs arrived 2/29

44.11 Additional Temp heat for East this week

PERMIT STATUS:	**HVAC** – Jason /Jeremy met with Chinn, Legacy, Via and the COMI on Friday 1-22-16 to discuss and resolve permit issues between CFM drawings and the City,s comments. Nine out of eleven issues were resolved and CFM will make corrections and resubmit and the plans examiner stated they will approve the drawings and allow acquisition of the permit by this Friday
Update	Via/ CFM to redesign Garage Exhaust due to code issues with existing. This is holding up permit until new plan is reviewed.
Latest	**CFM submittal questions answed now Legacy in line for missing info.**

RFIs: 44.09 RFI 217 – Patio Light Fixture Location – A couple of locations that are listed C4, C3, J, and G will not work. LB to email Architect.

NEW BUSINESS:

46.04 Wave and CenturyLink, Comcast Vaults/Conduit complete

46.05 The Roof top Mech units need to have flashing and isolation from the TPO. The fan for Stair 1 also needs relocation. Complete

46.06 SS stated the Earthbound System is complete.

46.07 Power from the Crane will be used for the Elevator

46.08 Elevator Permit in hand Otis start Monday

46.08 BCRA to Window re-test 3/2316. Inspections Complete

NEXT MEETING: 4/11/16, time 10:00, at Jobsite office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
4-4-2016

EXTERIORS

ID	Task Name	Duration	Start	Finish
1	**Garage**	**18 days**	**Mon 4/4/16**	**Wed 4/27/16**
2	**Level P**	**5 days**	**Mon 4/4/16**	**Fri 4/8/16**
3	Swing Elect HM doors	1 day	Mon 4/4/16	Mon 4/4/16
4	Light Fixtures Garage	5 days	Mon 4/4/16	Fri 4/8/16
5	Set Str 2 HM Frame	1 day	Mon 4/4/16	Mon 4/4/16
6	Complete Sheetrock	2 days	Mon 4/4/16	Tue 4/5/16
7				
8	**Level 1**	**13 days**	**Mon 4/4/16**	**Wed 4/20/16**
9	Swing HM	1 day	Tue 4/5/16	Tue 4/5/16
10	Garage Light Fixtures	5 days	Tue 4/5/16	Mon 4/11/16
11	Stick Pin/Insulate Lid	7 days	Tue 4/12/16	Wed 4/20/16
12	Complete Sheetrock	2 days	Mon 4/4/16	Tue 4/5/16
13	Swing Doors	1 day	Wed 4/6/16	Wed 4/6/16
14				
15	**Level 2**	**18 days**	**Mon 4/4/16**	**Wed 4/27/16**
16	Tyvek Wrap	1 day	Mon 4/4/16	Mon 4/4/16
17	Set Exterior Doors/Windows	3 days	Tue 4/5/16	Thu 4/7/16
18	Insulate Rem Walls	5 days	Thu 4/21/16	Wed 4/27/16
19	Garage Lights	5 days	Mon 4/4/16	Fri 4/8/16
20				
21	**Site/Structure**	**17 days**	**Fri 4/8/16**	**Mon 5/2/16**
22	**North**	**17 days**	**Fri 4/8/16**	**Mon 5/2/16**
23	Gas Main/Manifold	5 days	Fri 4/8/16	Thu 4/14/16
24	Install Gas Branch lines	3 days	Fri 4/15/16	Tue 4/19/16
25	Set Transformer/Pull Mains	3 days	Wed 4/20/16	Fri 4/22/16
26	Permanent Power	2 days	Mon 4/25/16	Tue 4/26/16
27	Set Unit Meters	4 days	Wed 4/27/16	Mon 5/2/16
28	Demob Temp Power	1 day	Fri 4/29/16	Fri 4/29/16
29				
30	**/Roofing**	**5 days**	**Mon 4/4/16**	**Fri 4/8/16**
31	**North/Southwest**	**5 days**	**Mon 4/4/16**	**Fri 4/8/16**
32	Walk Mats	3 days	Mon 4/4/16	Wed 4/6/16
33	Carlisle Inspection	1 day	Thu 4/7/16	Thu 4/7/16
34	BCRA Inspection	1 day	Fri 4/8/16	Fri 4/8/16

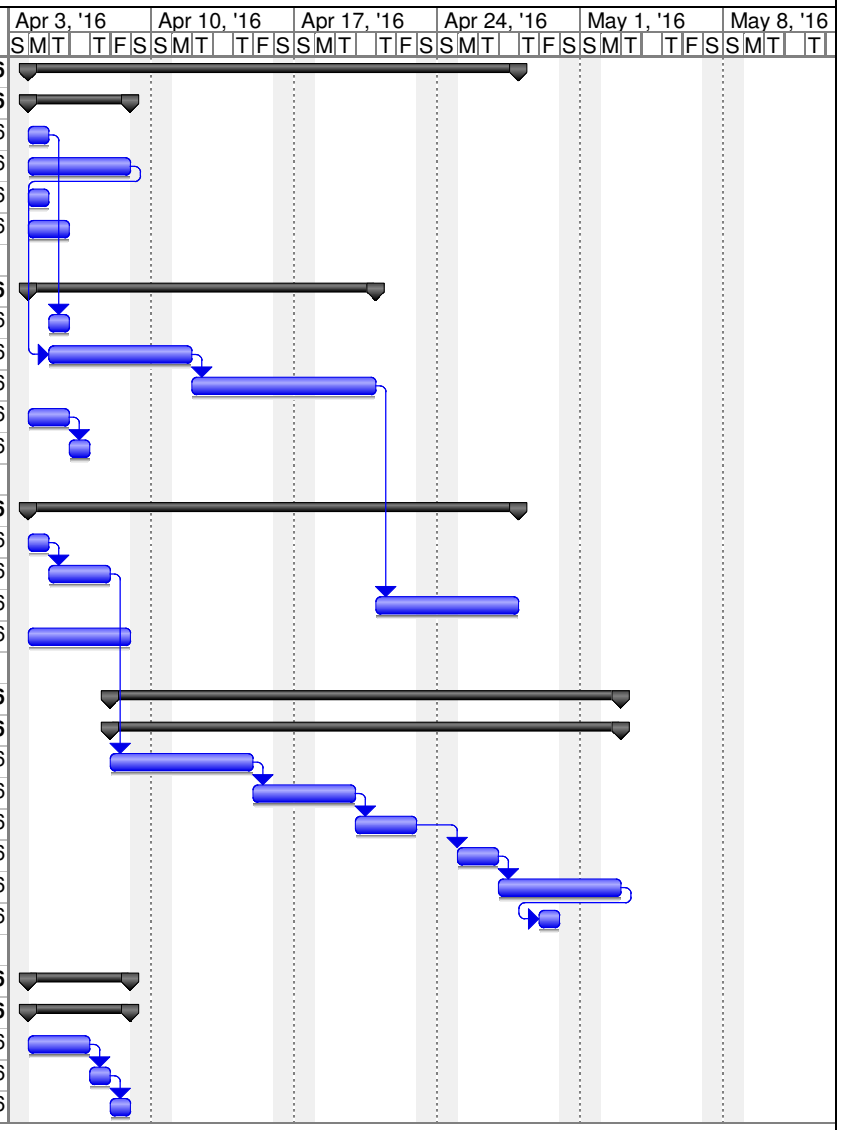

Project: 3wk 4-4-16 3wk
Date: Sat 4/2/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
4-4-2016

ID		Task Name	Duration	Start	Finish
35		**Penthouses**	**12 days**	**Mon 4/4/16**	**Tue 4/19/16**
40		Battons	3 days	Mon 4/4/16	Wed 4/6/16
41					
42		**Exterior**	**20 days?**	**Mon 4/4/16**	**Fri 4/29/16**
43		**West**	**20 days?**	**Mon 4/4/16**	**Fri 4/29/16**
44		Rem Stucco	5 days	Mon 4/4/16	Fri 4/8/16
45		Paint	5 days	Mon 4/4/16	Fri 4/8/16
46		Caukling	5 days	Mon 4/11/16	Fri 4/15/16
47		Inspection	1 day	Mon 4/18/16	Mon 4/18/16
48		Deck Tie Rods	1 day?	Tue 4/19/16	Tue 4/19/16
49		Remove Scafflod	3 days	Wed 4/20/16	Fri 4/22/16
50		Set Decks	5 days	Mon 4/25/16	Fri 4/29/16
51		**North**	**15 days**	**Mon 4/4/16**	**Fri 4/22/16**
52		Stucco	5 days	Mon 4/4/16	Fri 4/8/16
53		Siding	10 days	Mon 4/11/16	Fri 4/22/16
54		Tyvek L2	2 days	Mon 4/4/16	Tue 4/5/16
55					
56		**Courtyard**	**28 days?**	**Mon 4/4/16**	**Wed 5/11/16**
57		Siding/Panels	5 days	Mon 4/4/16	Fri 4/8/16
58		Sill Flashing	4 days	Wed 4/6/16	Mon 4/11/16
59		Paint	10 days	Fri 4/15/16	Thu 4/28/16
60		Caulk	4 days	Fri 4/29/16	Wed 5/4/16
61		Inspect	1 day	Thu 5/5/16	Thu 5/5/16
62		Remove Scaffolding	4 days	Fri 5/6/16	Wed 5/11/16
63		Deck Tie Rods	1 day?	Mon 4/4/16	Mon 4/4/16
64					
65		**East Perimeter**	**20 days**	**Mon 4/4/16**	**Fri 4/29/16**
66		Flashing	2 days	Mon 4/4/16	Tue 4/5/16
67		Stucco	4 days	Mon 4/4/16	Thu 4/7/16
68		Siding	13 days	Wed 4/6/16	Fri 4/22/16
69		Flashings/Storefront	15 days	Mon 4/11/16	Fri 4/29/16
70		**South**	**9 days**	**Mon 4/4/16**	**Thu 4/14/16**
71		Stucco	5 days	Mon 4/4/16	Fri 4/8/16
72		Siding	4 days	Mon 4/11/16	Thu 4/14/16

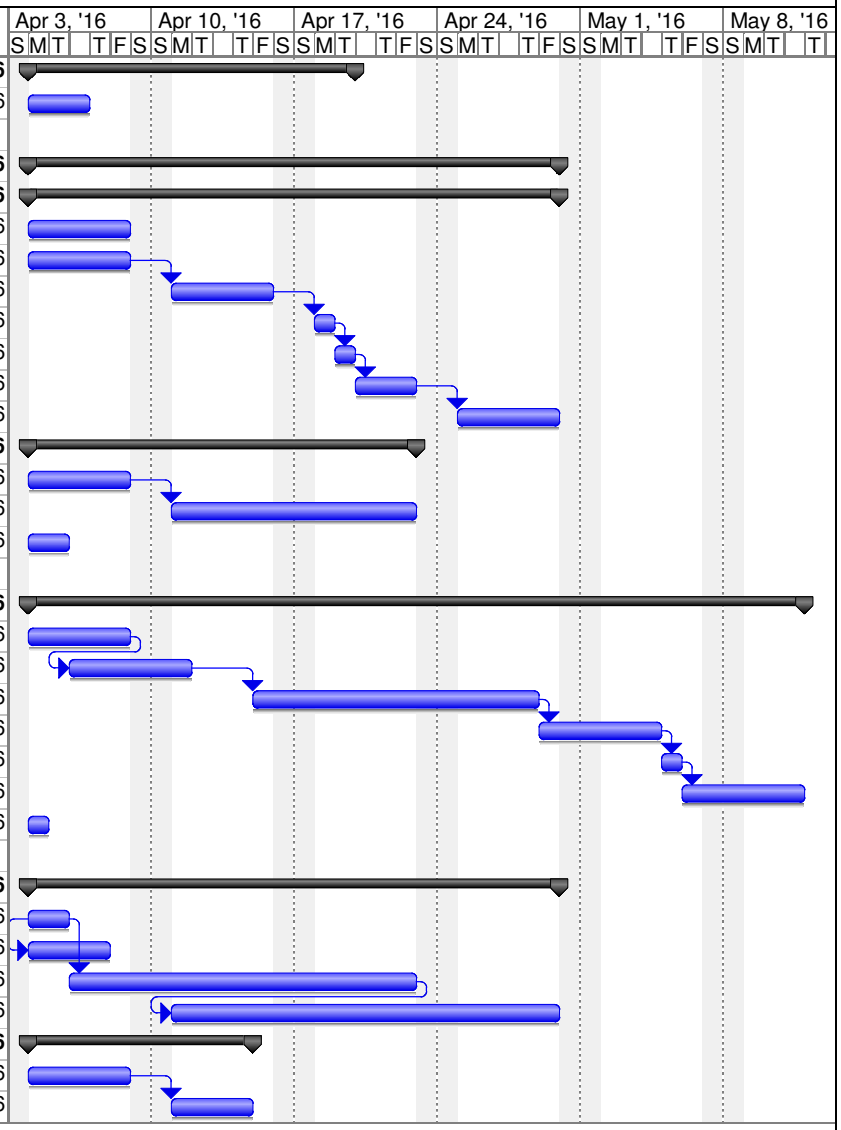

Project: 3wk 4-4-16 3wk
Date: Sat 4/2/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley 3 Week Schedule (Interior)
3-25-2016

INTERIORS

ID	Task Name	Duration	Start	Finish
1	**MEP Roof Down**	**122 days?**	**Tue 3/8/16**	**Wed 8/24/16**
2	**L5 Zone 1 (532-561)**	**79 days?**	**Tue 3/8/16**	**Fri 6/24/16**
3	Hang and tape soffits/Texture/PV/	7 days	Tue 3/8/16	Wed 3/16/16
4	Paint	2 days	Thu 3/17/16	Fri 3/18/16
5	Gypcrete	3 days	Mon 3/21/16	Wed 3/23/16
6	Gypcrete dry time	10 days	Thu 3/24/16	Wed 4/6/16
7	Electrical trim	5 days	Thu 3/31/16	Wed 4/6/16
8	Fire/Sprinkler Trim	1 day?	Thu 3/31/16	Thu 3/31/16
9	Install cabinets	6 days	Mon 4/4/16	Mon 4/11/16
10	Install Flooring	5 days	Tue 4/12/16	Mon 4/18/16
11	Install counter tops	3 days	Tue 4/19/16	Thu 4/21/16
12	Intsall Backsplash	3 days	Fri 4/22/16	Tue 4/26/16
13	Doors and Millwork	5 days	Wed 4/27/16	Tue 5/3/16
14	Paint doors and millwork	10 days	Wed 5/4/16	Tue 5/17/16
15	Closet Shelves	3 days	Wed 5/18/16	Fri 5/20/16
16	Deliver Appliances	3 days	Wed 5/18/16	Fri 5/20/16
17	Plumbing trim	4 days	Mon 5/23/16	Thu 5/26/16
18	Final Paint Walls	3 days	Fri 5/27/16	Tue 5/31/16
19	Window coverings	2 days	Wed 6/1/16	Thu 6/2/16
20	Final Clean	6 days	Fri 6/3/16	Fri 6/10/16
21	Punch List	7 days	Mon 6/13/16	Tue 6/21/16
22	Fluff Clean	3 days	Wed 6/22/16	Fri 6/24/16
23				
24	**L4 Zone 1 (432-461)**	**83 days?**	**Thu 3/10/16**	**Mon 7/4/16**
25	Drywall Hang/Tape	5 days	Thu 3/10/16	Wed 3/16/16
26	Hang and tape soffits/Texture/PV/	5 days	Thu 3/17/16	Wed 3/23/16
27	Paint	2 days	Mon 3/28/16	Tue 3/29/16
28	Gypcrete	3 days	Wed 3/30/16	Fri 4/1/16
29	Gypcrete dry time	10 days	Mon 4/4/16	Fri 4/15/16
30	Electrical trim	5 days	Mon 4/11/16	Fri 4/15/16
31	Fire/Sprinkler Trim	1 day?	Mon 4/11/16	Mon 4/11/16
32	Install cabinets	6 days	Wed 4/13/16	Wed 4/20/16
33	Install Flooring	5 days	Thu 4/21/16	Wed 4/27/16
34	Install counter tops	3 days	Thu 4/28/16	Mon 5/2/16
35	Intsall Backsplash	3 days	Tue 5/3/16	Thu 5/5/16
36	Doors and Millwork	5 days	Fri 5/6/16	Thu 5/12/16

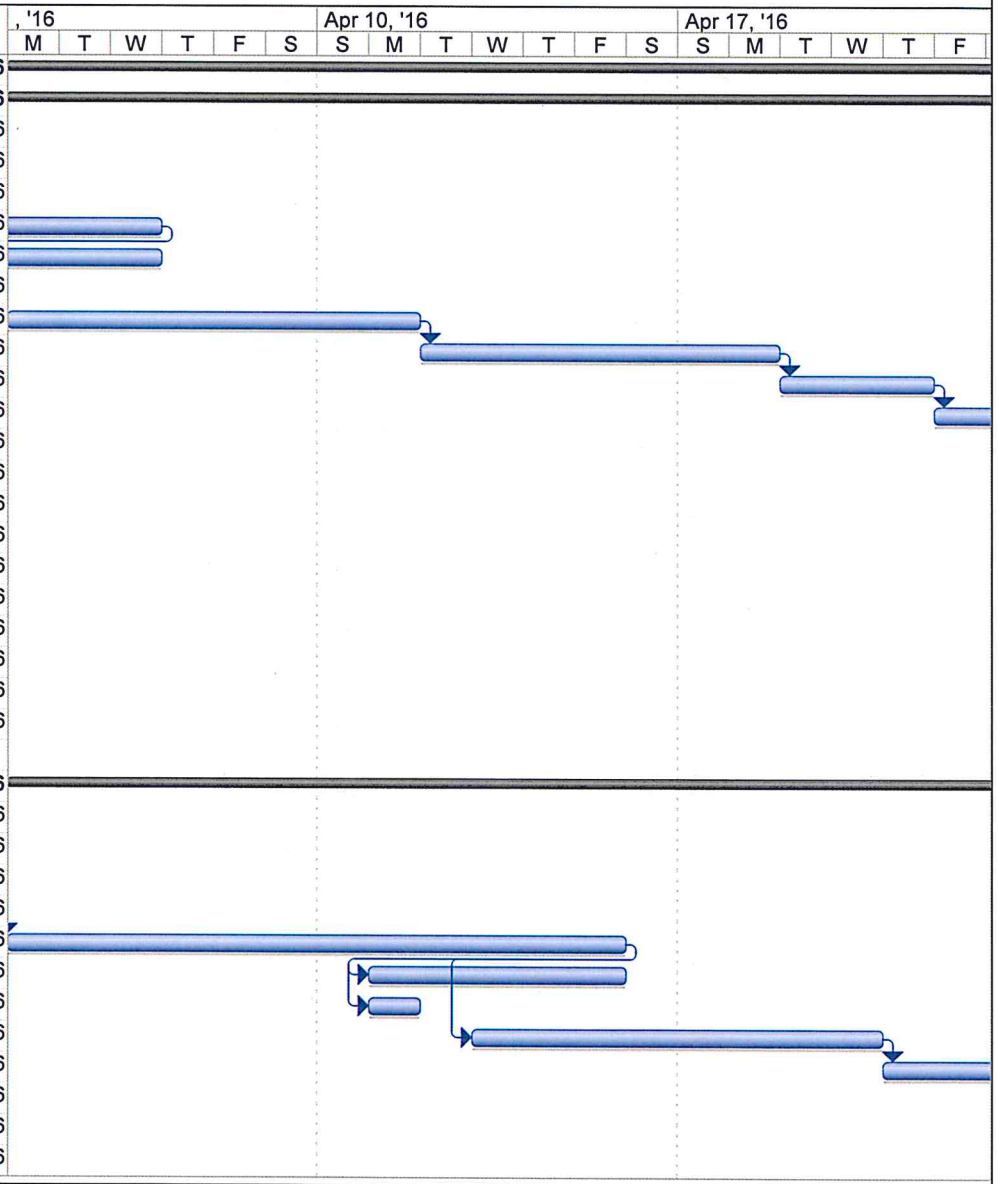

Project: MI Finish 4-4
Date: Mon 4/4/16

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

Hadley 3 Week Schedule (Interior)
3-25-2016

ID	Task Name	Duration	Start	Finish
37	Paint doors and millwork	10 days	Fri 5/13/16	Thu 5/26/16
38	Closet Shelves	3 days	Fri 5/27/16	Tue 5/31/16
39	Deliver Appliances	3 days	Fri 5/27/16	Tue 5/31/16
40	Plumbing trim	4 days	Wed 6/1/16	Mon 6/6/16
41	Final Paint Walls	3 days	Tue 6/7/16	Thu 6/9/16
42	Window coverings	2 days	Fri 6/10/16	Mon 6/13/16
43	Final Clean	5 days	Tue 6/14/16	Mon 6/20/16
44	Punch List	7 days	Tue 6/21/16	Wed 6/29/16
45	Fluff Clean	3 days	Thu 6/30/16	Mon 7/4/16
46				
47	**L6 Zone 1 (632-661)**	**87 days?**	**Thu 3/17/16**	**Fri 7/15/16**
48	Drywall Hang/Tape	5 days	Thu 3/17/16	Wed 3/23/16
49	Hang and tape soffits/Texture/PV/	9 days	Thu 3/24/16	Tue 4/5/16
50	Paint	3 days	Wed 4/6/16	Fri 4/8/16
51	Gypcrete	3 days	Mon 4/11/16	Wed 4/13/16
52	Gypcrete dry time	10 days	Thu 4/14/16	Wed 4/27/16
53	Electrical trim	5 days	Thu 4/21/16	Wed 4/27/16
54	Fire/Sprinkler Trim	1 day?	Thu 4/21/16	Thu 4/21/16
55	Install cabinets	6 days	Mon 4/25/16	Mon 5/2/16
56	Install Flooring	5 days	Tue 5/3/16	Mon 5/9/16
57	Install counter tops	3 days	Tue 5/10/16	Thu 5/12/16
58	Intsall Backsplash	3 days	Fri 5/13/16	Tue 5/17/16
59	Doors and Millwork	5 days	Wed 5/18/16	Tue 5/24/16
60	Paint doors and millwork	10 days	Wed 5/25/16	Tue 6/7/16
61	Closet Shelves	3 days	Wed 6/8/16	Fri 6/10/16
62	Deliver Appliances	3 days	Wed 6/8/16	Fri 6/10/16
63	Plumbing trim	4 days	Mon 6/13/16	Thu 6/16/16
64	Final Paint Walls	3 days	Fri 6/17/16	Tue 6/21/16
65	Window coverings	2 days	Wed 6/22/16	Thu 6/23/16
66	Final Clean	6 days	Fri 6/24/16	Fri 7/1/16
67	Punch List	7 days	Mon 7/4/16	Tue 7/12/16
68	Fluff Clean	3 days	Wed 7/13/16	Fri 7/15/16
69				
70	**L3 Zone 1 (332-360)**	**85 days**	**Mon 3/14/16**	**Fri 7/8/16**
71	Insulation Inspection	1 day	Mon 3/14/16	Mon 3/14/16
72	Drywall Hang/Tape	10 days	Tue 3/15/16	Mon 3/28/16

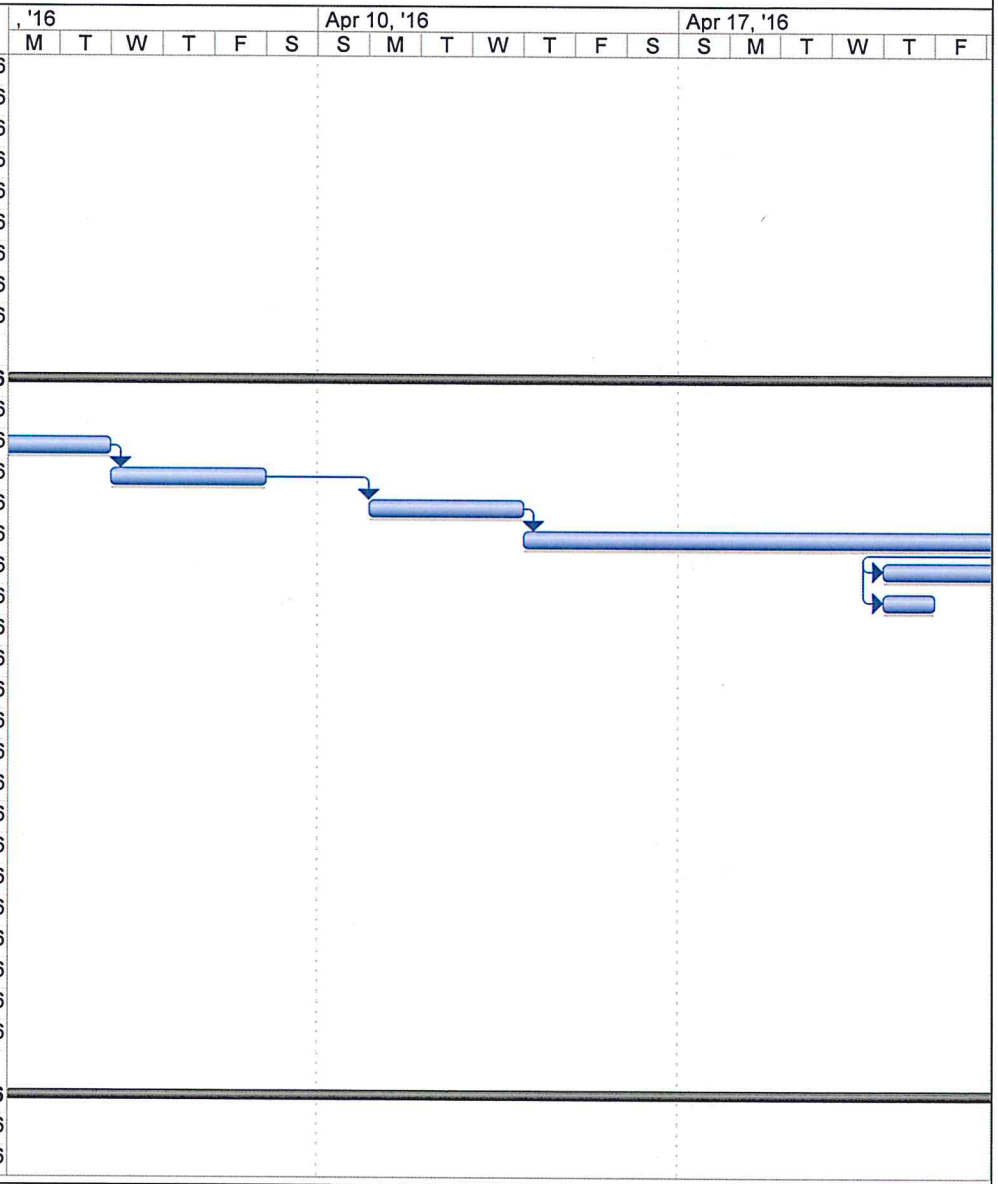

Project: MI Finish 4-4
Date: Mon 4/4/16

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

Hadley 3 Week Schedule (Interior)
3-25-2016

ID	Task Name	Duration	Start	Finish
73	Frame soffits	2 days	Tue 3/22/16	Wed 3/23/16
74	Electrical at soffits	1 day	Thu 3/24/16	Thu 3/24/16
75	Vent soffits	2 days	Mon 3/28/16	Tue 3/29/16
76	HVAC/ Electrical inspection at sof	1 day	Wed 3/30/16	Wed 3/30/16
77	Hang and tape soffits/Texture/PV/	8 days	Thu 3/31/16	Mon 4/11/16
78	Paint	3 days	Tue 4/12/16	Thu 4/14/16
79	Electrical trim	5 days	Fri 4/15/16	Thu 4/21/16
80	Fire/Sprinkler Trim	1 day	Fri 4/15/16	Fri 4/15/16
81	Install cabinets	6 days	Mon 4/18/16	Mon 4/25/16
82	Install Flooring	5 days	Tue 4/26/16	Mon 5/2/16
83	Install counter tops	3 days	Tue 5/3/16	Thu 5/5/16
84	Intsall Backsplash	3 days	Fri 5/6/16	Tue 5/10/16
85	Doors and Millwork	5 days	Wed 5/11/16	Tue 5/17/16
86	Paint doors and millwork	10 days	Wed 5/18/16	Tue 5/31/16
87	Closet Shelves	3 days	Wed 6/1/16	Fri 6/3/16
88	Deliver Appliances	3 days	Wed 6/1/16	Fri 6/3/16
89	Plumbing trim	4 days	Mon 6/6/16	Thu 6/9/16
90	Final Paint Walls	3 days	Fri 6/10/16	Tue 6/14/16
91	Window coverings	2 days	Wed 6/15/16	Thu 6/16/16
92	Final Clean	6 days	Fri 6/17/16	Fri 6/24/16
93	Punch List	7 days	Mon 6/27/16	Tue 7/5/16
94	Fluff Clean	3 days	Wed 7/6/16	Fri 7/8/16
95				
96	**L5 Zone 2 (501-531)**	**106 days**	**Wed 3/30/16**	**Wed 8/24/16**
97	Pre-rock at tubs	1 day	Wed 3/30/16	Wed 3/30/16
98	Install tubs	3 days	Thu 3/31/16	Mon 4/4/16
99	Shower remodel	6 days	Tue 4/5/16	Tue 4/12/16
100	Elec, Plmb Inspections	2 days	Mon 4/11/16	Tue 4/12/16
101	Fire Caulk	2 days	Wed 4/13/16	Thu 4/14/16
102	Framing inspection	2 days	Fri 4/15/16	Mon 4/18/16
103	Insulation	3 days	Tue 4/19/16	Thu 4/21/16
104	Insulation Inspection	1 day	Fri 4/22/16	Fri 4/22/16
105	Drywall Hang/Tape	5 days	Mon 4/25/16	Fri 4/29/16
106	Frame soffits	5 days	Fri 4/29/16	Thu 5/5/16
107	Electrical at soffits	2 days	Wed 5/4/16	Thu 5/5/16
108	Vent soffits	5 days	Wed 5/4/16	Tue 5/10/16

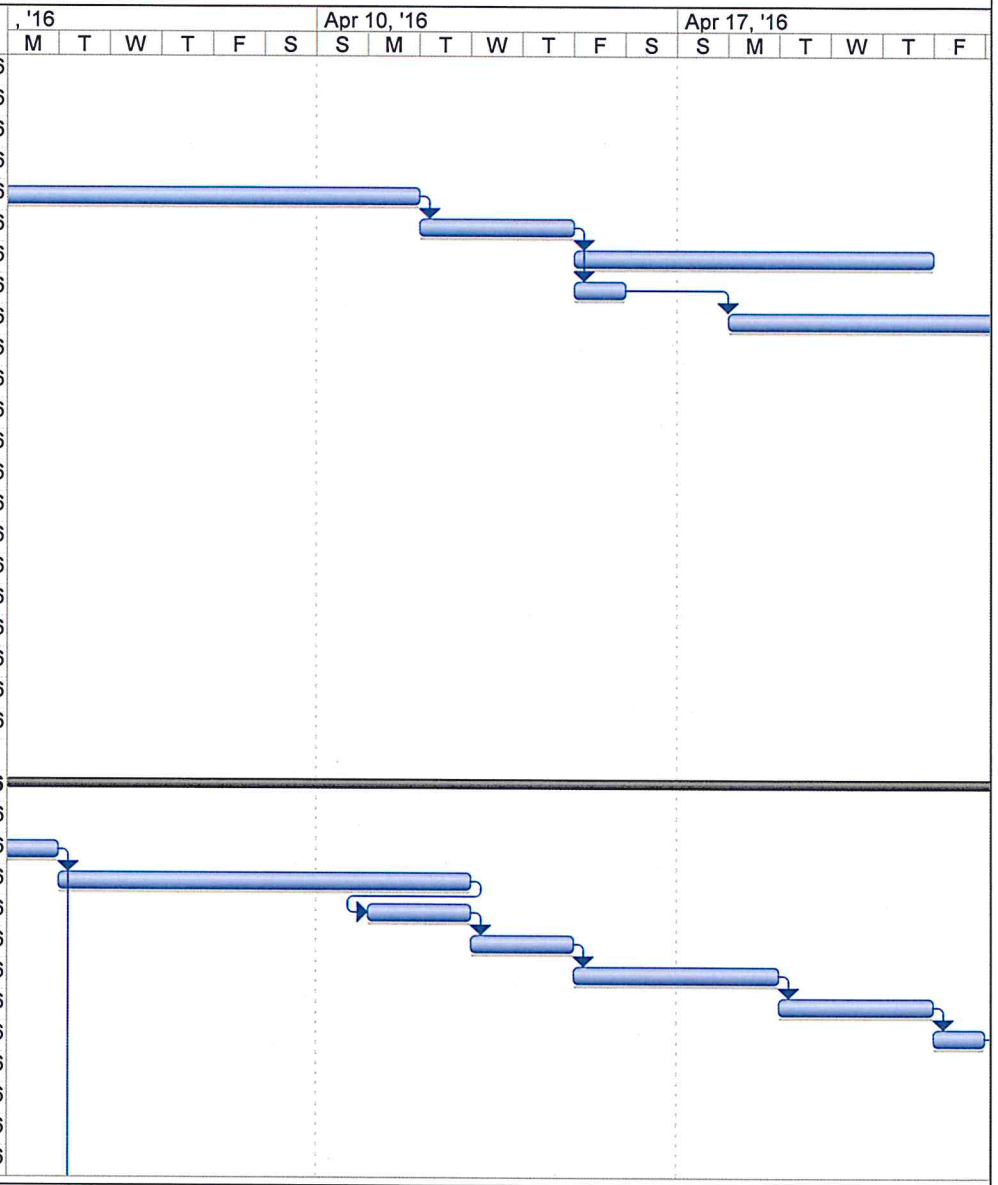

Project: MI Finish 4-4
Date: Mon 4/4/16

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

Hadley 3 Week Schedule (Interior)
3-25-2016

ID	Task Name	Duration	Start	Finish
109	Firecaulk soffits	2 days	Mon 5/9/16	Tue 5/10/16
110	HVAC/ Electrical inspection at sof	1 day	Wed 5/11/16	Wed 5/11/16
111	Hang and tape soffits/Texture/PV/	7 days	Thu 5/12/16	Fri 5/20/16
112	Paint	4 days	Mon 5/23/16	Thu 5/26/16
113	Gypcrete	3 days	Fri 5/27/16	Tue 5/31/16
114	Gypcrete dry time	10 days	Wed 6/1/16	Tue 6/14/16
115	Electrical trim	5 days	Wed 6/8/16	Tue 6/14/16
116	Fire/Sprinkler Trim	3 days	Wed 6/8/16	Fri 6/10/16
117	Install cabinets	10 days	Fri 6/10/16	Thu 6/23/16
118	Install Flooring	10 days	Fri 6/17/16	Thu 6/30/16
119	Install counter tops	6 days	Tue 6/28/16	Tue 7/5/16
120	Intsall Backsplash	6 days	Thu 6/30/16	Thu 7/7/16
121	Doors and Millwork	8 days	Tue 7/5/16	Thu 7/14/16
122	Paint doors and millwork	15 days	Tue 7/5/16	Mon 7/25/16
123	Deliver Appliances	4 days	Fri 7/22/16	Wed 7/27/16
124	Install carpet	4 days	Fri 7/22/16	Wed 7/27/16
125	Closet Shelves	4 days	Tue 7/26/16	Fri 7/29/16
126	Plumbing trim	4 days	Tue 7/26/16	Fri 7/29/16
127	Final Paint Walls	6 days	Thu 7/28/16	Thu 8/4/16
128	Window coverings	4 days	Thu 7/28/16	Tue 8/2/16
129	Final Clean	7 days	Fri 8/5/16	Mon 8/15/16
130	Punch List	7 days	Wed 8/10/16	Thu 8/18/16
131	Fluff Clean	4 days	Fri 8/19/16	Wed 8/24/16
132				
133	**L4 Zone 2 (401-431)**	**119 days**	**Thu 3/31/16**	**Tue 9/13/16**
134	Elec, Plmb RI	9 days	Thu 3/31/16	Tue 4/12/16
135	Install tubs	6 days	Mon 4/11/16	Mon 4/18/16
136	Shower remodel	5 days	Thu 4/14/16	Wed 4/20/16
137	Elec, Plmb Inspections	2 days	Thu 4/21/16	Fri 4/22/16
138	Fire Caulk	3 days	Mon 4/25/16	Wed 4/27/16
139	Framing inspection	2 days	Thu 4/28/16	Fri 4/29/16
140	Insulation	4 days	Mon 5/2/16	Thu 5/5/16
141	Insulation Inspection	1 day	Fri 5/6/16	Fri 5/6/16
142	Drywall Hang/Tape	5 days	Mon 5/9/16	Fri 5/13/16
143	Frame soffits	5 days	Fri 5/13/16	Thu 5/19/16
144	Electrical at soffits	2 days	Wed 5/18/16	Thu 5/19/16

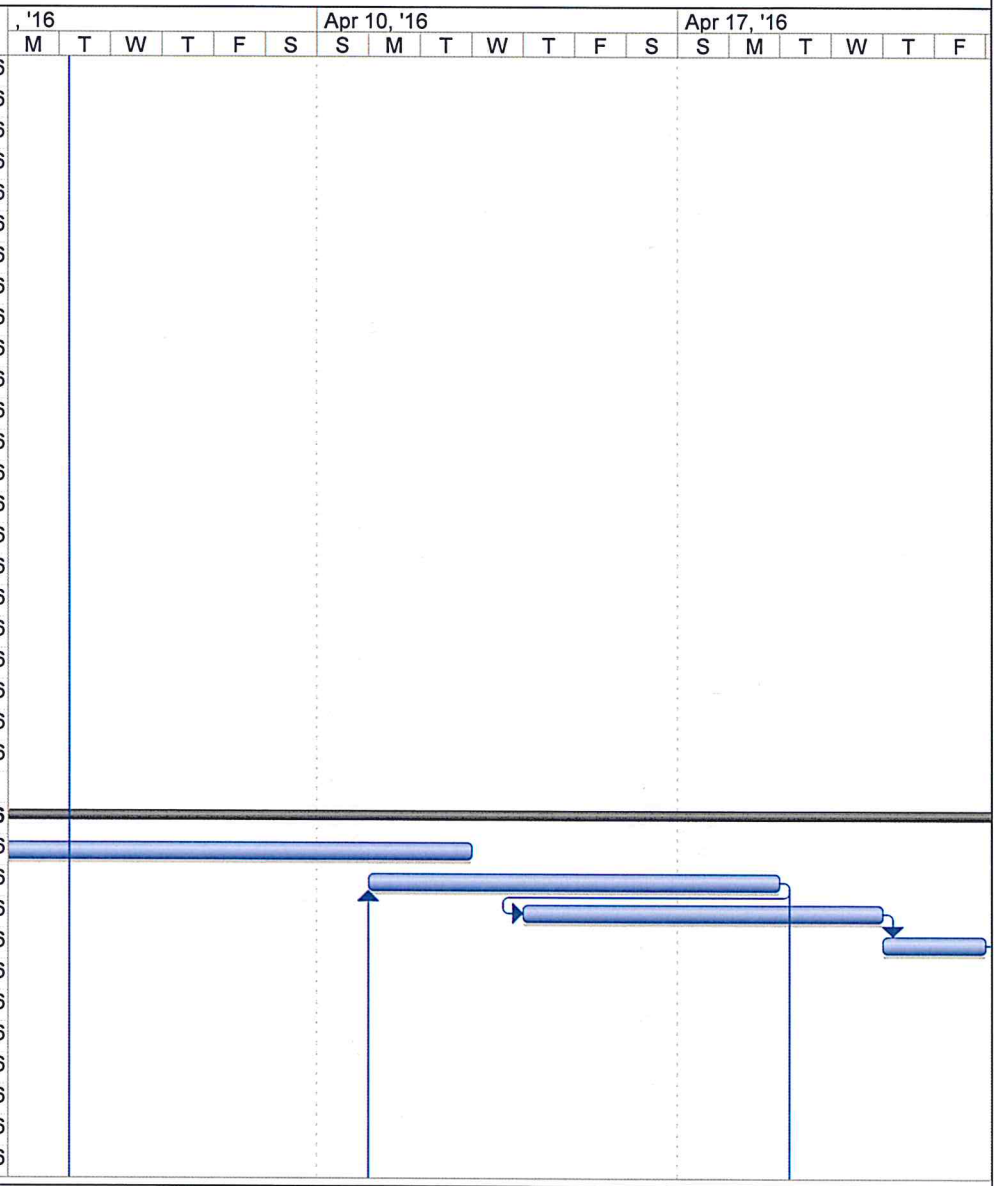

Project: MI Finish 4-4
Date: Mon 4/4/16

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

Hadley 3 Week Schedule (Interior)
3-25-2016

ID	Task Name	Duration	Start	Finish
145	Vent soffits	5 days	Wed 5/18/16	Tue 5/24/16
146	Firecaulk soffits	2 days	Mon 5/23/16	Tue 5/24/16
147	HVAC/ Electrical inspection at soffits	1 day	Wed 5/25/16	Wed 5/25/16
148	Hang and tape soffits/Texture/PVA	7 days	Thu 5/26/16	Fri 6/3/16
149	Paint	4 days	Mon 6/6/16	Thu 6/9/16
150	Gypcrete	3 days	Fri 6/10/16	Tue 6/14/16
151	Gypcrete dry time	10 days	Wed 6/15/16	Tue 6/28/16
152	Electrical trim	5 days	Wed 6/22/16	Tue 6/28/16
153	Fire/Sprinkler Trim	3 days	Wed 6/22/16	Fri 6/24/16
154	Install cabinets	10 days	Fri 6/24/16	Thu 7/7/16
155	Install Flooring	10 days	Fri 7/1/16	Thu 7/14/16
156	Install counter tops	6 days	Tue 7/12/16	Tue 7/19/16
157	Intsall Backsplash	6 days	Thu 7/14/16	Thu 7/21/16
158	Doors and Millwork	8 days	Tue 7/19/16	Thu 7/28/16
159	Paint doors and millwork	15 days	Tue 7/19/16	Mon 8/8/16
160	Deliver Appliances	4 days	Fri 8/5/16	Wed 8/10/16
161	Install carpet	4 days	Fri 8/5/16	Wed 8/10/16
162	Closet Shelves	4 days	Tue 8/9/16	Fri 8/12/16
163	Plumbing trim	4 days	Mon 8/15/16	Thu 8/18/16
164	Final Paint Walls	6 days	Wed 8/17/16	Wed 8/24/16
165	Window coverings	4 days	Thu 8/25/16	Tue 8/30/16
166	Final Clean	7 days	Thu 8/25/16	Fri 9/2/16
167	Punch List	7 days	Tue 8/30/16	Wed 9/7/16
168	Fluff Clean	4 days	Thu 9/8/16	Tue 9/13/16
169				
170	**L6 Zone 2 (601-631)**	**115 days**	**Wed 3/30/16**	**Tue 9/6/16**
171	Sandblast	4 days	Wed 3/30/16	Mon 4/4/16
172	Elec, Plmb RI	9 days	Tue 4/5/16	Fri 4/15/16
173	Install tubs	4 days	Tue 4/5/16	Fri 4/8/16
174	Elec, Plmb Inspections	2 days	Mon 4/18/16	Tue 4/19/16
175	Fire Caulk	3 days	Wed 4/20/16	Fri 4/22/16
176	Framing inspection	2 days	Mon 4/25/16	Tue 4/26/16
177	Insulation	4 days	Wed 4/27/16	Mon 5/2/16
178	Insulation Inspection	1 day	Tue 5/3/16	Tue 5/3/16
179	Drywall Hang/Tape	5 days	Wed 5/4/16	Tue 5/10/16
180	Frame soffits	5 days	Tue 5/10/16	Mon 5/16/16

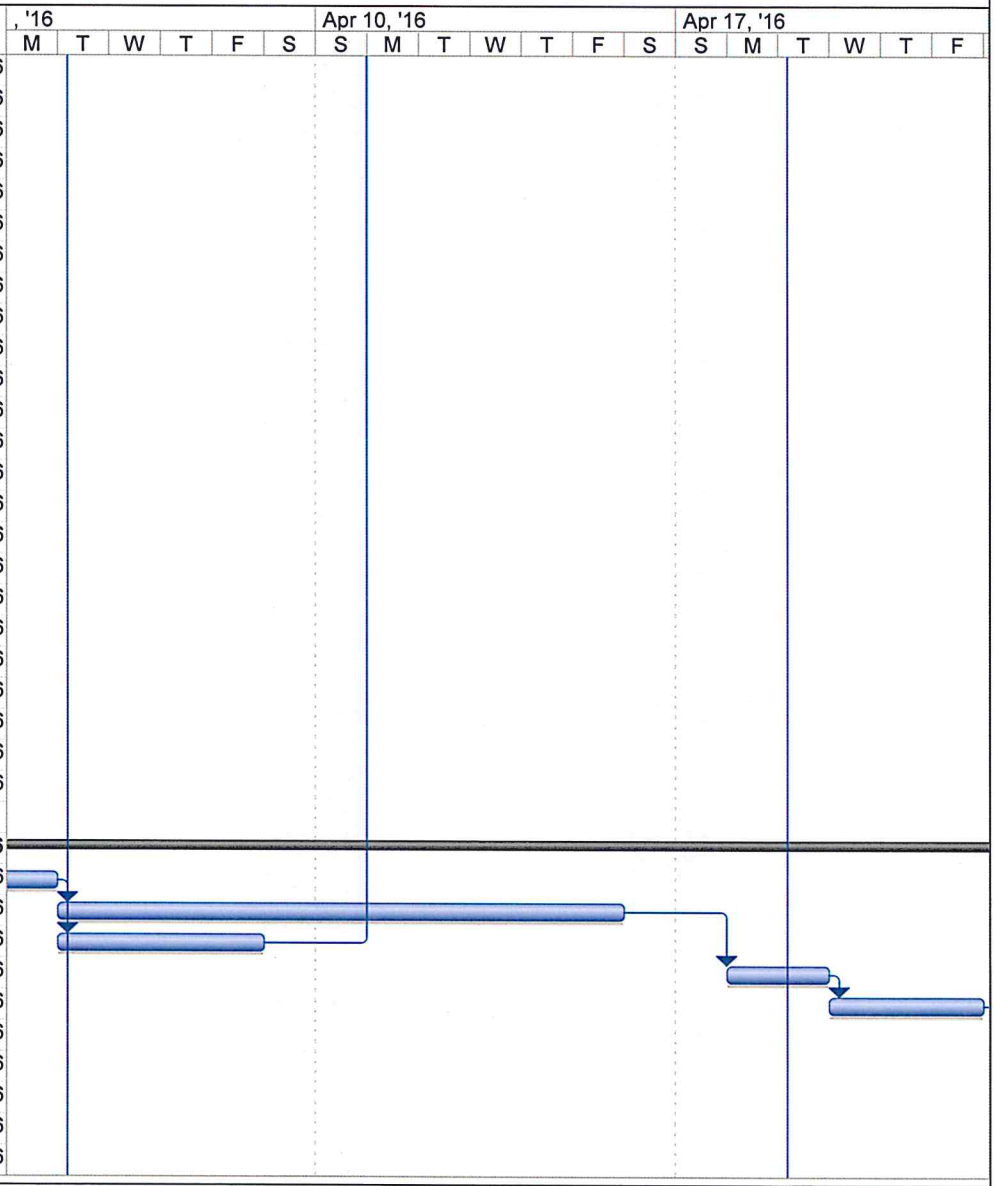

Project: MI Finish 4-4
Date: Mon 4/4/16

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline
