Hadley Mixed use
Legacy
3 wk Look ahead
11-23-2015

ID		Task Name	Duration	Start	Finish
1		**Site Grading/Utilities**	**7 days**	**Mon 11/23/15**	**Thu 12/3/15**
2		**West**	**1 day**	**Mon 11/23/15**	**Mon 11/23/15**
3		Exc/Backfill Rem Sitewall	1 day	Mon 11/23/15	Mon 11/23/15
4		**North**	**7 days**	**Mon 11/23/15**	**Thu 12/3/15**
5		Backfill Ret Wall	1 day	Mon 11/23/15	Mon 11/23/15
6		Exc Secondary Trench	1 day	Mon 11/23/15	Mon 11/23/15
7		Excavate Transformer room	1 day	Thu 12/3/15	Thu 12/3/15
8					
9		**Site/Structure**	**9 days**	**Mon 11/23/15**	**Mon 12/7/15**
10		**North**	**9 days**	**Mon 11/23/15**	**Mon 12/7/15**
11		Retaining Walls	7 days	Mon 11/23/15	Mon 12/7/15
12		**East**	**1 day**	**Mon 11/23/15**	**Mon 11/23/15**
13		Storefront Topping slab	1 day	Mon 11/23/15	Mon 11/23/15
14					
15					
16		**Wood Framing/Roofing**	**10 days**	**Mon 11/23/15**	**Tue 12/8/15**
17		**North/Southwest**	**10 days**	**Mon 11/23/15**	**Tue 12/8/15**
18		Roof	10 days	Mon 11/23/15	Tue 12/8/15
19		**Penthouse SE**	**8 days**	**Mon 11/23/15**	**Fri 12/4/15**
20		Frame	7 days	Mon 11/23/15	Thu 12/3/15
21		Joist/Sheath	3 days	Wed 12/2/15	Fri 12/4/15
22		**Southeast**	**21 days**	**Wed 12/2/15**	**Fri 1/1/16**
23		Complete Framing	5 days	Wed 12/2/15	Tue 12/8/15
24		Walkway Stanchions	5 days	Mon 12/7/15	Fri 12/11/15
25		Crickets	5 days	Mon 12/14/15	Fri 12/18/15
26		Roofing	8 days	Mon 12/21/15	Fri 1/1/16
27					
28		**Exterior**	**26 days**	**Mon 11/23/15**	**Fri 1/1/16**
29		Bonnet Scaffolds	3 days	Mon 11/23/15	Wed 11/25/15
30		Wrap/Set Door Pans/ Windows West/North	6 days	Mon 11/30/15	Mon 12/7/15
31		Deliver Windows Complete	11 days	Mon 11/23/15	Wed 12/9/15
32		Target Wall Stubs	4 days	Mon 11/23/15	Mon 11/30/15
33		Set Rm North Scaffold	2 days	Fri 12/4/15	Mon 12/7/15
34		Tyvek	2 days	Tue 12/8/15	Wed 12/9/15

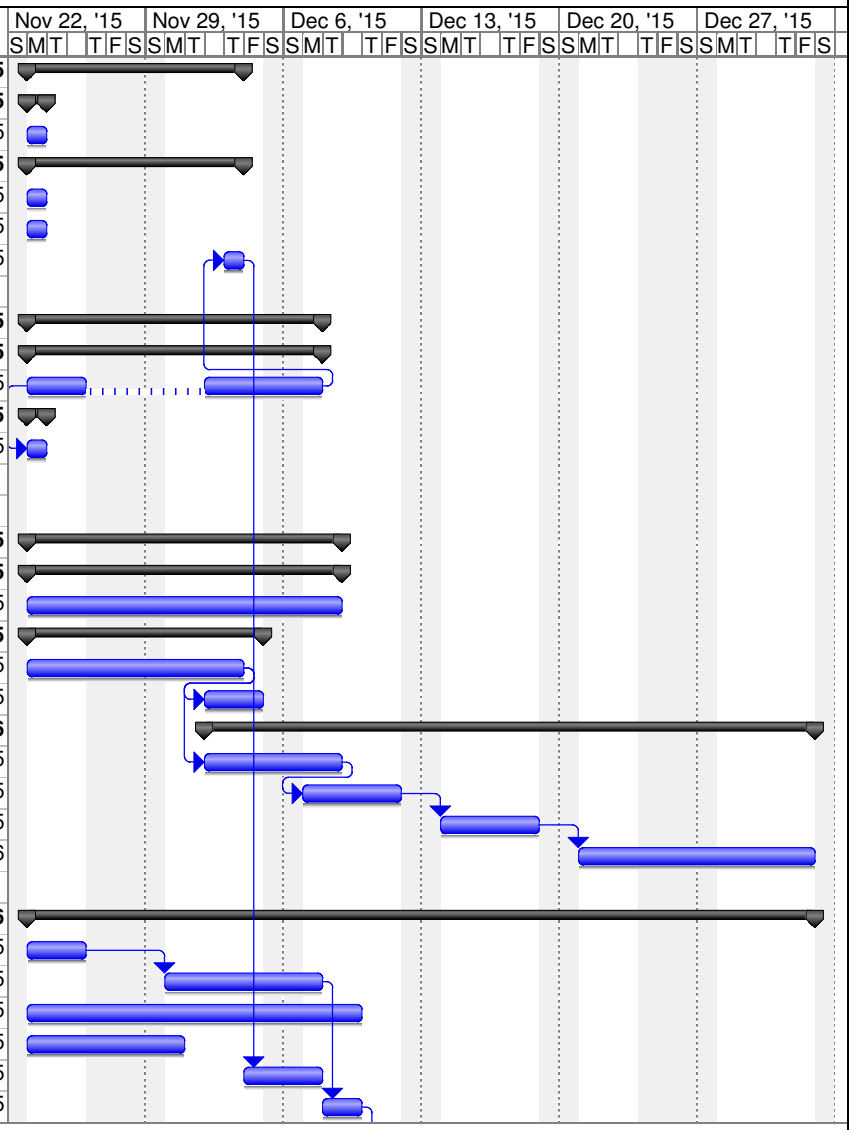

Project: 3wk 11-23-2015
Date: Fri 11/20/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
11-23-2015

ID		Task Name	Duration	Start	Finish
35		Siding	15 days	Thu 12/10/15	Fri 1/1/16
36					
37		**Mtl Stud Framing**	**8 days**	**Mon 11/23/15**	**Fri 12/4/15**
38		Rock Storefronts	4 days	Mon 11/23/15	Mon 11/30/15
39		Rock Ext Level 1-2 South	4 days	Tue 12/1/15	Fri 12/4/15
40					
41		**Temp Heat**	**3 days?**	**Mon 12/7/15**	**Wed 12/9/15**
42		Temp Gas to Meter	1 day?	Mon 12/7/15	Mon 12/7/15
43		Deliver/Set Equipment	1 day?	Tue 12/8/15	Tue 12/8/15
44		Heat West	1 day?	Wed 12/9/15	Wed 12/9/15
45					
46		**Waterproofing**	**1 day**	**Mon 11/23/15**	**Mon 11/23/15**
47		Bentonine Exhaust Shaft/N Wall	1 day	Mon 11/23/15	Mon 11/23/15

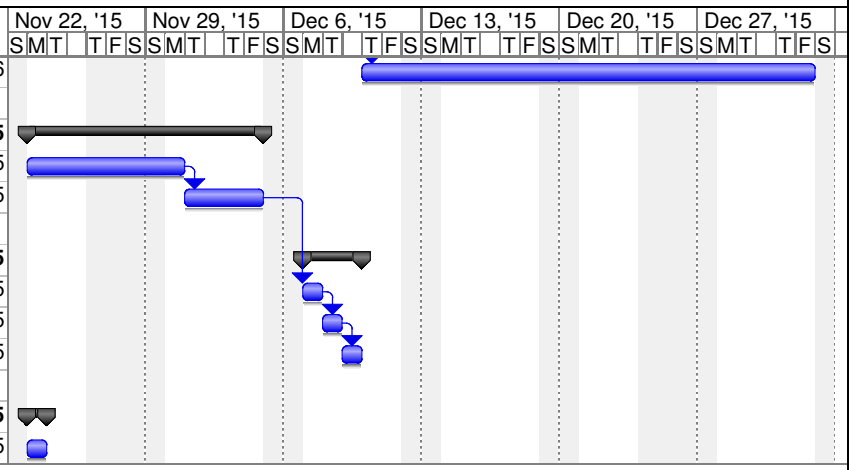

Project: 3wk 11-23-2015
Date: Fri 11/20/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
