Hadley Mixed use
Legacy
3 wk Look ahead
4-25-2016

Exterior

ID		Task Name	Duration	Start
1		**Garage**	**18 days**	**Mon 4/25/16**
2		**Level P**	**10 days**	**Mon 4/25/16**
3		Light Fixtures Garage	5 days	Mon 4/25/16
4		Shtrock Stair 2 Entry	1 day	Mon 4/25/16
5		PSE Seconday's	1 day	Mon 5/2/16
6		PSE Unit Meters	4 days	Tue 5/3/16
7				
8		**Level 1**	**13 days**	**Mon 4/25/16**
9		Garage Light Fixtures	5 days	Tue 4/26/16
10		Stick Pin/Insulate Lid	7 days	Tue 5/3/16
11		Complete 1-side Sheetrock	3 days	Mon 4/25/16
12		Retail Wall Insulation	5 days	Thu 4/28/16
13				
14		**Level 2**	**18 days**	**Mon 4/25/16**
15		Insulate Door Headers	5 days	Thu 5/12/16
16		Frame Unit Lids	5 days	Mon 4/25/16
17		Retail Wall Insulation	5 days	Thu 5/5/16
18		Garage Lights	5 days	Mon 4/25/16
19				
20		**Site/Structure**	**8 days**	**Mon 5/2/16**
21		**North**	**8 days**	**Mon 5/2/16**
22		Gas Main/Manifold	5 days	Mon 5/2/16
23		Install Gas Branch lines	3 days	Mon 5/9/16
24		Demob Temp Power	3 days	Mon 5/9/16
25				
26		**/Roofing**	**4 days**	**Mon 4/25/16**
27		**North/Southwest**	**4 days**	**Mon 4/25/16**
28		Walk Mats	3 days	Mon 4/25/16
29		BCRA Inspection	1 day	Thu 4/28/16
30				
31		**Penthouses**	**12 days**	**Mon 4/25/16**
36		Battons/Siding	10 days	Mon 4/25/16
37				
38		**Exterior**	**14 days**	**Mon 4/25/16**

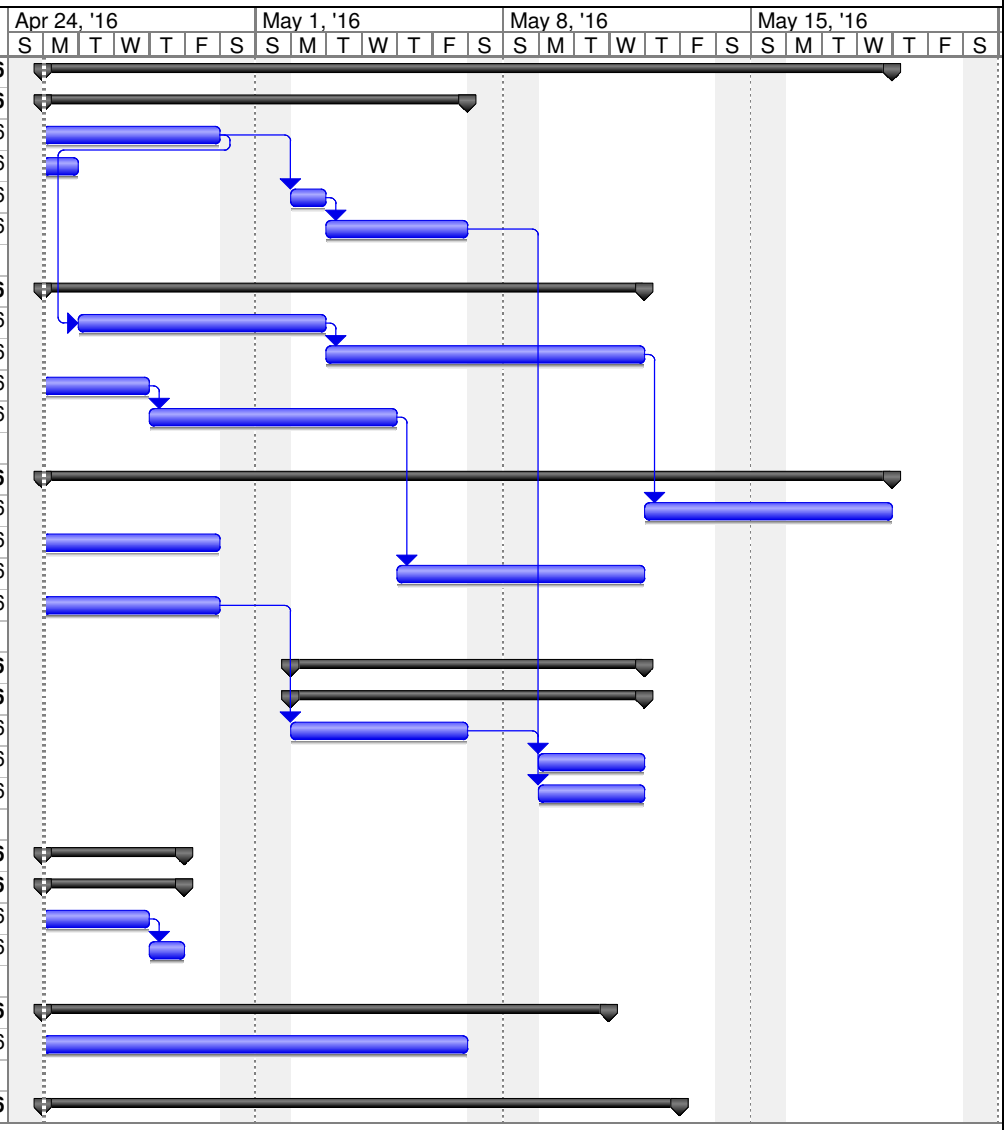

Project: 3wk 4-25-16 3wk
Date: Mon 4/25/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
4-25-2016

ID	Task Name	Duration	Start
39	**West**	**13 days**	**Mon 4/25/16**
40	Rem Stucco	5 days	Mon 4/25/16
41	Caukling	3 days	Mon 4/25/16
42	Remove Scafflod	5 days	Thu 4/28/16
43	Set Decks	5 days	Thu 5/5/16
44	**North**	**14 days**	**Mon 4/25/16**
45	Siding	5 days	Mon 4/25/16
46	Stucco	7 days	Wed 4/27/16
47	Paint	5 days	Fri 5/6/16
48			
49	**Courtyard**	**20 days**	**Mon 4/25/16**
50	Paint	10 days	Mon 4/25/16
51	Inspect	1 day	Mon 5/9/16
52	Deck Rods	5 days	Wed 5/4/16
53	Remove Scaffolding	6 days	Wed 5/11/16
54			
55	**East Perimeter**	**20 days**	**Mon 4/25/16**
56	Flashing	2 days	Mon 4/25/16
57	Siding	10 days	Wed 4/27/16
58	Paint	7 days	Wed 5/11/16
59	Finish Stucco	4 days	Tue 5/17/16
60			
61	**Storefront**	**20 days**	**Mon 4/25/16**
62	Lower Frames/Mullians	10 days	Mon 4/25/16
63	Glass Upper	5 days	Wed 4/27/16
64	Glass Lower	10 days	Mon 5/2/16
65	Entry Doors	5 days	Mon 5/16/16
66	Caulking	5 days	Mon 5/16/16
67			
68	**South**	**9 days**	**Mon 4/25/16**
69	Stucco	3 days	Mon 4/25/16
70	Flashing	2 days	Thu 4/28/16
71	Siding	4 days	Mon 5/2/16

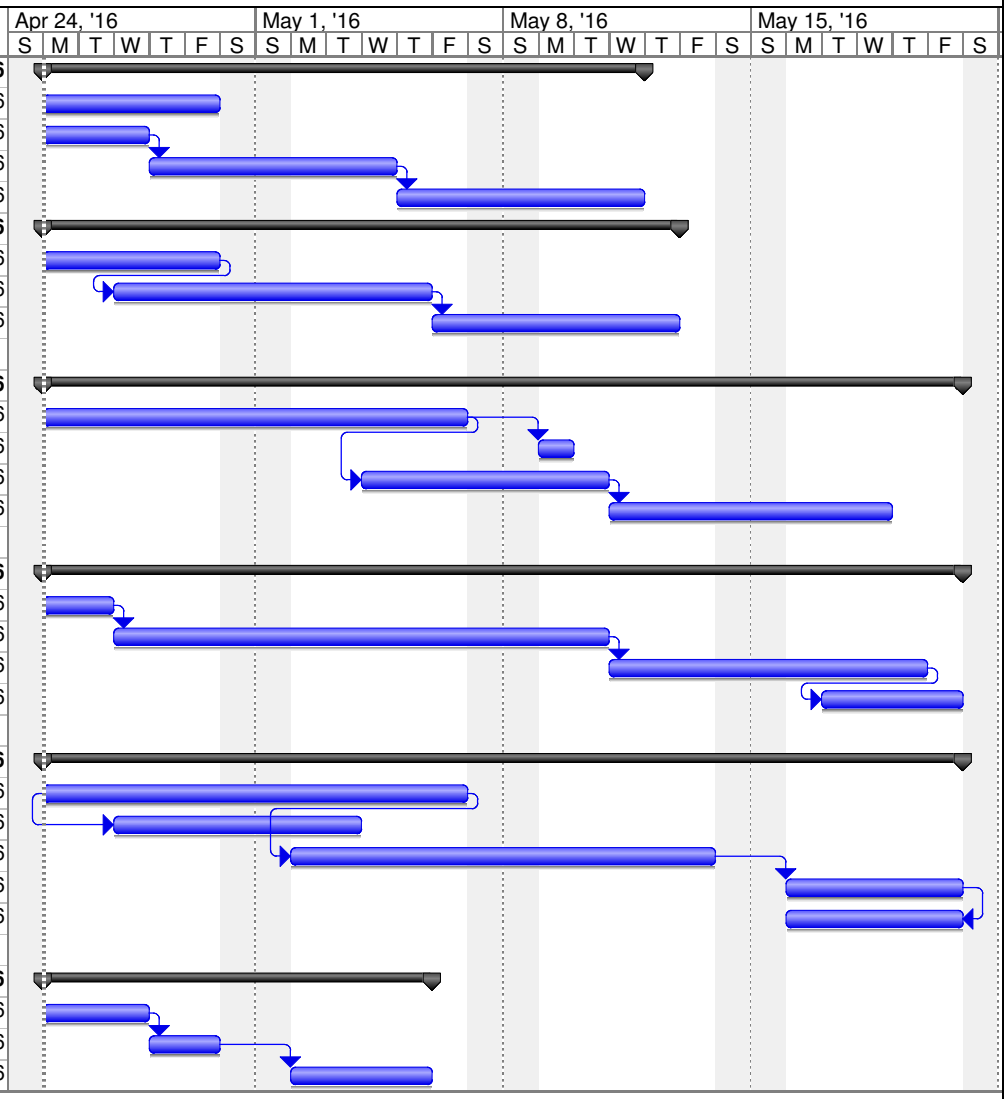

Project: 3wk 4-25-16 3wk
Date: Mon 4/25/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
