Hadley Mixed use
Legacy
3 wk Look ahead
6-13-2016

Exterior Schedule

ID	Task Name	Duration	Start	Finish
1	**Garage**	**18 days**	**Mon 6/13/16**	**Wed 7/6/16**
2	**Level P**	**5 days**	**Mon 6/13/16**	**Fri 6/17/16**
3	Sheetrock Stairs 1/4	4 days	Mon 6/13/16	Thu 6/16/16
4	PSE East Unit Meters	2 days	Thu 6/16/16	Fri 6/17/16
5				
6	**Level 1**	**8 days**	**Mon 6/13/16**	**Wed 6/22/16**
7	Stick Pin/Insulate Lid	7 days	Mon 6/13/16	Tue 6/21/16
8	Girts/Insulation	4 days	Fri 6/17/16	Wed 6/22/16
9				
10	**Level 2**	**11 days**	**Wed 6/22/16**	**Wed 7/6/16**
11	Insulate Ext. Door Headers	1 day	Wed 6/22/16	Wed 6/22/16
12	Garage/Retail Insulation	10 days	Thu 6/23/16	Wed 7/6/16
13				
14	**Site/Structure**	**1 day**	**Mon 6/13/16**	**Mon 6/13/16**
15	**North**	**1 day**	**Mon 6/13/16**	**Mon 6/13/16**
16	Bsckfill/Grade Gas main	1 day	Mon 6/13/16	Mon 6/13/16
17				
18	**/Roofing**	**10 days**	**Mon 6/13/16**	**Fri 6/24/16**
19	**North/Southwest**	**10 days**	**Mon 6/13/16**	**Fri 6/24/16**
20	Remove Replace @ Roof Drains	5 days	Mon 6/20/16	Fri 6/24/16
21	Walk Mats	3 days	Mon 6/20/16	Wed 6/22/16
22	Cap Flashing	5 days	Mon 6/13/16	Fri 6/17/16
23	BCRA Inspection	1 day	Wed 6/22/16	Wed 6/22/16
24				
25	**Exterior**	**25 days**	**Mon 6/13/16**	**Fri 7/15/16**
26	**Penthouses**	**25 days**	**Mon 6/13/16**	**Fri 7/15/16**
31	Battons/Siding	10 days	Mon 6/13/16	Fri 6/24/16
32	Parapet Caps	5 days	Mon 7/11/16	Fri 7/15/16
33				
34	**South**	**2 days**	**Mon 6/13/16**	**Tue 6/14/16**
35	Remove Scaffold	1 day	Mon 6/13/16	Mon 6/13/16
36	Set Decks	2 days	Mon 6/13/16	Tue 6/14/16
37				
38	**East**	**6 days**	**Mon 6/13/16**	**Mon 6/20/16**

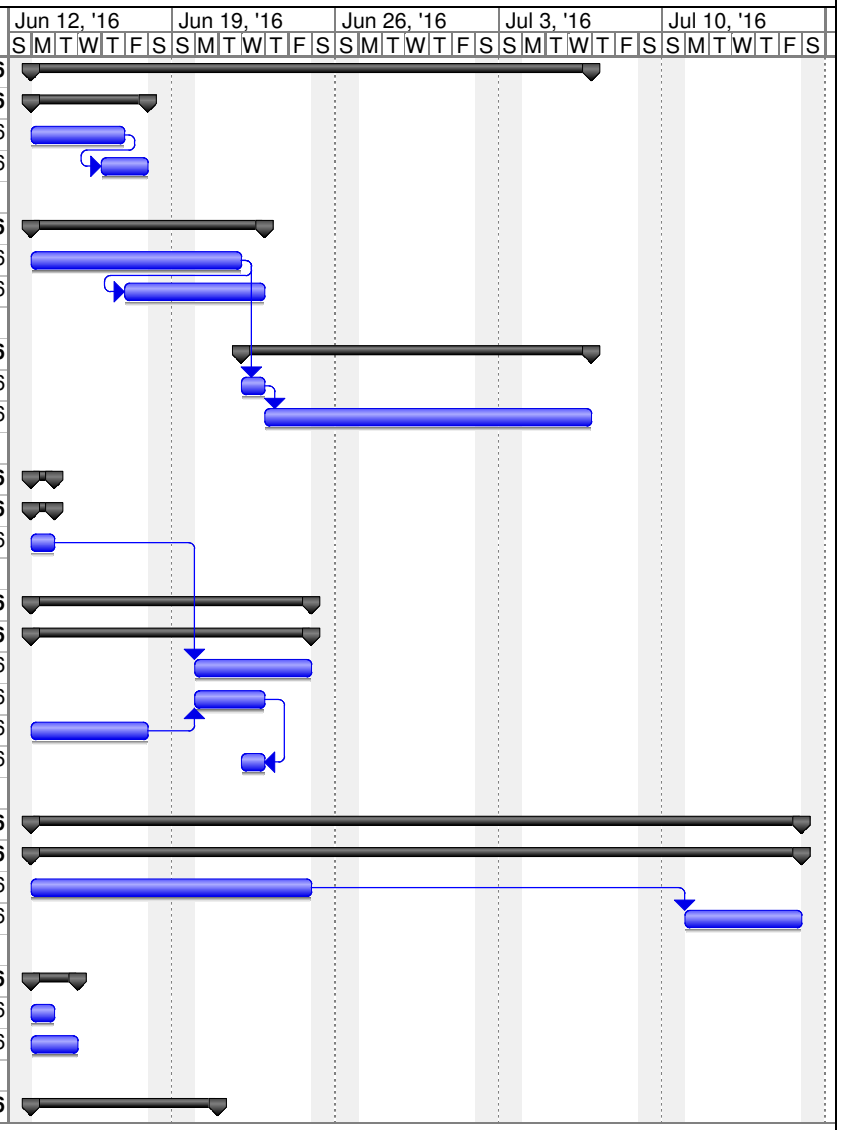

Project: 3wk 6-13-16 3wk
Date: Fri 6/10/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
6-13-2016

ID		Task Name	Duration	Start	Finish
39		Wash Windows	2 days	Mon 6/13/16	Tue 6/14/16
40		Remainder Paint	2 days	Mon 6/13/16	Tue 6/14/16
41		Remove Scaffold	4 days	Wed 6/15/16	Mon 6/20/16
42					
43		**North**	**12 days**	**Mon 6/13/16**	**Tue 6/28/16**
44		Paint	4 days	Mon 6/13/16	Thu 6/16/16
45		Rem Stucco	4 days	Fri 6/17/16	Wed 6/22/16
46		Remove Scaffold	4 days	Thu 6/23/16	Tue 6/28/16
47					
48		**Site**	**16 days**	**Mon 6/13/16**	**Mon 7/4/16**
49		**East**	**10 days**	**Mon 6/13/16**	**Fri 6/24/16**
50		F&P Rem Walls	6 days	Mon 6/13/16	Mon 6/20/16
51		Backfill Retail Entry	6 days	Fri 6/17/16	Fri 6/24/16
52		**South**	**16 days**	**Mon 6/13/16**	**Mon 7/4/16**
53		Exc Rem Site Walls	3 days	Mon 6/13/16	Wed 6/15/16
54		F&P Walls	10 days	Thu 6/16/16	Wed 6/29/16
55		Demo/GradeSidewalk	3 days	Thu 6/30/16	Mon 7/4/16
56		**West**	**7 days**	**Mon 6/20/16**	**Tue 6/28/16**
57		F&P Site Concrete	7 days	Mon 6/20/16	Tue 6/28/16
58					
59		**Power**	**2 days**	**Tue 6/14/16**	**Wed 6/15/16**
60		East Meter Set	2 days	Tue 6/14/16	Wed 6/15/16

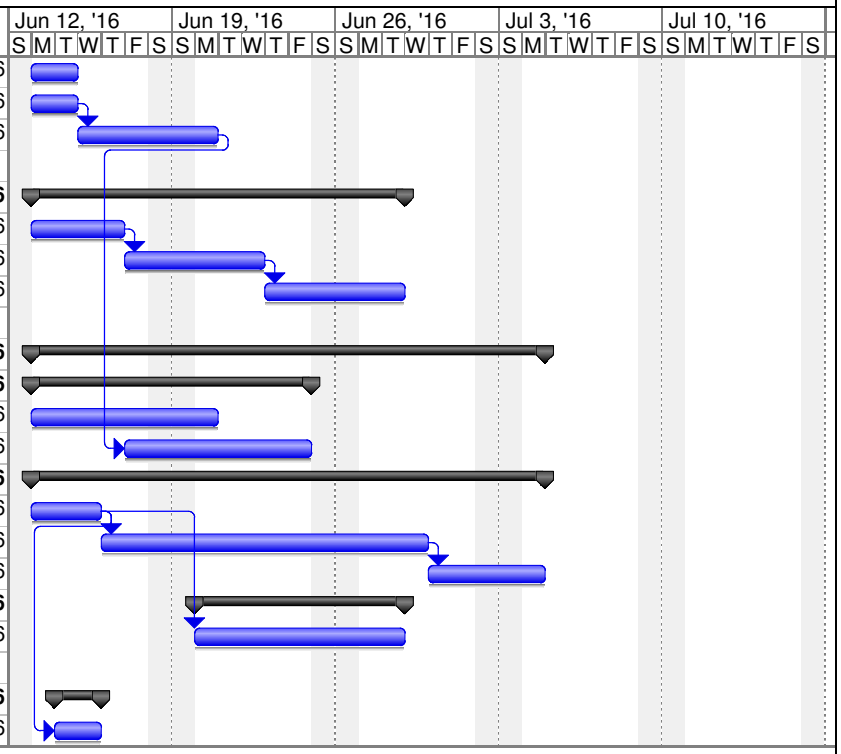

Project: 3wk 6-13-16 3wk
Date: Fri 6/10/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
