Hadley Mixed use
Legacy
3 wk Look ahead
6-6-2016

# Exterior Sched.

| ID | | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1 | | **Garage** | **18 days** | **Mon 6/6/16** | **Wed 6/29/16** |
| 2 | | **Level P** | **10 days** | **Mon 6/6/16** | **Fri 6/17/16** |
| 3 | | Shtrock Stair 2 Entry | 2 days | Mon 6/6/16 | Tue 6/7/16 |
| 4 | | PSE East Unit Meters | 2 days | Thu 6/16/16 | Fri 6/17/16 |
| 5 | | | | | |
| 6 | | **Level 1** | **8 days** | **Mon 6/6/16** | **Wed 6/15/16** |
| 7 | | Stick Pin/Insulate Lid | 7 days | Mon 6/6/16 | Tue 6/14/16 |
| 8 | | Girts/Insulation | 4 days | Fri 6/10/16 | Wed 6/15/16 |
| 9 | | | | | |
| 10 | | **Level 2** | **11 days** | **Wed 6/15/16** | **Wed 6/29/16** |
| 11 | | Insulate Ext. Door Headers | 1 day | Wed 6/15/16 | Wed 6/15/16 |
| 12 | | Garage/Retail Insulation | 10 days | Thu 6/16/16 | Wed 6/29/16 |
| 13 | | | | | |
| 14 | | **Site/Structure** | **5 days** | **Mon 6/6/16** | **Fri 6/10/16** |
| 15 | | **North** | **5 days** | **Mon 6/6/16** | **Fri 6/10/16** |
| 16 | | Install Gas Branch lines | 3 days | Mon 6/6/16 | Wed 6/8/16 |
| 17 | | Bsckfill/Grade | 2 days | Thu 6/9/16 | Fri 6/10/16 |
| 18 | | | | | |
| 19 | | **/Roofing** | **9 days** | **Mon 6/6/16** | **Thu 6/16/16** |
| 20 | | **North/Southwest** | **9 days** | **Mon 6/6/16** | **Thu 6/16/16** |
| 21 | | Walk Mats | 3 days | Mon 6/13/16 | Wed 6/15/16 |
| 22 | | Cap Flashing | 5 days | Mon 6/6/16 | Fri 6/10/16 |
| 23 | | BCRA Inspection | 1 day | Thu 6/16/16 | Thu 6/16/16 |
| 24 | | | | | |
| 25 | | **Exterior** | **25 days** | **Mon 6/6/16** | **Fri 7/8/16** |
| 26 | | **Penthouses** | **25 days** | **Mon 6/6/16** | **Fri 7/8/16** |
| 31 | | Battons/Siding | 10 days | Mon 6/6/16 | Fri 6/17/16 |
| 32 | | Parapet Caps | 5 days | Mon 7/4/16 | Fri 7/8/16 |
| 33 | | | | | |
| 34 | | **West** | **9 days** | **Mon 6/6/16** | **Thu 6/16/16** |
| 35 | | Rem Stucco | 3 days | Mon 6/6/16 | Wed 6/8/16 |
| 36 | | Remove Scaffold | 1 day | Thu 6/9/16 | Thu 6/9/16 |
| 37 | | | | | |
| 38 | | **South** | **9 days** | **Mon 6/6/16** | **Thu 6/16/16** |

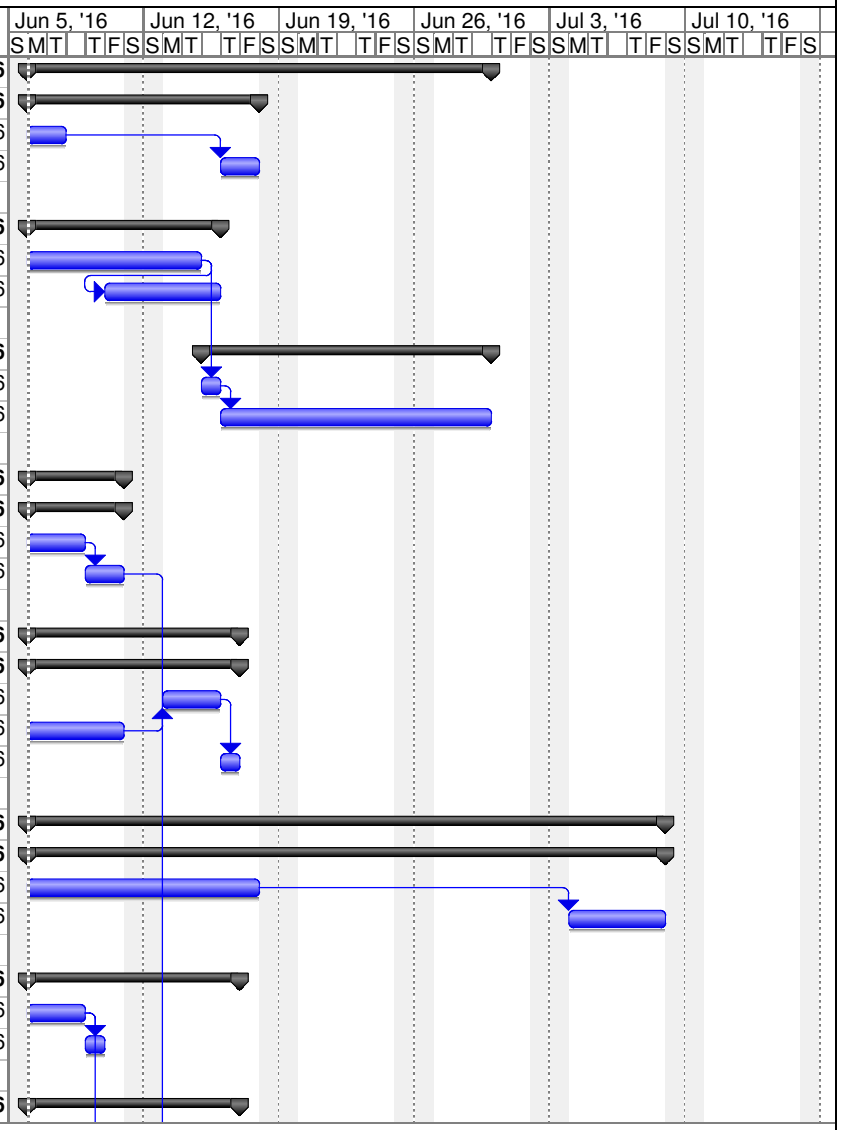


Project: 3wk 6-6-16 3wk
Date: Mon 6/6/16

| | | | | | |
|---|---|---|---|---|---|
| Task | | Milestone | | External Tasks | |
| Split | | Summary | | External Milestone | |
| Progress | | Project Summary | | Deadline | |

Hadley Mixed use
Legacy
3 wk Look ahead
6-6-2016

| ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|
| 39 | Clean Windows | 2 days | Mon 6/6/16 | Tue 6/7/16 |
| 40 | Punch | 1 day | Tue 6/7/16 | Tue 6/7/16 |
| 41 | Scaffold Removal | 3 days | Wed 6/8/16 | Fri 6/10/16 |
| 42 | Decks | 4 days | Mon 6/13/16 | Thu 6/16/16 |
| 43 | | | | |
| 44 | **Courtyard** | **30 days** | **Mon 6/6/16** | **Fri 7/15/16** |
| 45 | Set Decks | 4 days | Mon 6/6/16 | Thu 6/9/16 |
| 46 | | | | |
| 47 | **East Perimeter** | **20 days** | **Mon 6/6/16** | **Fri 7/1/16** |
| 48 | Stucco/Siding | 2 days | Thu 6/9/16 | Fri 6/10/16 |
| 49 | Clean/Prep | 2 days | Mon 6/6/16 | Tue 6/7/16 |
| 50 | Paint | 7 days | Tue 6/7/16 | Wed 6/15/16 |
| 51 | Inspection/Repair | 3 days | Thu 6/16/16 | Mon 6/20/16 |
| 52 | Remove Scaffold | 5 days | Tue 6/21/16 | Mon 6/27/16 |
| 53 | Decks | 7 days | Thu 6/23/16 | Fri 7/1/16 |
| 54 | | | | |
| 55 | **Storefront** | **3 days** | **Wed 6/8/16** | **Fri 6/10/16** |
| 56 | South Windows | 3 days | Wed 6/8/16 | Fri 6/10/16 |
| 57 | | | | |
| 58 | **North** | **30 days** | **Mon 6/6/16** | **Fri 7/15/16** |
| 59 | Stucco | 3 days | Mon 6/6/16 | Wed 6/8/16 |
| 60 | Siding | 5 days | Thu 6/9/16 | Wed 6/15/16 |
| 61 | Paint | 6 days | Thu 6/16/16 | Thu 6/23/16 |
| 62 | Inspect/Repair | 3 days | Fri 6/24/16 | Tue 6/28/16 |
| 63 | Remove Scaffold | 5 days | Wed 6/29/16 | Tue 7/5/16 |
| 64 | Decks | 8 days | Wed 7/6/16 | Fri 7/15/16 |
| 65 | | | | |
| 66 | **Site** | **18 days** | **Mon 6/6/16** | **Wed 6/29/16** |
| 67 | **East** | **18 days** | **Mon 6/6/16** | **Wed 6/29/16** |
| 68 | F&P Rem Walls | 6 days | Mon 6/6/16 | Mon 6/13/16 |
| 69 | Backfill Retail Entry | 6 days | Wed 6/22/16 | Wed 6/29/16 |
| 70 | **South** | **13 days** | **Mon 6/13/16** | **Wed 6/29/16** |
| 71 | Exc Rem Site Walls | 3 days | Mon 6/13/16 | Wed 6/15/16 |
| 72 | F&P Walls | 10 days | Thu 6/16/16 | Wed 6/29/16 |

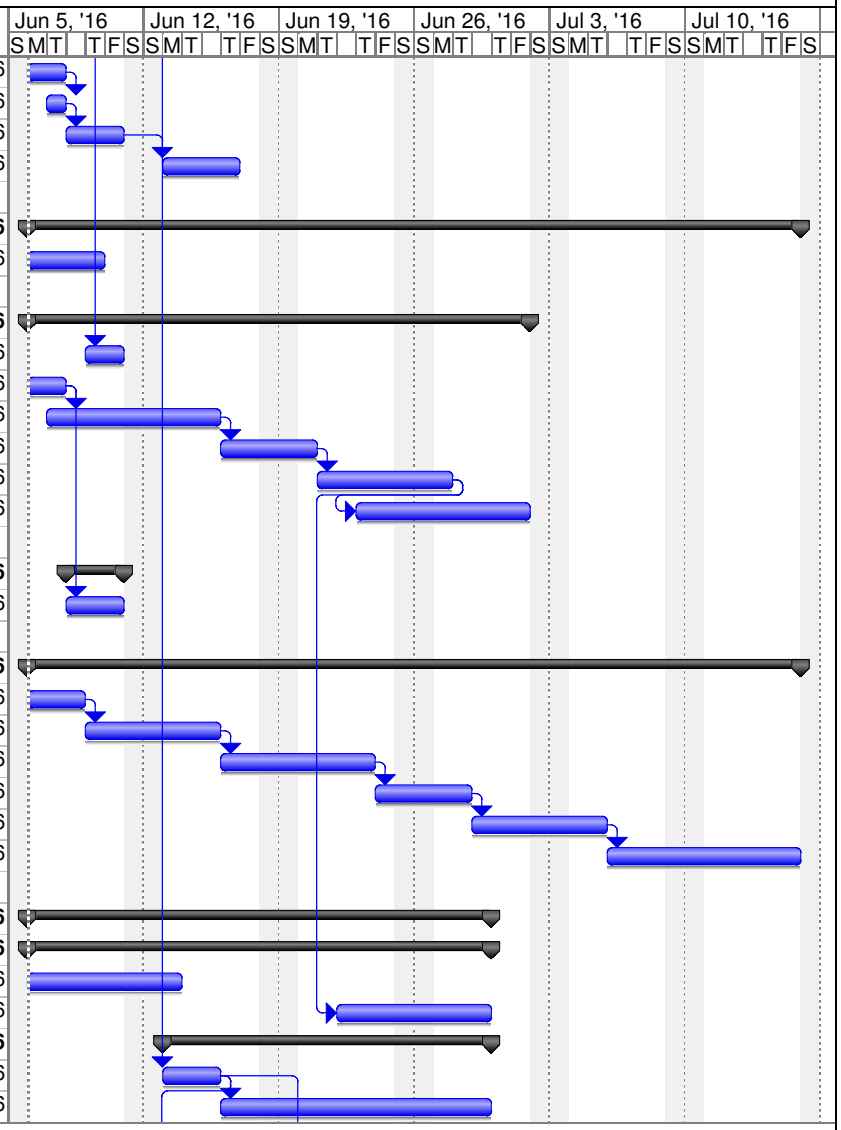


Project: 3wk 6-6-16 3wk
Date: Mon 6/6/16

Task | Milestone | External Tasks
Split | Summary | External Milestone
Progress | Project Summary | Deadline

Hadley Mixed use
Legacy
3 wk Look ahead
6-6-2016

| ID | | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 73 | | **West** | **7 days** | **Mon 6/20/16** | **Tue 6/28/16** |
| 74 | | Site Concrete | 7 days | Mon 6/20/16 | Tue 6/28/16 |
| 75 | | | | | |
| 76 | | **Power** | **7 days** | **Tue 6/7/16** | **Wed 6/15/16** |
| 77 | | East Meter Set | 2 days | Tue 6/14/16 | Wed 6/15/16 |
| 78 | | Remove Temp Power | 1 day | Tue 6/7/16 | Tue 6/7/16 |

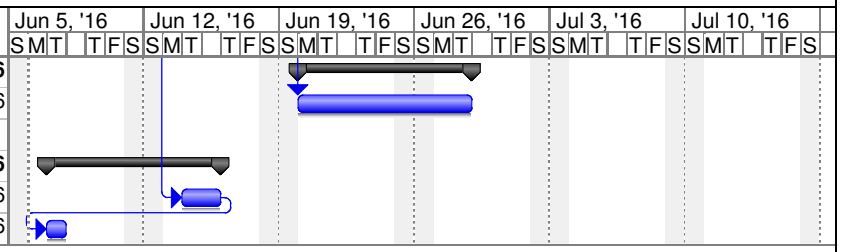


Project: 3wk 6-6-16 3wk
Date: Mon 6/6/16

| | | | | | |
|---|---|---|---|---|---|
| Task | | Milestone | | External Tasks | |
| Split | | Summary | | External Milestone | |
| Progress | | Project Summary | | Deadline | |
