Hadley Mixed use
Legacy
3 wk Look ahead
1-12-2015

ID		Task Name	Duration	Start
1		**Mass Excavation**	**6 days**	**Mon 1/12/15**
2		Mass Exc North to South	5 days	Mon 1/12/15
3		Struct Exc Northwest	2 days	Mon 1/12/15
4		Excavate South/West for Lagging	4 days	Mon 1/12/15
5		Export Cont Soil South	5 days	Mon 1/12/15
6		Backfill Crane Footing	2 days	Fri 1/16/15
7				
8		**Shoring**	**8 days**	**Mon 1/12/15**
9		Lag West/South Piles	4 days	Mon 1/12/15
10				
11		**CIP Concrete**	**14 days**	**Mon 1/12/15**
12		F&P Footings NW	6 days	Mon 1/12/15
13		Restl Walls/Columns	5 days	Thu 1/15/15
14		F&P Walls/Columns Level P	8 days	Tue 1/20/15
15				
16		**Below Slab Utilities**	**8 days**	**Tue 1/20/15**
17		Sewer Drains	5 days	Tue 1/20/15
18		Slab Drainage	5 days	Fri 1/23/15
19				
20		**Crane**	**2 days**	**Mon 1/26/15**
21		Erect Crane	2 days	Mon 1/26/15
22				
23		**Geo Piers**	**10 days**	**Mon 1/12/15**
24		Mobilize	1 day	Mon 1/12/15
25		Drill/Place SE	10 days	Mon 1/12/15
26				
27		**Waterproofing**	**10 days**	**Fri 1/16/15**
28		Shoring Walls	10 days	Fri 1/16/15
29				
30		**Power**	**8 days**	**Mon 1/12/15**
31		Temp	8 days	Mon 1/12/15
32				
33		**Storm Water Discharge**	**0 days**	**Mon 1/12/15**
34		Discharge to Storm	0 days	Mon 1/12/15

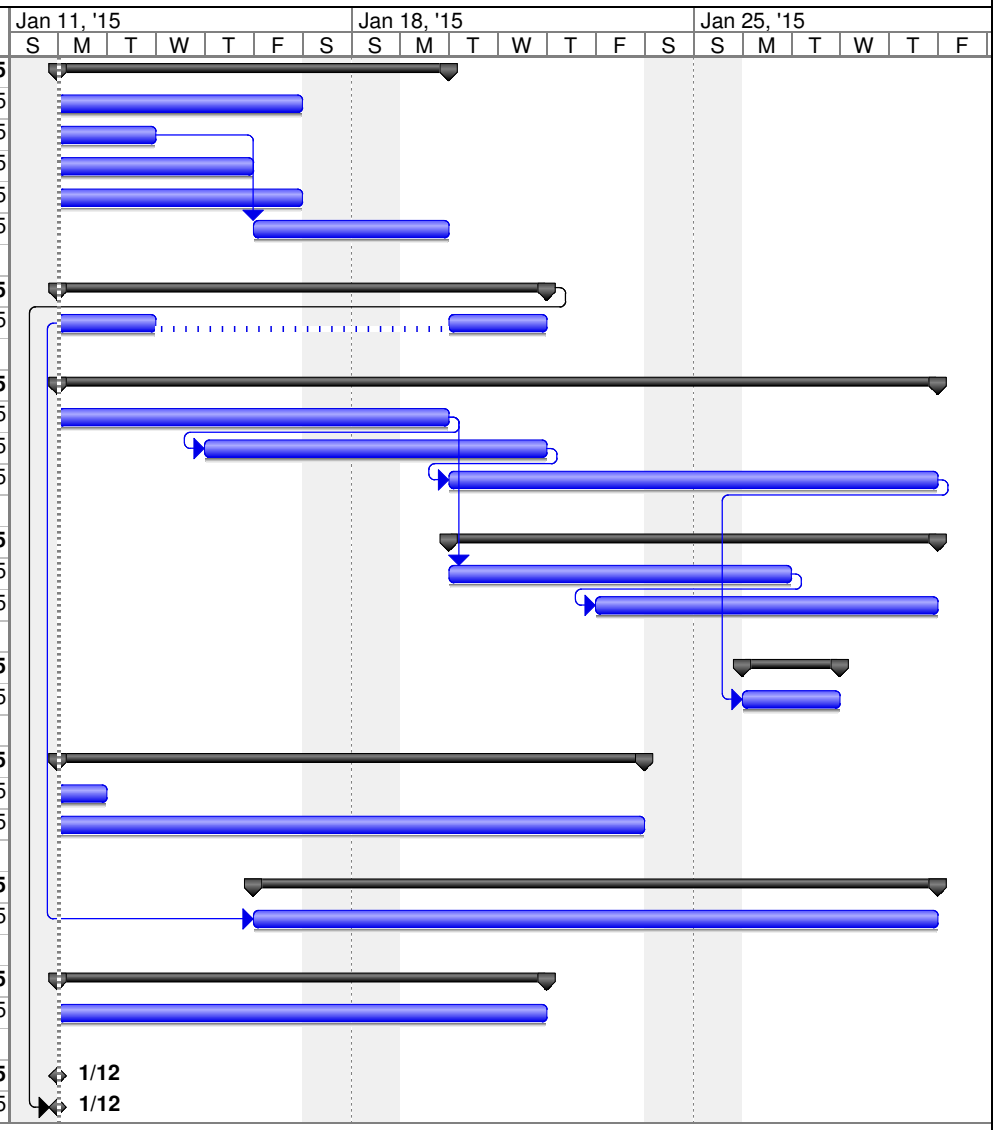

Project: 3wk Look ahead 1-12-15
Date: Mon 1/12/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
