Hadley Mixed use
Legacy
3 wk Look ahead
2-16-2015

ID		Task Name	Duration	Start	Finish
1		**Mass Excavation**	**14 days**	**Mon 2/16/15**	**Thu 3/5/15**
2		Backfill/Grade NW	5 days	Mon 2/16/15	Fri 2/20/15
3		Export Cont. South	2 days	Mon 2/16/15	Tue 2/17/15
4		Pipe Trenching NW	4 days	Mon 2/23/15	Thu 2/26/15
5		Vapor Barrier/Cap Break NW	5 days	Fri 2/27/15	Thu 3/5/15
6					
7		**Survey**	**1 day**	**Tue 2/17/15**	**Tue 2/17/15**
8		Layout NE Geopier	1 day	Tue 2/17/15	Tue 2/17/15
9					
10		**Geopiers**	**3 days**	**Wed 2/18/15**	**Fri 2/20/15**
11		Southeast	1 day	Wed 2/18/15	Wed 2/18/15
12		Northeast	2 days	Thu 2/19/15	Fri 2/20/15
13					
14		**CIP Concrete**	**16 days**	**Mon 2/16/15**	**Mon 3/9/15**
15		F&P Footings NE/A line	5 days	Mon 2/16/15	Fri 2/20/15
16		F&P Walls/Columns Level P NE	5 days	Mon 2/23/15	Fri 2/27/15
17		Shotcrete Northwest	2 days	Thu 2/19/15	Fri 2/20/15
18		F&P Columns NW	2 days	Mon 2/16/15	Tue 2/17/15
19		SOG NW	2 days	Fri 3/6/15	Mon 3/9/15
20					
21		**Below Slab Utilities**	**4 days**	**Mon 2/23/15**	**Thu 2/26/15**
22		Sewer NW	4 days	Mon 2/23/15	Thu 2/26/15
23		Slab Drainage NW	4 days	Mon 2/23/15	Thu 2/26/15
24					
25					
26		**Waterproofing**	**2 days**	**Mon 2/16/15**	**Tue 2/17/15**
27		Elevator 1&2	2 days	Mon 2/16/15	Tue 2/17/15
28					
29		**Temp Power**	**5 days**	**Mon 2/16/15**	**Fri 2/20/15**
30		Install Panels 5 line	5 days	Mon 2/16/15	Fri 2/20/15

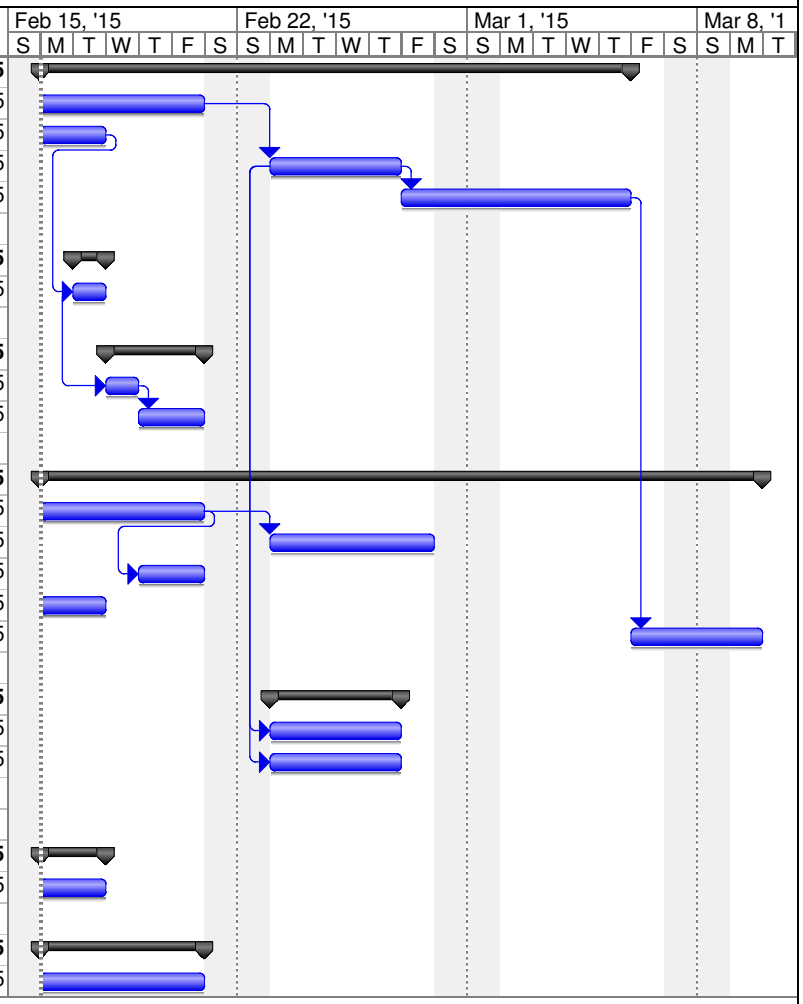

Project: 3wk Look ahead 2-16-15
Date: Mon 2/16/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
