Hadley Mixed use
Legacy
3 wk Look ahead
11-16-2015

ID		Task Name	Duration	Start	Finish
1		**Site Grading/Utilities**	**6 days**	**Mon 11/16/15**	**Mon 11/23/15**
2		**West**	**6 days**	**Mon 11/16/15**	**Mon 11/23/15**
3		Exc/Backfill Rem Sitewall	2 days	Mon 11/16/15	Mon 11/23/15
4		**North**	**4 days**	**Mon 11/16/15**	**Thu 11/19/15**
5		Set Vaults/Conduit	1 day	Mon 11/16/15	Mon 11/16/15
6		Backfill Elect Vaults	1 day	Tue 11/17/15	Tue 11/17/15
7		Backfill Conduit Runs	1 day	Wed 11/18/15	Wed 11/18/15
8		Open Secondary Trench	1 day	Thu 11/19/15	Thu 11/19/15
9					
10		**Site/Structure**	**10 days**	**Mon 11/16/15**	**Tue 12/1/15**
11		**West**	**4 days**	**Mon 11/16/15**	**Thu 11/19/15**
12		F&P Retaing walls	4 days	Mon 11/16/15	Thu 11/19/15
13		**North**	**7 days**	**Thu 11/19/15**	**Tue 12/1/15**
14		Retaining Walls	7 days	Thu 11/19/15	Tue 12/1/15
15		**East**	**1 day**	**Thu 11/19/15**	**Thu 11/19/15**
16		Storefront Topping slab	1 day	Thu 11/19/15	Thu 11/19/15
17					
18					
19		**Wood Framing/Roofing**	**13 days**	**Mon 11/16/15**	**Fri 12/4/15**
20		**North/Southwest**	**13 days**	**Mon 11/16/15**	**Fri 12/4/15**
21		Remaining Crickets	3 days	Mon 11/16/15	Wed 11/18/15
22		Roof	10 days	Thu 11/19/15	Fri 12/4/15
23		**Penthouse**	**10 days**	**Mon 11/23/15**	**Tue 12/8/15**
24		Frame	5 days	Mon 11/23/15	Tue 12/1/15
25		Joist/Sheath	5 days	Wed 12/2/15	Tue 12/8/15
26		**Southeast**	**21 days**	**Mon 11/16/15**	**Wed 12/16/15**
27		Complete Framing	5 days	Mon 11/16/15	Fri 11/20/15
28		Walkway Stanchions	5 days	Mon 11/23/15	Tue 12/1/15
29		Crickets	3 days	Wed 12/2/15	Fri 12/4/15
30		Roofing	8 days	Mon 12/7/15	Wed 12/16/15
31					
32		**Exterior**	**23 days**	**Mon 11/16/15**	**Fri 12/18/15**
33		Wrap/Set Door Pans/ Windows West	6 days	Mon 11/16/15	Mon 11/23/15
34		Deliver Windows Complete	11 days	Mon 11/16/15	Wed 12/2/15

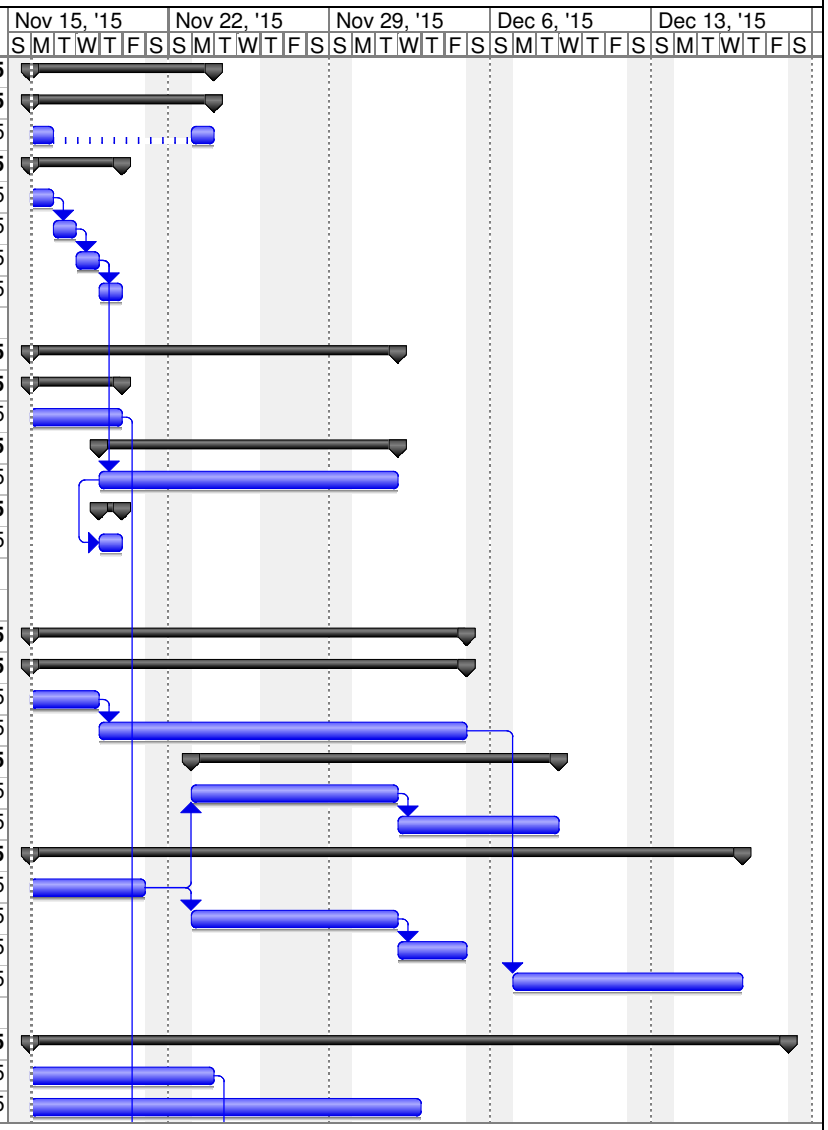

Project: 3wk 11-16-2015
Date: Mon 11/16/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
11-16-2015

ID		Task Name	Duration	Start	Finish
35		Target Wall Stubs	4 days	Mon 11/16/15	Thu 11/19/15
36		Set Rm West Scaffold	2 days	Mon 11/16/15	Tue 11/17/15
37		Tyvek	2 days	Tue 11/24/15	Wed 11/25/15
38		Siding	15 days	Mon 11/30/15	Fri 12/18/15
39					
40		**Mtl Stud Framing**	**8 days**	**Mon 11/16/15**	**Wed 11/25/15**
41		Rock Storefronts	4 days	Mon 11/16/15	Thu 11/19/15
42		Rock Ext Level 1-2 South	4 days	Fri 11/20/15	Wed 11/25/15
43					
44		**Hollow metal**	**2 days**	**Mon 11/16/15**	**Tue 11/17/15**
45		Swing Doors	2 days	Mon 11/16/15	Tue 11/17/15
46					
47		**Waterproofing**	**1 day**	**Fri 11/20/15**	**Fri 11/20/15**
48		Bentonine Exhaust Shaft/N Wall	1 day	Fri 11/20/15	Fri 11/20/15

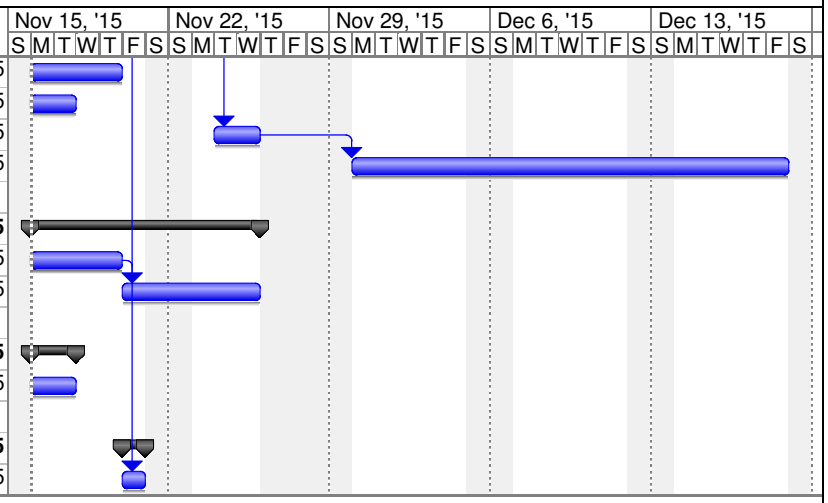

Project: 3wk 11-16-2015
Date: Mon 11/16/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
