Hadley Mixed use
Legacy
3 wk Look ahead
11-30-2015

ID	Task Name	Duration	Start	Finish
1	**Site Grading/Utilities**	**5 days**	**Mon 11/30/15**	**Fri 12/4/15**
2	**West**	**1 day**	**Mon 11/30/15**	**Mon 11/30/15**
3	Rock Sidewalk Subgrade	1 day	Mon 11/30/15	Mon 11/30/15
4	**North**	**5 days**	**Mon 11/30/15**	**Fri 12/4/15**
5	Backfill NW	1 day	Mon 11/30/15	Mon 11/30/15
6	Excavate Transformer room	2 days	Mon 11/30/15	Tue 12/1/15
7	Backfill NE Ret wall	3 days	Wed 12/2/15	Fri 12/4/15
8				
9	**Site/Structure**	**9 days**	**Mon 11/30/15**	**Thu 12/10/15**
10	**North**	**9 days**	**Mon 11/30/15**	**Thu 12/10/15**
11	Retaining Walls	7 days	Mon 11/30/15	Thu 12/10/15
12	**South**	**5 days**	**Mon 11/30/15**	**Fri 12/4/15**
13	F&P Planters	5 days	Mon 11/30/15	Fri 12/4/15
14				
15	**Wood Framing/Roofing**	**24 days**	**Mon 11/30/15**	**Mon 1/4/16**
16	**North/Southwest**	**10 days**	**Mon 11/30/15**	**Fri 12/11/15**
17	Roof	10 days	Mon 11/30/15	Fri 12/11/15
18	**Penthouse SE**	**8 days**	**Mon 11/30/15**	**Wed 12/9/15**
19	Frame	7 days	Mon 11/30/15	Tue 12/8/15
20	Joist/Sheath	3 days	Mon 12/7/15	Wed 12/9/15
21	**Southeast**	**19 days**	**Mon 12/7/15**	**Mon 1/4/16**
22	Complete Framing	3 days	Mon 12/7/15	Wed 12/9/15
23	Frame Trellis Walls	5 days	Mon 12/7/15	Fri 12/11/15
24	Walkway Stanchions	5 days	Tue 12/8/15	Mon 12/14/15
25	Crickets	5 days	Tue 12/15/15	Mon 12/21/15
26	Roofing	8 days	Tue 12/22/15	Mon 1/4/16
27				
28	**Exterior**	**20 days**	**Mon 11/30/15**	**Tue 12/29/15**
29	**West**	**19 days**	**Mon 11/30/15**	**Mon 12/28/15**
30	Bonnet Scaffold	3 days	Mon 11/30/15	Wed 12/2/15
31	Pre Wrap Inspection West	1 day	Tue 12/1/15	Tue 12/1/15
32	Wrap/Set Door Pans/ Windows West	4 days	Wed 12/2/15	Mon 12/7/15
33	Knife Plates/Target Wall Stubs	1 day	Mon 11/30/15	Mon 11/30/15
34	Spray Parapet Insulation	1 day	Wed 12/2/15	Wed 12/2/15

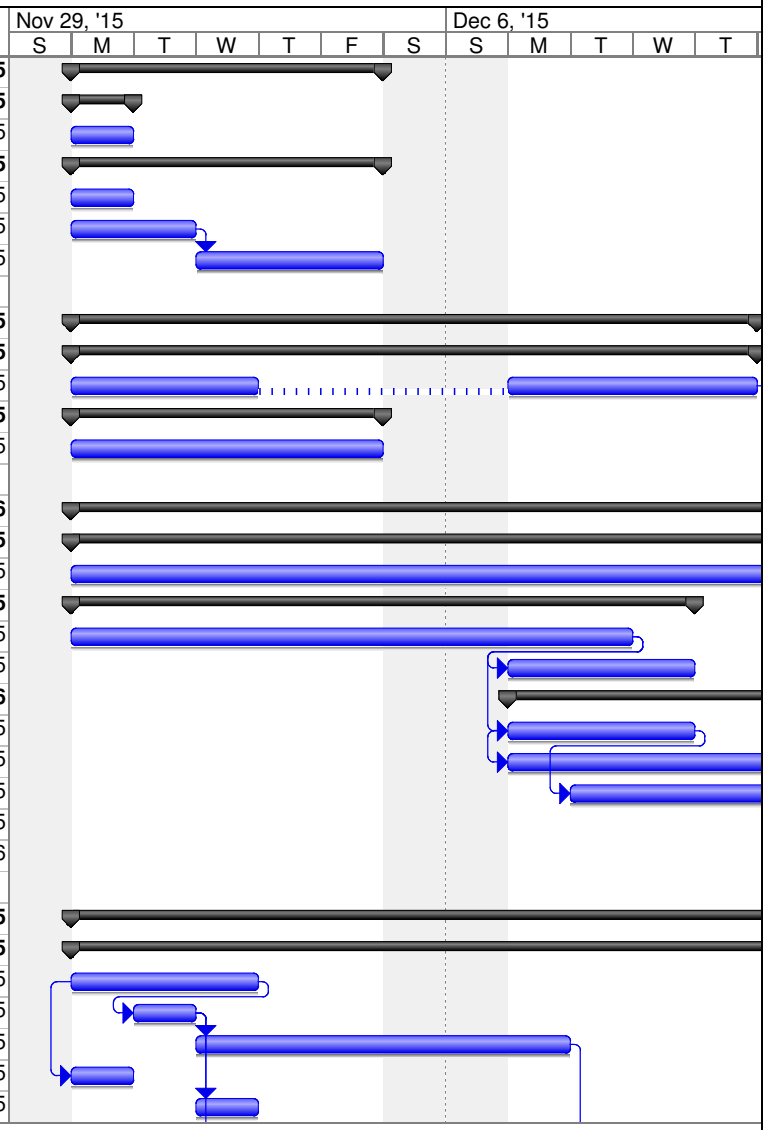

Project: 3wk 11-30-2015
Date: Fri 11/27/15

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

Hadley Mixed use
Legacy
3 wk Look ahead
11-30-2015

ID		Task Name	Duration	Start	Finish
35		Tyvek West	2 days	Wed 12/2/15	Thu 12/3/15
36		Siding West	15 days	Fri 12/4/15	Mon 12/28/15
37					
38		**North**	**11 days**	**Fri 12/11/15**	**Tue 12/29/15**
39		Set Rem Scaffold	2 days	Fri 12/11/15	Mon 12/14/15
40		Prep Densglass/Trim Openings	3 days	Tue 12/15/15	Thu 12/17/15
41		Wrap Openings/Set Windows	8 days	Wed 12/16/15	Tue 12/29/15
42					
43		**Courtyard**	**22 days**	**Tue 12/8/15**	**Fri 1/8/16**
44		**West**	**22 days**	**Tue 12/8/15**	**Fri 1/8/16**
45		Prep D-Glass/Openings	2 days	Tue 12/8/15	Wed 12/9/15
46		Wrap/Set Windows	8 days	Thu 12/10/15	Mon 12/21/15
47		Siding W Crtyrd	15 days	Thu 12/17/15	Fri 1/8/16
48					
49		**Mtl Stud Framing**	**8 days**	**Mon 11/30/15**	**Wed 12/9/15**
50		Rock Storefronts	4 days	Mon 11/30/15	Thu 12/3/15
51		Rock Ext Level 1-2 South	4 days	Fri 12/4/15	Wed 12/9/15
52					
53		**Temp Heat**	**5 days**	**Thu 12/10/15**	**Wed 12/16/15**
54		Temp Gas to Meter	1 day	Thu 12/10/15	Thu 12/10/15
55		Deliver/Set Equipment	3 days	Fri 12/11/15	Tue 12/15/15
56		Temp Heat West	1 day	Wed 12/16/15	Wed 12/16/15

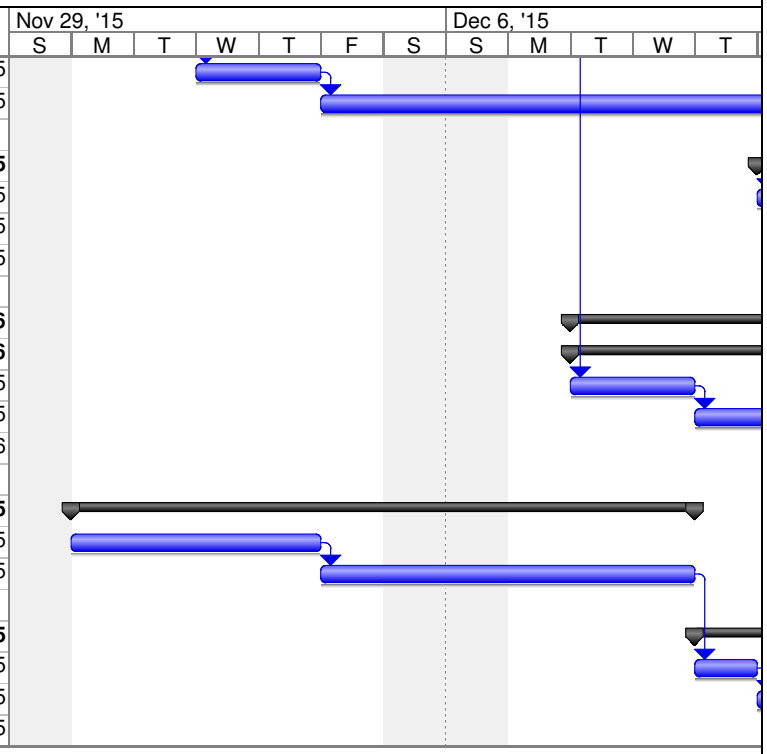

Project: 3wk 11-30-2015
Date: Fri 11/27/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
11-30-2015

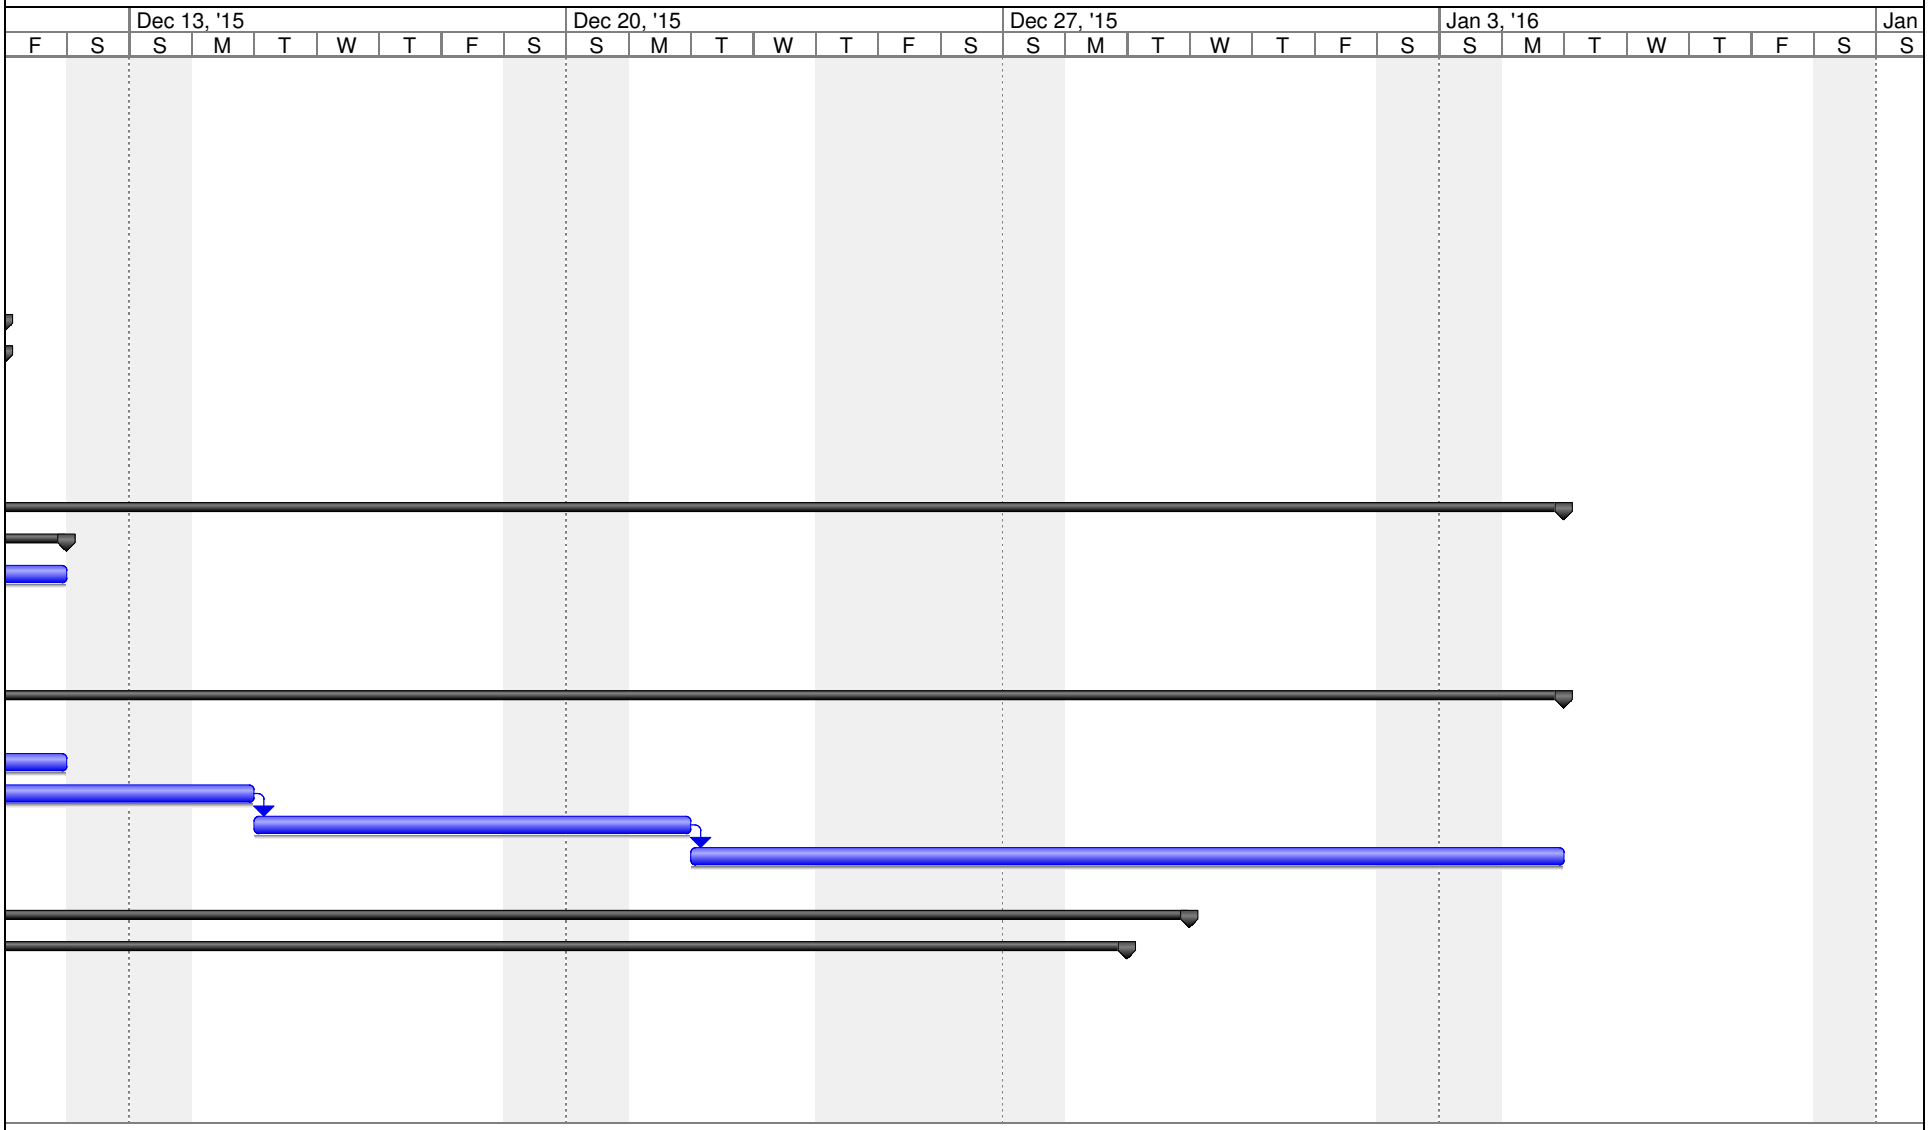

Project: 3wk 11-30-2015
Date: Fri 11/27/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
11-30-2015

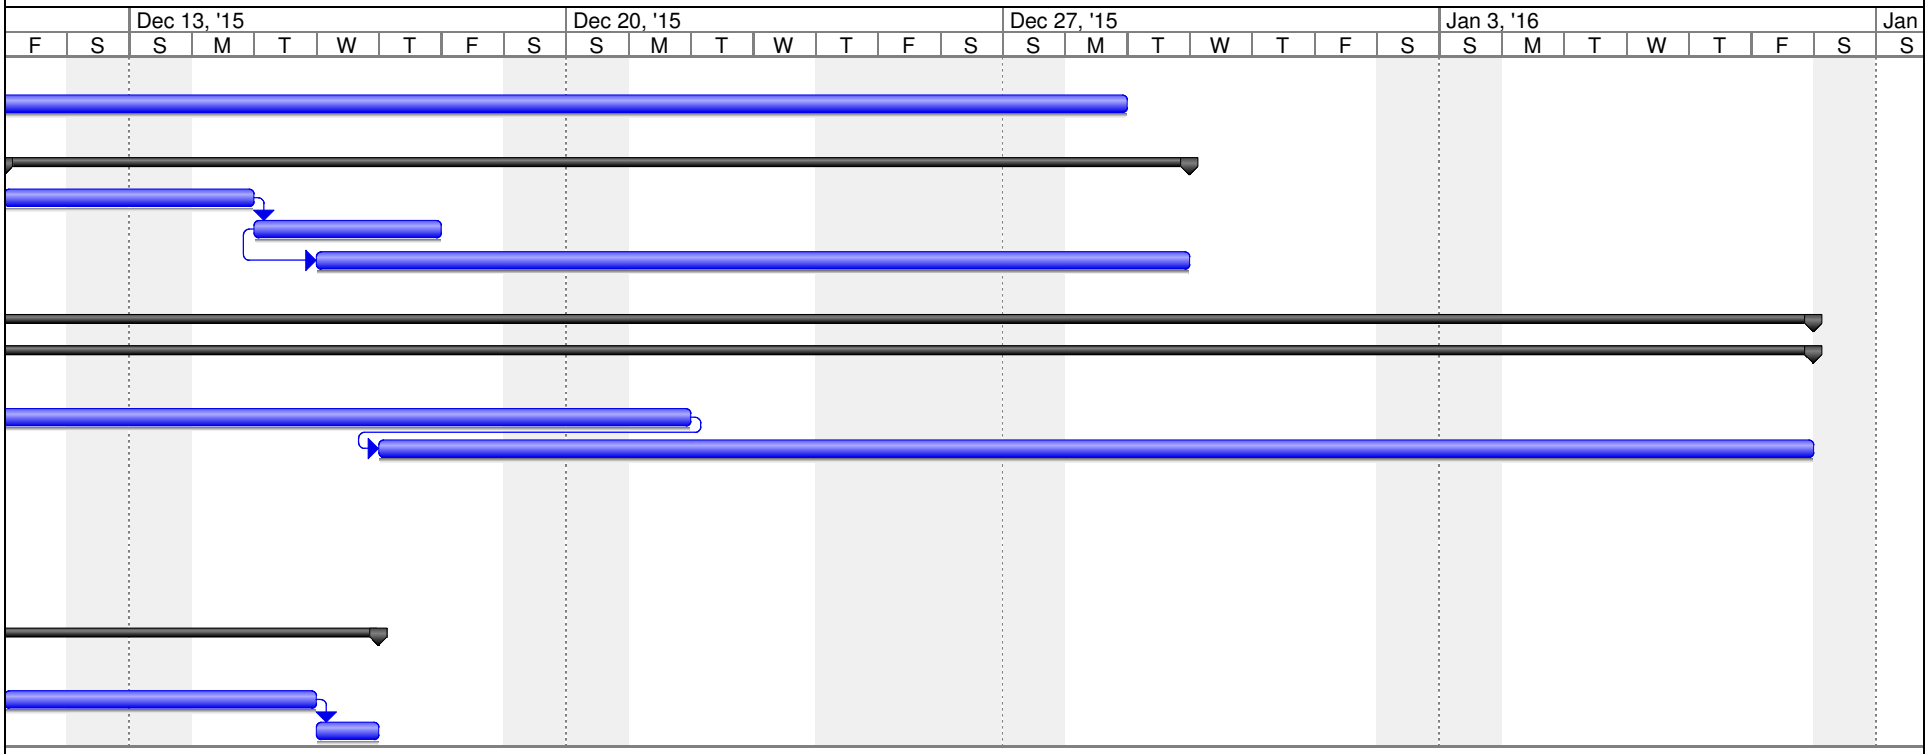

Project: 3wk 11-30-2015
Date: Fri 11/27/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
