Hadley Mixed use
Legacy
3 wk Look ahead
3-23-2015

ID		Task Name	Duration	Start	Finish
1		**Excavation**	**13 days**	**Mon 3/23/15**	**Wed 4/8/15**
2		Backfill/Grade NE	5 days	Mon 3/23/15	Fri 3/27/15
3		Pipe Trenching NE	5 days	Thu 3/26/15	Wed 4/1/15
4		Vapor Barrier/Cap Break NE	5 days	Thu 4/2/15	Wed 4/8/15
5		Backfill 5, 7,H.5Line Walls	7 days	Mon 3/23/15	Tue 3/31/15
6		Exc Srair 4 ftg	1 day	Thu 3/26/15	Thu 3/26/15
7					
8		**Crane**	**1 day**	**Wed 3/25/15**	**Wed 3/25/15**
9		Demob 90 Ton	1 day	Wed 3/25/15	Wed 3/25/15
10		Repair Boom	1 day	Wed 3/25/15	Wed 3/25/15
11					
12		**Utilities**	**1 day**	**Wed 3/25/15**	**Wed 3/25/15**
13		Site Utility Precon	1 day	Wed 3/25/15	Wed 3/25/15
14					
15		**Underslab Piping**	**7 days?**	**Mon 3/23/15**	**Tue 3/31/15**
16		Northeast Storm/Slab Drainage	7 days	Mon 3/23/15	Tue 3/31/15
17		Trench Drain NE Entry	2 days	Mon 3/30/15	Tue 3/31/15
18		Run L1 to LP Drain Piping	1 day?	Fri 3/27/15	Fri 3/27/15
19					
20		**CIP Concrete**	**15 days**	**Mon 3/23/15**	**Fri 4/10/15**
21		F&P Walls/Columns Level P NE	6 days	Mon 3/23/15	Mon 3/30/15
22		Pour Stair 4 Ftg	3 days	Fri 3/27/15	Tue 3/31/15
23		Pour SOG NE	1 day	Thu 4/9/15	Thu 4/9/15
24		Sawcut	1 day	Fri 4/10/15	Fri 4/10/15
25		L1 Deck Shoring NW	1 day	Mon 3/23/15	Mon 3/23/15
26		Edgeform/Bottom mat	1 day	Mon 3/23/15	Mon 3/23/15
27		MEP Cans	0.5 days	Tue 3/24/15	Tue 3/24/15
28		Cables /Top mat	2 days	Tue 3/24/15	Wed 3/25/15
29		Smurf	0.5 days	Thu 3/26/15	Thu 3/26/15
30		Inspections	0.5 days	Thu 3/26/15	Thu 3/26/15
31		Pour L1 PT NW	1 day	Fri 3/27/15	Fri 3/27/15
32		Stress/Strip	7 days	Mon 3/30/15	Tue 4/7/15

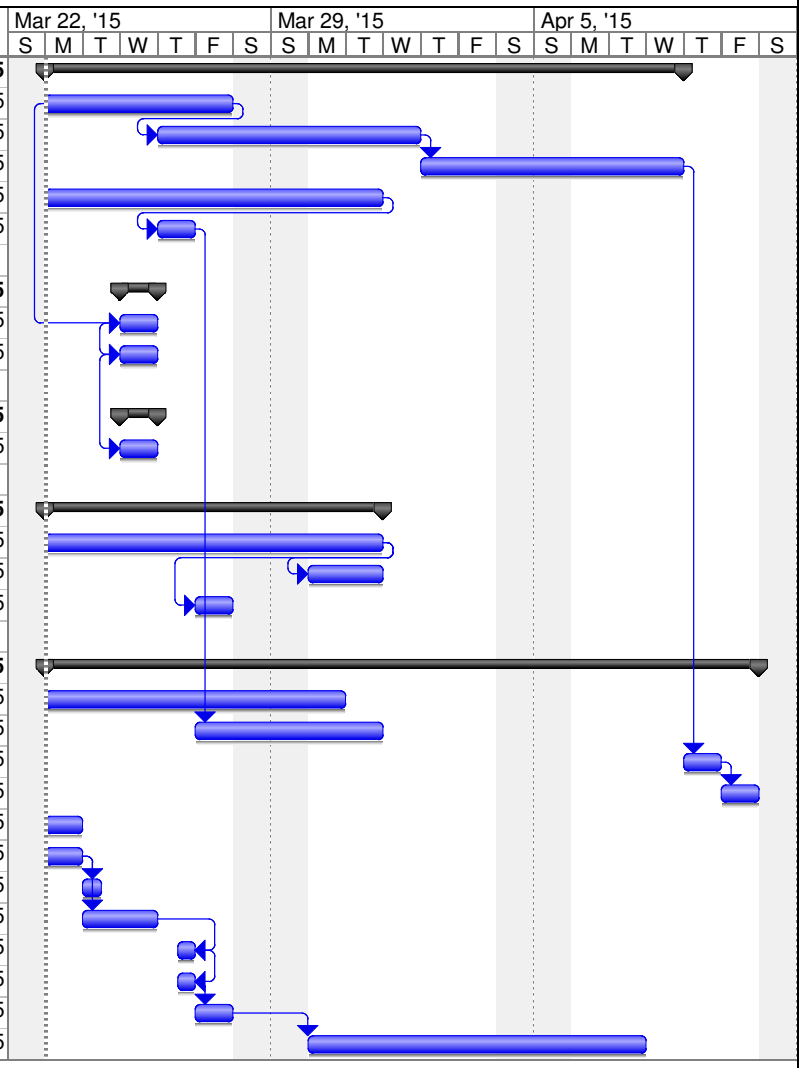

Project: 3wk look ahead 3-23-15
Date: Mon 3/23/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
