Hadley Mixed use
Legacy
3 wk Look ahead
3-30-2015

ID		Task Name	Duration	Start	Finish
1		**Excavation**	**7 days**	**Mon 3/30/15**	**Tue 4/7/15**
2		Backfill/Grade NE	5 days	Mon 3/30/15	Fri 4/3/15
3		Pipe Trenching NE	5 days	Mon 3/30/15	Fri 4/3/15
4		Vapor Barrier/Cap Break NE	5 days	Wed 4/1/15	Tue 4/7/15
5		Backfill 5, 7,H.5Line Walls	7 days	Mon 3/30/15	Tue 4/7/15
6		Exc Srair 4/10 Line ftgs	2 days	Mon 3/30/15	Tue 3/31/15
7					
8		**Waterproofing**	**7 days**	**Mon 3/30/15**	**Tue 4/7/15**
9		1 Line Wall North	2 days	Mon 3/30/15	Tue 3/31/15
10		Epro 7/M Line	1 day	Tue 4/7/15	Tue 4/7/15
11					
12		**Utilities**	**10 days**	**Mon 3/30/15**	**Fri 4/10/15**
13		Pothole	1 day	Fri 4/10/15	Fri 4/10/15
14		Elect mains Level P	3 days	Mon 3/30/15	Wed 4/1/15
15					
16		**Underslab Piping**	**3 days**	**Wed 4/1/15**	**Fri 4/3/15**
17		Northeast Storm/Slab Drainage	3 days	Wed 4/1/15	Fri 4/3/15
18		Trench Drain NE Entry	1 day	Fri 4/3/15	Fri 4/3/15
19		Run L1 to LP Drain Piping	2 days	Wed 4/1/15	Thu 4/2/15
20					
21		**CIP Concrete**	**11 days**	**Mon 3/30/15**	**Mon 4/13/15**
22		Pour Stair 4/10 Line Ftgs	3 days	Wed 4/1/15	Fri 4/3/15
23		Pour SOG NE	1 day	Thu 4/9/15	Thu 4/9/15
24		Sawcut	1 day	Fri 4/10/15	Fri 4/10/15
25		Cables /Top mat	1 day	Mon 3/30/15	Mon 3/30/15
26		Inspections	0.5 days	Mon 3/30/15	Mon 3/30/15
27		Pour L1 PT NW	1 day	Tue 3/31/15	Tue 3/31/15
28		Stress/Strip	7 days	Fri 4/3/15	Mon 4/13/15
29		Pour Rem Level P walls	2 days	Thu 4/2/15	Fri 4/3/15
30		Shotcrete South	1 day	Thu 4/9/15	Thu 4/9/15

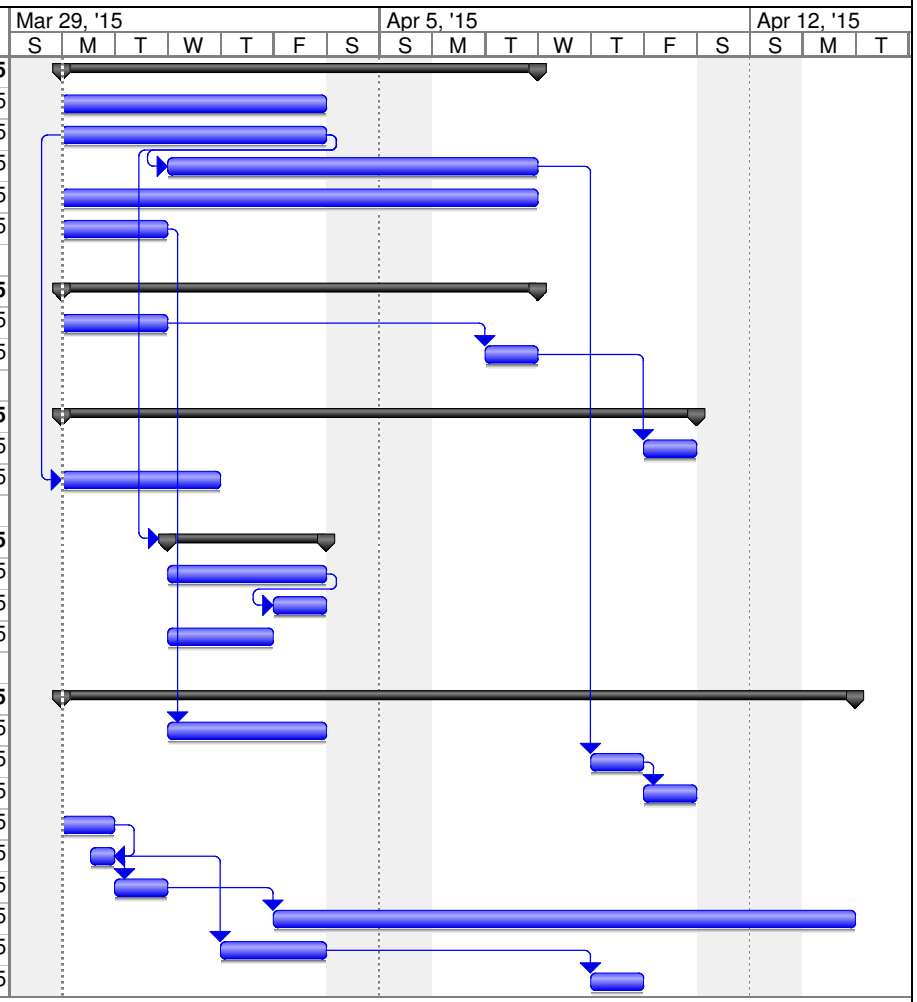

Project: 3wk look ahead 3-30-15
Date: Mon 3/30/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
