Hadley Mixed use
Legacy
3 wk Look ahead
4-13-2015

ID		Task Name	Duration	Start	Finish
1		**Excavation**	**5 days**	**Mon 4/13/15**	**Fri 4/17/15**
2		Backfill 5, 7,H.5Line Walls	4 days	Mon 4/13/15	Thu 4/16/15
3		Grade Ramp	1 day	Tue 4/14/15	Tue 4/14/15
4		Excavate Ftgs SW	2 days	Thu 4/16/15	Fri 4/17/15
5					
6		**Southwest Shoring**	**3 days**	**Mon 4/13/15**	**Wed 4/15/15**
7		Remove Waterproofing	2 days	Mon 4/13/15	Tue 4/14/15
8		Drill/Grout South Wall	2 days	Mon 4/13/15	Tue 4/14/15
9		Repair Waterproofing	1 day	Wed 4/15/15	Wed 4/15/15
10					
11		**Underslab Piping**	**1 day**	**Mon 4/13/15**	**Mon 4/13/15**
12		Ramp Drain Line	1 day	Mon 4/13/15	Mon 4/13/15
13					
14		**CIP Concrete**	**18 days**	**Mon 4/13/15**	**Wed 5/6/15**
15		Strip/Reshore L1 NW	1 day	Mon 4/13/15	Mon 4/13/15
16		Strip Rem Level 1 walls NW	1 day	Mon 4/13/15	Mon 4/13/15
17		F&P Ftgs SW	5 days	Mon 4/20/15	Fri 4/24/15
18					
19		**Level 1 PT NE**	**12 days**	**Mon 4/13/15**	**Tue 4/28/15**
20		Shore/Deck L1 NE	6 days	Mon 4/13/15	Mon 4/20/15
21		MEP Layout	0.5 days	Tue 4/21/15	Tue 4/21/15
22		Bottom Mat	1 day	Tue 4/21/15	Tue 4/21/15
23		Profile PT	2 days	Wed 4/22/15	Thu 4/23/15
24		Smurf/Top Mat	2 days	Fri 4/24/15	Mon 4/27/15
25		Inspections	0.5 days	Mon 4/27/15	Mon 4/27/15
26		Pour	1 day	Tue 4/28/15	Tue 4/28/15
27		**Level 2 PT NW**	**12 days**	**Tue 4/21/15**	**Wed 5/6/15**
28		Shore Deck	6 days	Tue 4/21/15	Tue 4/28/15
29		MEP Layout	0.5 days	Wed 4/29/15	Wed 4/29/15
30		Bottom Mat	1 day	Wed 4/29/15	Wed 4/29/15
31		Profile PT	2 days	Thu 4/30/15	Fri 5/1/15
32		Smurf/Top Mat	2 days	Mon 5/4/15	Tue 5/5/15
33		Inspections	0.5 days	Tue 5/5/15	Tue 5/5/15
34		Pour	1 day	Wed 5/6/15	Wed 5/6/15

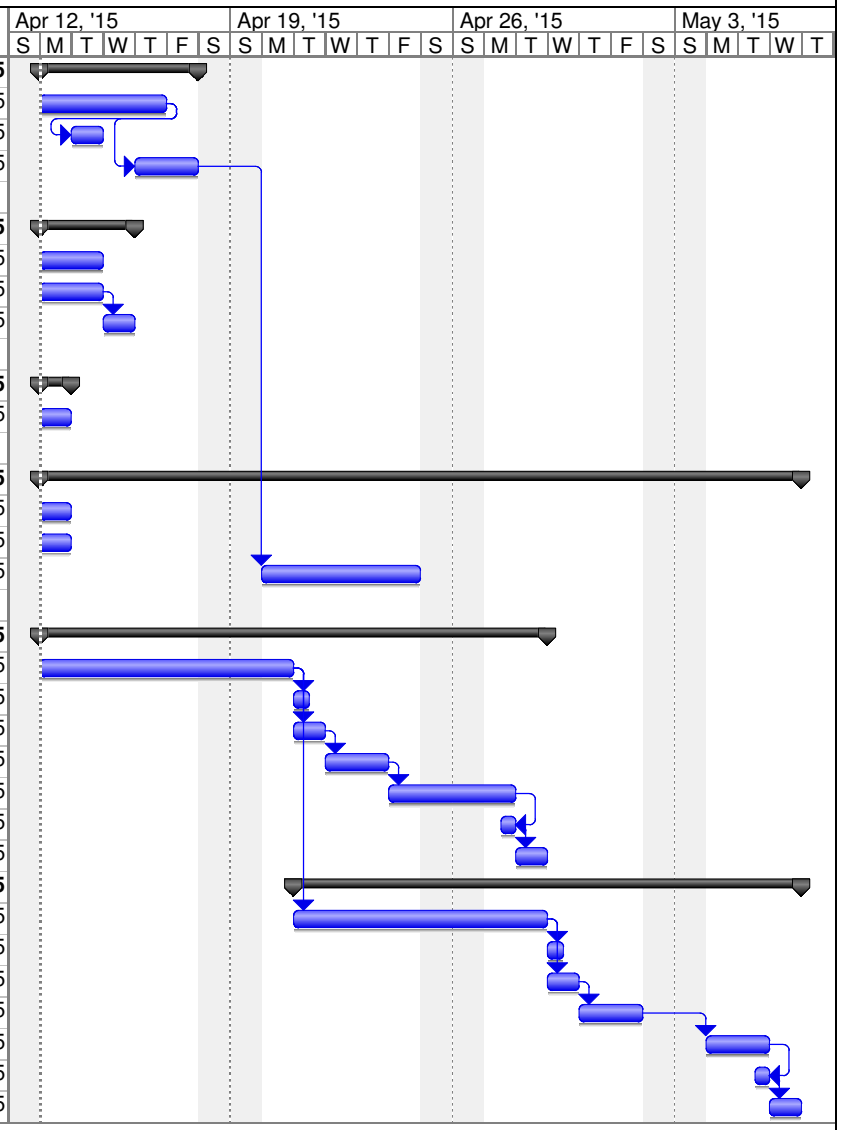

Project: 3wk look ahead 4-13-15
Date: Mon 4/13/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
