Hadley Mixed use
Legacy
3 wk Look ahead
4-20-2015

ID		Task Name	Duration	Start	Finish
1		**Excavation**	**11 days**	**Mon 4/20/15**	**Mon 5/4/15**
2		Backfill 5, 7,H.5Line Walls	5 days	Tue 4/28/15	Mon 5/4/15
3		Excavate Ftgs SW	3 days	Mon 4/20/15	Wed 4/22/15
4		Backfill 1 Line North	5 days	Thu 4/23/15	Wed 4/29/15
5					
6		**Underslab Piping**	**4 days**	**Thu 4/30/15**	**Tue 5/5/15**
7		Below Slab Drain Lines L1 SW	4 days	Thu 4/30/15	Tue 5/5/15
8					
9		**CIP Concrete**	**14 days**	**Mon 4/20/15**	**Thu 5/7/15**
10		F&P Ftgs SW	5 days	Tue 4/21/15	Mon 4/27/15
11		Shotcrete 10 Line ?	1 day	Tue 4/28/15	Tue 4/28/15
12					
13		**Level 1 PT NE**	**8 days**	**Mon 4/20/15**	**Wed 4/29/15**
14		MEP Layout	0.5 days	Mon 4/20/15	Mon 4/20/15
15		Bottom Mat	1 day	Mon 4/20/15	Mon 4/20/15
16		Profile PT	2 days	Tue 4/21/15	Wed 4/22/15
17		Smurf/Top Mat	2 days	Thu 4/23/15	Fri 4/24/15
18		Inspections	0.5 days	Fri 4/24/15	Fri 4/24/15
19		Pour	1 day	Wed 4/29/15	Wed 4/29/15
20					
21		**Level 2 PT NW**	**14 days**	**Mon 4/20/15**	**Thu 5/7/15**
22		Shore Deck	7 days	Mon 4/20/15	Tue 4/28/15
23		MEP Layout	0.5 days	Wed 4/29/15	Wed 4/29/15
24		Bottom Mat	1 day	Wed 4/29/15	Wed 4/29/15
25		Profile PT	2 days	Thu 4/30/15	Fri 5/1/15
26		Smurf/Top Mat	2 days	Mon 5/4/15	Tue 5/5/15
27		Inspections	0.5 days	Tue 5/5/15	Tue 5/5/15
28		Pour	1 day	Thu 5/7/15	Thu 5/7/15

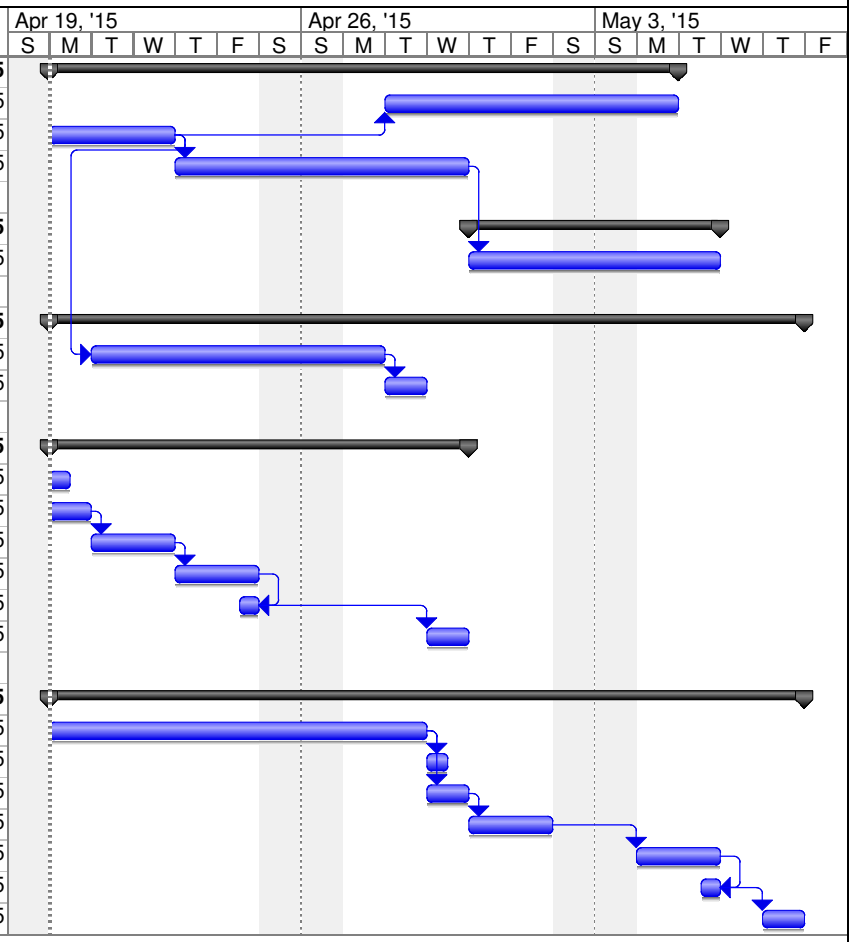

Project: 3wk look ahead 4-20-15
Date: Mon 4/20/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
