Hadley Mixed use
Legacy
3 wk Look ahead
4-27-2015

ID		Task Name	Duration	Start	Finish
1		**Excavation**	**18 days**	**Mon 4/27/15**	**Wed 5/20/15**
2		Export Cont.Soils	1 day	Mon 4/27/15	Mon 4/27/15
3		Backfill 5, 7,H.5Line Walls	3 days	Wed 4/29/15	Fri 5/1/15
4		Excavate Rem. Ftgs SW	3 days	Thu 4/30/15	Mon 5/4/15
5		Backfill 1 Line North	5 days	Mon 5/4/15	Fri 5/8/15
6		Slab on Grade Prep SW	12 days	Tue 5/5/15	Wed 5/20/15
7		Subgrade Retail SE	1 day	Mon 4/27/15	Mon 4/27/15
8					
9		**Instreet Utilities**	**1 day**	**Mon 4/27/15**	**Mon 4/27/15**
10		ROW Permit	1 day	Mon 4/27/15	Mon 4/27/15
11					
12		**Underslab Piping**	**6 days**	**Wed 4/29/15**	**Wed 5/6/15**
13		Below Slab Drain Lines L1 SW	6 days	Wed 4/29/15	Wed 5/6/15
14					
15		**CIP Concrete**	**17 days**	**Mon 4/27/15**	**Tue 5/19/15**
16		Restl Stair 3 Ftg.	2 days	Mon 4/27/15	Tue 4/28/15
17		Pour Stair 3 Ftg	1 day	Wed 4/29/15	Wed 4/29/15
18		Restl South wall Ftg. D to G @ GL10	3 days	Mon 4/27/15	Wed 4/29/15
19		Restl/Wire GL10 A to G	4 days	Thu 4/30/15	Tue 5/5/15
20		Shotcrete GL10 A to G	1 day	Mon 5/11/15	Mon 5/11/15
21		F&P Stair 3 Walls	4 days	Thu 4/30/15	Tue 5/5/15
22		F&P Stair 4 Walls	6 days	Tue 5/12/15	Tue 5/19/15
23		F&P Remaining L1 South Ftgs	4 days	Thu 4/30/15	Tue 5/5/15
24		F&P Remaining Walls/Columns L1 South	8 days	Wed 5/6/15	Fri 5/15/15
25					
26		**Level 1 PT NE**	**15 days**	**Mon 4/27/15**	**Fri 5/15/15**
27		Inspections	1 day	Mon 4/27/15	Mon 4/27/15
28		Pour	1 day	Tue 4/28/15	Tue 4/28/15
29		Strip/Reshore	6 days	Tue 5/5/15	Tue 5/12/15
30		F&P Walls/Columns to L2 NE	11 days	Fri 5/1/15	Fri 5/15/15
31					
32		**Level 2 PT NW**	**16 days**	**Mon 4/27/15**	**Mon 5/18/15**
33		MEP Layout	4 days	Mon 4/27/15	Thu 4/30/15
34		Bottom Mat	1 day	Thu 4/30/15	Thu 4/30/15

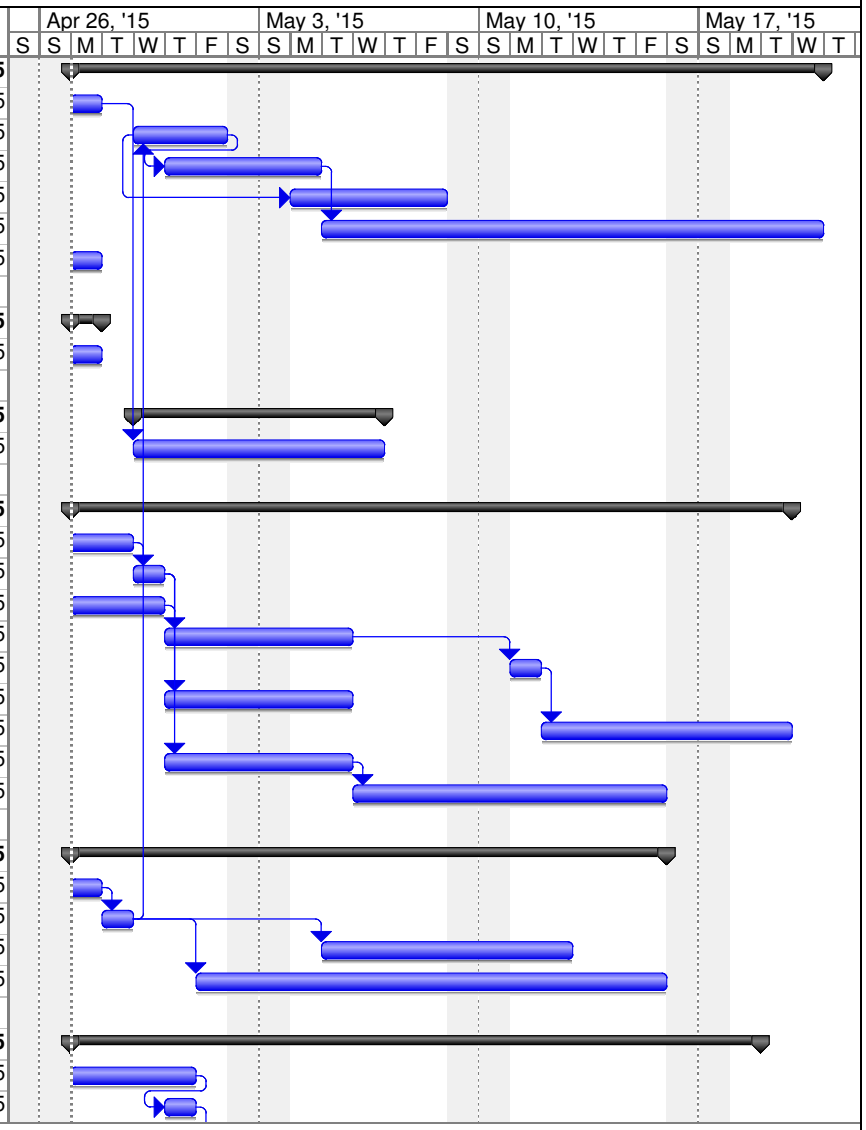

Project: 3wk look ahead 4-27-15
Date: Mon 4/27/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
4-27-2015

ID		Task Name	Duration	Start	Finish
35		Profile PT	2 days	Fri 5/1/15	Mon 5/4/15
36		Smurf/Top Mat	2 days	Tue 5/5/15	Wed 5/6/15
37		Inspections	1 day	Wed 5/6/15	Wed 5/6/15
38		Pour	1 day	Thu 5/7/15	Thu 5/7/15
39		Strip/Reshore	7 days	Fri 5/8/15	Mon 5/18/15



Project: 3wk look ahead 4-27-15
Date: Mon 4/27/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
