Hadley Mixed use
Legacy
3 wk Look ahead
4-6-2015

ID		Task Name	Duration	Start	Finish
1		**Excavation**	**7 days**	**Mon 4/6/15**	**Tue 4/14/15**
2		Backfill/Grade NE	1 day	Mon 4/6/15	Mon 4/6/15
3		Pipe Trenching NE	1 day	Mon 4/6/15	Mon 4/6/15
4		Vapor Barrier/Cap Break NE	3 days	Tue 4/7/15	Thu 4/9/15
5		Backfill 5, 7,H.5Line Walls	7 days	Mon 4/6/15	Tue 4/14/15
6		Grade Ramp	1 day	Wed 4/8/15	Wed 4/8/15
7					
8		**Waterproofing**	**1 day**	**Tue 4/7/15**	**Tue 4/7/15**
9		Epro Rem M Line Walls	1 day	Tue 4/7/15	Tue 4/7/15
10					
11		**Utilities**	**1 day**	**Mon 4/6/15**	**Mon 4/6/15**
12		Pothole	1 day	Mon 4/6/15	Mon 4/6/15
13		Profile	1 day	Mon 4/6/15	Mon 4/6/15
14					
15		**Underslab Piping**	**2 days**	**Mon 4/6/15**	**Tue 4/7/15**
16		Northeast Storm/Slab Drainage	1 day	Mon 4/6/15	Mon 4/6/15
17		Trench Drain NE Entry	1 day	Tue 4/7/15	Tue 4/7/15
18		Ramp Drain Line	1 day	Tue 4/7/15	Tue 4/7/15
19					
20		**CIP Concrete**	**14 days**	**Mon 4/6/15**	**Thu 4/23/15**
21		Pour SOG NE	1 day	Fri 4/10/15	Fri 4/10/15
22		Sawcut Saturday 11th	1 day	Fri 4/10/15	Fri 4/10/15
23		Strip/Reshore	5 days	Mon 4/6/15	Fri 4/10/15
24		Strip Rem Level P walls	1 day	Mon 4/6/15	Mon 4/6/15
25		Shotcrete L1 West	1 day	Tue 4/7/15	Tue 4/7/15
26		F&P Walls/Columns L1 NW	6 days	Mon 4/6/15	Mon 4/13/15
27		Shore/Deck L1 NE	6 days	Wed 4/8/15	Wed 4/15/15
28		MEP Layout	0.5 days	Thu 4/16/15	Thu 4/16/15
29		Bottom Mat	1 day	Thu 4/16/15	Thu 4/16/15
30		Profile PT	2 days	Fri 4/17/15	Mon 4/20/15
31		Smurf/Top Mat	2 days	Tue 4/21/15	Wed 4/22/15
32		Inspections	0.5 days	Wed 4/22/15	Wed 4/22/15
33		Pour	1 day	Thu 4/23/15	Thu 4/23/15

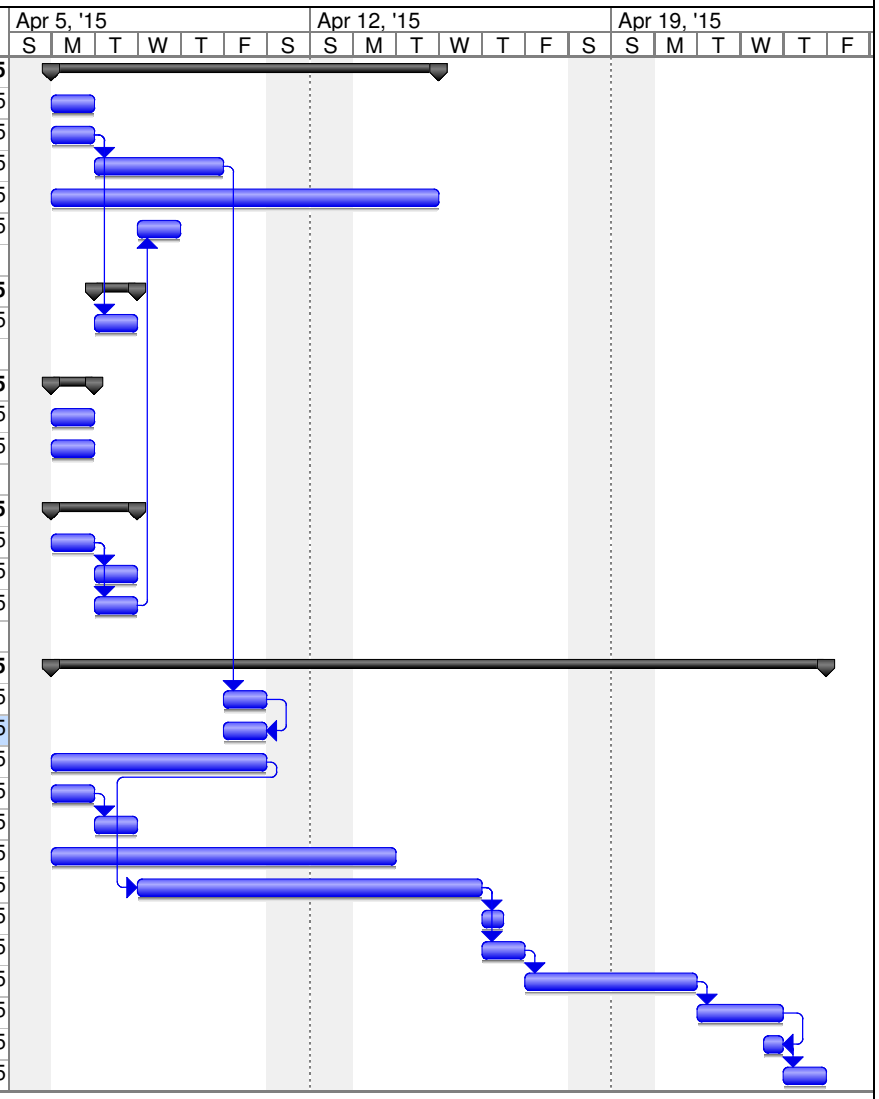

Project: 3wk look ahead 4-6-15
Date: Fri 4/3/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
