Hadley Mixed use
Legacy
3 wk Look ahead
6-29-2015

ID	Task Name	Duration	Start	Finish
1	**Excavation**	**7 days**	**Mon 6/29/15**	**Wed 7/8/15**
2	Exc Retail Ftgs	1 day	Mon 6/29/15	Mon 6/29/15
3	Slab Drain Trenches	1 day	Mon 6/29/15	Mon 6/29/15
4	SOG Prep SE Retail	2 days	Tue 7/7/15	Wed 7/8/15
5	Backfill West	5 days	Mon 6/29/15	Mon 7/6/15
6				
7	**Instreet Utilities**	**5 days**	**Mon 6/29/15**	**Mon 7/6/15**
8	Sanitary South	5 days	Mon 6/29/15	Mon 7/6/15
9				
10	**Underslab Piping**	**1 day**	**Mon 6/29/15**	**Mon 6/29/15**
11	Below Slab Drain Lines L1 SE Retail	1 day	Mon 6/29/15	Mon 6/29/15
12				
13	**CIP Concrete**	**43 days**	**Mon 6/29/15**	**Thu 8/27/15**
14	F&P Remaining L1 South Ftgs/Col's Retail	2 days	Tue 6/30/15	Wed 7/1/15
15	Stair 4/Columns	5 days	Tue 6/30/15	Tue 7/7/15
16	Pour Retail SOG	1 day	Thu 7/9/15	Thu 7/9/15
17				
18	**Level 3 PT NW**	**18 days**	**Mon 6/29/15**	**Thu 7/23/15**
19	Profile Tendons	2 days	Mon 6/29/15	Tue 6/30/15
20	Top Matt/Smurf	2 days	Wed 7/1/15	Thu 7/2/15
21	Raised Slab Edge/Blockouts	3 days	Mon 7/6/15	Wed 7/8/15
22	Inspections	1 day	Wed 7/8/15	Wed 7/8/15
23	Pour	1 day	Thu 7/9/15	Thu 7/9/15
24	Stress/Strip	7 days	Wed 7/15/15	Thu 7/23/15
25				
26	**Level 3 PT NE**	**30 days**	**Mon 6/29/15**	**Mon 8/10/15**
27	Shore/Deck	8 days	Mon 6/29/15	Thu 7/9/15
28	Layout/Sleeves	2 days	Fri 7/10/15	Mon 7/13/15
29	Bottom Mat/Sleeves	3 days	Tue 7/14/15	Thu 7/16/15
30	Edgeform/Misc Sleeves	2 days	Fri 7/17/15	Mon 7/20/15
31	Raised Slab Edge/Blockouts	2 days	Mon 7/20/15	Tue 7/21/15
32	Inspections	1 day	Wed 7/22/15	Wed 7/22/15
33	Pour	1 day	Thu 7/23/15	Thu 7/23/15
34	Stress/Strip	7 days	Wed 7/29/15	Thu 8/6/15

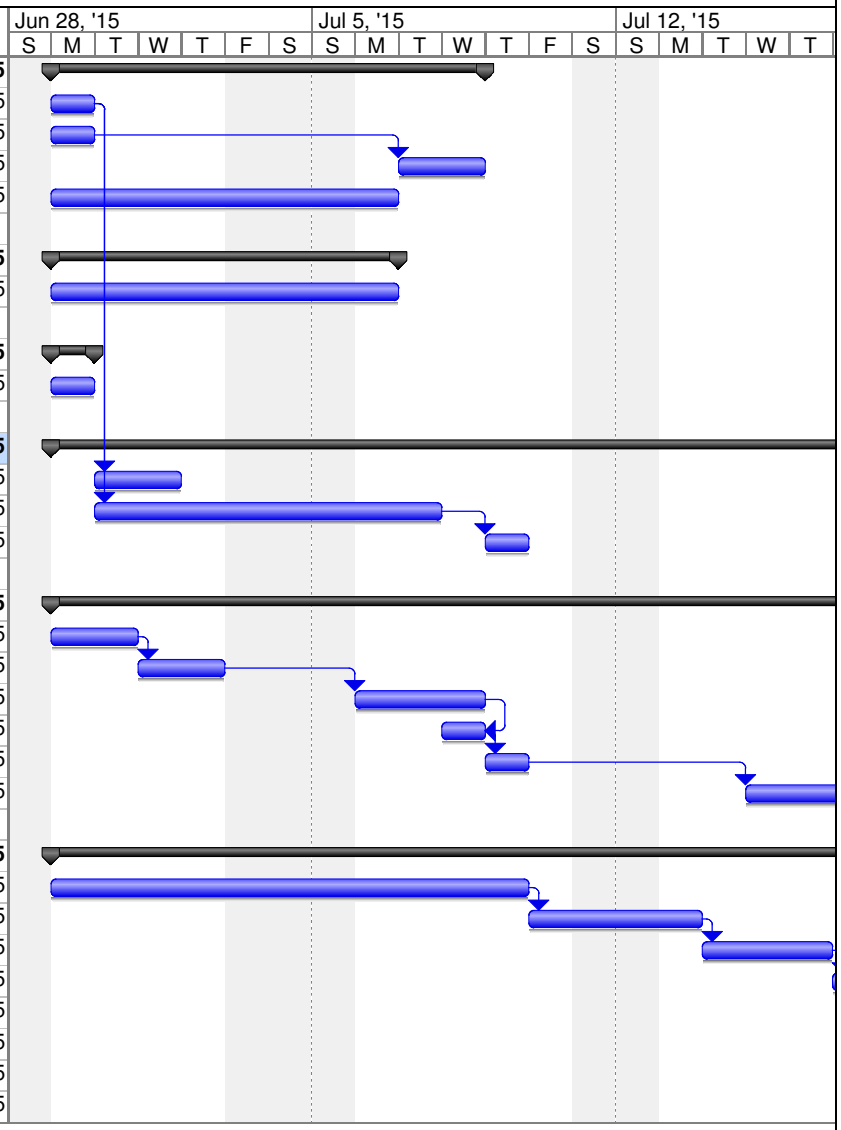

Project: 3wk look ahead 6-22-15
Date: Fri 6/26/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
6-29-2015

ID		Task Name	Duration	Start	Finish
35		Remove Reshores North	2 days	Fri 8/7/15	Mon 8/10/15
36					
37		**Level 3 PT SW**	**25 days**	**Fri 7/24/15**	**Thu 8/27/15**
38		Shore/Deck	8 days	Fri 7/24/15	Tue 8/4/15
39		Layout/Sleeves	2 days	Wed 8/5/15	Thu 8/6/15
40		Bottom Mat/Sleeves	2 days	Fri 8/7/15	Mon 8/10/15
41		Edgeform/Misc	2 days	Tue 8/11/15	Wed 8/12/15
42		Raised Slab Edge	2 days	Thu 8/13/15	Fri 8/14/15
43		Inspections	1 day	Thu 8/13/15	Thu 8/13/15
44		Pour	1 day	Fri 8/14/15	Fri 8/14/15
45		Stress/Strip	7 days	Wed 8/19/15	Thu 8/27/15
46					
47		**Wood Framing NW**	**14 days**	**Mon 8/3/15**	**Thu 8/20/15**
48		Layout Walls	1 day	Mon 8/3/15	Mon 8/3/15
49		Frame	5 days	Tue 8/4/15	Mon 8/10/15
50		TJI Joists	4 days	Tue 8/11/15	Fri 8/14/15
51		Deck	4 days	Mon 8/17/15	Thu 8/20/15

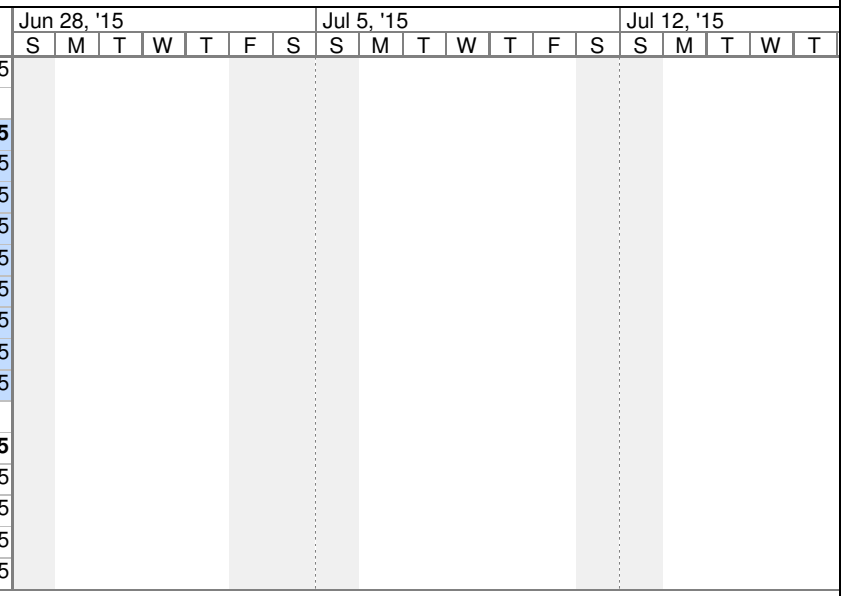

Project: 3wk look ahead 6-22-15
Date: Fri 6/26/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
6-29-2015

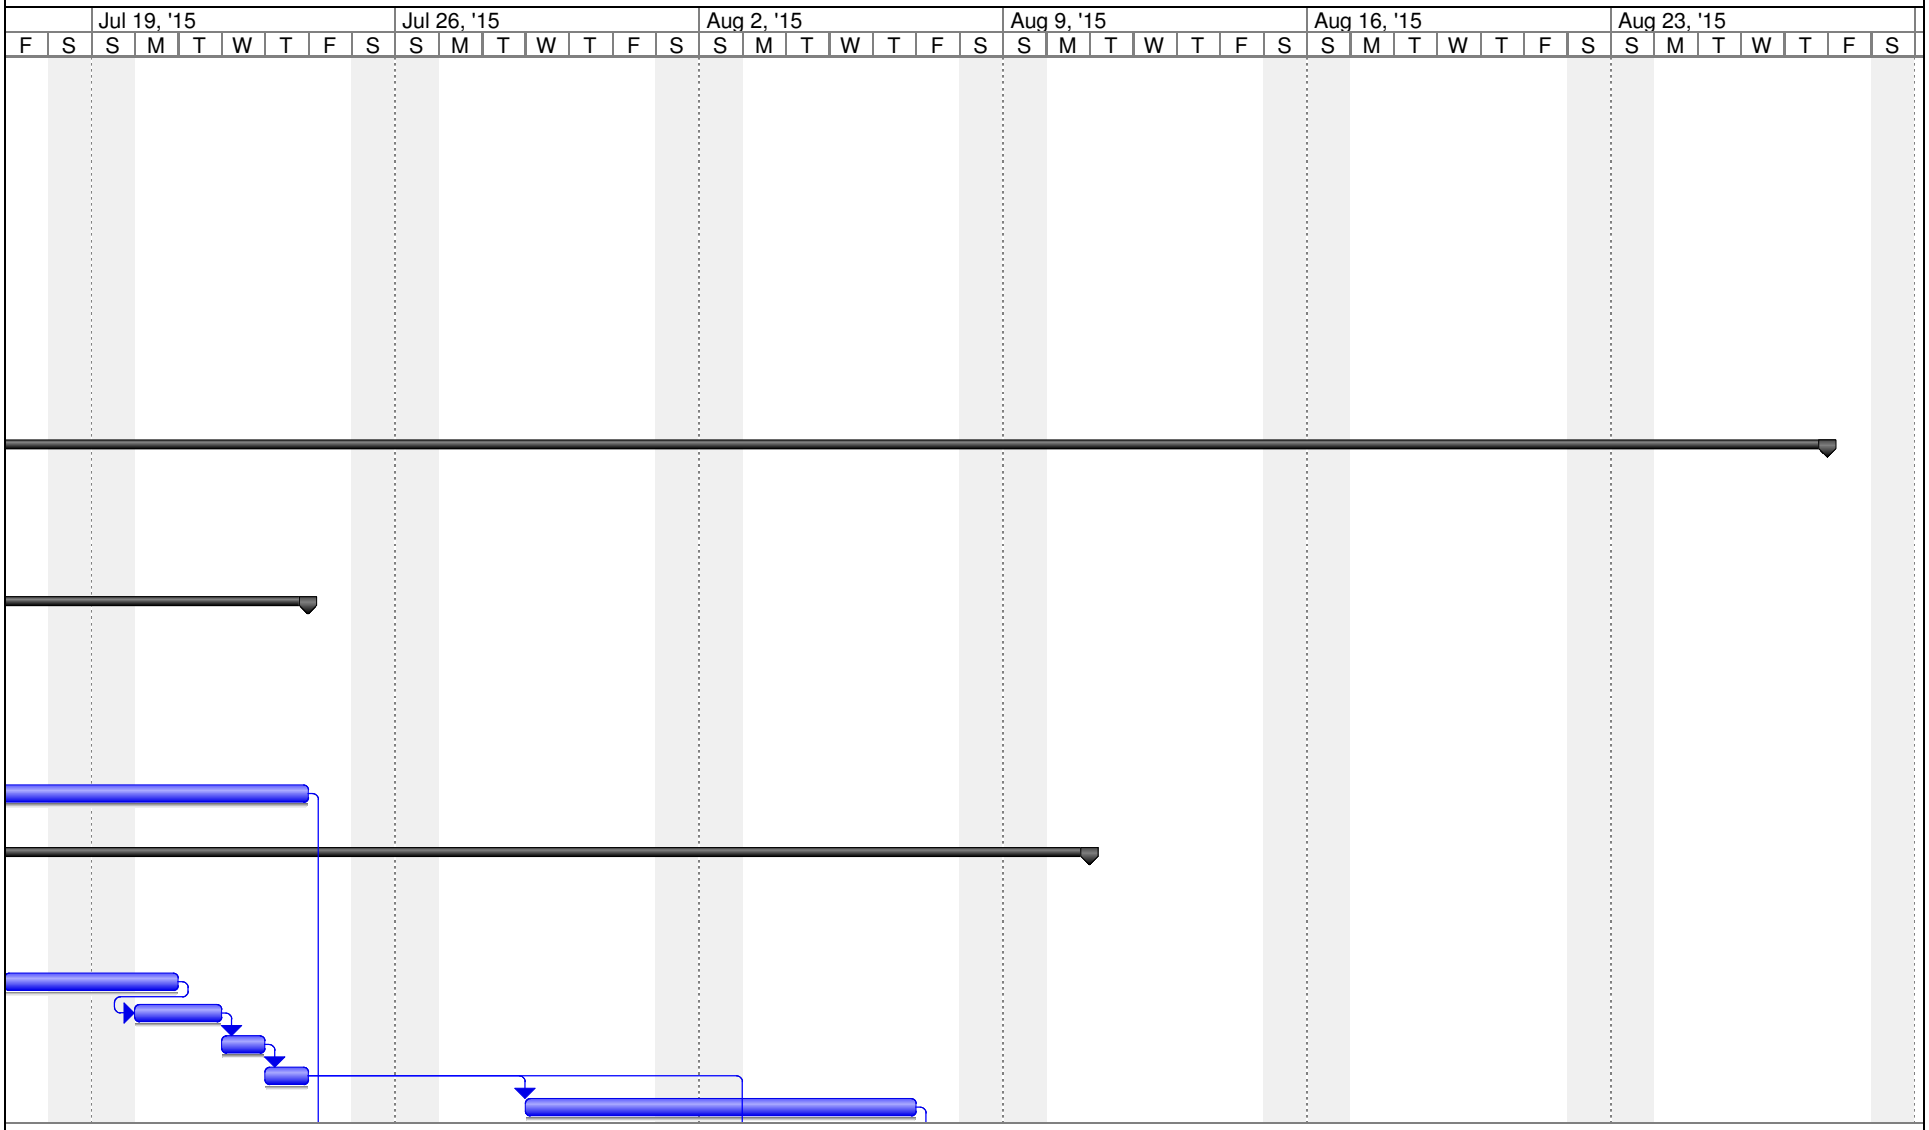

Project: 3wk look ahead 6-22-15
Date: Fri 6/26/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
6-29-2015

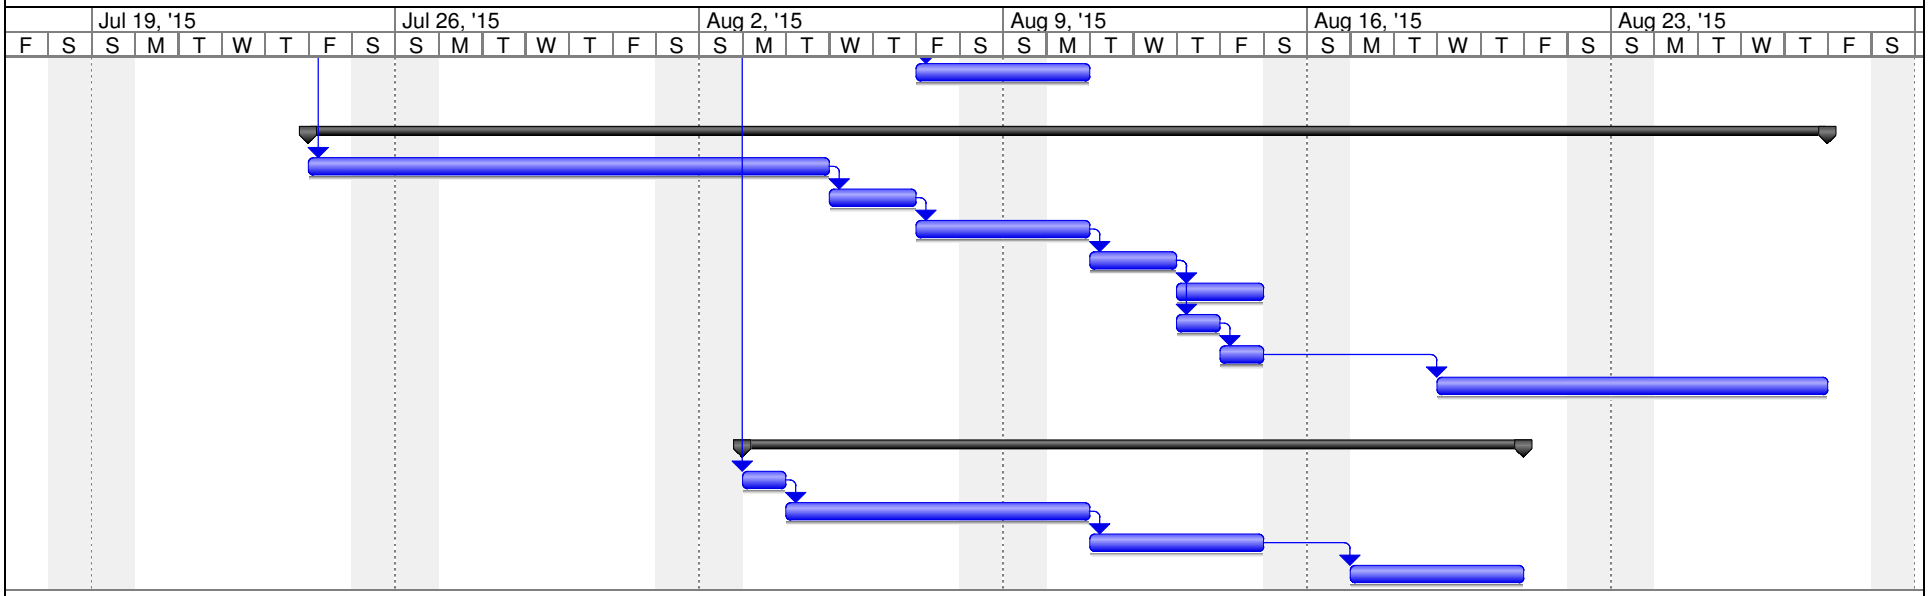

Project: 3wk look ahead 6-22-15
Date: Fri 6/26/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
