Hadley Mixed use
Legacy
3 wk Look ahead
7-13-2015

ID		Task Name	Duration	Start	Finish
1		**Excavation**	**5 days**	**Thu 8/13/15**	**Wed 8/19/15**
2		Backfill West	5 days	Thu 8/13/15	Wed 8/19/15
3					
4		**Instreet Utilities**	**5 days**	**Mon 7/13/15**	**Fri 7/17/15**
5		Sanitary South	5 days	Mon 7/13/15	Fri 7/17/15
6					
7		**CIP Concrete**	**7 days**	**Mon 7/13/15**	**Tue 7/21/15**
8		F&P Remaining L1 South Col's Retail	2 days	Mon 7/13/15	Tue 7/14/15
9		F&P NW Placing Boom Blockouts	5 days	Wed 7/15/15	Tue 7/21/15
10					
11		**Level 2 PT Southeast**	**31 days**	**Mon 7/13/15**	**Mon 8/24/15**
12		Shoring/Deck	5 days	Mon 7/13/15	Fri 7/17/15
13		Layout/Sleeves	1 day	Mon 7/20/15	Mon 7/20/15
14		Bottom Mat	1 day	Tue 7/21/15	Tue 7/21/15
15		Edgeform	1 day	Wed 7/22/15	Wed 7/22/15
16		Profile Tendons	2 days	Thu 7/23/15	Fri 7/24/15
17		Inspections	1 day	Mon 7/27/15	Mon 7/27/15
18		Pour	1 day	Wed 7/29/15	Wed 7/29/15
19		Strip/Reshore	5 days	Tue 8/4/15	Mon 8/10/15
20					
21		**Level 3 PT NE**	**21 days**	**Mon 7/13/15**	**Mon 8/10/15**
22		Shore/Deck	1 day	Mon 7/13/15	Mon 7/13/15
23		Layout/Sleeves	1 day	Tue 7/14/15	Tue 7/14/15
24		Bottom Mat/Sleeves	2 days	Wed 7/15/15	Thu 7/16/15
25		Edgeform/Misc Sleeves	2 days	Fri 7/17/15	Mon 7/20/15
26		Raised Slab Edge/Blockouts	2 days	Mon 7/20/15	Tue 7/21/15
27		Inspections	1 day	Wed 7/22/15	Wed 7/22/15
28		Pour	1 day	Thu 7/23/15	Thu 7/23/15
29		Stress/Strip	7 days	Wed 7/29/15	Thu 8/6/15
30		Remove Reshores North	2 days	Fri 8/7/15	Mon 8/10/15
31					
32		**Level 3 PT SW**	**25 days**	**Tue 7/21/15**	**Mon 8/24/15**
33		Shore/Deck	9 days	Tue 7/21/15	Fri 7/31/15
34		Layout/Sleeves	2 days	Mon 8/3/15	Tue 8/4/15

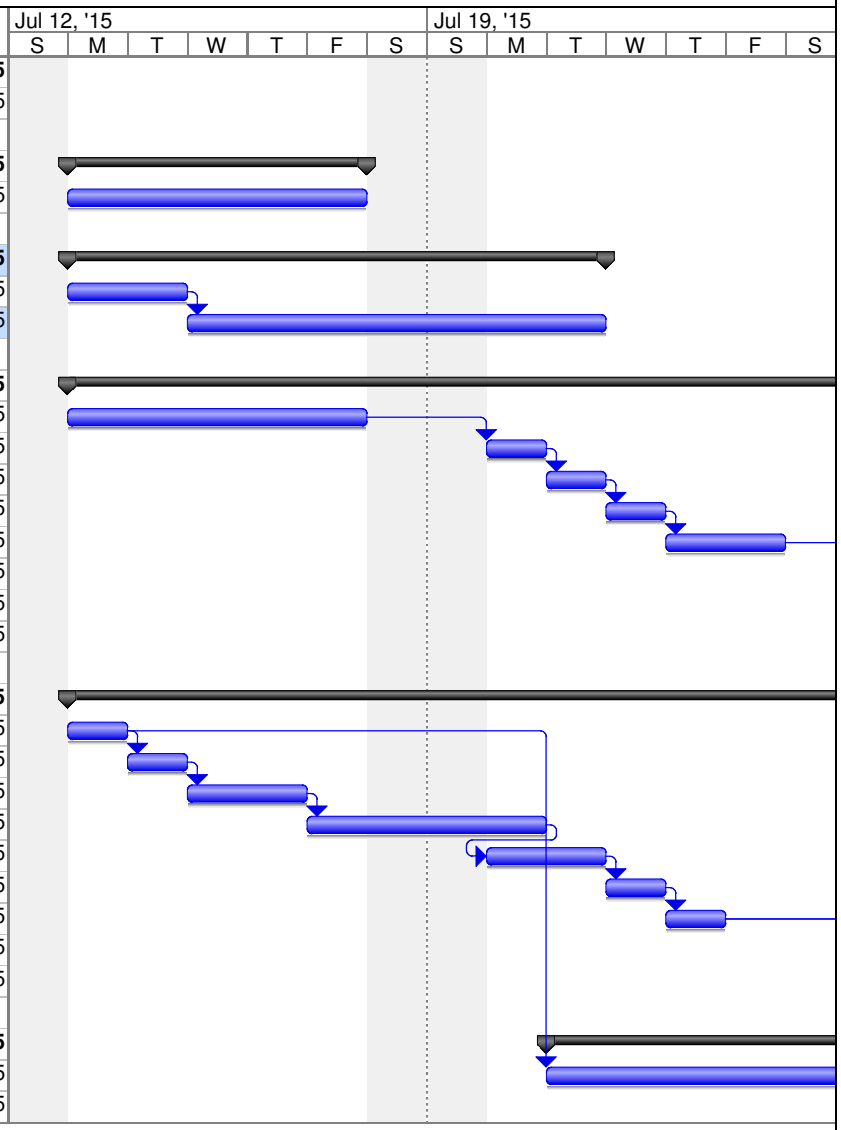

Project: 3wk look ahead 7-13-15
Date: Thu 7/9/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
7-13-2015

ID		Task Name	Duration	Start	Finish
35		Bottom Mat/Sleeves	2 days	Wed 8/5/15	Thu 8/6/15
36		Edgeform/Misc	2 days	Fri 8/7/15	Mon 8/10/15
37		Raised Slab Edge	2 days	Tue 8/11/15	Wed 8/12/15
38		Inspections	1 day	Tue 8/11/15	Tue 8/11/15
39		Pour	1 day	Wed 8/12/15	Wed 8/12/15
40		Stress/Strip	6 days	Mon 8/17/15	Mon 8/24/15
41					
42		**Wood Framing NW**	**14 days**	**Mon 8/3/15**	**Thu 8/20/15**
43		Layout Walls	1 day	Mon 8/3/15	Mon 8/3/15
44		Frame	5 days	Tue 8/4/15	Mon 8/10/15
45		TJI Joists	4 days	Tue 8/11/15	Fri 8/14/15
46		Deck	4 days	Mon 8/17/15	Thu 8/20/15

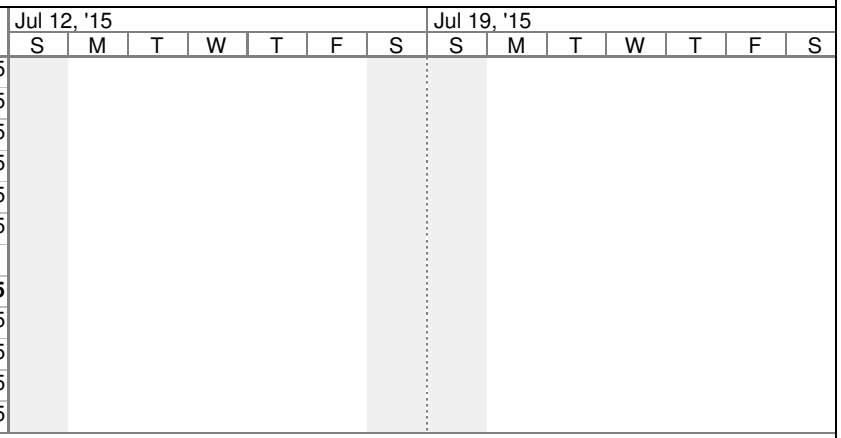

Project: 3wk look ahead 7-13-15
Date: Thu 7/9/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
7-13-2015

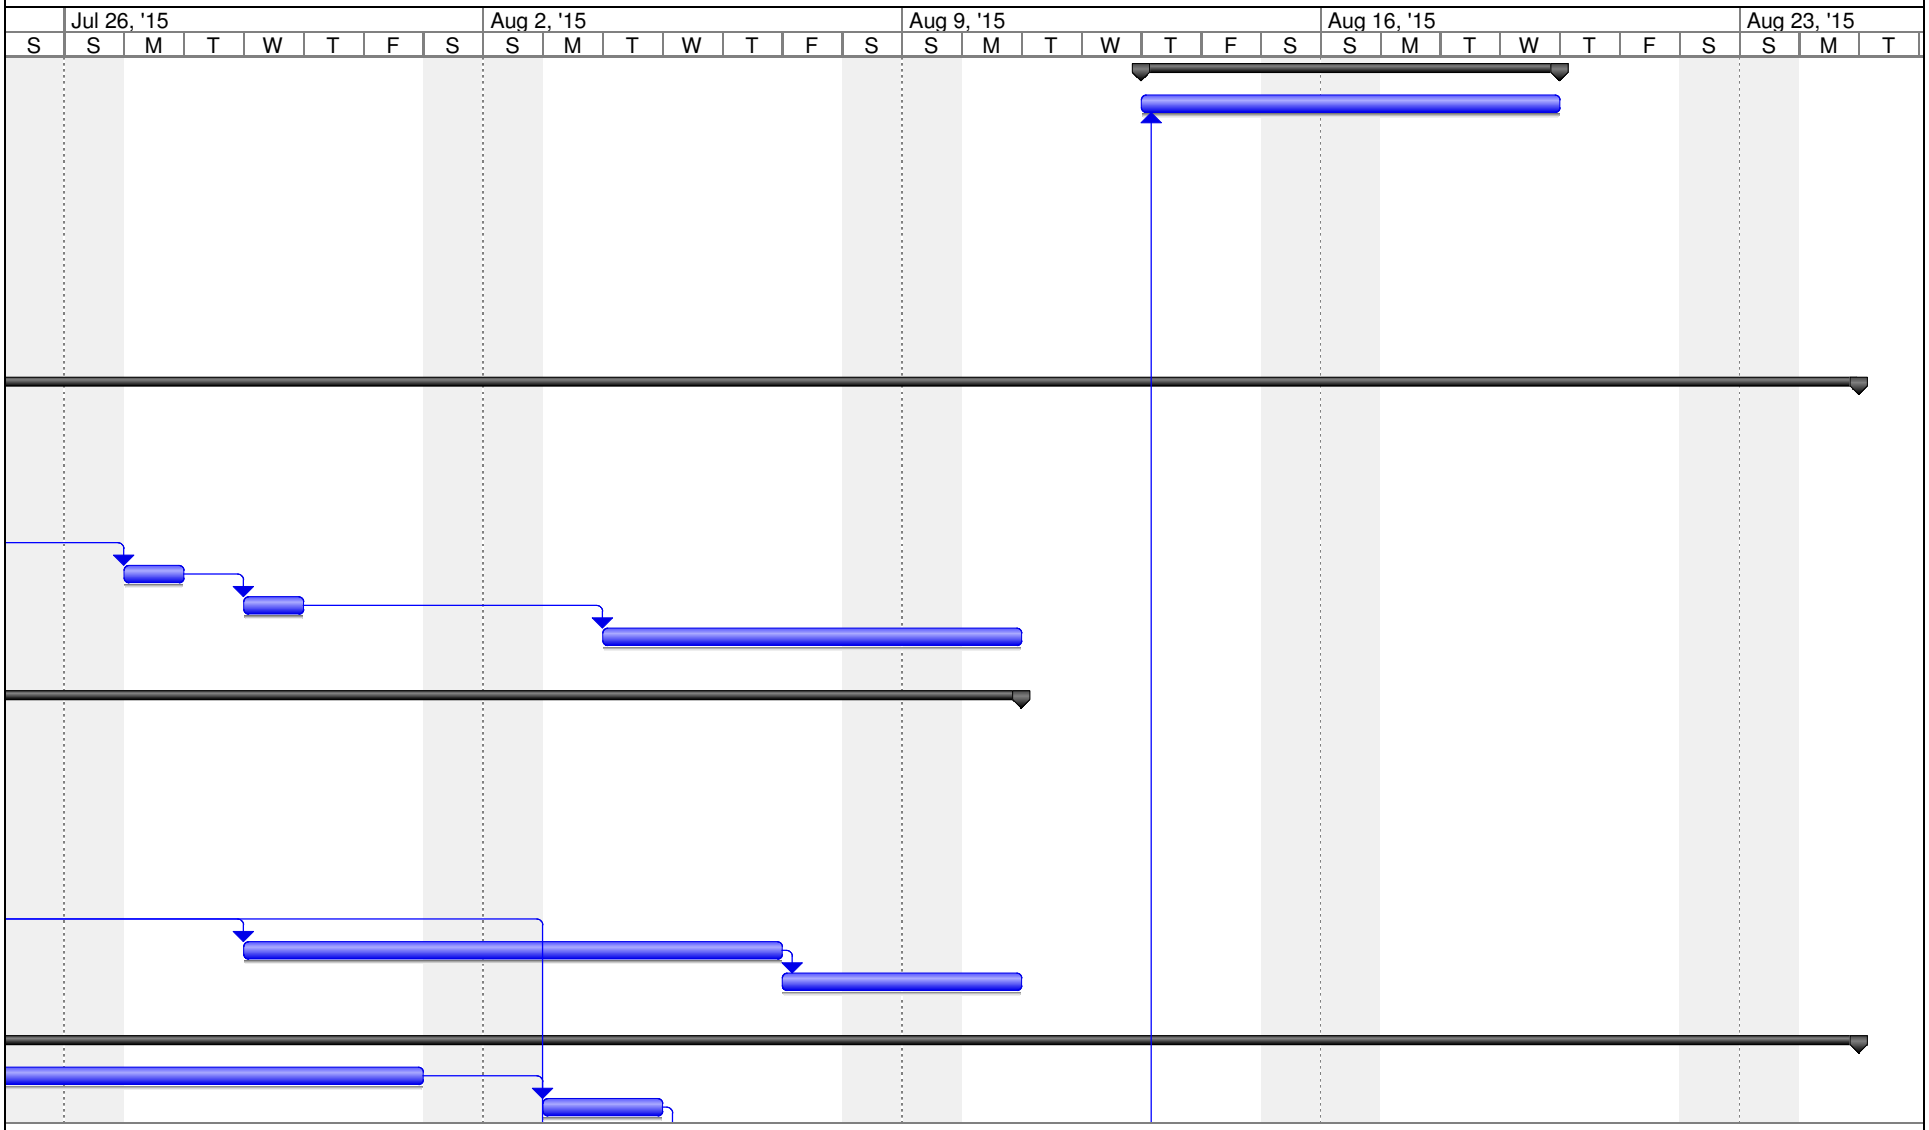

Project: 3wk look ahead 7-13-15
Date: Thu 7/9/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
7-13-2015

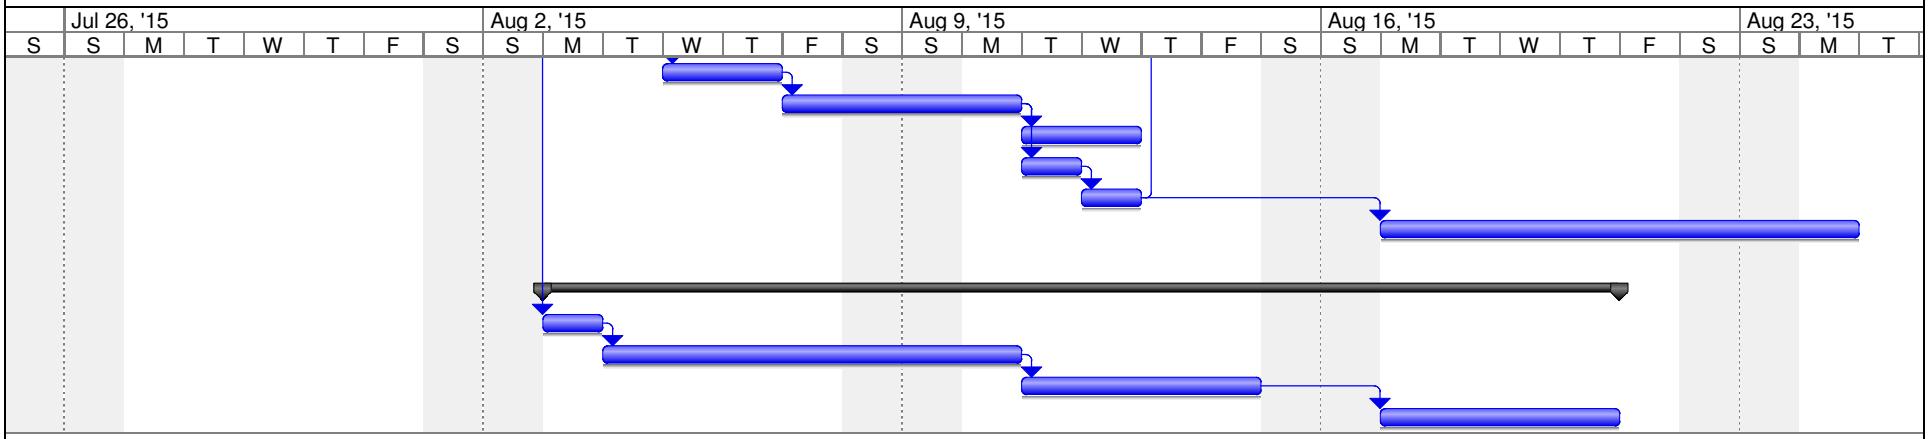

Project: 3wk look ahead 7-13-15
Date: Thu 7/9/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
