Hadley Mixed use
Legacy
3 wk Look ahead
7-20-2015

ID	Task Name	Duration	Start	Finish
1	**Instreet Utilities**	**5 days**	**Tue 7/28/15**	**Mon 8/3/15**
2	Sanitary South	5 days	Tue 7/28/15	Mon 8/3/15
3	PSE In Street Conduit	5 days	Tue 7/28/15	Mon 8/3/15
4				
5	**CIP Concrete**	**7 days**	**Mon 7/20/15**	**Tue 7/28/15**
6	F&P Remaining L1 South Col's Retail	2 days	Mon 7/20/15	Tue 7/21/15
7	F&P NW Placing Boom Blockouts	5 days	Wed 7/22/15	Tue 7/28/15
8				
9	**Level 2 PT Southeast**	**26 days**	**Mon 7/20/15**	**Mon 8/24/15**
10	Layout/Sleeves	1 day	Mon 7/20/15	Mon 7/20/15
11	Bottom Mat	1 day	Tue 7/21/15	Tue 7/21/15
12	Edgeform	1 day	Wed 7/22/15	Wed 7/22/15
13	Profile Tendons	2 days	Thu 7/23/15	Fri 7/24/15
14	Inspections	1 day	Mon 7/27/15	Mon 7/27/15
15	Pour	1 day	Wed 7/29/15	Wed 7/29/15
16	Strip/Reshore	5 days	Tue 8/4/15	Mon 8/10/15
17				
18	**Level 3 PT NE**	**16 days**	**Mon 7/20/15**	**Mon 8/10/15**
19	Raised Slab Edge/Blockouts	2 days	Mon 7/20/15	Tue 7/21/15
20	Inspections	1 day	Wed 7/22/15	Wed 7/22/15
21	Pour	1 day	Thu 7/23/15	Thu 7/23/15
22	Stress/Strip	7 days	Wed 7/29/15	Thu 8/6/15
23	Remove Reshores North	2 days	Fri 8/7/15	Mon 8/10/15
24				
25	**Level 3 PT SW**	**26 days**	**Mon 7/20/15**	**Mon 8/24/15**
26	Shore/Deck	10 days	Mon 7/20/15	Fri 7/31/15
27	Layout/Sleeves	2 days	Mon 8/3/15	Tue 8/4/15
28	Bottom Mat/Sleeves	2 days	Wed 8/5/15	Thu 8/6/15
29	Edgeform/Misc	2 days	Fri 8/7/15	Mon 8/10/15
30	Raised Slab Edge	2 days	Tue 8/11/15	Wed 8/12/15
31	Inspections	1 day	Tue 8/11/15	Tue 8/11/15
32	Pour	1 day	Wed 8/12/15	Wed 8/12/15
33	Stress/Strip	6 days	Mon 8/17/15	Mon 8/24/15
34				

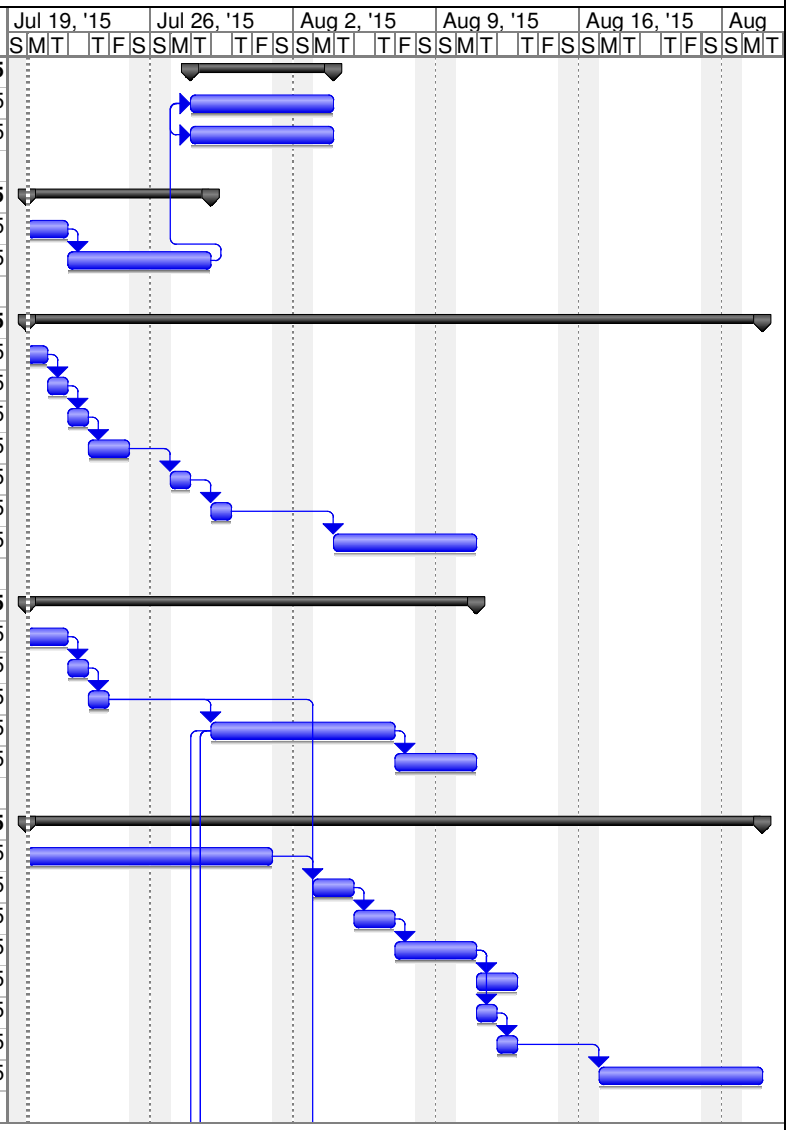

Project: 3wk look ahead 7-20-15
Date: Mon 7/20/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
7-20-2015

ID		Task Name	Duration	Start	Finish
35		**Wood Framing NW**	**14 days**	**Mon 8/3/15**	**Thu 8/20/15**
36		Layout Walls	1 day	Mon 8/3/15	Mon 8/3/15
37		Frame	5 days	Tue 8/4/15	Mon 8/10/15
38		TJI Joists	4 days	Tue 8/11/15	Fri 8/14/15
39		Deck	4 days	Mon 8/17/15	Thu 8/20/15
40					
41		**Struct Steel**	**3 days**	**Wed 7/29/15**	**Fri 7/31/15**
42		Set Stair 1 LP to L3	3 days	Wed 7/29/15	Fri 7/31/15
43					
44		**Fire Sprinkler**	**2 days**	**Fri 7/31/15**	**Mon 8/3/15**
45		FDC Standpipe to L3	2 days	Fri 7/31/15	Mon 8/3/15
46					
47		**Level P**	**5 days**	**Fri 7/31/15**	**Thu 8/6/15**
48		MEP RI LP	5 days	Fri 7/31/15	Thu 8/6/15

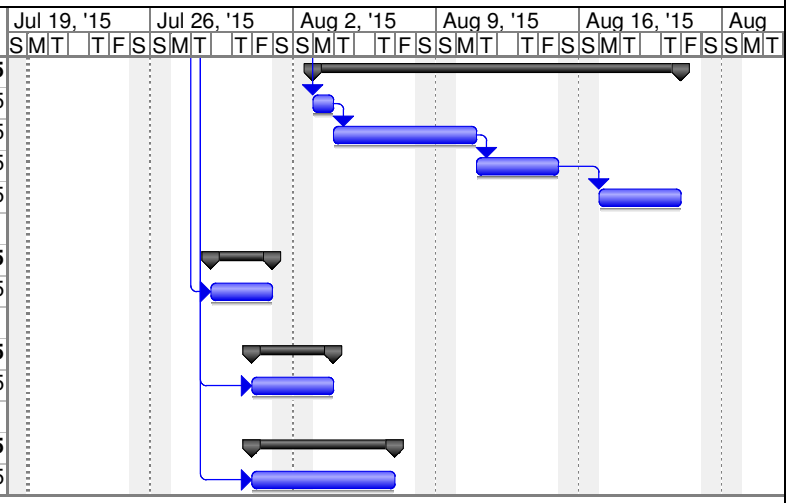

Project: 3wk look ahead 7-20-15
Date: Mon 7/20/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
