Hadley Mixed use
Legacy
3 wk Look ahead
7-20-2015

ID		Task Name	Duration	Start	Finish
1		**Instreet Utilities**	**5 days**	**Mon 8/3/15**	**Fri 8/7/15**
2		Sanitary South	2 days	Tue 8/4/15	Wed 8/5/15
3		PSE In Street Conduit	5 days	Mon 8/3/15	Fri 8/7/15
4					
5		**CIP Concrete**	**7 days**	**Mon 7/27/15**	**Tue 8/4/15**
6		F&P Remaining L1 South Col's Retail	2 days	Mon 7/27/15	Tue 7/28/15
7		F&P NW Placing Boom Blockouts	5 days	Wed 7/29/15	Tue 8/4/15
8					
9		**Level 2 PT Southeast**	**23 days**	**Mon 7/27/15**	**Wed 8/26/15**
10		Inspections	1 day	Mon 7/27/15	Mon 7/27/15
11		Pour	1 day	Wed 7/29/15	Wed 7/29/15
12		Strip/Reshore	5 days	Tue 8/4/15	Mon 8/10/15
13					
14		**Level 3 PT NE**	**9 days**	**Mon 7/27/15**	**Thu 8/6/15**
15		Stress/Strip	7 days	Mon 7/27/15	Tue 8/4/15
16		Remove Reshores North	2 days	Wed 8/5/15	Thu 8/6/15
17					
18		**Level 3 PT SW**	**23 days**	**Mon 7/27/15**	**Wed 8/26/15**
19		Shore/Deck	7 days	Mon 7/27/15	Tue 8/4/15
20		Layout/Sleeves	2 days	Wed 8/5/15	Thu 8/6/15
21		Bottom Mat/Sleeves	2 days	Fri 8/7/15	Mon 8/10/15
22		Edgeform/Misc	2 days	Tue 8/11/15	Wed 8/12/15
23		Raised Slab Edge	2 days	Thu 8/13/15	Fri 8/14/15
24		Inspections	1 day	Thu 8/13/15	Thu 8/13/15
25		Pour	1 day	Fri 8/14/15	Fri 8/14/15
26		Stress/Strip	6 days	Wed 8/19/15	Wed 8/26/15
27					
28		**Wood Framing NW**	**14 days**	**Mon 8/3/15**	**Thu 8/20/15**
29		Layout Walls	1 day	Mon 8/3/15	Mon 8/3/15
30		Frame	5 days	Tue 8/4/15	Mon 8/10/15
31		TJI Joists	4 days	Tue 8/11/15	Fri 8/14/15
32		Deck	4 days	Mon 8/17/15	Thu 8/20/15
33					
34		**Struct Steel**	**3 days**	**Mon 8/3/15**	**Wed 8/5/15**

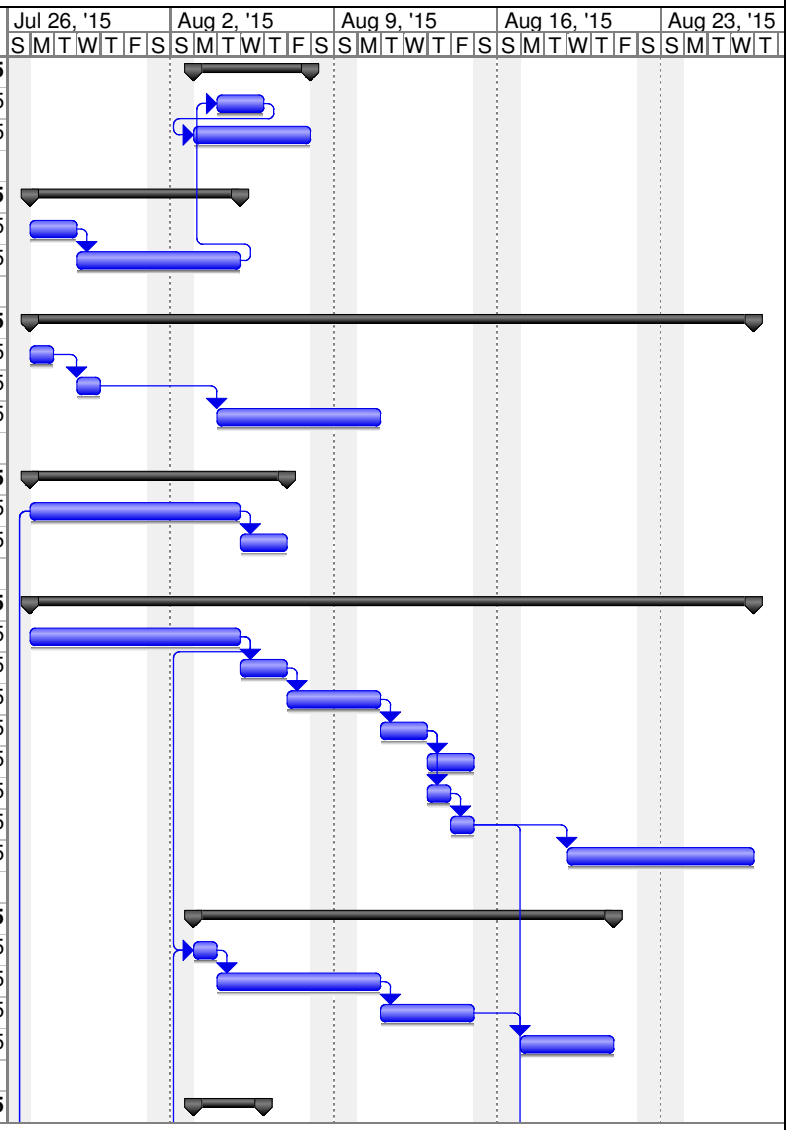

Project: 3wk look ahead 7-27-15
Date: Fri 7/24/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
7-20-2015

ID		Task Name	Duration	Start	Finish
35		Set Stair 1 LP to L3	3 days	Mon 8/3/15	Wed 8/5/15
36					
37		**Fire Sprinkler**	**2 days**	**Wed 7/29/15**	**Thu 7/30/15**
38		FDC Standpipe to L3	2 days	Wed 7/29/15	Thu 7/30/15
39					
40		**Level P**	**5 days**	**Fri 7/31/15**	**Thu 8/6/15**
41		MEP RI LP	5 days	Fri 7/31/15	Thu 8/6/15
42					
43		**Subgrade**	**4 days**	**Mon 8/17/15**	**Thu 8/20/15**
44		West exterior	4 days	Mon 8/17/15	Thu 8/20/15
45					
46		**Shoring**	**4 days**	**Fri 8/21/15**	**Wed 8/26/15**
47		Drill/Set Addl. Piles	4 days	Fri 8/21/15	Wed 8/26/15

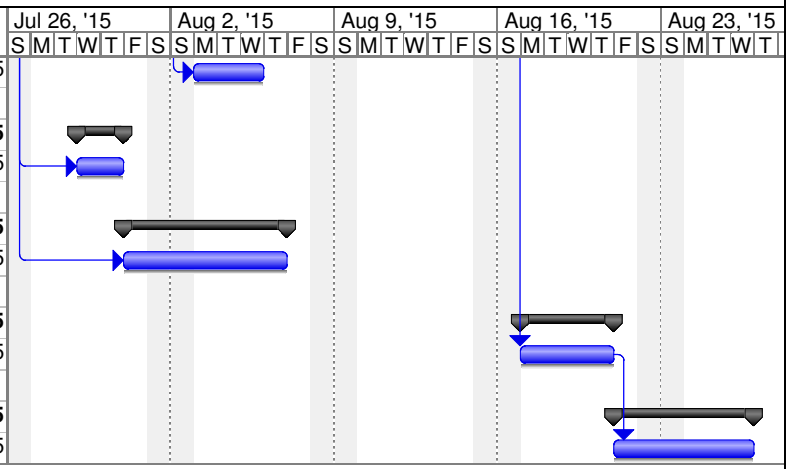

Project: 3wk look ahead 7-27-15
Date: Fri 7/24/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
