Hadley Mixed use
Legacy
3 wk Look ahead
8-10-2015

ID		Task Name	Duration	Start	Finish
1		**Instreet Utilities**	**5 days**	**Mon 8/10/15**	**Fri 8/14/15**
2		PSE In Street Conduit	5 days	Mon 8/10/15	Fri 8/14/15
3					
4		**CIP Concrete**	**5 days**	**Mon 8/10/15**	**Fri 8/14/15**
5		F&P Remaining L1 South Col's Retail	2 days	Mon 8/10/15	Tue 8/11/15
6		F&P NW Placing Boom Blockouts	5 days	Mon 8/10/15	Fri 8/14/15
7					
8		**Level 2 PT Southeast**	**5 days**	**Mon 8/10/15**	**Fri 8/14/15**
9		Strip	5 days	Mon 8/10/15	Fri 8/14/15
10					
11		**Level 3 PT NE**	**2 days**	**Mon 8/10/15**	**Tue 8/11/15**
12		Strip	2 days	Mon 8/10/15	Tue 8/11/15
13		Remove Reshores North	2 days	Mon 8/10/15	Tue 8/11/15
14					
15		**Level 3 PT SW**	**11 days**	**Mon 8/10/15**	**Mon 8/24/15**
16		Edgeform/Misc	1 day	Mon 8/10/15	Mon 8/10/15
17		Raised Slab Edge	1 day	Tue 8/11/15	Tue 8/11/15
18		Inspections	2 days	Wed 8/12/15	Thu 8/13/15
19		Pour	1 day	Fri 8/14/15	Fri 8/14/15
20		Stress/Strip	6 days	Mon 8/17/15	Mon 8/24/15
21					
22		**Level 3 SE PT**	**29 days**	**Mon 8/10/15**	**Thu 9/17/15**
23		Shore/Deck	8 days	Mon 8/10/15	Wed 8/19/15
24		Layout/Sleeves	2 days	Thu 8/20/15	Fri 8/21/15
25		Rebar/PT	3 days	Mon 8/24/15	Wed 8/26/15
26		Edgeform/Misc	2 days	Thu 8/27/15	Fri 8/28/15
27		Raised Slab edge	2 days	Mon 8/31/15	Tue 9/1/15
28		Inspections	1 day	Wed 9/2/15	Wed 9/2/15
29		Pour	1 day	Fri 9/4/15	Fri 9/4/15
30		Stress/Strip	8 days	Tue 9/8/15	Thu 9/17/15
31					
32		**Wood Framing L3**	**16 days**	**Mon 8/10/15**	**Mon 8/31/15**
33		**Northwest**	**12 days**	**Mon 8/10/15**	**Tue 8/25/15**
34		Frame	5 days	Mon 8/10/15	Fri 8/14/15

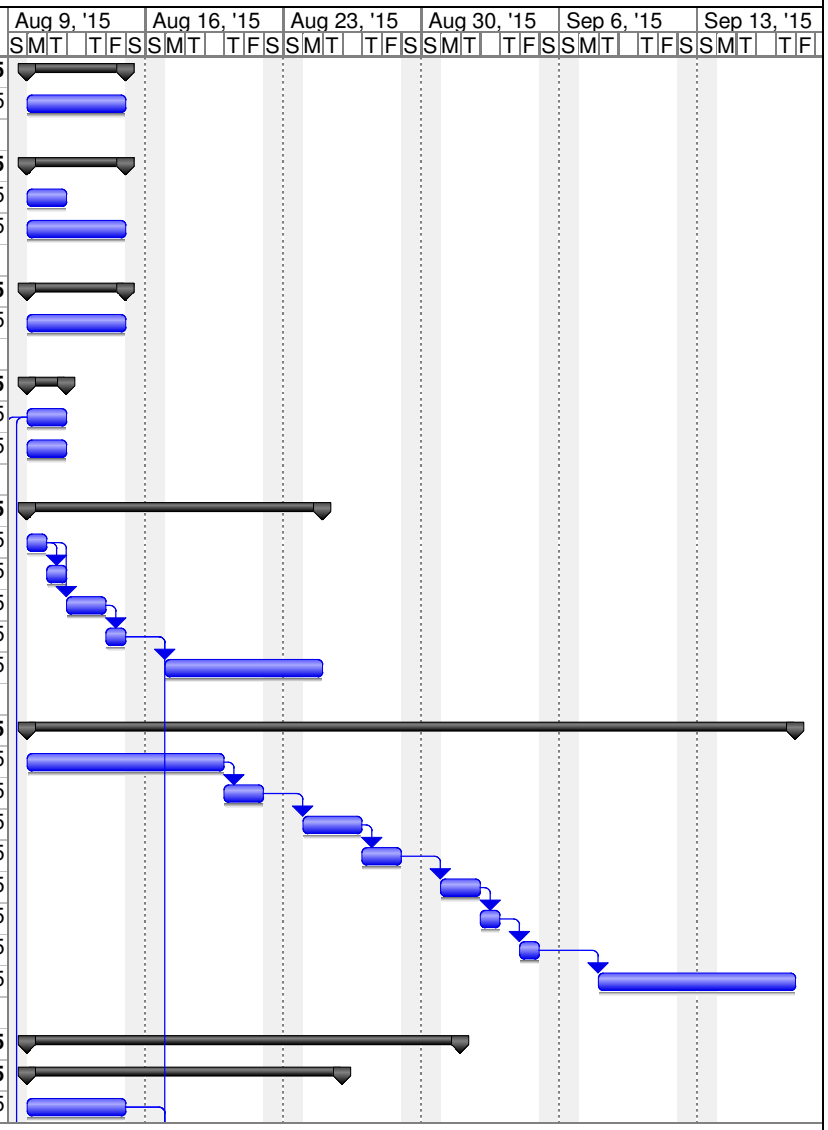

Project: 3wk look ahead 8-10-15
Date: Fri 8/7/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
8-10-2015

ID		Task Name	Duration	Start	Finish
35		TJI Joists	5 days	Mon 8/17/15	Fri 8/21/15
36		Deck	4 days	Thu 8/20/15	Tue 8/25/15
37		**Northeast**	**11 days**	**Mon 8/17/15**	**Mon 8/31/15**
38		Frame	5 days	Mon 8/17/15	Fri 8/21/15
39		TJI Joist	4 days	Mon 8/24/15	Thu 8/27/15
40		Deck	4 days	Wed 8/26/15	Mon 8/31/15
41					
42		**Fire Sprinkler**	**10 days**	**Tue 8/11/15**	**Mon 8/24/15**
43		Mains North Garage	10 days	Tue 8/11/15	Mon 8/24/15
44					
45		**Level P**	**15 days**	**Mon 8/10/15**	**Fri 8/28/15**
46		MEP RI LP/ 1	15 days	Mon 8/10/15	Fri 8/28/15
47					
48		**Subgrade**	**4 days**	**Mon 8/17/15**	**Thu 8/20/15**
49		West exterior	4 days	Mon 8/17/15	Thu 8/20/15
50					
51		**Shoring**	**5 days**	**Fri 8/21/15**	**Thu 8/27/15**
52		Drill/Set Addl. Piles	4 days	Fri 8/21/15	Wed 8/26/15
53		Lagging	2 days	Wed 8/26/15	Thu 8/27/15

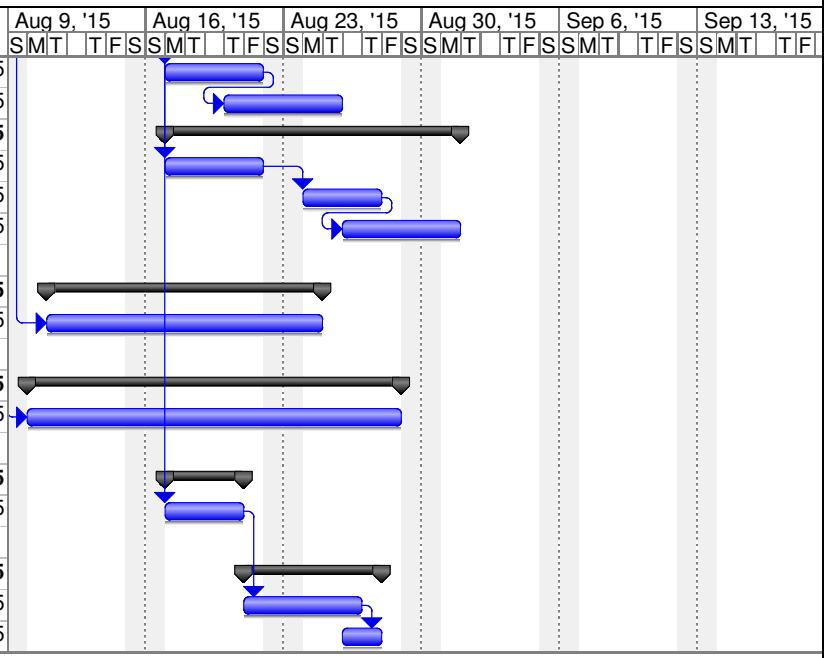

Project: 3wk look ahead 8-10-15
Date: Fri 8/7/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
