Hadley Mixed use
Legacy
3 wk Look ahead
8-17-2015

| ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|
| 1 | **CIP Concrete** | **10 days** | **Mon 8/17/15** | **Fri 8/28/15** |
| 2 | F&P Remaining L1 South Col's Retail | 2 days | Mon 8/17/15 | Tue 8/18/15 |
| 3 | F&P NW Placing Boom Blockouts | 10 days | Mon 8/17/15 | Fri 8/28/15 |
| 4 | Shotcrete Southwest | 1 day | Fri 8/28/15 | Fri 8/28/15 |
| 5 | | | | |
| 6 | **Level 3 PT SW** | **9 days** | **Mon 8/17/15** | **Thu 8/27/15** |
| 7 | Strip Edgeform/Misc | 1 day | Mon 8/17/15 | Mon 8/17/15 |
| 8 | Stress/Strip | 8 days | Tue 8/18/15 | Thu 8/27/15 |
| 9 | | | | |
| 10 | **Level 3 SE PT** | **24 days** | **Mon 8/17/15** | **Thu 9/17/15** |
| 11 | Shore/Deck | 5 days | Mon 8/17/15 | Fri 8/21/15 |
| 12 | Layout/Sleeves | 2 days | Mon 8/24/15 | Tue 8/25/15 |
| 13 | Rebar/PT | 3 days | Wed 8/26/15 | Fri 8/28/15 |
| 14 | Edgeform/Misc | 2 days | Mon 8/31/15 | Tue 9/1/15 |
| 15 | Raised Slab edge | 2 days | Wed 9/2/15 | Thu 9/3/15 |
| 16 | Inspections | 1 day | Thu 9/3/15 | Thu 9/3/15 |
| 17 | Pour | 1 day | Fri 9/4/15 | Fri 9/4/15 |
| 18 | Stress/Strip | 8 days | Tue 9/8/15 | Thu 9/17/15 |
| 19 | | | | |
| 20 | **Wood Framing L3** | **16 days** | **Mon 8/17/15** | **Mon 9/7/15** |
| 21 | **North** | **11 days** | **Mon 8/17/15** | **Mon 8/31/15** |
| 22 | Frame | 3 days | Mon 8/17/15 | Wed 8/19/15 |
| 23 | TJI Joists | 6 days | Thu 8/20/15 | Thu 8/27/15 |
| 24 | Deck | 4 days | Wed 8/26/15 | Mon 8/31/15 |
| 25 | **Southwest** | **13 days** | **Thu 8/20/15** | **Mon 9/7/15** |
| 26 | Frame | 6 days | Thu 8/20/15 | Thu 8/27/15 |
| 27 | TJI/Joist | 5 days | Fri 8/28/15 | Thu 9/3/15 |
| 28 | Deck | 4 days | Wed 9/2/15 | Mon 9/7/15 |
| 29 | | | | |
| 30 | **Level 4 North** | **10 days** | **Fri 8/28/15** | **Thu 9/10/15** |
| 31 | Frame | 10 days | Fri 8/28/15 | Thu 9/10/15 |
| 32 | | | | |
| 33 | **Fire Sprinkler** | **10 days** | **Mon 8/17/15** | **Fri 8/28/15** |
| 34 | Mains North Garage | 10 days | Mon 8/17/15 | Fri 8/28/15 |

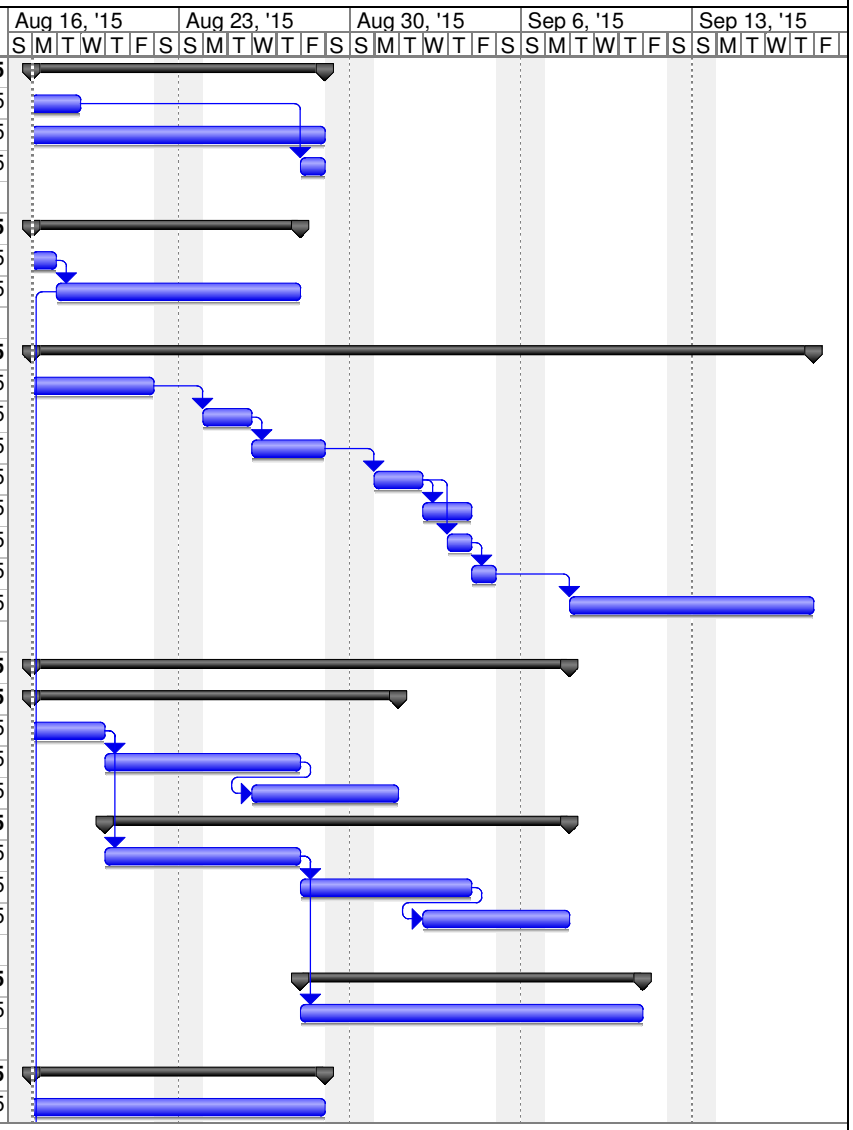


Project: 3wk look ahead 8-17-15
Date: Mon 8/17/15

| | | | | | |
|---|---|---|---|---|---|
| Task | | Milestone | | External Tasks | |
| Split | | Summary | | External Milestone | |
| Progress | | Project Summary | | Deadline | |

Hadley Mixed use
Legacy
3 wk Look ahead
8-17-2015

| ID | | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 35 | | | | | |
| 36 | | **Garage** | **15 days** | **Mon 8/17/15** | **Fri 9/4/15** |
| 37 | | MEP RI LP/ 1 | 15 days | Mon 8/17/15 | Fri 9/4/15 |
| 38 | | | | | |
| 39 | | **Waterproofing** | **4 days** | **Tue 8/18/15** | **Fri 8/21/15** |
| 40 | | West wall | 1 day | Tue 8/18/15 | Tue 8/18/15 |
| 41 | | Blockouts/Tiebacks | 3 days | Wed 8/19/15 | Fri 8/21/15 |
| 42 | | | | | |
| 43 | | **Subgrade** | **4 days** | **Wed 8/19/15** | **Mon 8/24/15** |
| 44 | | West exterior | 4 days | Wed 8/19/15 | Mon 8/24/15 |
| 45 | | | | | |
| 46 | | **Shoring** | **11 days** | **Mon 8/17/15** | **Mon 8/31/15** |
| 47 | | Remove Horz Braces | 1 day | Mon 8/17/15 | Mon 8/17/15 |
| 48 | | Destress Tie-backs | 2 days | Tue 8/18/15 | Wed 8/19/15 |
| 49 | | Weld Shoring Plates | 2 days | Thu 8/20/15 | Fri 8/21/15 |
| 50 | | Drill/Set Additional Piles | 4 days | Mon 8/24/15 | Thu 8/27/15 |
| 51 | | Lagging | 2 days | Fri 8/28/15 | Mon 8/31/15 |

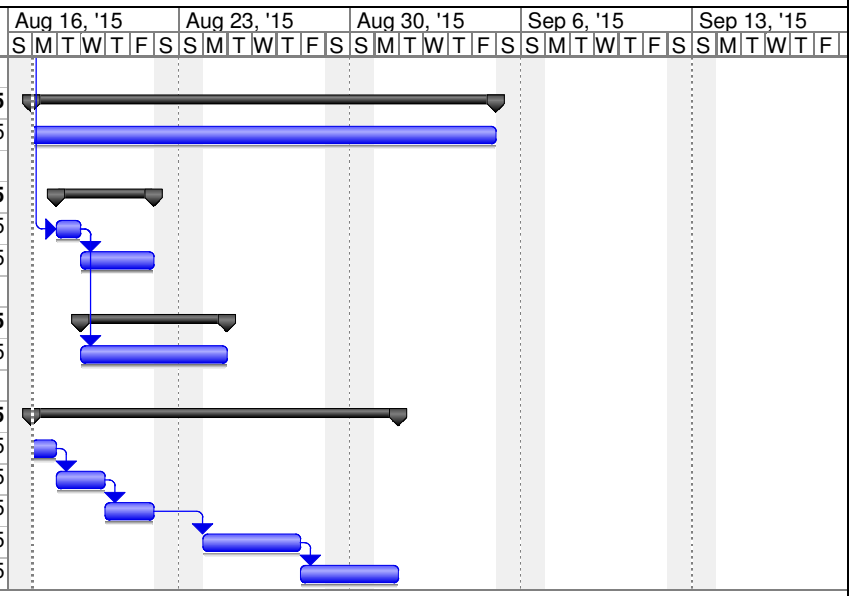


Project: 3wk look ahead 8-17-15
Date: Mon 8/17/15

| | | | | | |
|---|---|---|---|---|---|
| Task | | Milestone | | External Tasks | |
| Split | | Summary | | External Milestone | |
| Progress | | Project Summary | | Deadline | |
